




2023 BOND

MAJOR PROJECTS UPDATE

NOVEMBER 2024



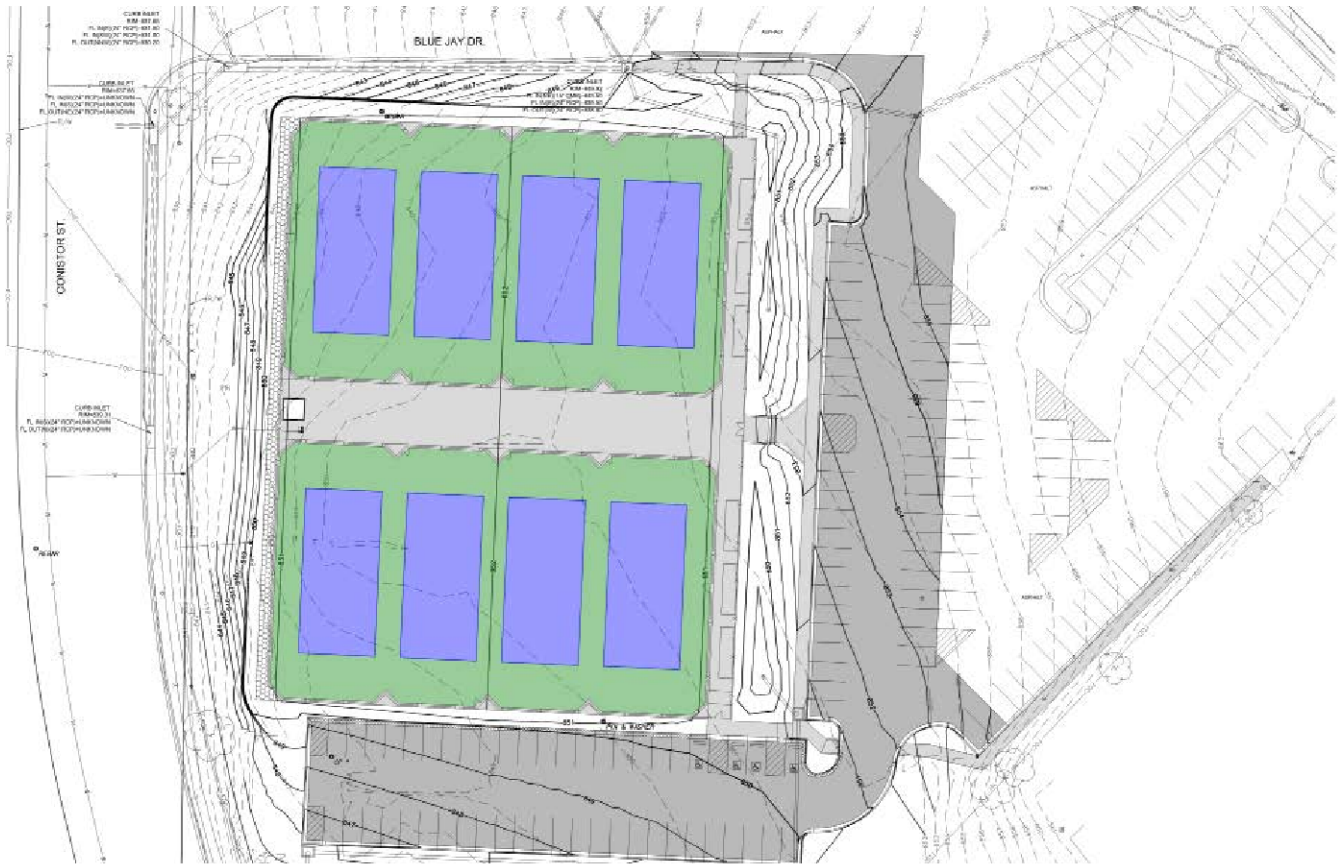

Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

Construction Start: Spring 2023

Construction Complete: Fall 2023

**WEEKLY
PROGRESS
REPORT**

Tennis Courts 11/13/2023

Liberty Public Schools



PROJECT STATUS

- Courts Substantially Complete
- Turned Over 10/31
- Final Punch List Items Being Completed

UPCOMING

Project Completion October 2023



North Courts Looking West



North Courts Looking Southwest



East Concourse Looking South



East Concourse Looking North


WEEKLY PROGRESS REPORT



South Courts Looking West



Center Spectator Concourse Looking West

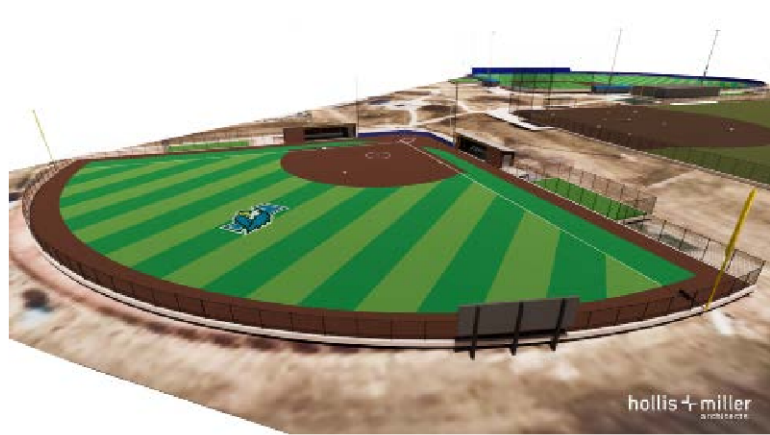

Liberty High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

Softball Field

- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

Construction Start: Fall 2023

Construction Complete: Summer 2024



Liberty North High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Construction Start: Fall 2023

Construction Complete: Summer 2024

**WEEKLY
PROGRESS
REPORT**

LPS Ball Fields 08/09/2024

Liberty Public Schools



PROJECT STATUS

- LNHS
- Punch List Completion
 - Final Inspection Passed

- LHS
- Punch List Completion
 - Retaining Wall Ongoing
 - Final Sod Ongoing

UPCOMING

- LHS
- City Inspection

Project Completion
Baseball March 2024/Softball May 2024



LHS - Overall Site



LHS - Overall Site



LNHS - Overall Site



LNHS - Overall Site



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

PROJECT STATUS

- South Valley MS - Upgrades Complete
- Discovery MS - Upgrades Complete
- EPiC Elementary - Upgrades Complete
- Liberty North High School - Upgrades Ongoing

UPCOMING

- Energy Inspections - All Four Schools
- Emergency LED Fixtures

Project Completion
December 2023




Liberty North HS



Liberty North HS



Liberty North HS

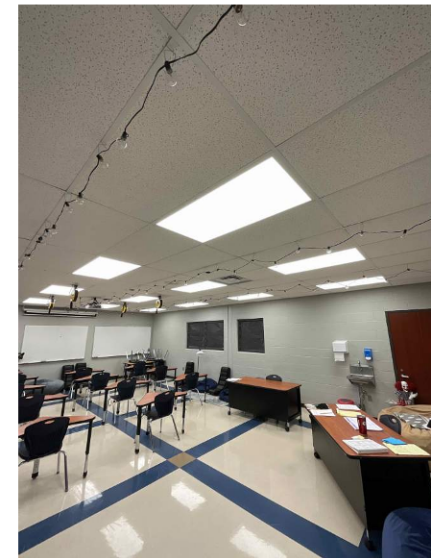

Liberty North HS

PROJECT STATUS

South Valley MS- Upgrades Complete

Discovery MS - Upgrades Complete


EPiC Elementary - Upgrades Complete

LNHS - Upgrades Ongoing


UPCOMING

Energy Inspections All Four Schools
Emergency LED Fixtures

Project Completion
December 2023

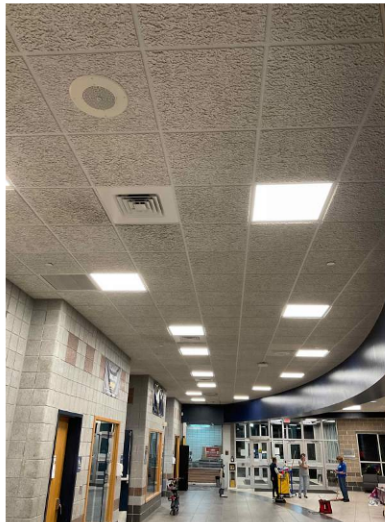


South Valley Middle School

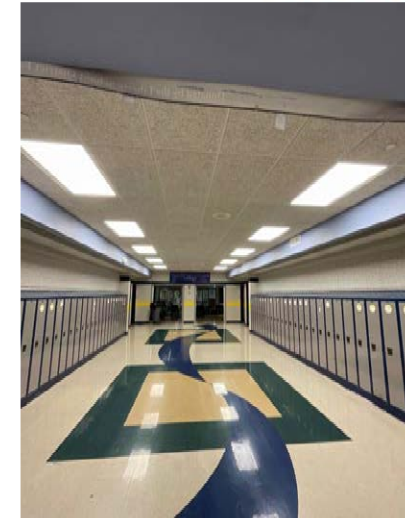

South Valley Middle School



Discovery Middle School

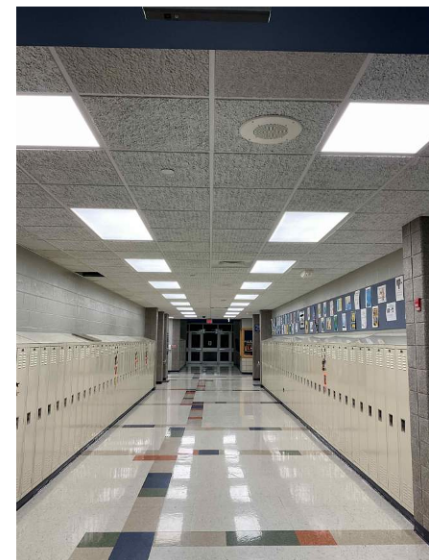

Discovery Middle School

WEEKLY PROGRESS REPORT



Epic Elementary



Epic Elementary



Liberty North High School




Liberty North High School



EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother's Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

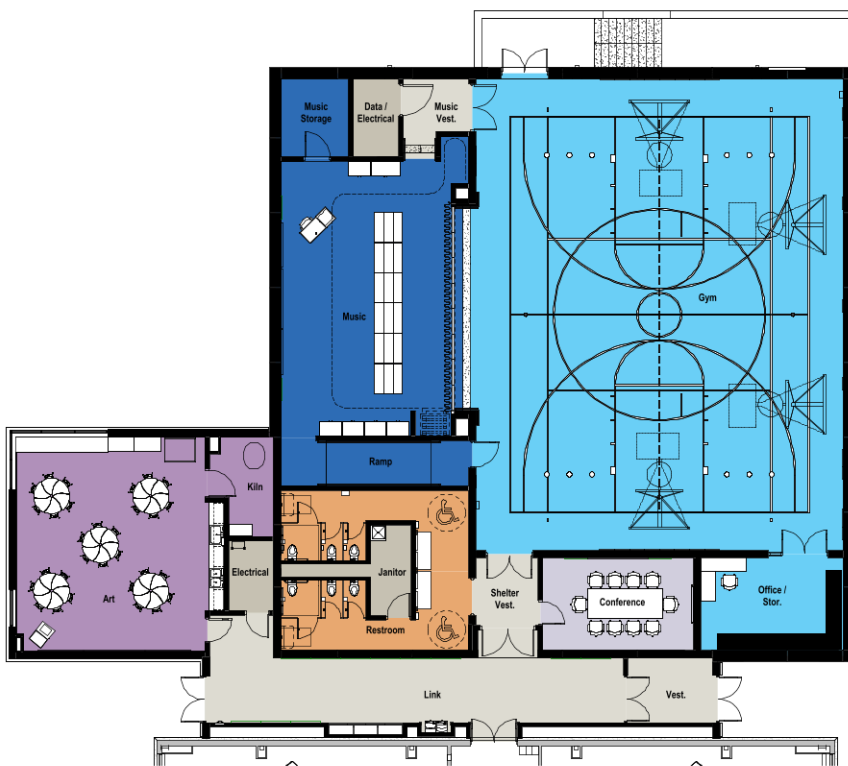

▲ Addition



▲ Renovation Area


PROJECT STATUS

- EPiC Elementary
- Roofing Complete
- Interior masonry complete
- Metal Panels on-going
- Interior pre-cast joint sealants on-going
- Fire sprinkler overhead rough in on going
- Ceiling tectum panels on-going
- North gym retaining wall on-going

UPCOMING

- EPiC Elementary
- Exterior pre-cast joint sealants
- Wall panels
- Painting
- Gym equipment install
- RTU hook up
- Art room ceiling grid


Project Completion
EPiC February 2025

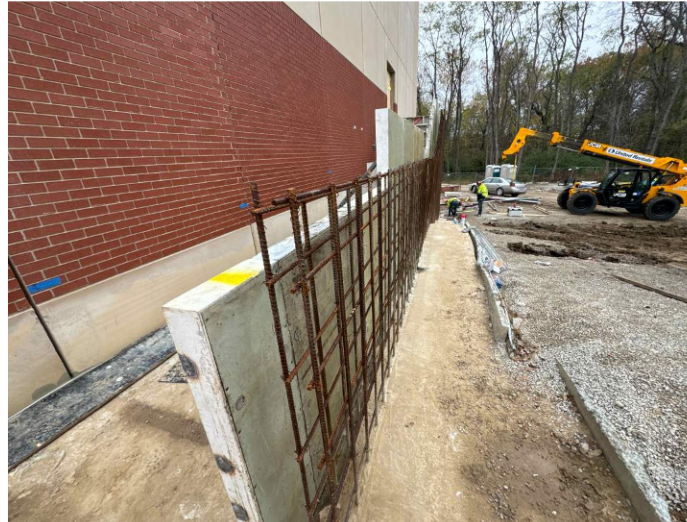

EPiC Elementary - N Retaining Wall



EPiC Elementary - RTU/Screens

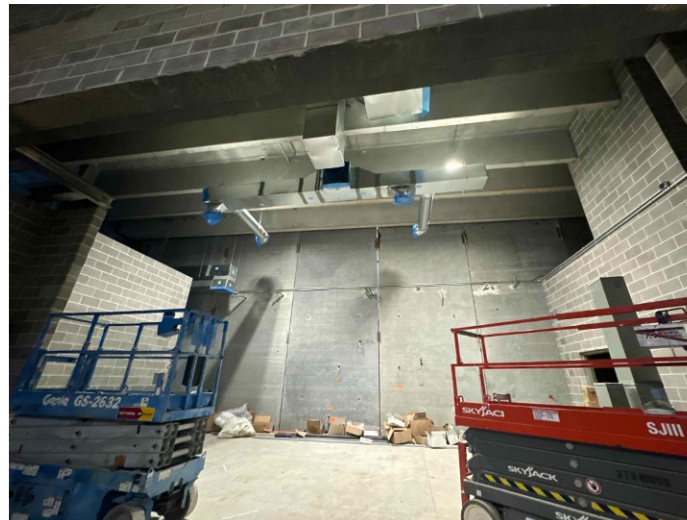

EPiC Elementary - Music Stage





EPiC Elementary - Aerial View



Discovery Middle School

- 11,000 square foot addition
 - ICC 500 rated shelter
 - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
 - Additional storage
- Projected Construction Schedule:
Spring 2024–Summer 2025

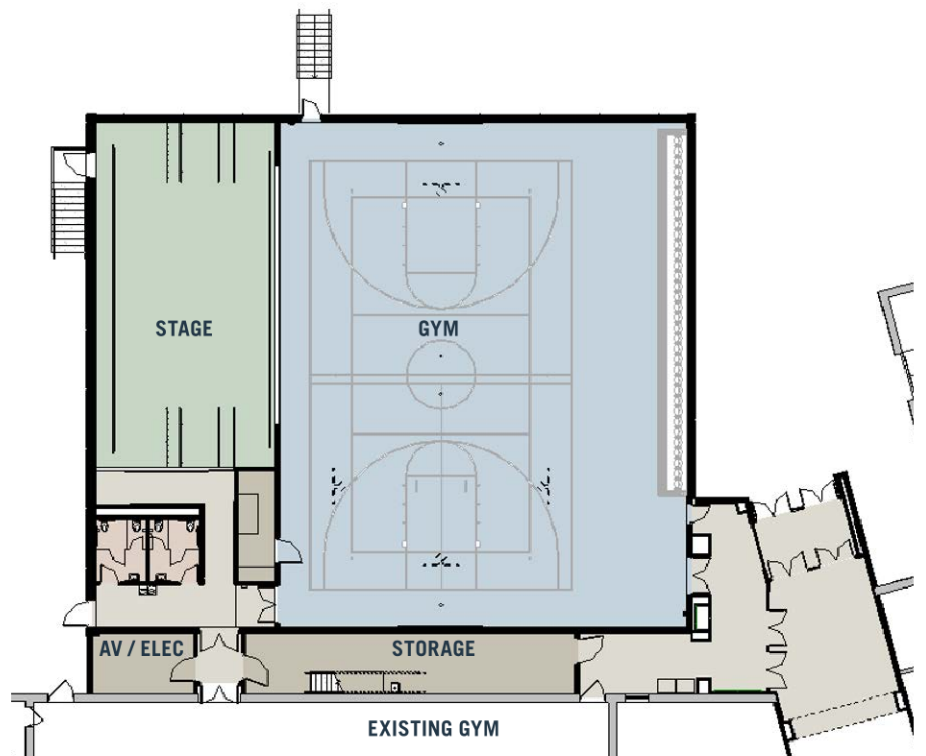

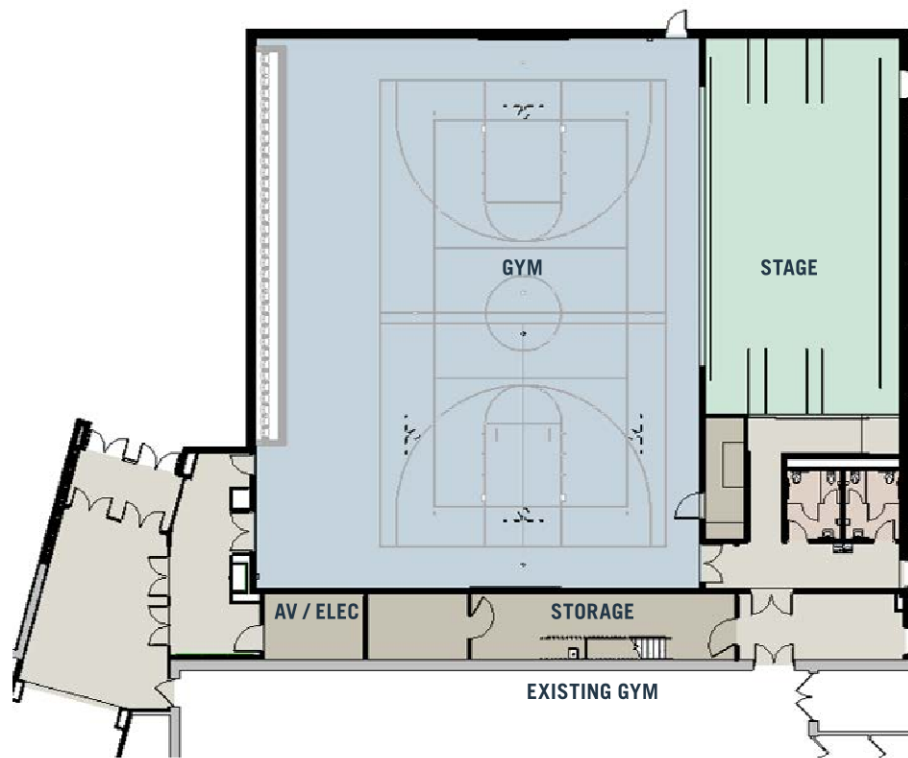

South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025

PROJECT STATUS

SVMS and DMS


- Gym slabs complete
- CMU MEP rough-in complete
- Interior CMU on-going
- Metal framing on-going
- MEP rough-in on-going
- SVMS roofing on-going
- Soffit framing on-going

UPCOMING

SVMS and DMS

- SOG at theater
- MEP overhead rough-in
- DMS roofing
- Extend existing utilities to addition
- Set remaining pre-cast panels
- Bathroom ceiling framing
- In wall rough-in

Project Completion
DMS&SVMS June 2025

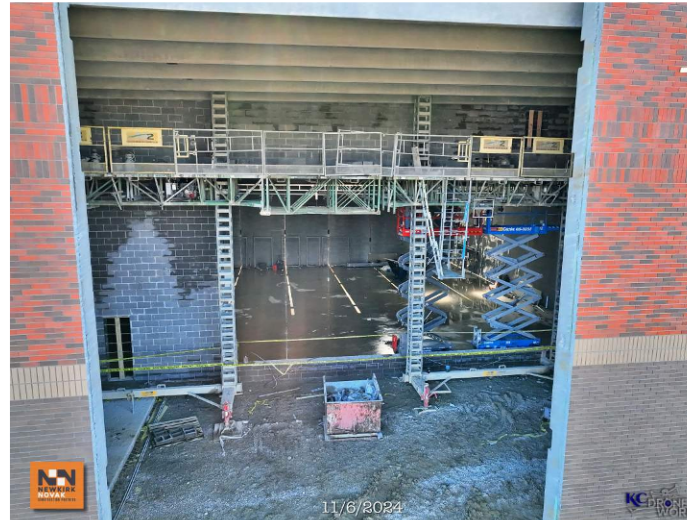

SVMS -CMU stage wall



SVMS/DMS Aerial



DMS - Gym SOG



DMS - Entry framing



hollis + miller



hollis + miller



hollis + miller



hollis + miller

Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule: Fall 2023–Spring 2025



▲ First Floor

11/8/24

PROJECT STATUS

- MEP rough ongoing
- In wall rough-in ongoing
- Drywall ongoing at warehouse wall
- RTU-1 removed and patched back
- Curb Installation at East lot
- Mezz handrail and gate complete

UPCOMING

- Freezer panel install ongoing
- Eat lost paving upcoming
- Drywall office space upcoming
- Generator installation
- Dock levelers & overhead doors upcoming.
- Canopy west framing ongoing

Project Completion
June 2025



East Lot Construction



Overall Site



Overall Site



Dry Storage Divider Wall



Dry Storage Divider Wall



Cooler/Freezer



Cooler/Freezer



Mezz rail/gate

Fine Arts
 Kid's Zone
 Technology
 Shared Amenities
 Building Systems
 Future Phase



District Technology Center

- Renovated workspace for District's Technology, Fine Arts, and Kid's Zone departments
- Shell space for future growth
- Minor exterior patch + repair improvements
- Projected Construction Schedule:
 Fall 2023 - Summer 2024

7/12/24

PROJECT STATUS

- District Technology Center:
- Completed Communications Install
 - Completed Interior Paint
 - Completed All Exterior Paint
 - Completed Floor Install
 - Completed Data Pod Install
 - Completed HVAC Equipment Install
 - Completed Landscaping/Fence Install
 - Completed Generator Install
 - Certificate of Occupancy - Received July 9th

UPCOMING

- District Technology Center:
- Complete Punchlist Work
 - Complete Furniture Move In
 - Server Switchover July 13th
 - Staff Move in July 16th

Project Completion July 2024



IT Reception



Exterior



Kid's Zone Open Office



Fine Arts Open Office



Fine Arts Workshop



Restrooms



Breakroom



Data Pod Install



Exterior



Medium Conference Room



Kid's Zone Storage




IT Open Office



Heritage Middle School

- 39,000 square feet academic renovation
- Grade level neighborhoods with flex collaboration spaces
 - Integrated SPED resources
 - Renovated cafeteria & scramble
 - Restroom renovations
- Exterior masonry repair & window replacement
 - Elevator replacement
- Projected Construction Schedule: Spring 2024–Fall 2025

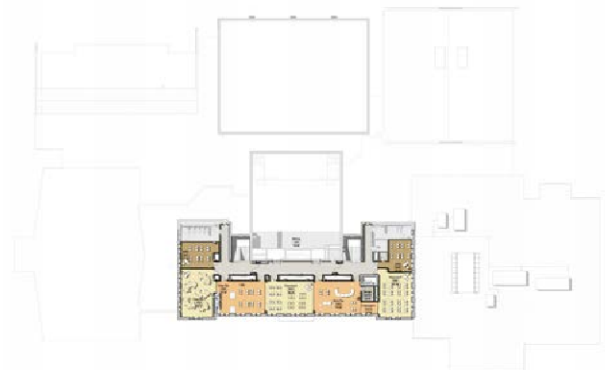

LEVEL 3



LEVEL 2



LEVEL 1



LEVEL 0

11/8/24

PROJECT STATUS

Heritage Middle School

1964 Wing:

- Completed Drywall Install/Finish
- Completed Casework Install
- Continued Paint
- Completed Storefront Install
- Completed Tile Install
- Began Ceiling Tile Install
- Continued MEP Trimout and Fixture Install
- Began Floor Preparation

UPCOMING

Heritage Middle School

1964 Wing:

- Complete Paint
- Complete Ceiling Grid Install
- Complete Tile Install
- Complete Exterior Window Installation
- Complete MEP Trimout
- Begin Flooring Install
- Begin Wall Paneling Install
- Complete Wheelchair Lift Install
- Complete Specialty Finish Install

Projected Completion; December 2024



1964 (Area A) Progress



1964 (Area A) Progress



1964 (Area A) Progress



1964 (Area A) Progress



1964 (Area A) Progress




1964 (Area A) Progress



1964 (Area A) Progress



1964 (Area A) Progress

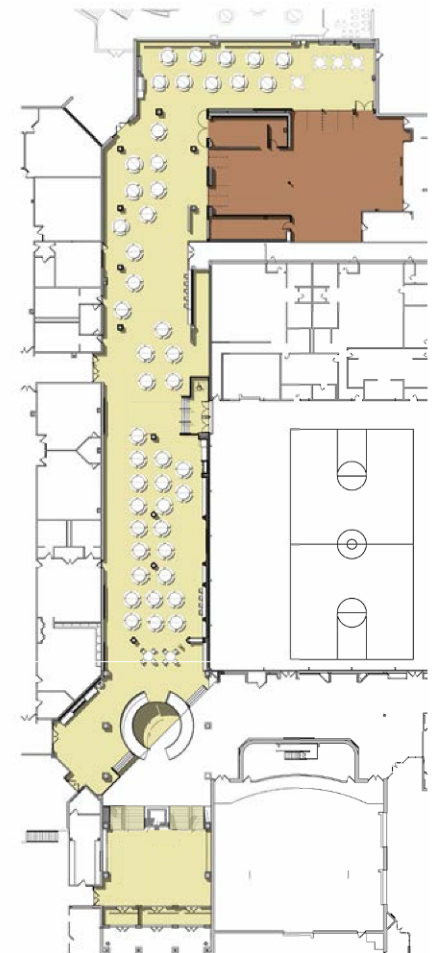

PHASE 2

Liberty High School

- Square footage: 40,800 SF
- Renovation to FACS, SPED and Art classrooms
- Renovated scramble & dining area
- LED lighting replacement
- Project Construction Schedule: Summer – Fall 2024 & 2025



PHASE 1

**WEEKLY
PROGRESS
REPORT**

Liberty High School

Liberty Public Schools



11/8/24

PROJECT STATUS

- Liberty High School
Build Back of 100's Wing Classrooms
- Completed Ceiling Tile Install
 - Continued Paint
 - Continued Casework Install
 - Continued Tile Install
 - Began Flooring Install
 - Began Door and Hardware Install
 - Began Glazing Install
 - Installed Solo Step Walking Assist System

UPCOMING

- Liberty High School
Build Back of 100s Wing Classrooms:
- Complete Paint
 - Complete Casework Install
 - Complete Flooring Install
 - Complete Doors and Hardware
 - Install all Specialty Finishes
 - Finish all MEP Trimout and Fixtures
 - Begin Punchlist
 - TCO Inspections

Project Completion: November 2024



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing



Progress 100's Wing




Progress 100's Wing



Shop Building

- 1,800 Square Foot New Building
- Flexible Open Plan
- Patio & Secure Breezway
- Woodworking Area
- Metalworking Area
- Flex-space for Lectures or Large Projects
- Projected Construction Schedule: Spring 2024–Spring 2025

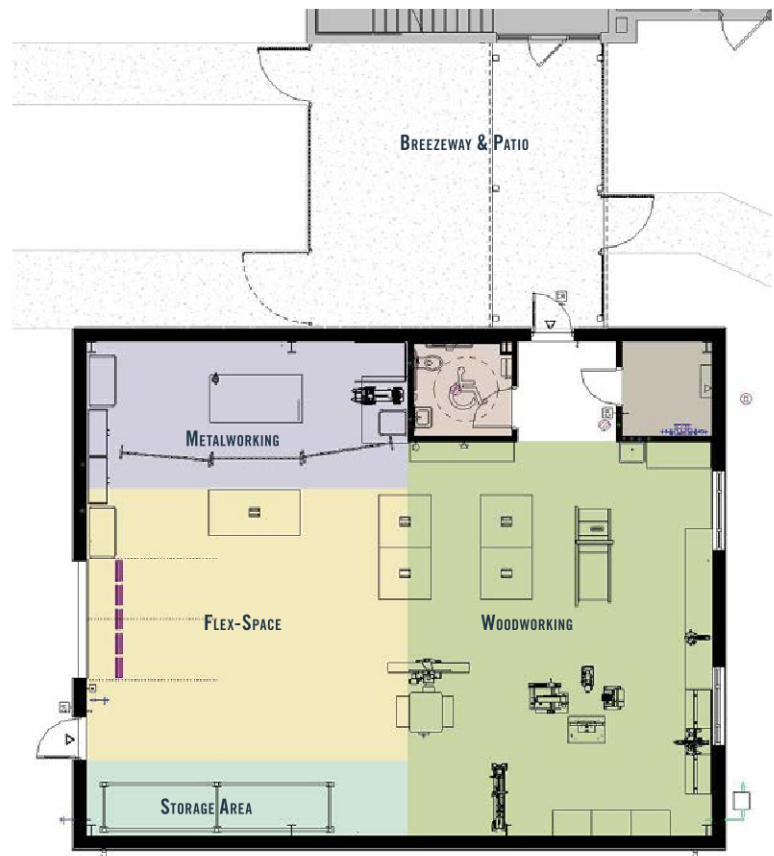

▲ Floor Plan

11/8/24

PROJECT STATUS

Building:

- Footings completed
- Stem wall poured
- Under slab ground rough complete
- SOG complete

Site:

- 90% site utilities complete

UPCOMING

- PEMB delivery 11/12
- PEMB install begins 11/13
- IMP delivery 12/23
- Install East storm drains per PR04

Project Completion
June 2025



SOG



Pouring SOG





Footings



EIFS Repair


Recreation Court

- 3,531 Square Foot New Court
- Court Lines for Basketball & Pickleball
- Additional Area for Temporary Bleachers
- Projected Construction Schedule:
Spring 2024–Spring 2025

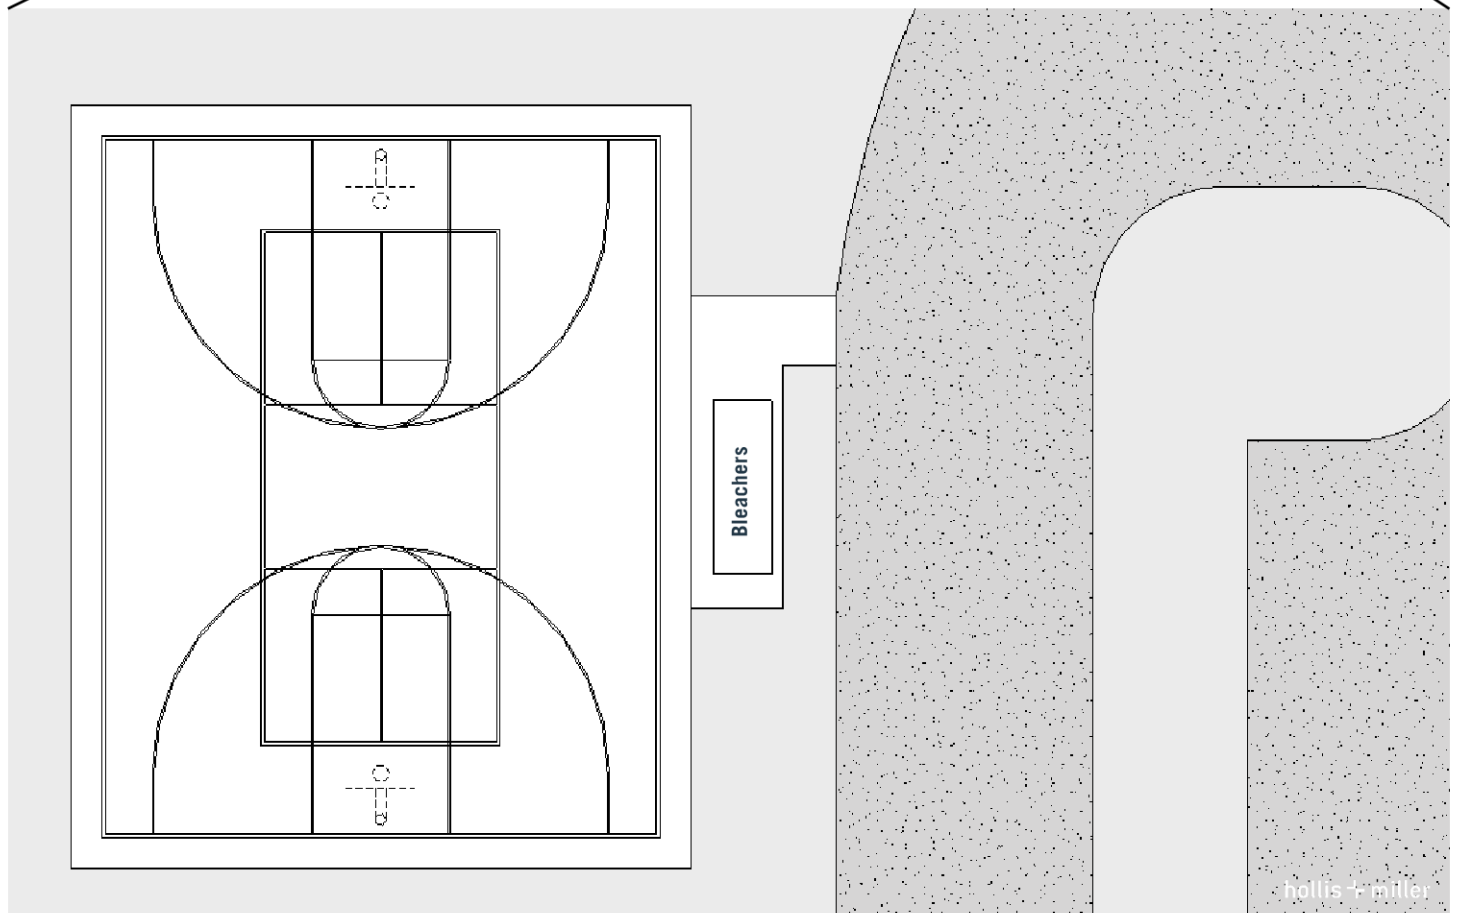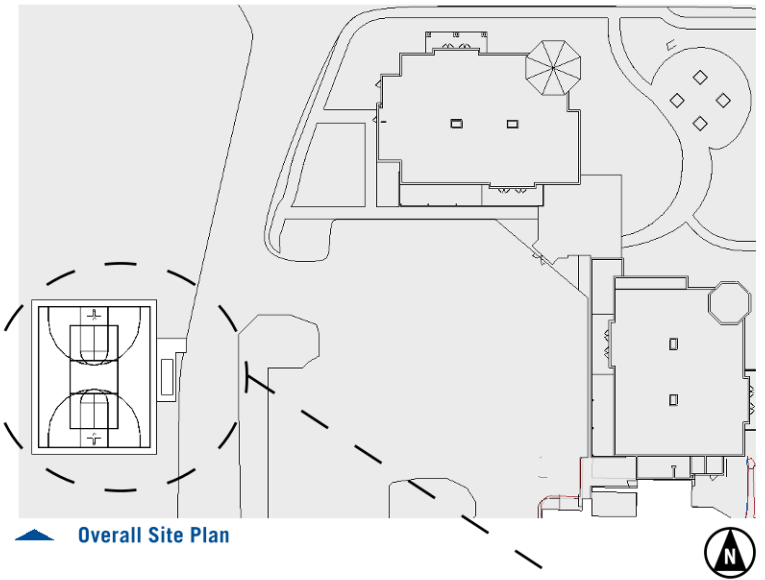

Interior Renovation

- Nurse Room Relocation
- Renovated Teacher Workroom
- SPED Classroom Toilet Renovation
- New Admin Reception Entry Door & Counter
- Staff Restroom Renovation
- Lactation Room
- Projected Construction Schedule:
May 2024 - August 2025

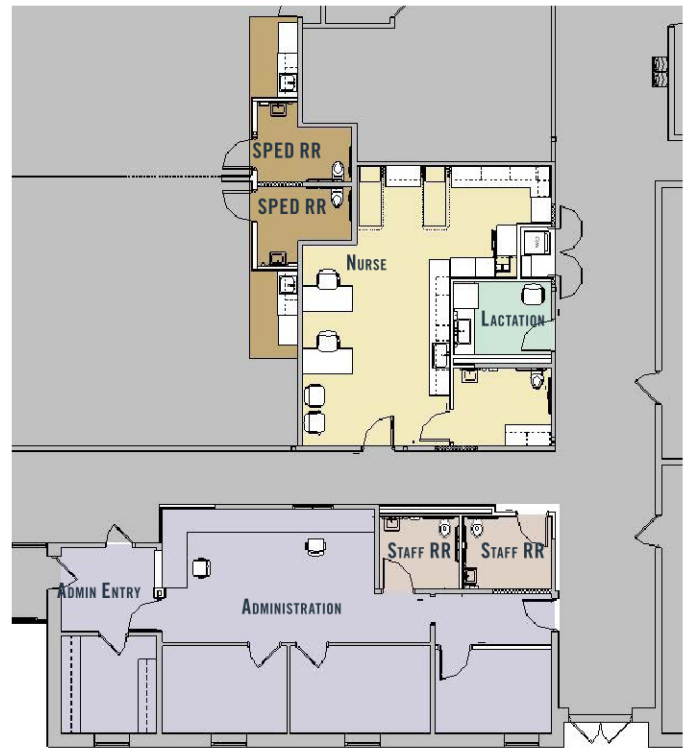

▲ Enlarged Floor Plan




▲ Overall Floor Plan

Interior Renovation


- Nurse Room Renovation
- Administration Office Renovation
- New Admin Reception Desk & Entry Door
- Lactation Room
- Group & Staff Restroom Renovation
- LED Lighting Replacement
- HVAC Replacement
- Projected Construction Schedule:
May 2024 - August 2025



Administration

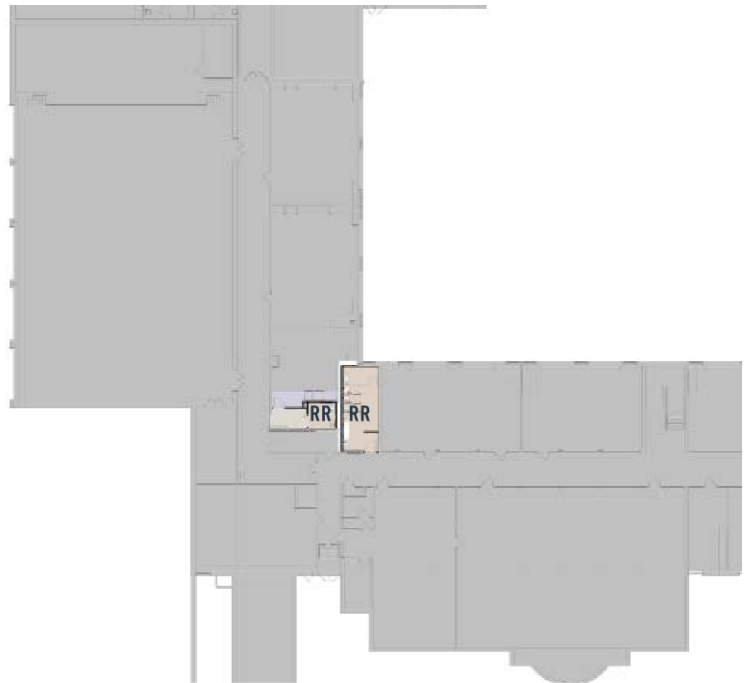

Partial First Level Floor Plan

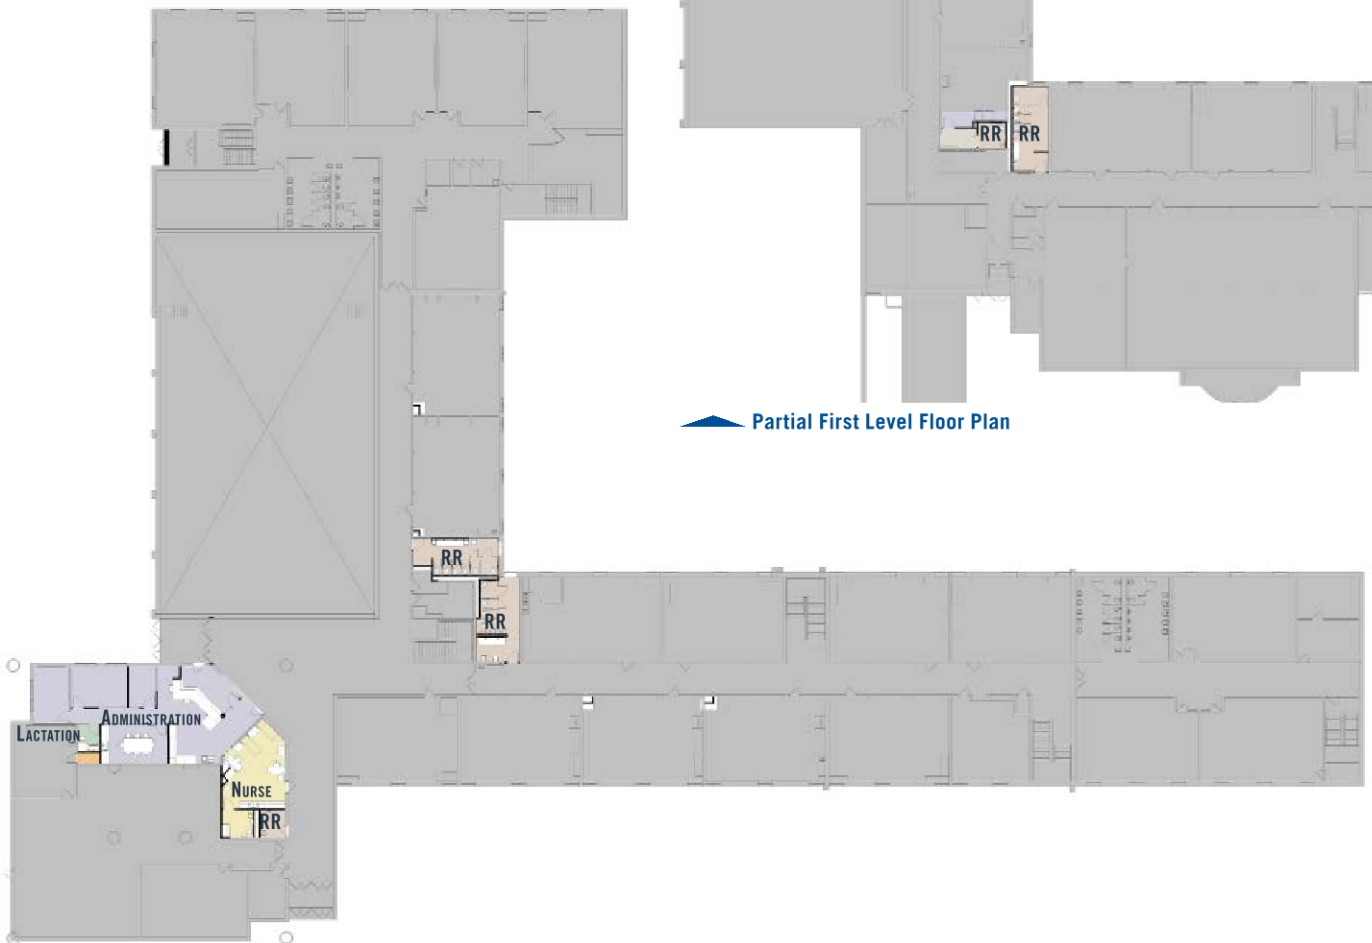


Overall Second Level Floor Plan

Interior Renovation

- Nurse Room Relocation
- Group & Staff Restroom Renovation
- New Admin Reception Desk & Entry Door
- Gym Stage Renovation into Staff Offices & PE Storage
- Lactation Room
- Media Center Wing LED Lighting
- Projected Construction Schedule:
May 2024 - August 2025



Administration

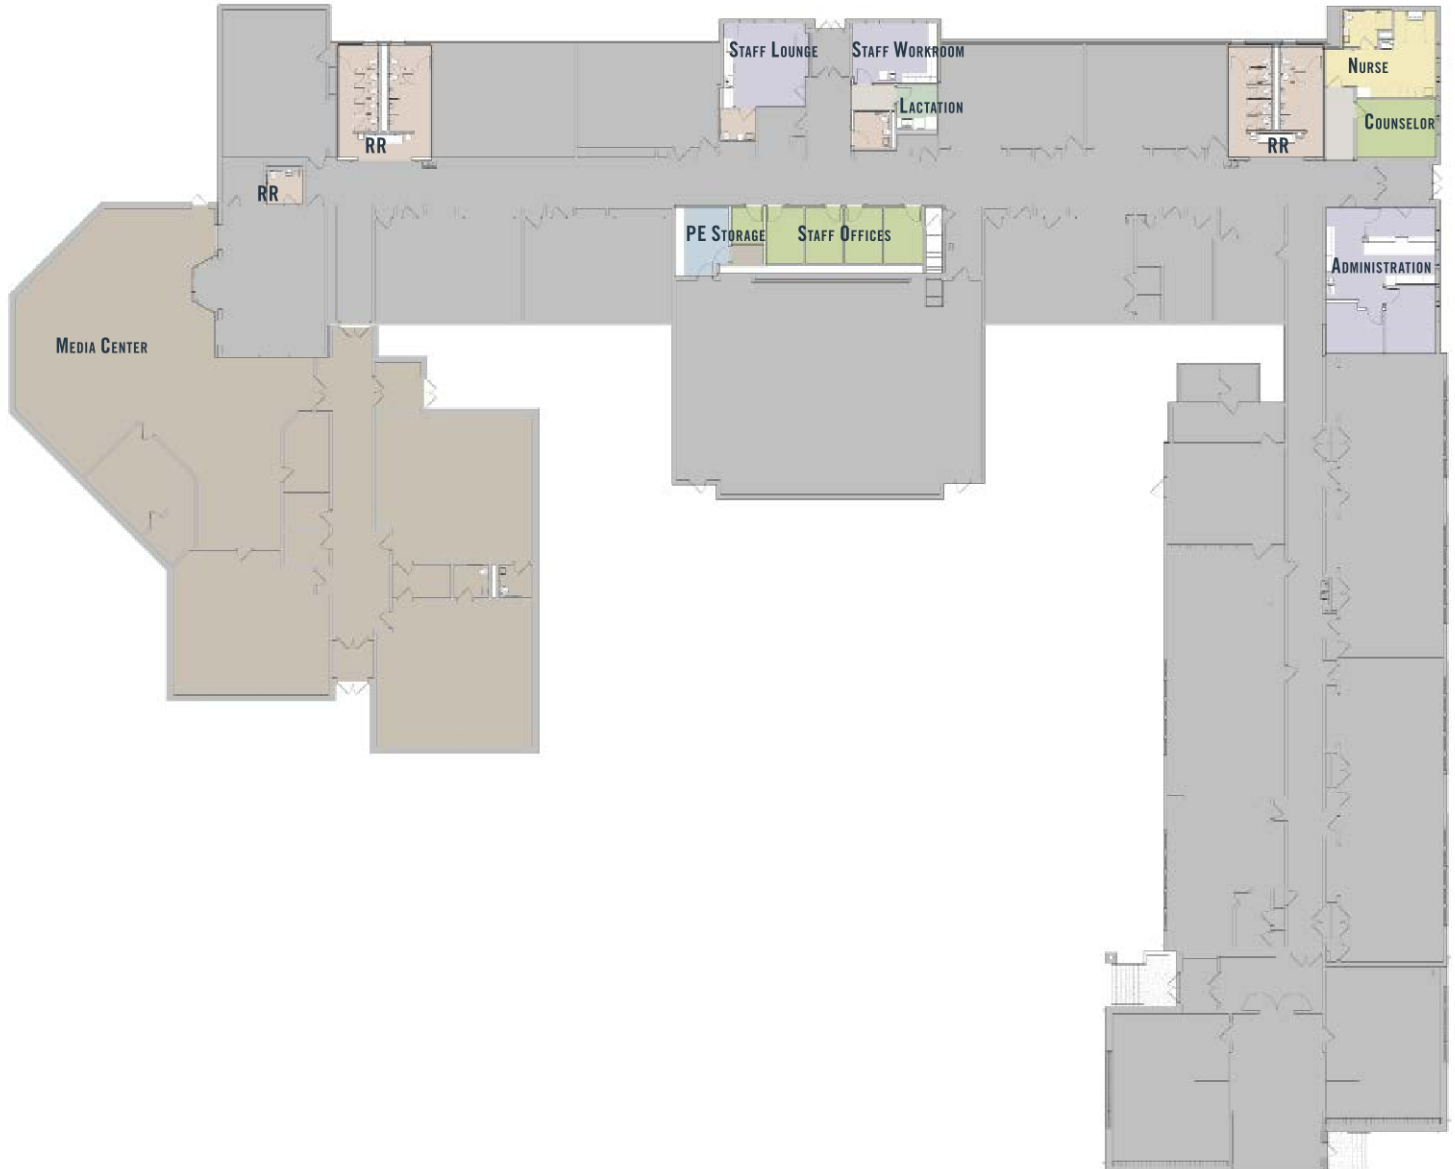

▲ Overall Floor Plan

**WEEKLY
PROGRESS
REPORT**

**Doniphan, Franklin, and Ridgeview
Summer Renovation Projects
Liberty Public Schools**



8/9/24

PROJECT STATUS

- Doniphan, Franklin, and Ridgeview:
- Completed MEP Install
 - Completed Drywall Install
 - Completed Ceiling Grid Install
 - Completed Paint
 - Completed Tile
 - Completed Casework Install
 - Completed Flooring Install
 - Completed Epoxy Install
 - Completed Specialties Install
 - Began Punch List Work

UPCOMING

- Doniphan, Franklin, and Ridgeview:
- Complete Punch List Work
 - Complete Final Inspections
 - Furniture Move-In

Project Completion: August 2024



Franklin - Main Office



Franklin - Restrooms



Franklin - Workroom



Ridgeview - Level 2 Restroom



Ridgeview - Main Office



Doniphan - Main Office



Doniphan - Assistant Principal Office



Doniphan - Teacher's Lounge
