



Projects in Construction

Cherokee HS Replacement

Replacement Facility

Carroll Daniel Construction

Substantial Completion: 02.2026

Anticipated Occupancy: 08.2026

- ADA and life safety inspections continue, alongside fire alarm testing across the campus.
- Identification and completion of punch list items are advancing.
- Furniture delivery and installation are underway.
- Technology staff are actively working to complete the installation of technology hardware.
- Transition meetings with district staff and the school administration and staff continue, and plans are being finalized to begin relocation of the staff at the beginning of post-planning.
- Project is on schedule for student occupancy in August 2026.
- Emergency plans and evacuation routes are in progress.
- Bi-directional Radio Repeater for public safety has been installed.
- Security film has been installed on exterior glass, and interior installation is in progress.
- Security cameras are in progress and expected to be completed by the end of April.
- School mapping assets and crisis alert system installation are scheduled for spring break.





River Ridge HS



Auxiliary Gymnasium

SmithBuilt Construction Group

Substantial Completion: 04.2026

Anticipated Occupancy: 08.2026

- Overhead MEP, ductwork, and installation of interior ceiling grid are complete.
- Painting, placement of ceiling tiles, and lighting fixtures are underway.
- Installation of storefront glass is nearing completion.
- Epoxy flooring application has been scheduled.
- Furniture orders were completed in December, with delivery and installation scheduled for late April, early May.
- Project is on schedule for student occupancy in August 2026.

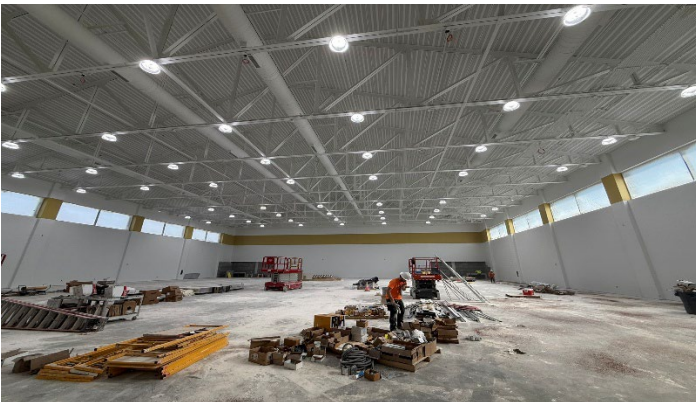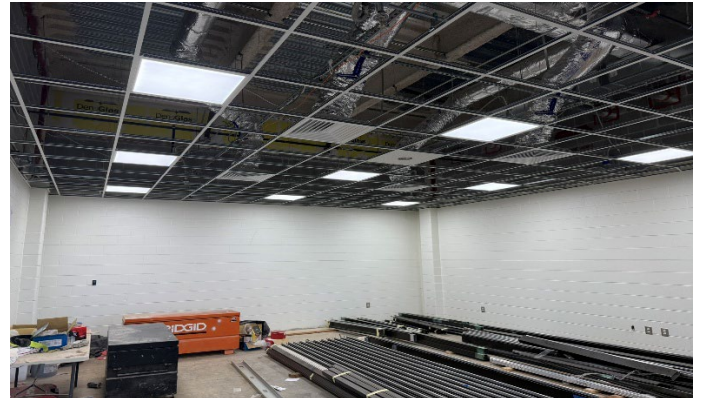



Sequoyah HS

Auxiliary Gym and Facility Improvements


(Press Box & Field House)

Carroll Daniel Construction

Substantial Completion: 11.2026

Anticipated Occupancy: 01.2027

- Construction activities for the auxiliary gym continue, including the placement of the TPO roofing system, interior masonry walls, and installation of overhead mechanical, electrical, and plumbing services.
- Underground electrical and plumbing work at the home concession building have been completed. Slab preparation is underway.
- At the visitor's concessions, placement of the interior masonry walls and installation of the electrical service continue.
- Installation of the underground sewer and waterproofing at the home field house is underway.

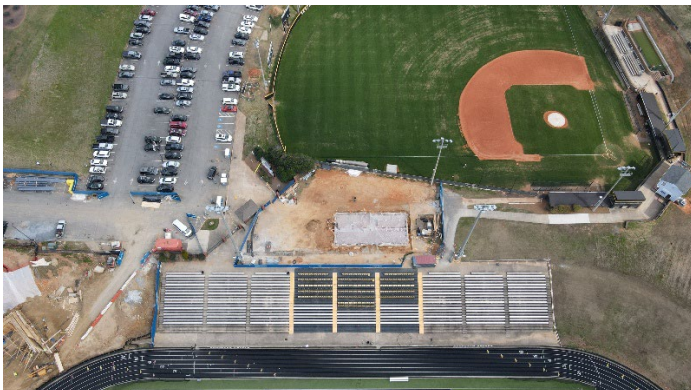

Capital Outlay Report

Work Session | 03.19.2026



Woodstock HS

Classroom Addition

SmithBuilt Construction Group

Substantial Completion: 01.2026

Anticipated Occupancy: 08.2026

- The general contractor has secured the certificate of occupancy.
- This project is 99% complete, apart from completion of the remaining punch list items and receipt of all closeout and warranty documentation.
- Furniture installation is complete.
- Technology staff are actively working to complete the installation of technology hardware.
- Project is on schedule for student occupancy in August 2026.

