




# Monthly Progress Report

March 2026

Hempstead Union Free School District (ABGS MS)



Report prepared by Idris Mashriqi





# Table of Contents

**Section I** – Program Summary

**Section II** – Work Progress **March 2026**

**Section III** – Work Projected for **April 2026**

**Section IV** – Progress Photos

**Section V** – Monthly Workforce Summary



## Section I – Program Summary

### March 2026

- **Hempstead UFSD – ABGS MS**
  - New addition to the existing building.
  - Abatement work throughout the existing building.
  - Classroom upgrades in the existing building.
  - New boilers installation in the existing building.
  - MEP upgrades throughout the existing building.



## Section II - Work Progress March 2026

### Hempstead UFSD – ABGS MS

- **VRD:**
  - Completed installation of footings, Foundation walls formwork, rebar, and poured concrete.
  - Completed interior piers and interior walls.
  - Backfilled around perimeter of building and all opened excavated areas.
- **Relle:**
  - Continued the rough-in for existing classrooms and the boiler room.
  - Completed underground conduit runs in new addition.
  - Installed sleeves as needed in foundation walls.
- **Hirsch:**
  - Installed waste pipe sleeves.
  - Installed water main.
  - Delivered grease trap.



## Section III - Work Planned April 2026

### Hempstead UFSD – ABGS MS

- **VRD:**
  - Deliver steel to site.
  - Start erecting steel.
  - Open boiler room door for equipment rigging.
- **Relle:**
  - Continue roughing for existing building and boiler room.
- **Hirsch:**
  - Continue crawl space domestic water piping. After abatement is completed in crawl space.
  - Deliver and install water heater in boiler room.
- **RMS:**
  - Deliver and install boilers in boiler room.
  - Start preliminary boiler piping.



## Section IV – Progress Photos



Hempstead ABGS MS – Footings



## Section IV – Progress Photos



Hempstead ABGS MS – Foundation Walls



## Section IV – Progress Photos



Hempstead ABGS MS – Foundation Walls



## Section IV – Progress Photos



Hempstead ABGS MS – Interior Piers and Walls



## Section IV – Progress Photos



Hempstead ABGS MS – Drain Piping



## Section IV – Progress Photos




### Hempstead ABGS MS – Underground Conduit Feeds



# Section V – Workforce Summary – Company/Hours

## March 2026

### MANPOWER GRAPH

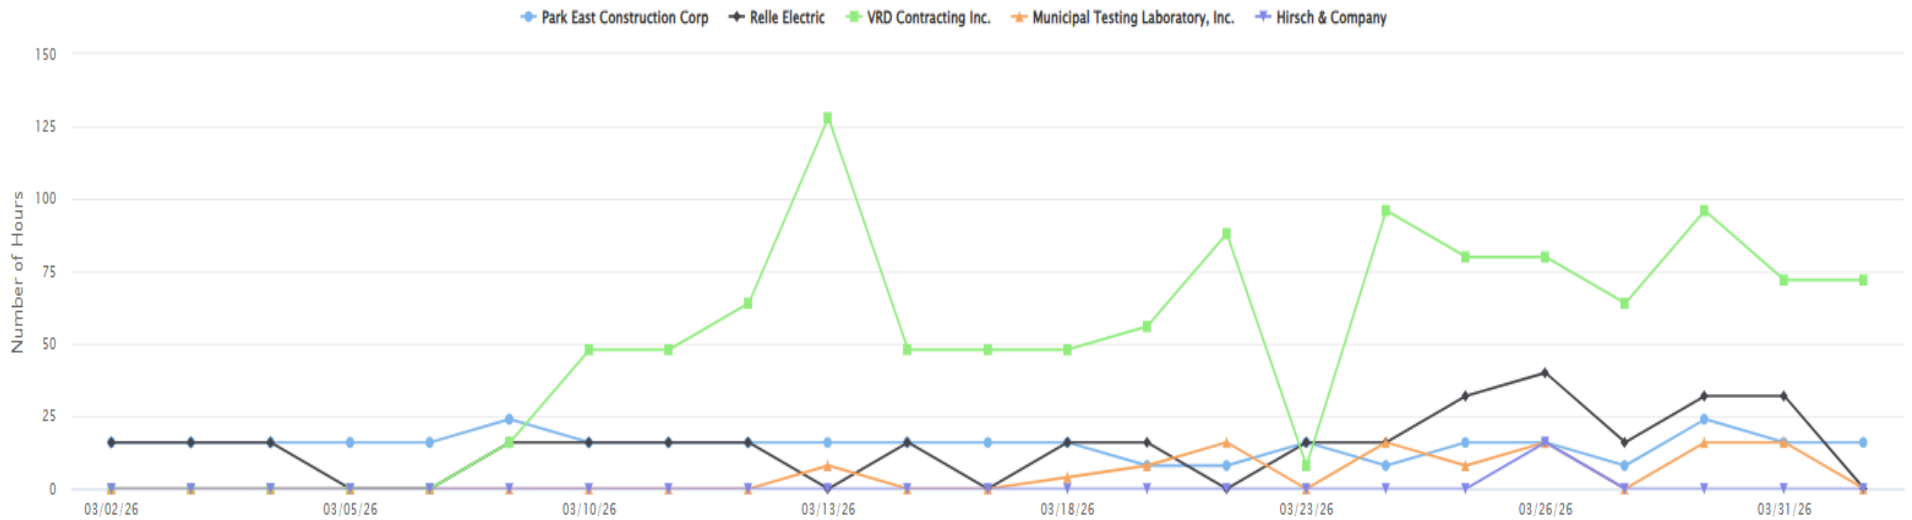

### Hempstead ABGS MS



Hempstead Union Free School District (ABGS MS)

March 2026

## End of Progress Report
