




Monthly Progress Report

April 2026

Hempstead Union Free School District (ABGS MS)



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress **April 2026**

Section III – Work Projected for **May 2026**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

April 2026

- **Hempstead UFSD – ABGS MS**
 - New addition to the existing building.
 - Abatement work throughout the existing building.
 - Classroom upgrades in the existing building.
 - New boilers installation in the existing building.
 - MEP upgrades throughout the existing building.



Section II - Work Progress April 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Delivered steel to job site.
 - Started installing steel beams and columns. 90% complete.
 - Started installing decking, 30% complete.
- **Relle:**
 - Continued the rough-in for existing classrooms and the boiler room.
 - Continued to rough underground runs for new addition.
 - Worked on the indoor transformer for library.
- **Hirsch:**
 - Installed domestic water in crawl space.
 - Installed underground waste roughing in new addition.
 - Installed grease trap.



Section III - Work Planned May 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continue erecting steel and installing building decking.
 - Open boiler room door for equipment rigging.
- **Relle:**
 - Continue roughing for existing building and boiler room.
 - Continue roughing as needed for new addition.
- **Hirsch:**
 - Deliver and install water heater in boiler room.
 - Continue underground roughing and riser installation for new addition.
- **RMS:**
 - Deliver and install boilers in boiler room.
 - Start preliminary boiler piping.



Section IV – Progress Photos



Hempstead ABGS MS – Steel



Section IV – Progress Photos



Hempstead ABGS MS – Steel



Section IV – Progress Photos



Hempstead ABGS MS – Steel



Section IV – Progress Photos



Hempstead ABGS MS – Steel Decking



Section IV – Progress Photos



Hempstead ABGS MS – UG Drain Piping



Section IV – Progress Photos




Hempstead ABGS MS – UG Drain Piping



Section V – Workforce Summary – Company/Hours

April 2026

MANPOWER GRAPH

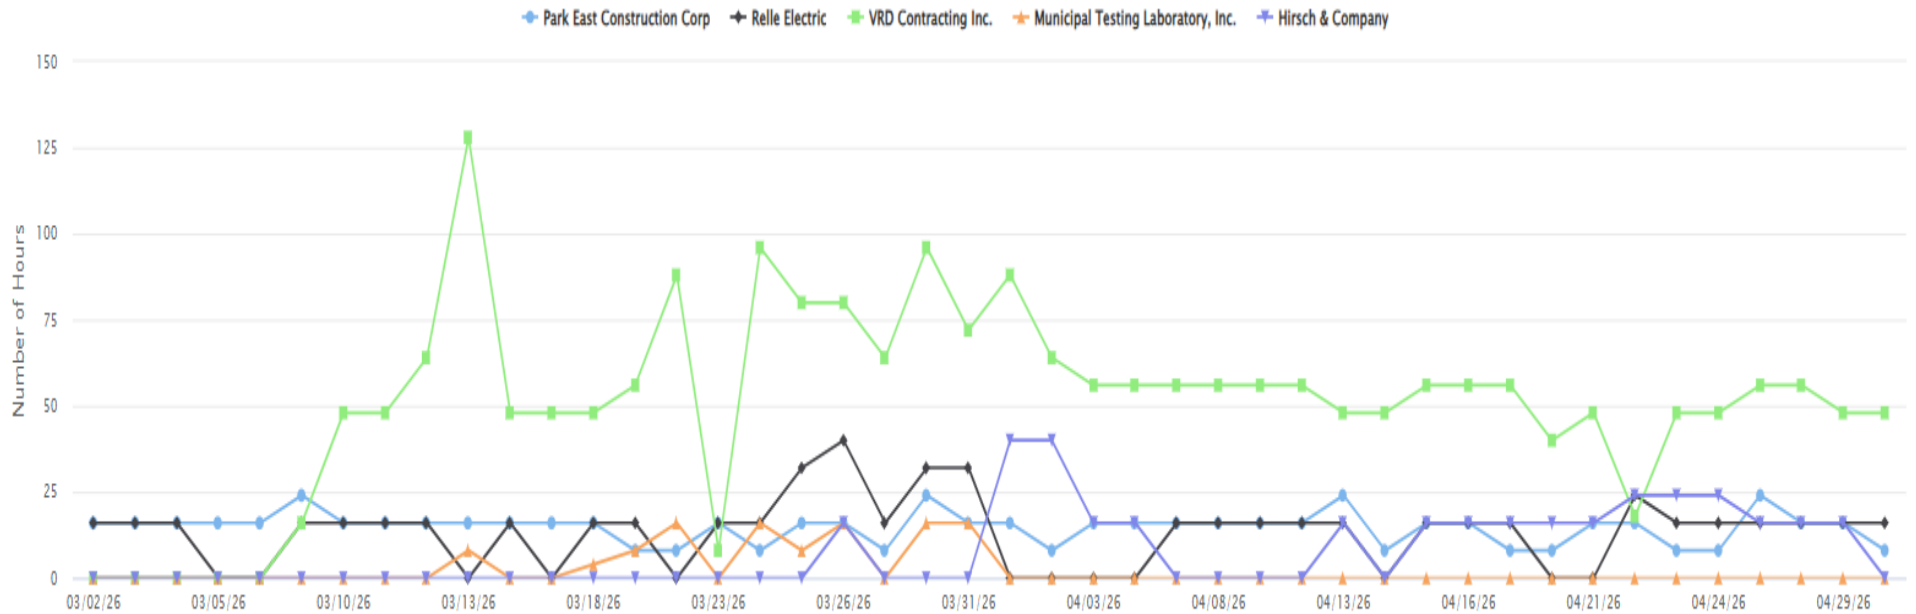

Hempstead ABGS MS



Hempstead Union Free School District (ABGS MS)

April 2026

End of Progress Report
