



Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

PROGRESS THIS WEEK:

- Precast Plank Installation started Area C
- Initial Site Grading For Playfield
- CMU Complete East Natatorium Wall and Backfill of Area B following precast completion.

GOALS NEXT 2 WEEKS:

- Complete Precast Plank Installation Area C1
- Complete Area A2 One-sided Masonry Wall, Stair Shaft & Elevator Shaft.
- Continue Load Bearing Masonry Following Precast Erection & Continue Main Frame Steel Erection.







PROJECT HIGHLIGHT THIS WEEK:

- Precast Erection Area C
- Playfield Site Grading And Completion Of Playfield Access Roads

DATE: April 17, 2026

MRCC PROJECT PROGRESS:




MILESTONE CHECKLIST:

- Construction Start – 9/18/25
- Foundations Complete 3/25/26
- Steel Complete
- Enclosed
- MRCC Substantial Completion
- Playfield Completion

Photos or Visual Assets:



South Elevation– Area B & Area C

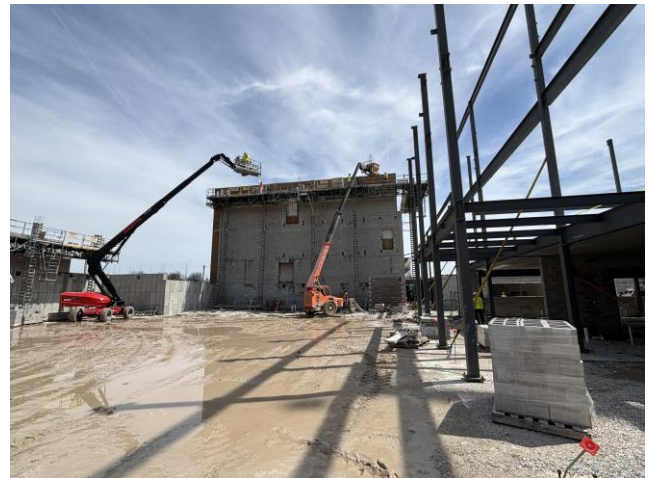

One-Sided Masonry Wall – Area A2



Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

DATE: April 17, 2026

MORE PROGRESS PHOTOS:



Exterior CMU Walls- Storage & Fire Pump Rooms Area B



Playfield Site Grading & Stone Access Roads- Pump Track



Southeast Elevation- Area B



East Foundation Backfill Following Precast Erection- Area B
