




# Quarterly Executive Summary Aynor High School Renovations Q1 2026

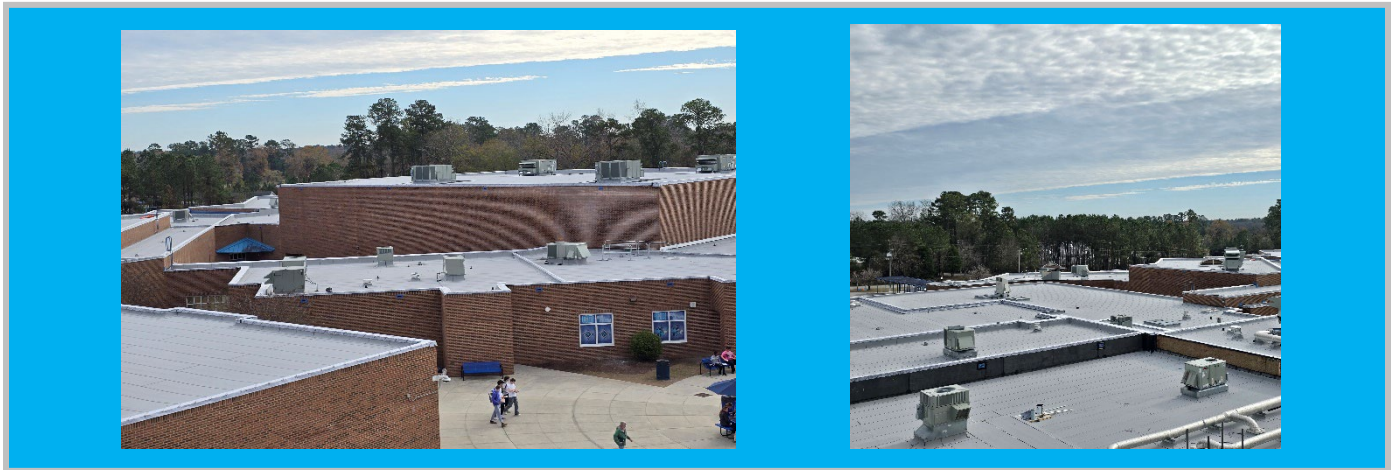

**HCS Project Manager:** Trevor Turner

**Principal:** Michael McCracken

**Architect/Engineer:** Little Architects

**Contractor:** Montieth Construction

**Project Scope:** Critical Systems that are in the scope include: investigate and remediate electrical services and distributions (if needed), upgrade fire alarm, upgrade low voltage wiring, kitchen/servery renovations, investigate and remediate plumbing (if needed), improve exterior envelope, investigate and remediate elevator (if needed), full roof replacement. Refresh items that may be addressed include interior layout revisions, gym floor refinish, gym bleachers, wall paint, ceiling – tiles and grid, carpet/flooring, lighting, interior doors, cabinets/counters/lockers, and bathrooms/locker rooms.

**Current Status:** Construction underway. Major progress made summer of 2025.

**Budget:** Original Budget: **\$14,000,000** Board Approved Date: May 15, 2023

**Budget Issues:** None.

**Schedule:**  
Design: Winter 2024/Spring 2025  
Construction Start: Summer 2025  
Completion: Summer 2026

**Schedule Issues:** None.

**Achievements:** Building Permit issued. Construction began June of 2025.
