




Monthly Progress Report

May 2026

Hempstead Union Free School District (ABGS MS)



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress **May 2026**

Section III – Work Projected for **June 2026**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary May 2026

- **Hempstead UFSD – ABGS MS**
 - New addition to the existing building.
 - Abatement work throughout the existing building.
 - Classroom upgrades in the existing building.
 - New boilers installation in the existing building.
 - MEP upgrades throughout the existing building.



Section II - Work Progress May 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continued installing steel beams and columns. 95% complete.
 - Started installing decking, 75% complete.
 - Removed boiler room door and cut wall for rigging purposes.
 - Started preparing 1st and 2nd floor for concrete. Section behind gym.
- **Relle:**
 - Continued the rough-in for existing classrooms and the boiler room.
 - Continued to rough underground runs for new addition.
 - Installed risers and sleeves as needed for addition.
 - Temp lighting installed in new addition. 40% complete.
- **Hirsch:**
 - Installed domestic water in crawl space.
 - Installed underground waste roughing in new addition.
 - Installed new water heater in boiler room.
 - Welded sections of gas main header and painted yellow.
- **RMS**
 - Delivered and installed new boilers in the boiler room.
 - Started installing piping for new boilers.




Section III - Work Planned June 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continue erecting steel and installing building decking.
 - Continue preparing floors for concrete and pour concrete.
 - Start CMU block installation.
- **Relle:**
 - Continue roughing for existing building and boiler room.
 - Continue roughing as needed for new addition.
- **Hirsch:**
 - Continue underground roughing and riser installation for new addition.
 - Continue gas piping installation.
- **RMS:**
 - Continue installing piping in boiler room.
 - Start installing hangers in the new addition.




Section IV – Progress Photos

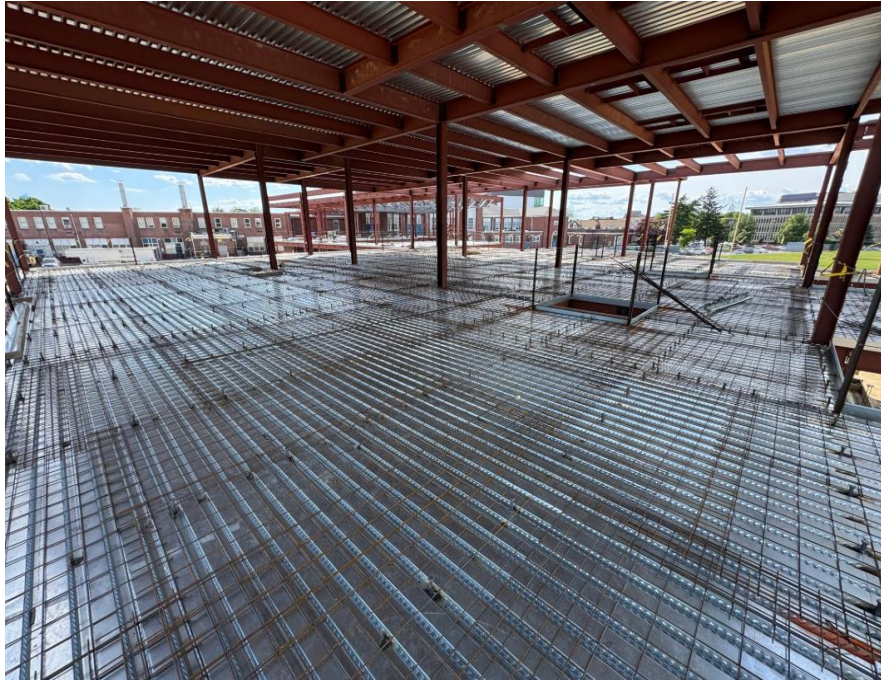

Hempstead ABGS MS – Steel/Decking



Section IV – Progress Photos

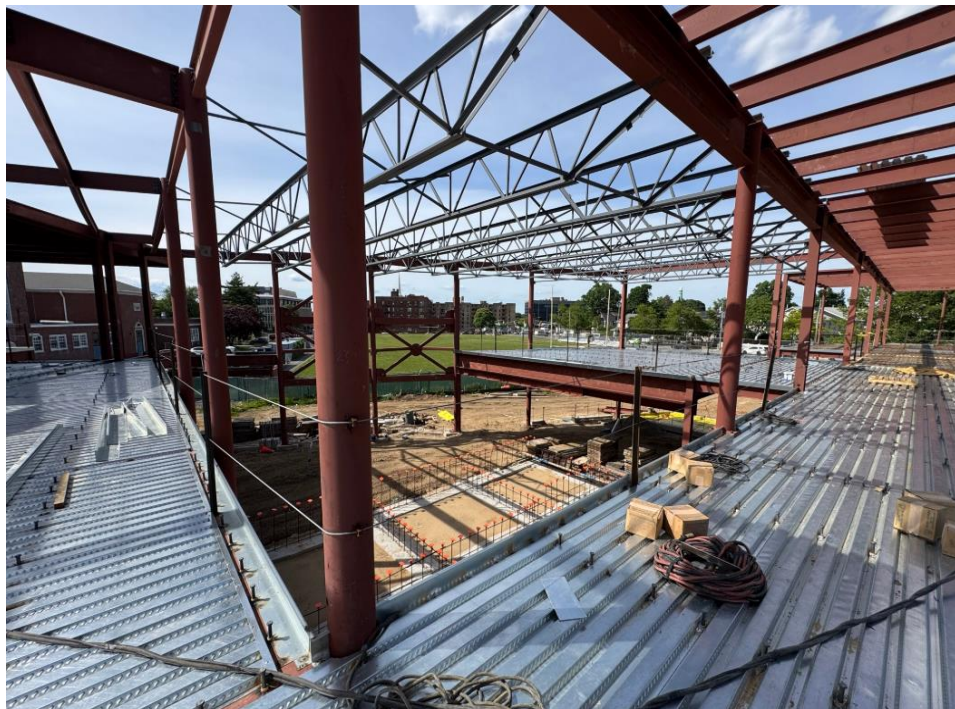

Hempstead ABGS MS – Steel/Decking



Section IV – Progress Photos



Hempstead ABGS MS – Slab Vapor Barrier/Wire Mesh



Section IV – Progress Photos



Hempstead ABGS MS – Underground Electric Roughing




Section IV – Progress Photos



Hempstead ABGS MS – Boiler Room Equipment



Section IV – Progress Photos

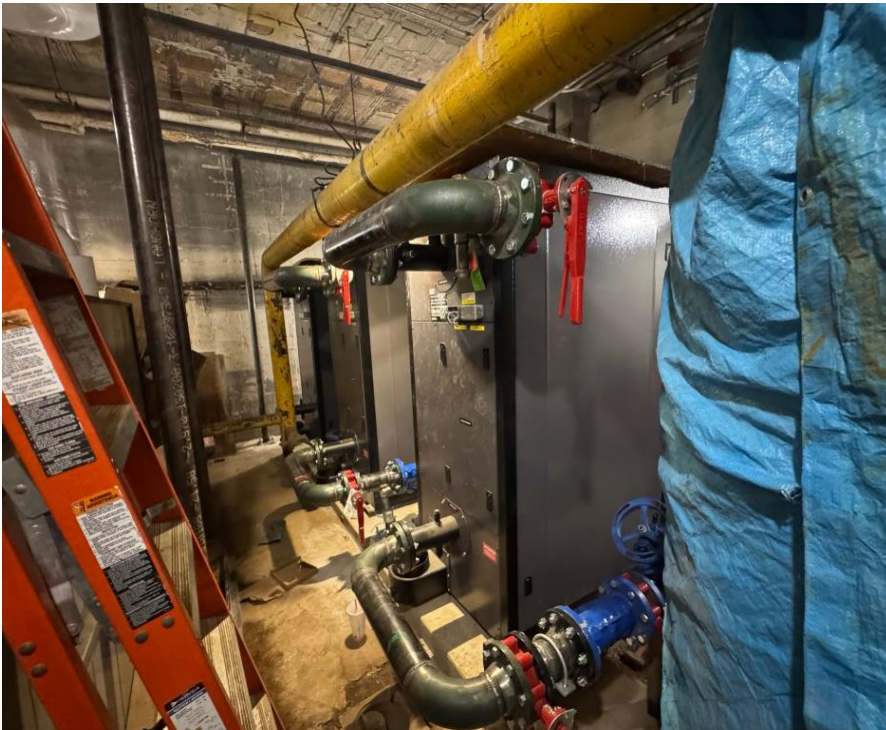


Hempstead ABGS MS – Boiler Room Equipment



Section V – Workforce Summary – Company/Hours

May 2026

MANPOWER GRAPH

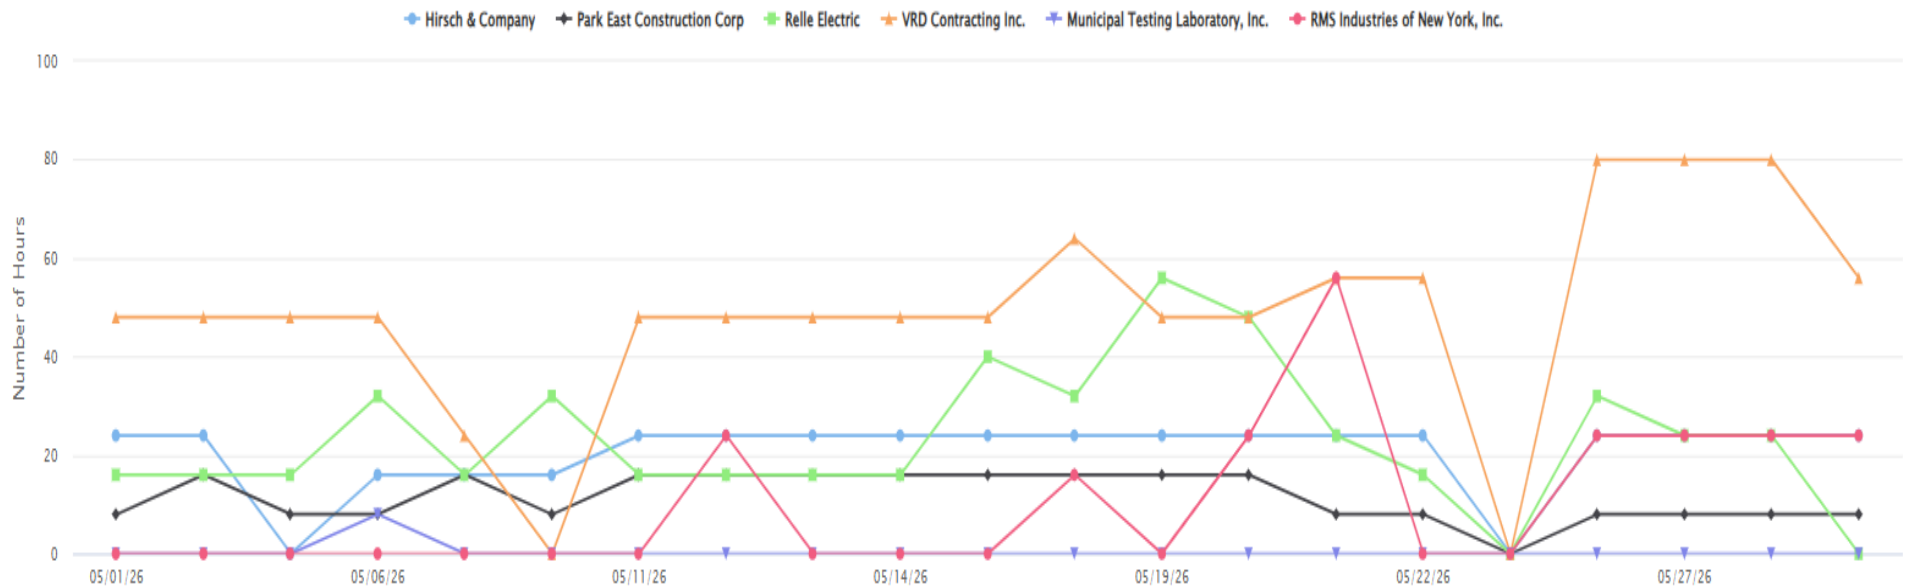

Hempstead ABGS MS



Hempstead Union Free School District (ABGS MS)

May 2026

End of Progress Report
