





Mount Nittany Elementary School

Expansion Project Update

06/01/2026

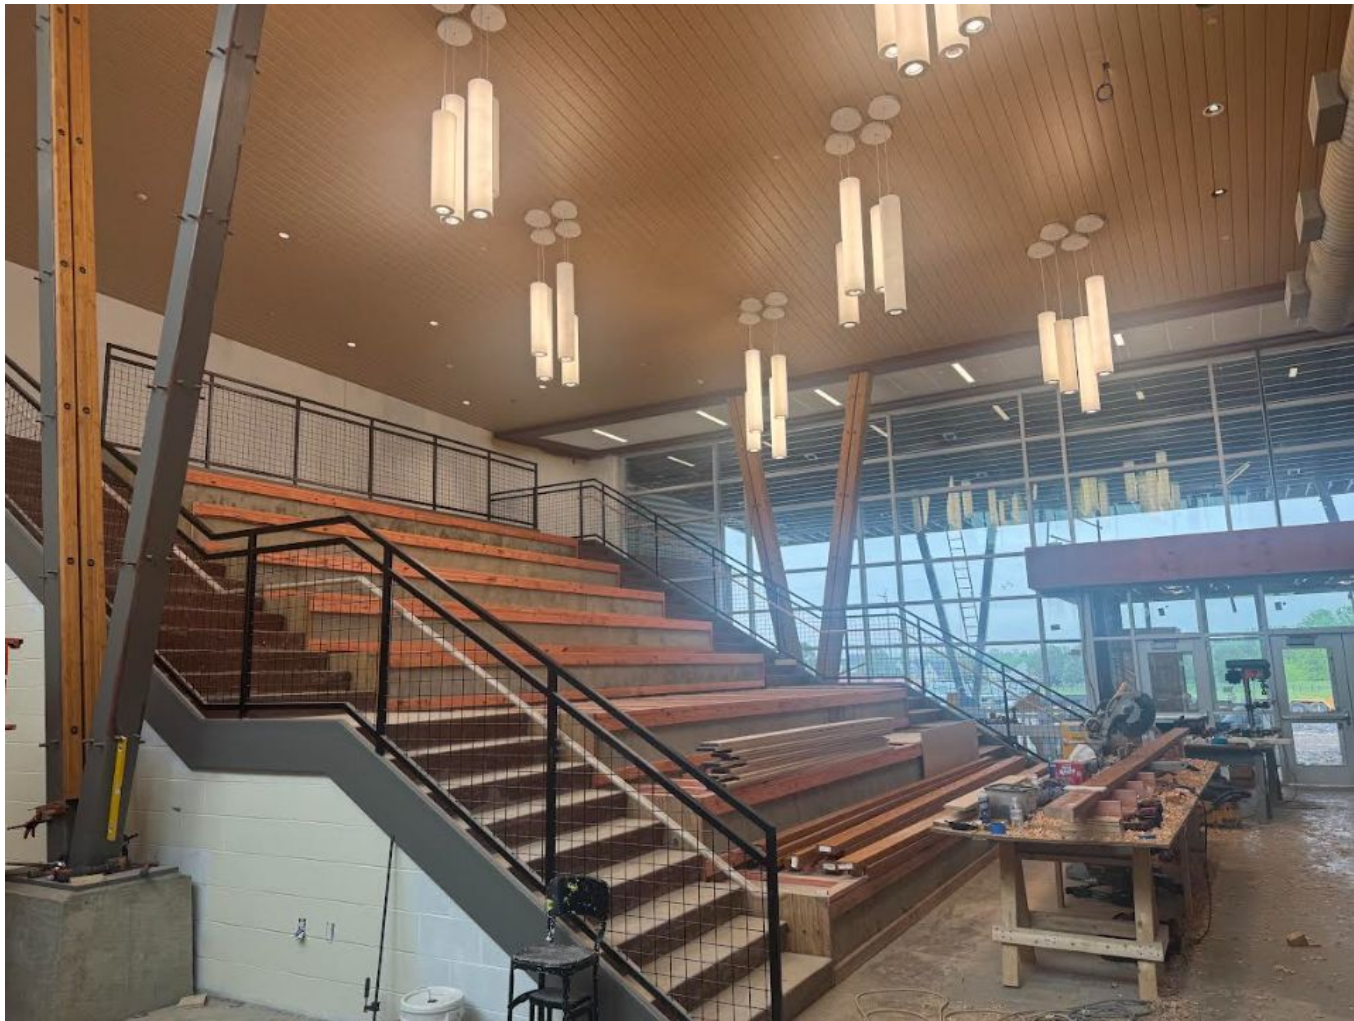

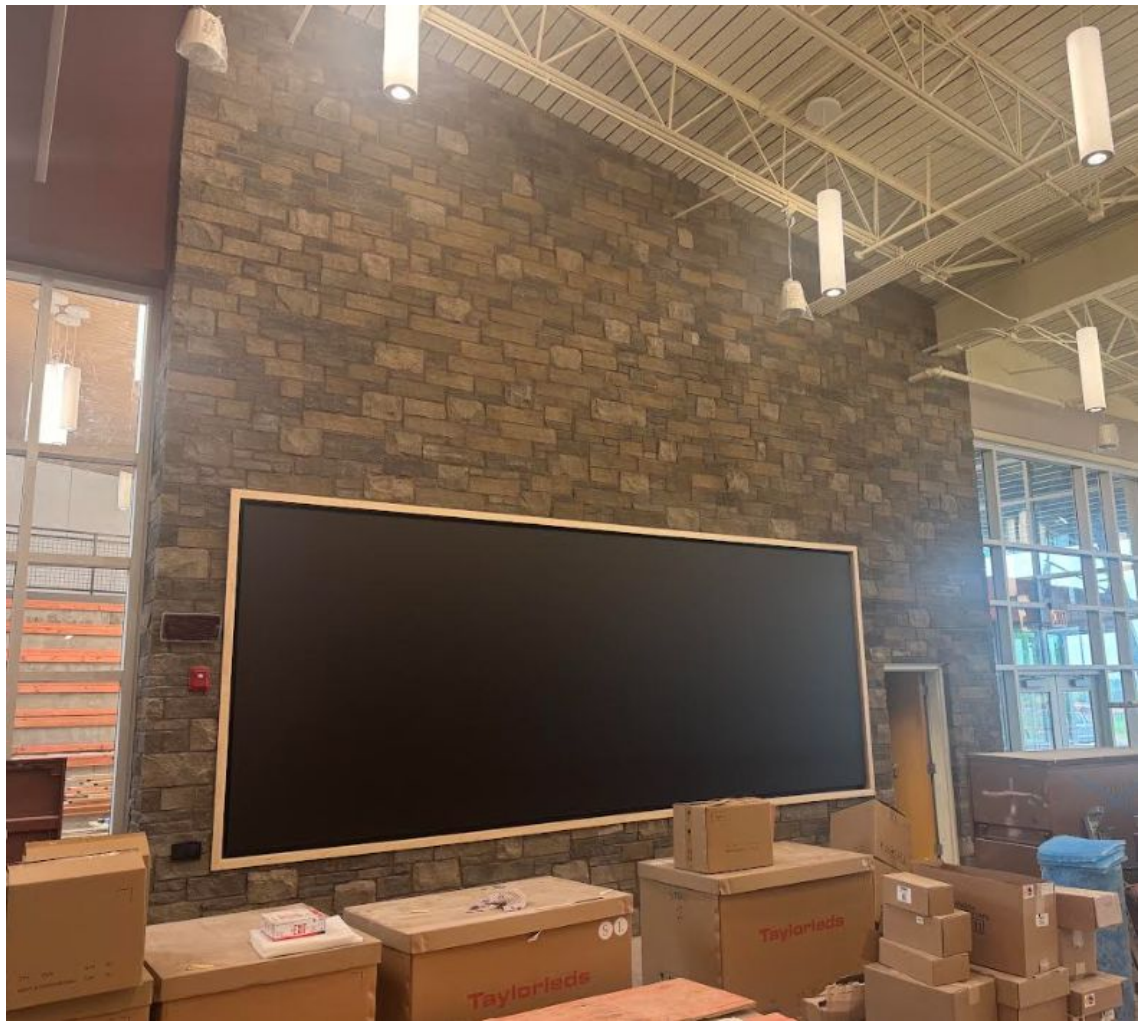





Mount Nittany Elementary School

Current Progress

- Flooring is ongoing - West Wing complete
- Painting complete except for punch list
- Kitchen equipment installed
- Brick is complete
- Ceilings and casework is all installed
- Lighting is all installed and programmed



Mount Nittany Elementary School

Next Steps:

- Finish paving
- Outdoor metal panels to finish
- Finishing interior doors and hardware
- Finish programming of fire alarm system
- Moving in furniture
- Final cleaning



Mount Nittany Elementary School

Current Schedule:

- Schedule Update #10
 - Final clean of new addition week of June 15th
 - Final clean of work in existing school week of August 3rd
- No anticipated disruptions for the start of the 2026-27 school year



Mount Nittany Elementary School

Questions?
