


CARNEGIE ELEMENTARY RENOVATION AND ADDITION

CONSTRUCTION UPDATE

06-09-2026



Auditorium Demolition

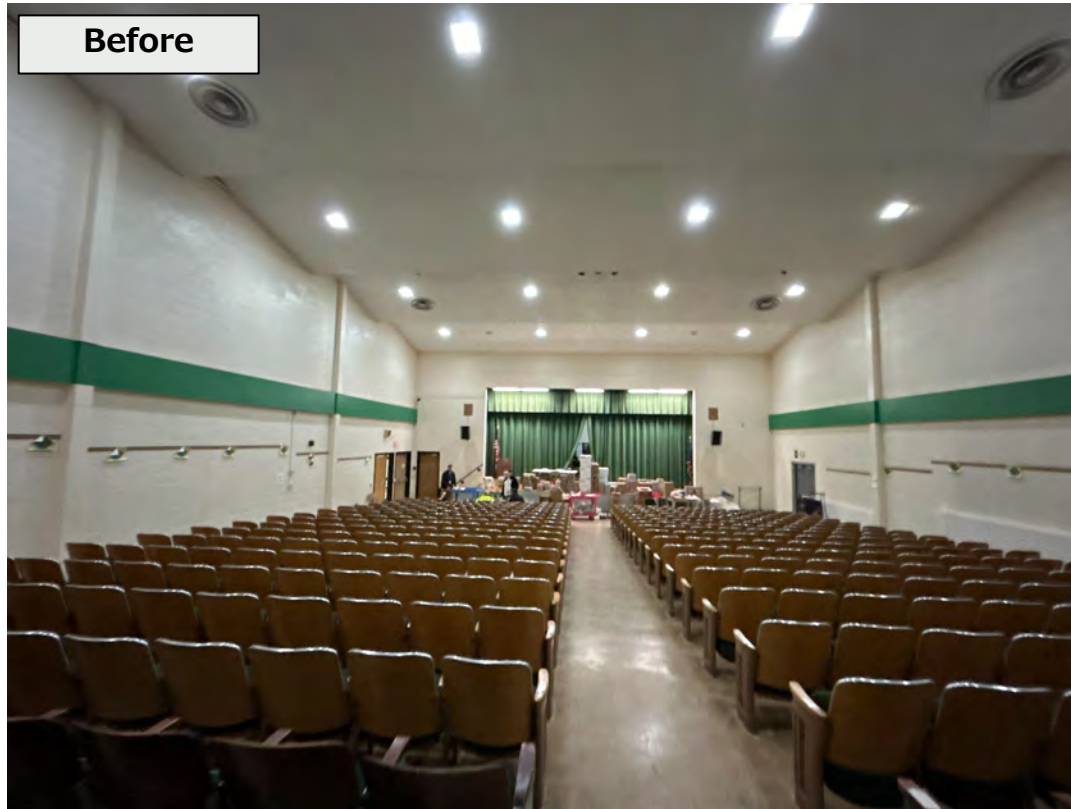


- The GC demoed seating, decorative electrical chases, and front of the stage in auditorium. The GC also tarped walls in preparation for abatement.

Stage Demolition




- The GC demoed curtain rigging and mechanical contractors demoed ducts in ceiling.

Storage & Para Break Room Demolition

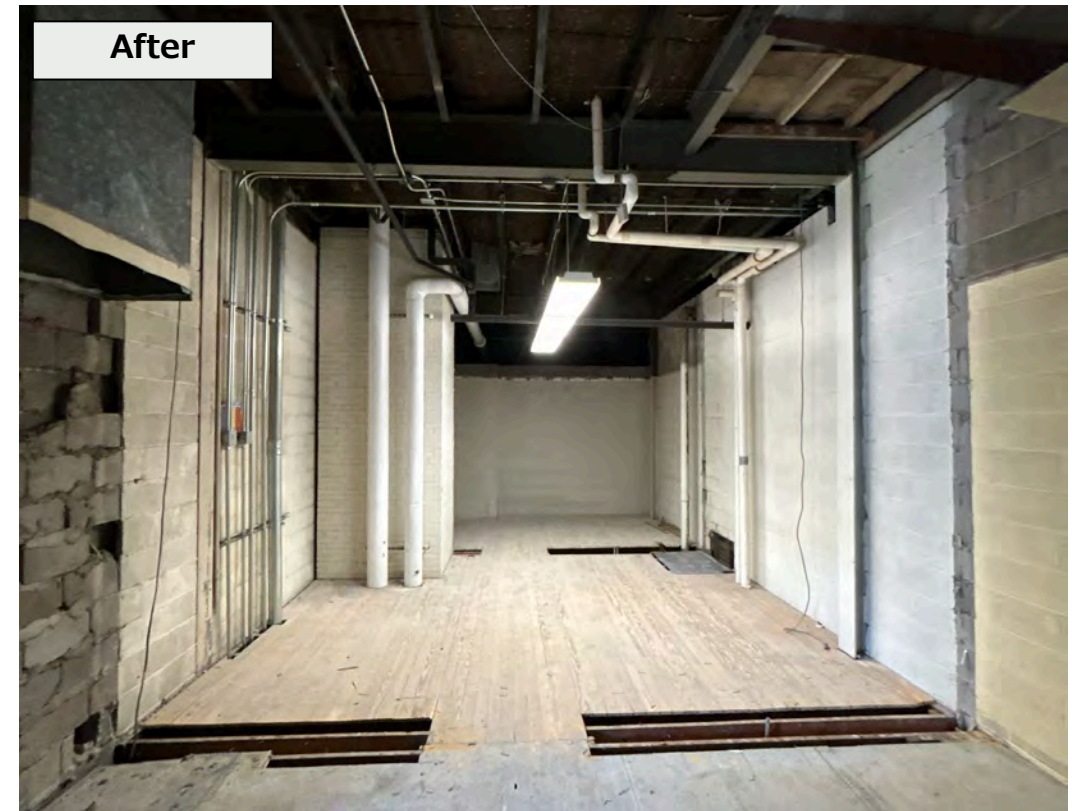

- The GC demoed CMU walls and lath ceilings, mechanical contractors demoed ducts, and electrical contractors demoed electrical in existing storage and para break room behind stage.

Mechanical Room

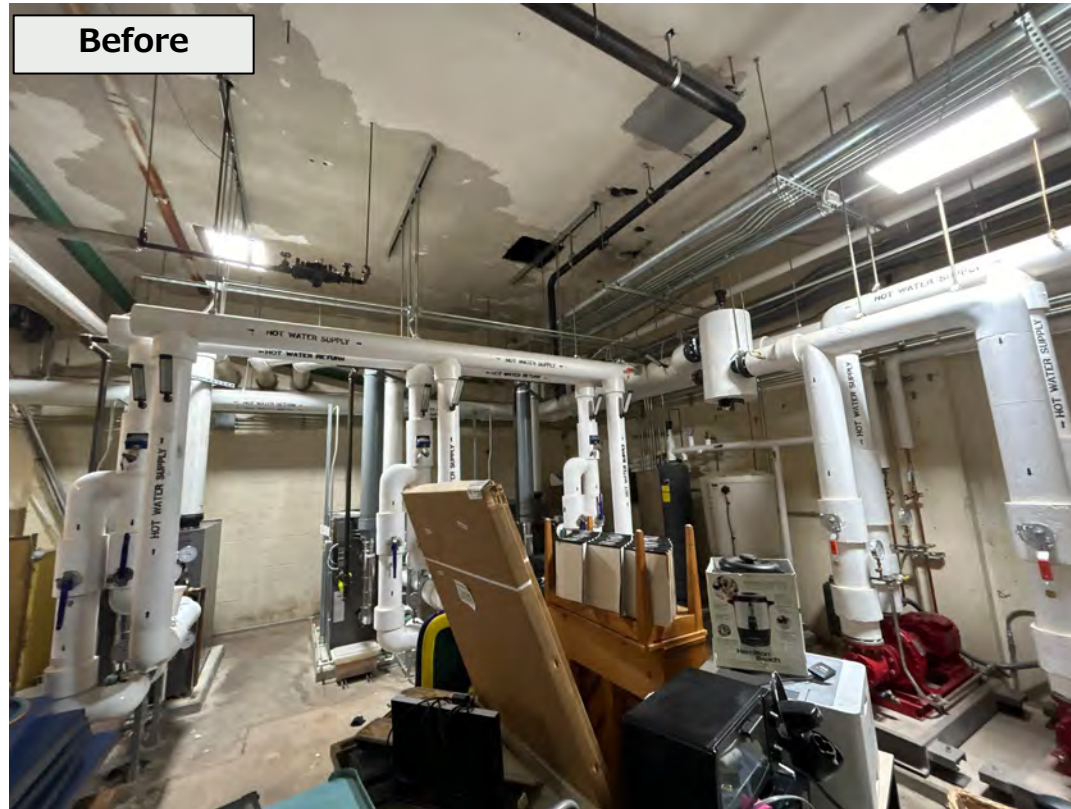

- The mechanical contractor installed a buffer tank and drained glycol in the basement mechanical room.

Supporting Spaces



- Abatement contractor mobilized and placed dumpsters in preparation for abatement (left).
- The excavation contractor mobilized and began demo in courtyard area (right).

Project Site Setup



Groundbreaking



Project Overview

Upcoming Work

- Complete abatement in auditorium
- Abatement in corridors
- Excavation in courtyard for addition foundations
- Start foundations
- Install sediment pond
- Start grading areas around playground
- Stormwork
- Continue work in mechanical room
- Waterproofing of existing exterior wall



Project Stats

- Project is at 17 Days with no recordable injury

THANK YOU



CARLYNTON
SCHOOL DISTRICT

COMMUNITY EXCELLENCE CHARACTER

QUESTIONS?

