




Monthly Progress Report

June 2026

Hempstead Union Free School District



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress June 2026

Section III – Work Projected for July 2026

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

June 2026

Project List

- **Hempstead UFSD – IAQ at Various School – In Progress**
 - Indoor air quality and mechanical upgrades.
 - Electrical upgrades.
- **Hempstead UFSD – 2022 Bond Phase 3 – In Progress**
 - Infrastructure upgrades throughout all schools.
- **Hempstead UFSD – Boiler replacement at Prospect Elementary School – In Progress**
 - Boiler and piping replacement.
- **Hempstead UFSD – 2022 Bond Phase 4 – In Progress**
 - Infrastructure upgrades throughout all schools.
- **Hempstead UFSD – 2024 Bond Phase 2 – In Progress**
 - Infrastructure upgrades throughout all schools.



Section II - Work Progress

June 2026

Hempstead UFSD – IAQ at Various Schools

- **Reliance:**
 - Install 3 condensate pumps.
- **Eldor:**
 - Paterson ES work on switchgear transfer.

Hempstead UFSD – 2022 Bond Phase 3

- **J Cole:**
 - Received railing delivery.
 - Grease trap excavation.
 - Started masonry repairs @ the HS.
- **Eldor:**
 - Continued to rough at McNeil ES.
 - Started to mobilize to all schools.
- **RMS:**
 - Marked out openings for HVAC upgrades.
- **IPS:**
 - Started kitchen waste lines and grease trap.

Hempstead UFSD – Boiler replacement at Prospect Elementary School

- **KG Mechanical**
 - Completed demo of existing boilers.
 - Marked out boiler pad locations.

Hempstead UFSD – 2022 Bond Phase 4

- In process of submittal approvals.
- GC to be rebid.

Hempstead UFSD – 2024 Bond Phase 2

- Started bathroom HS demo.
- Started excavation at McNeil ES for elevator footings and foundation.



Section III - Work Planned July 2026

Hempstead UFSD – IAQ at Various Schools

- **Eldor:**
 - Complete Paterson ES switchgear.
- **RMS:**
 - UV change order.

Hempstead UFSD – 2022 Bond Phase 3

- **J Cole:**
 - Complete openings for HVAC upgrades
 - Complete railing installs.
 - Complete grease trap.
 - Complete masonry repairs.
 - Complete elevator replacement @ the HS.
- **IPS:**
 - Complete kitchen waste lines.
- **RMS:**
 - Complete duct work.
 - Install exhaust fans and curbs.
 - Start up fans.
- **Eldor:**
 - Start HS parking lot light pole replacements.
 - Complete electrical upgrades.

Hempstead UFSD – Boiler replacement at Prospect Elementary School

- **KG Mechanical**
 - Pour concrete pads.
 - Rig Boilers and pumps.
 - Start piping for new boilers.



Section III - Work Planned July 2026

Hempstead UFSD – 2022 Bond Phase 4

- Prep for start of work. While submittal approvals come in.
- GC Rebid to take place.

Hempstead UFSD – 2024 Bond Phase 2

- McNeil elevator footing/foundation start.
 - Start structural for elevator shaft.
- Abatement at multiple schools.
- Electrical roofing.
- Potentially start some roof work at various schools.



Section IV – Progress Photos



Hempstead McNeil ES – Elevator Excavation



Section IV – Progress Photos




Hempstead UFSD



Section V – Workforce Summary – Company/Hours

June 2026

▼ MANPOWER GRAPH

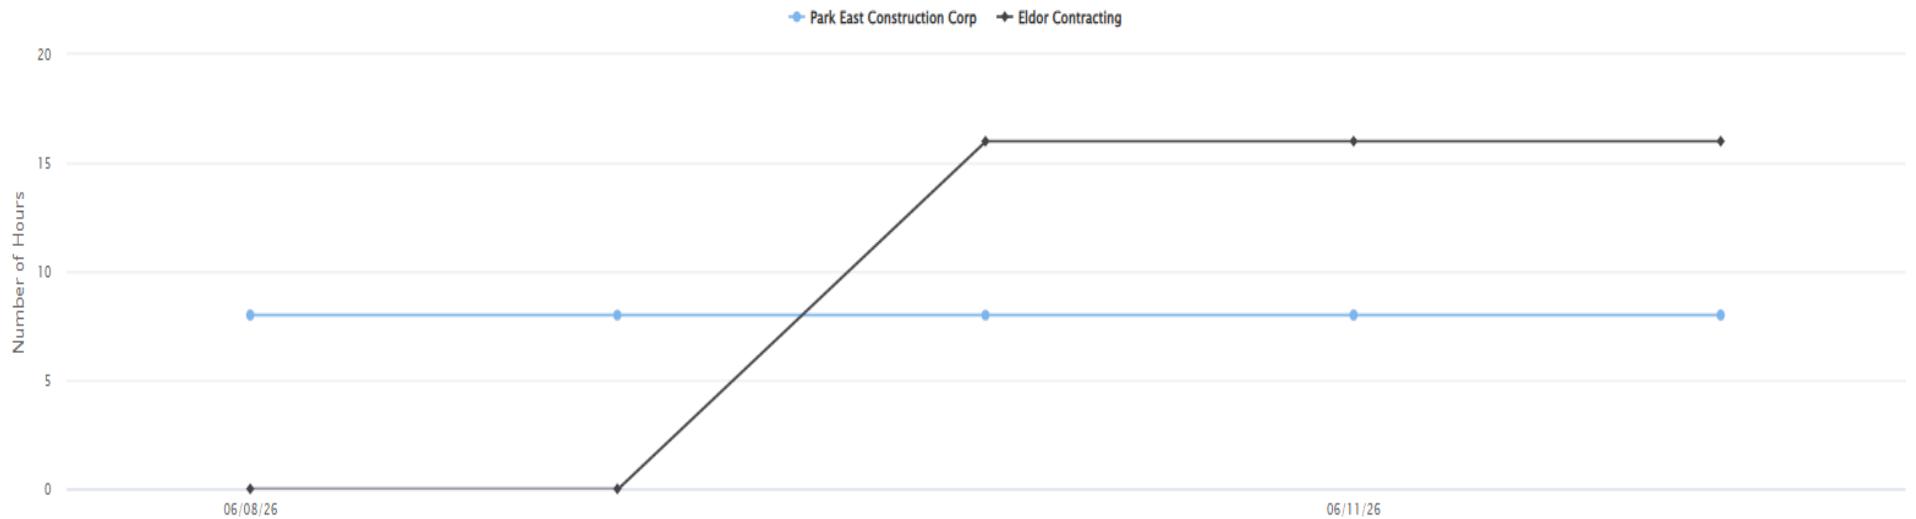


Hempstead UFSD – IAQ at Various Schools



Section V – Workforce Summary – Company/Hours

June 2026

▼ MANPOWER GRAPH

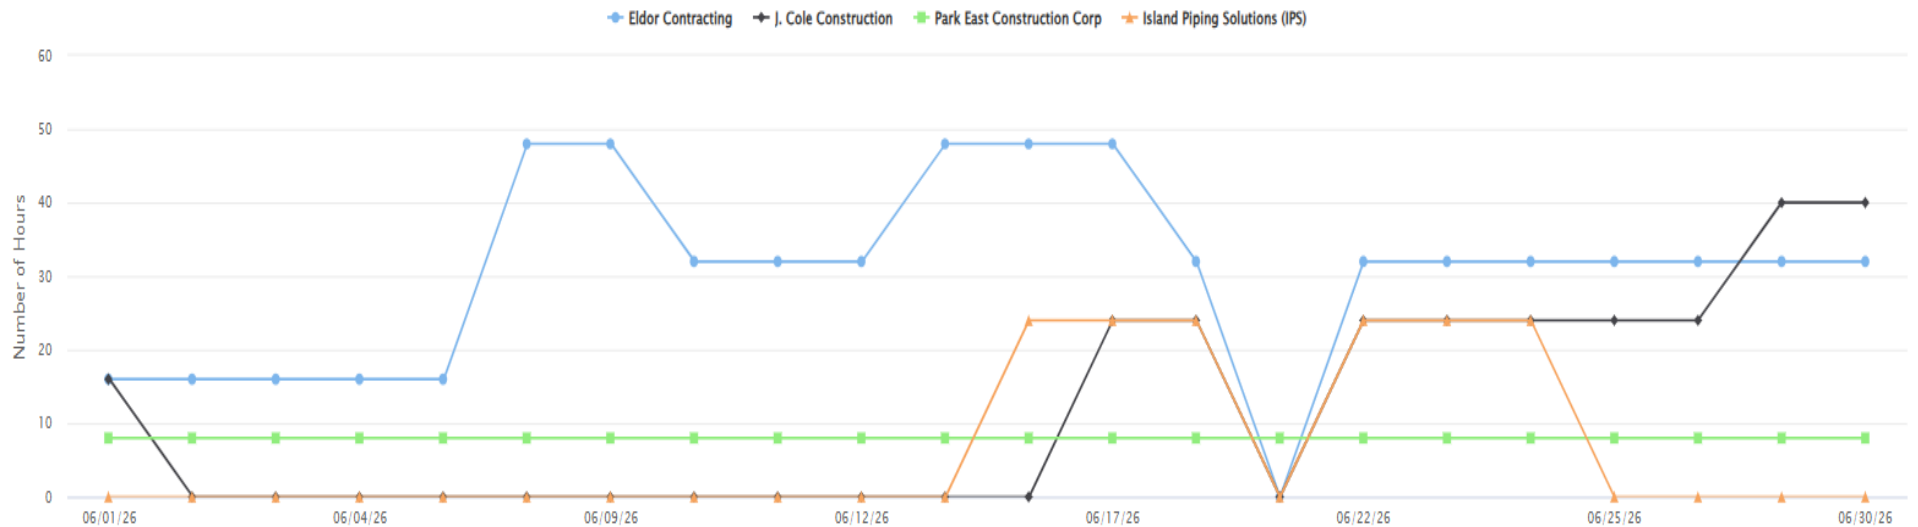


Hempstead UFSD – 2022 Bond Phase 3



Section V – Workforce Summary – Company/Hours

June 2026

▼ MANPOWER GRAPH

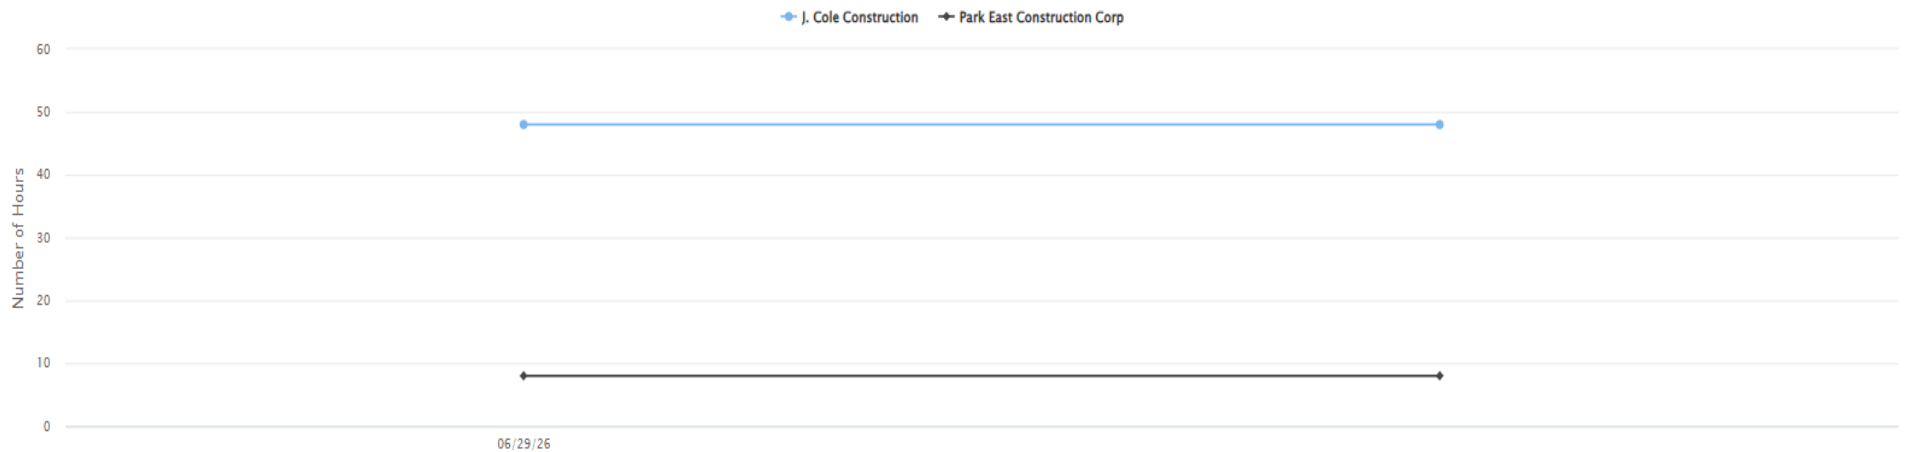


Hempstead UFSD – 2024 Bond Phase 2



Section V – Workforce Summary – Company/Hours

June 2026

▼ MANPOWER GRAPH

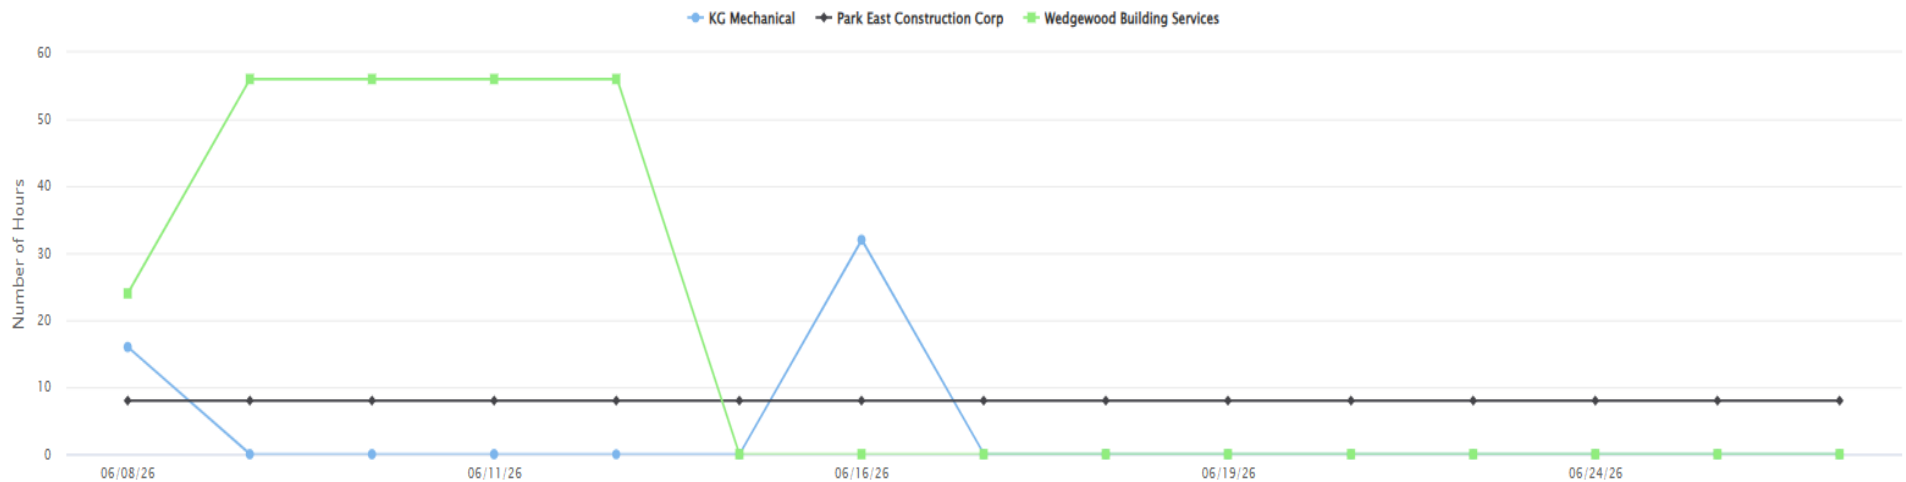

Hempstead UFSD – Paterson Boiler



Hempstead Union Free School District

June 2026

End of Progress Report
