



Monthly Progress Report

June 2026

Hempstead Union Free School District (ABGS MS)



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress June 2026

Section III – Work Projected for July 2026

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

June 2026

- **Hempstead UFSD – ABGS MS**
 - New addition to the existing building.
 - Abatement work throughout the existing building.
 - Classroom upgrades in the existing building.
 - New boilers installation in the existing building.
 - MEP upgrades throughout the existing building.



Section II - Work Progress

June 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continued installing steel beams and columns. 99% complete.
 - Continued installation of steel decking, 95% complete.
 - Poured concrete on 1st and 2nd floor behind gym area.
 - Started installing CMU block.
 - Started installed door frames on 1st and 2nd floor behind gym area.
- **Relle:**
 - Continued the rough-in for existing classrooms and the boiler room.
 - Installed risers and sleeves as needed for addition.
 - Temp lighting installed in new addition. 60% complete.
 - Roughing installed in CMU walls.
 - Roughing installed in ceilings.
- **Hirsch:**
 - Installed underground waste roughing in new addition.
 - Completed grease trap.
 - Completed toilet and sink carriers installation behind gym area.
 - Continued roughing for new addition.
- **RMS**
 - Continued installing piping for new boilers.
 - Marked out CUH locations on block walls.
 - Installed expansion tank and associated piping.
 - Started installing duct work roughing.



Section III - Work Planned July 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continue erecting steel and installing building decking.
 - Continue preparing floors for concrete and pour concrete.
 - Continue CMU block installation.
 - Demo girl's locker room, 207/209, and L2/L4.
- **Relle:**
 - Disconnect girl's locker room, 207/209, and L2/L4.
 - Continue roughing as needed for new addition.
- **Hirsch:**
 - Continue underground roughing and riser installation for new addition.
 - Disconnect girl's locker room, and 207/209.
- **RMS:**
 - Continue installing piping in boiler room.
 - Start installing hangers in the new addition.
 - Continue with duct roughing.




Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos

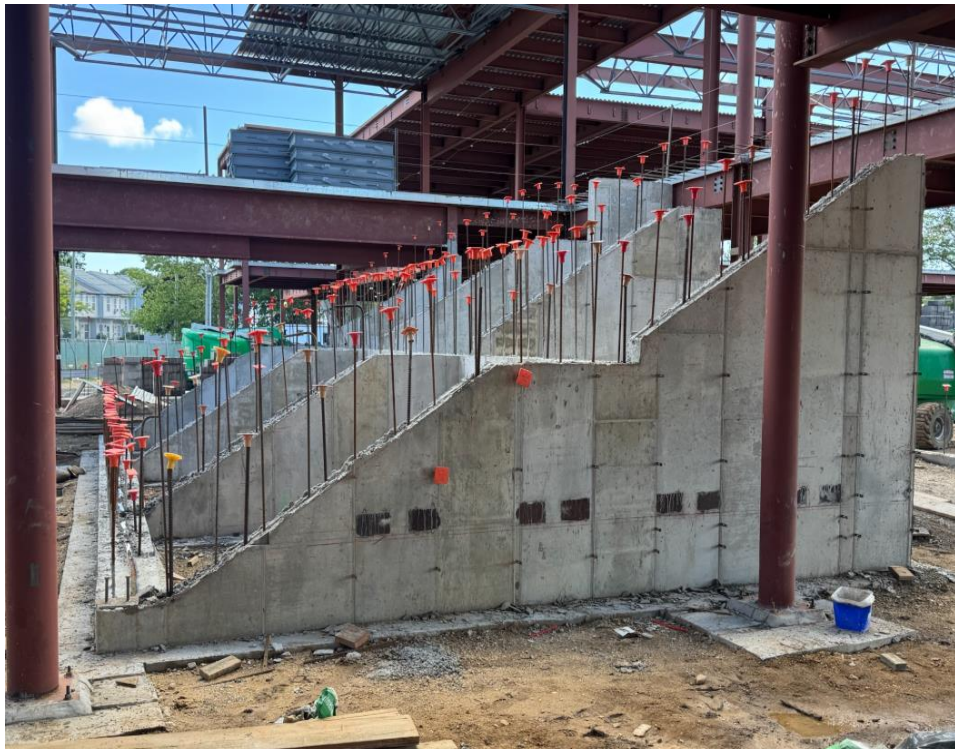

Hempstead ABGS MS



Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos



Hempstead ABGS MS




Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos

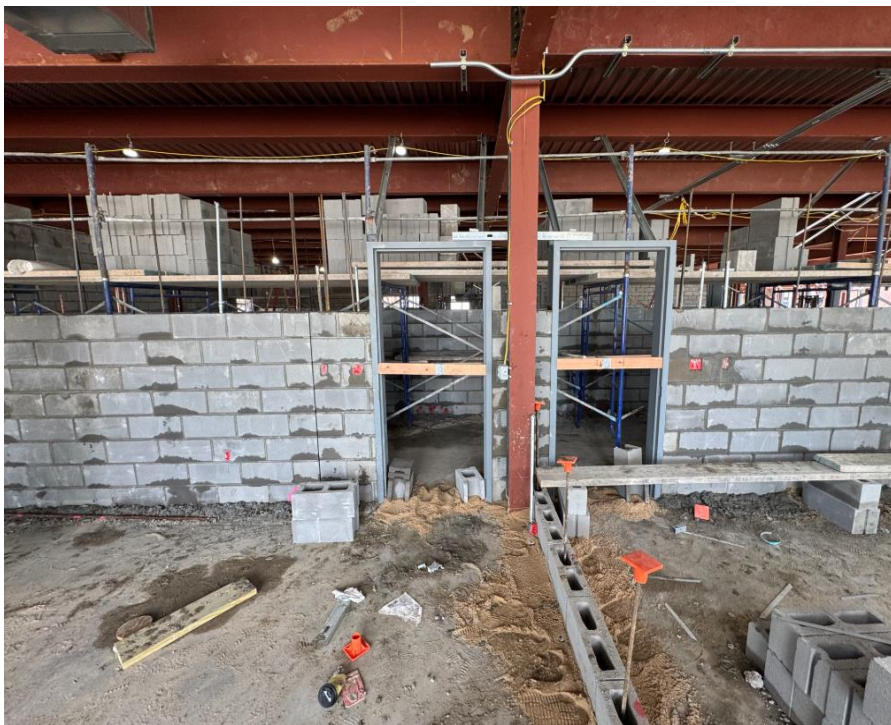


Hempstead ABGS MS



Section V – Workforce Summary – Company/Hours

June 2026

MANPOWER GRAPH

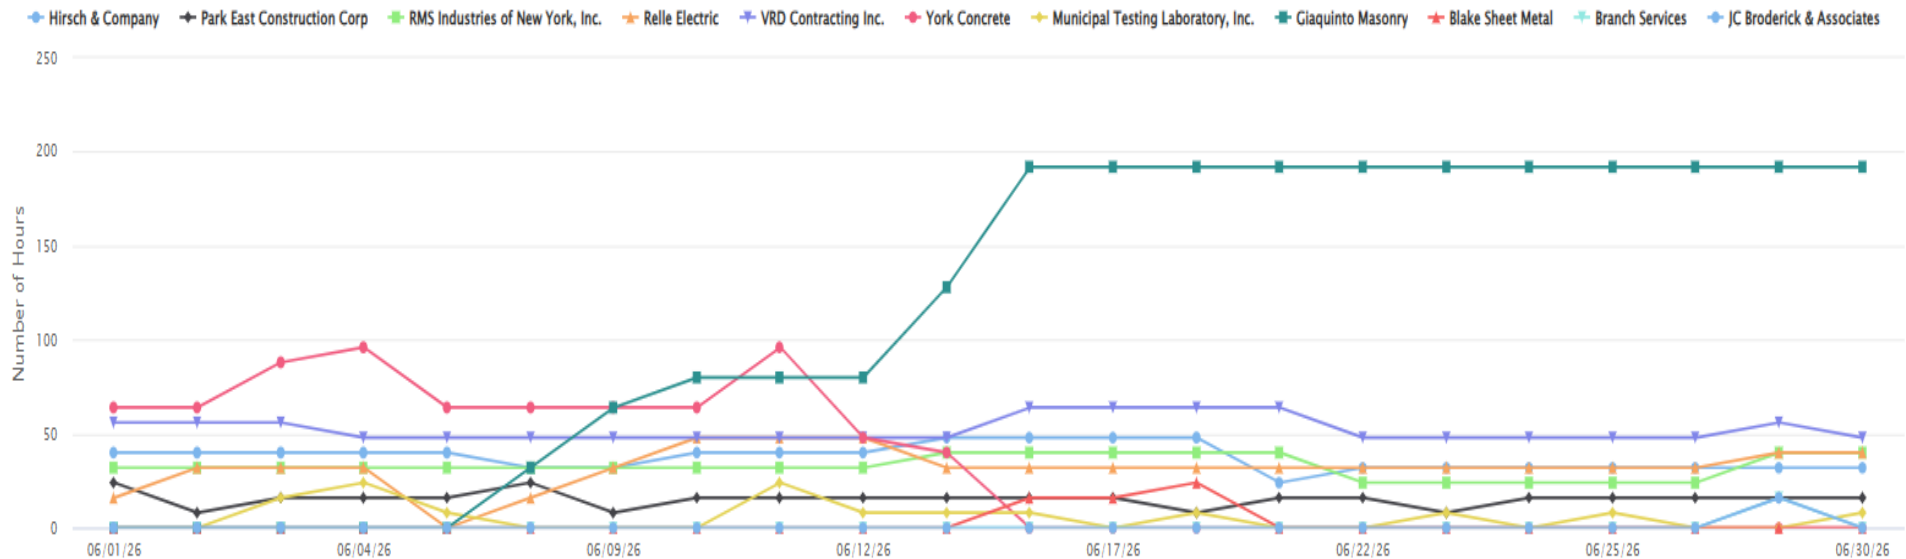

Hempstead ABGS MS



Hempstead Union Free School District (ABGS MS)

June 2026

End of Progress Report
