

Helen Caise Wade Elementary School

Week Ending July 03, 2026



➤ Completed Work:

- Installation of metal roof joists appears to be complete except at the gymnasium.
- MEP Installation of sprinklers heads have been installed. Partial sprinkler system has been tested.
- Installation metal roof deck appears to be approximately 85% complete except at the gymnasium.
- Placement of stone is complete at the gymnasium.
- Installation of the cable trays has begun at the second floor.
- Installation of furring channels for the metal panels and interior gypsum board has begun appears to be nearing completion.

➤ Upcoming Work / Look Ahead:

- Begin brick masonry.
- Continue Place concrete slab at the gymnasium.
- Continue setting roof joists and metal roof deck at the gymnasium and complete at the remainder of the building.
- Continue the installation of MEP.
- Construction Installation of roof to continue at the upper level.

Helen Caise Wade Elementary School



North Side of the Site and Building



Week Ending July 3, 2026

Helen Caise Wade Elementary School



Stone Placement at the Gymnasium



Week Ending July 3, 2026
3

Helen Caise Wade Elementary School



Installation of Sprinkler Heads and MEP at the Administration



Week Ending July 3, 2026

Helen Caise Wade Elementary School



Installation of Cable Tray at the Second Floor




Week Ending July 3, 2026

Helen Caise Wade Elementary School



Installation of Roofing above the Second Floor

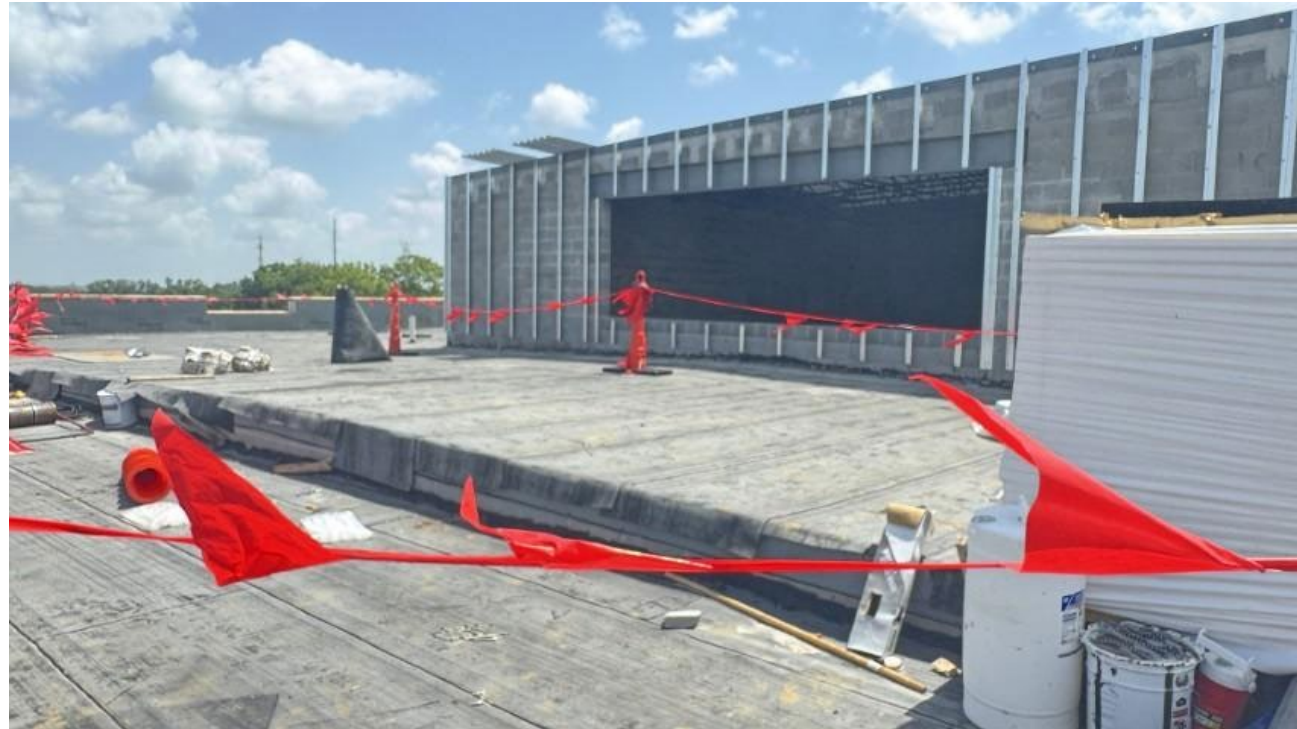

Week Ending July 3, 2026
6

Helen Caise Wade Elementary School



Metal Stud Framing for the Ceiling in the Media Center



Week Ending July 3, 2026

Helen Caise Wade Elementary School



Installation furring channels in the Media Center



Week Ending July 3, 2026

Helen Caise Wade Elementary School



Lawn has been Sown at the Street and Beginning to Establish



Week Ending July 3, 2026
