

New Henry Clay High School


Week Ending July 03, 2026

➤ Completed/Work in Progress:

- ICF placing and pouring, and the installation of IFAs at ICF walls is in progress.
- Laying of CMU walls and the installation of hollow metal frames is underway.
- Under-slab plumbing/electrical and concrete slabs are in progress.
- Steel erection is underway in all areas.
- Area D concrete roof structure is complete.
- Above ceiling MEP installation is in progress at areas A,B and C.
- Installation of stairs in all areas but the Gym is complete.
- West driveway retaining wall construction is complete.
- Interior metal stud wall & soffit framing in progress at Areas A, B & C.
- Area A & Area B roofing is in progress.
- Mechanical penthouse construction is in progress.
- CMU finishing & painting, and hanging drywall is in progress at areas A & B.

➤ Upcoming Look Ahead:

- Continue site grading.
- Continue with ICF walls, IFA frames, laying CMU walls and installing hollow metal frames.
- Continue with under-slab plumbing and electrical at Areas F & C.
- Continue pouring concrete slabs on grade at Areas F & C.
- Continue with steel erection A, C, E, F and G.
- Continue with above ceiling MEP installation at all areas.

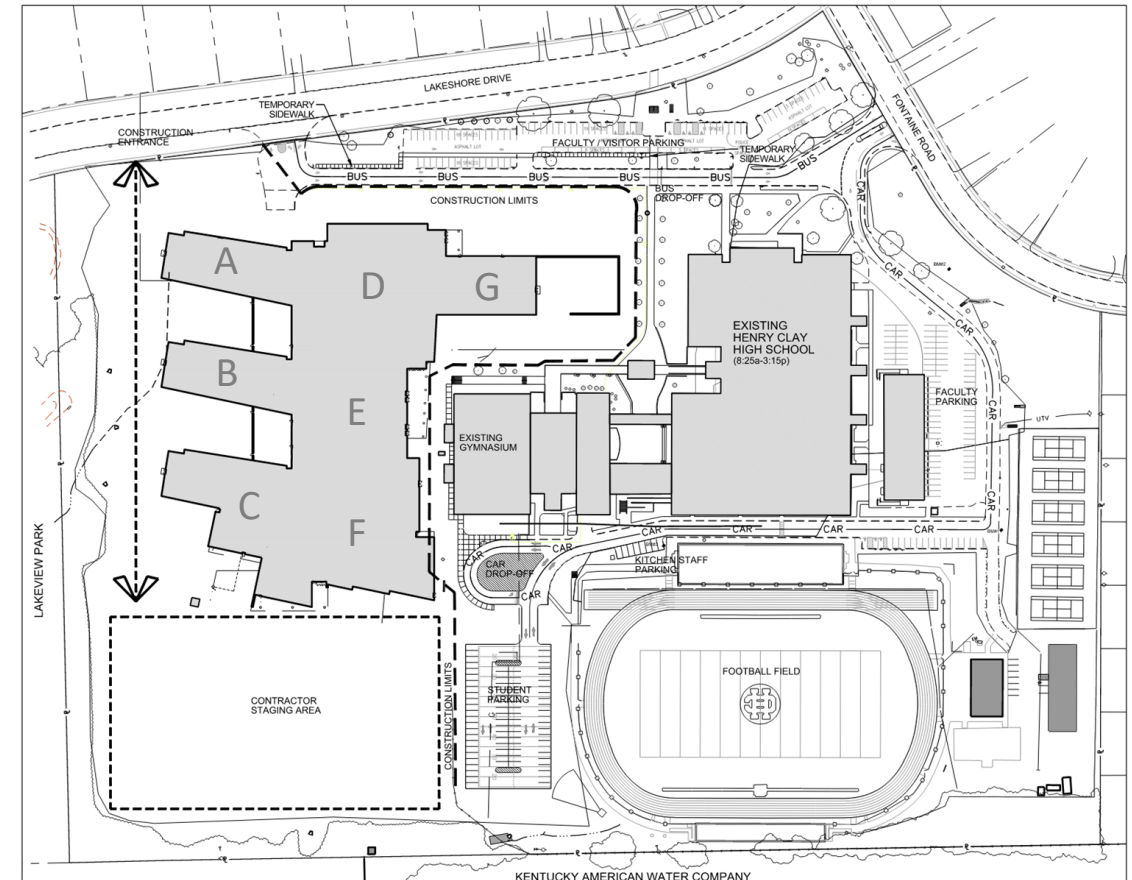

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School

Week Ending July 03, 2026

Areas A, B & C (Classroom Wings): Stone & Brick Veneer Masonry in Progress



New Henry Clay High School

Week Ending July 03, 2026

Level 1 Area G (Gym Lobby Entrance, Weight Room, ROTC & Health Classrooms): Stair G Installation is Complete with the Erection of Steel for the Curtain Wall in Progress



New Henry Clay High School

Week Ending July 03, 2026

Level 2 Area G (Media Center & Med Clinic): Floor Slab is Complete, ICF Walls & Framed Openings in Progress



New Henry Clay High School


Week Ending July 03, 2026

Level 2 Area G (Media Center & Med Clinic): Floor Slab & Stair G Installation is Complete, CMU Furring Walls are in Progress



New Henry Clay High School

Week Ending July 03, 2026



Area E (Gym): Concrete Floor Slab is Complete with South Locker Room CMU Walls in Progress



New Henry Clay High School

Week Ending July 03, 2026



Level 1 Area C (Cafeteria): Erection of Roof Structural Steel, ICF Construction at Cafeteria Perimeter Continues



New Henry Clay High School

Week Ending July 03, 2026



Area A Levels 1, 2, 3 (Classroom Wing): Painting of Hollow Metal Frames is in Progress

