

New London Spicer: MS/HS Phase 2

2026 Renovations

Weekly Update: Ending 07/19/26

Ongoing/ Completed:


- **Willmar Electric:** 90% complete with Main Level electrical items. Lower Level work starting 7/20/2026.
- **Acoustic Associates:** Lower Level E Hallway is 100% complete with new ACT padding & gridwork.
- **Acoustic Associates:** Working through pad completion within Lower Level E classrooms, 20% complete with gridwork within Lower Level D classrooms.
- **RJ Mechanical:** Flush and fill of the glycol system 100% complete. On 7/15/2026 water testing occurred, all areas passed. New glycol for Chiller arriving on 7/22/2026.
- **Chappel Central:** 100% complete with Main Level Mechanical installs. Lower Level work starting 7/22/2026.
- **BCI/Boulder Creek:** 100% complete with infill masonry work, four areas were patched.
- **BCI/MD Cleaners:** Ongoing final clean in 100% completed areas, 50% complete with Main Level final clean.
- **BCI/Rickway Carpet:** 100% complete with Weight Room resilient flooring.

2-Week Look Ahead:

- **BCI/MD Cleaners:** BCI & MD Cleaners to continue removing floor protection followed by final cleaning. 100% of Main Level to be turned over by 7/24/2026.
- **Acoustic Associates:** Complete grid and pad installation of lower level classrooms, Acoustic's to be done by 7/31/2026.
- **Balancing Pros:** Hydronic balancing to occur after chiller startup of 7/28/2026.
- **SitelogIQ:** Closeout process to begin taking place, SIQ to gather any outstanding contractor documentation.

Issues/Concerns/Other:

- **SitelogIQ:** NLS staff are no longer required to wear hard hats with grid & pad being completed in school working areas.
- **SitelogIQ:** Multiple 2x4 light screens, and a few desks/chairs within the building have been damaged. SitelogIQ to document affected rooms.

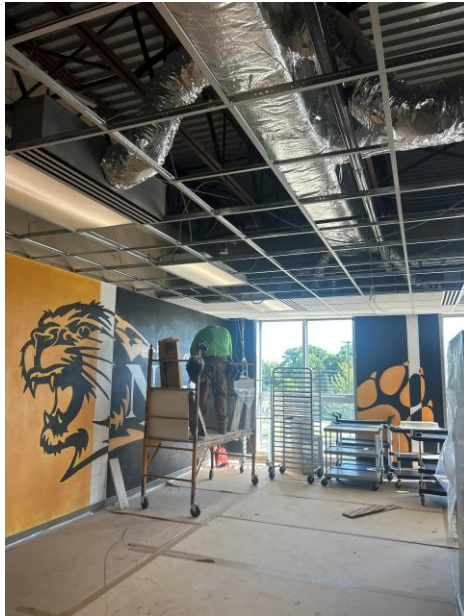


Area E – Cafeteria Pad Out



Weight Room Flooring Install



Area E - Stairwell Pad Out

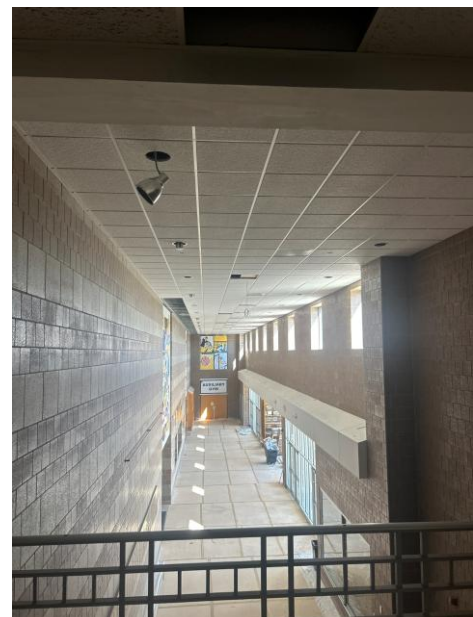

Area F – Finishing Touches
