




2023 BOND

# MAJOR PROJECTS UPDATE

JULY 2026



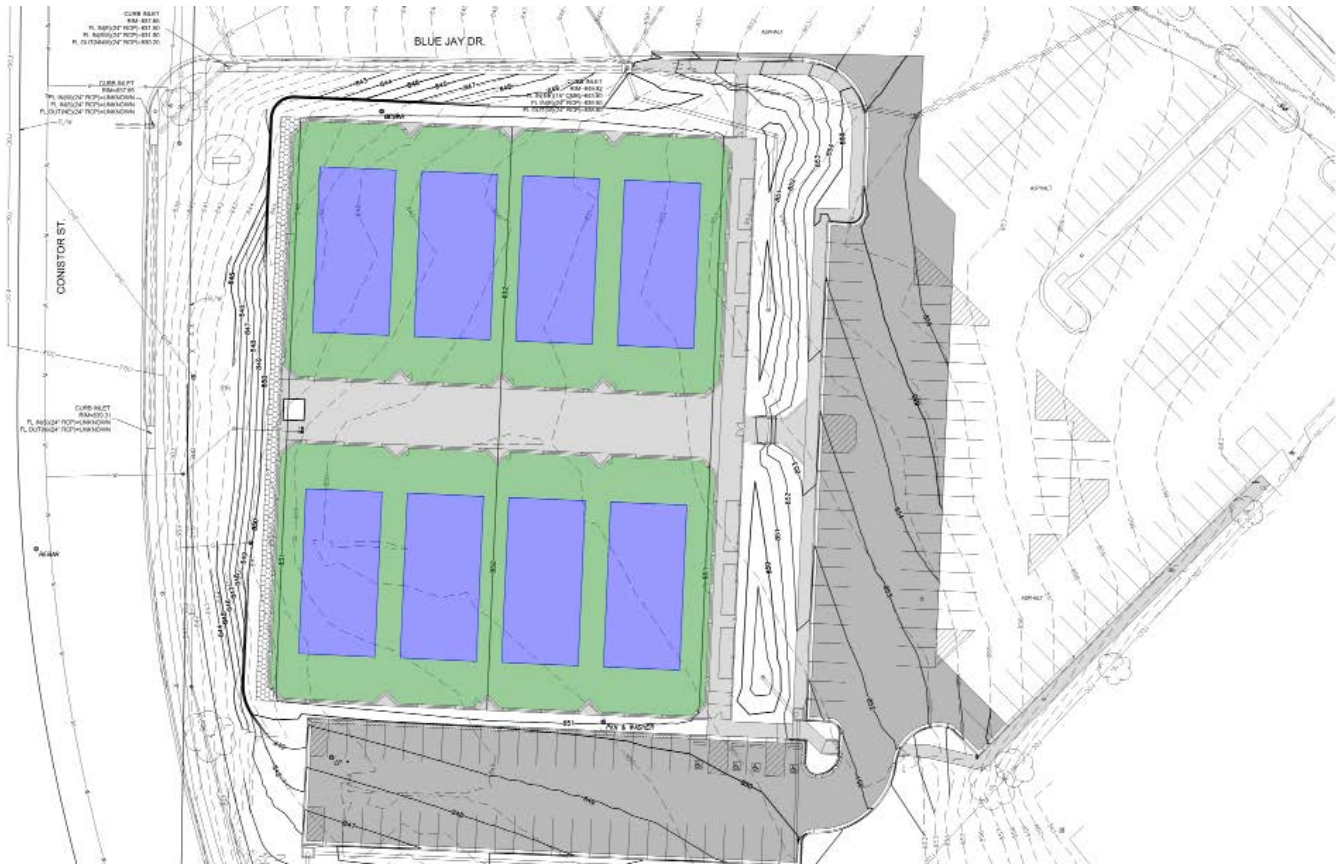

## Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

**Construction Start:** Spring 2023

**Construction Complete:** Fall 2023

**WEEKLY  
PROGRESS  
REPORT**

# Tennis Courts 11/13/2023

Liberty Public Schools



## PROJECT STATUS

- Courts Substantially Complete
- Turned Over 10/31
- Final Punch List Items Being Completed

## UPCOMING

Project Completion October 2023



North Courts Looking West



North Courts Looking Southwest



East Concourse Looking South



East Concourse Looking North

# WEEKLY PROGRESS REPORT



South Courts Looking West



Center Spectator Concourse Looking West



## Liberty High School Baseball/Softball Complex

### Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

### Softball Field

- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

### Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

**Construction Start:** Fall 2023

**Construction Complete:** Summer 2024



## Liberty North High School Baseball/Softball Complex

### Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

### Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

**Construction Start:** Fall 2023

**Construction Complete:** Summer 2024

WEEKLY  
PROGRESS  
REPORT

# LPS Ball Fields 08/09/2024

Liberty Public Schools



## PROJECT STATUS

### LNHS

- Punch List Completion
- Final Inspection Passed

### LHS

- Punch List Completion
- Retaining Wall Ongoing
- Final Sod Ongoing

## UPCOMING

### LHS

- City Inspection

Project Completion  
Baseball March 2024/Softball May 2024



LHS - Overall Site



LHS - Overall Site



LNHS - Overall Site



LNHS - Overall Site



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

**WEEKLY  
PROGRESS  
REPORT**

# LED Upgrades 12/11/2023

Liberty Public Schools



## PROJECT STATUS

South Valley MS - Upgrades Complete

Discovery MS - Upgrades Complete

EPiC Elementary - Upgrades Complete

Liberty North High School - Upgrades  
Ongoing

## UPCOMING

Everygy Inspections - All Four Schools  
Emergency LED Fixtures

Project Completion  
December 2023



Liberty North HS



Liberty North HS



Liberty North HS



Liberty North HS

**WEEKLY  
PROGRESS  
REPORT**

# LED Upgrades 11/13/2023

Liberty Public Schools



## PROJECT STATUS

South Valley MS- Upgrades Complete

Discovery MS - Upgrades Complete

EPiC Elementary - Upgrades Complete

LNHS - Upgrades Ongoing


## UPCOMING

Every Inspection All Four Schools  
Emergency LED Fixtures

Project Completion  
December 2023



South Valley Middle School

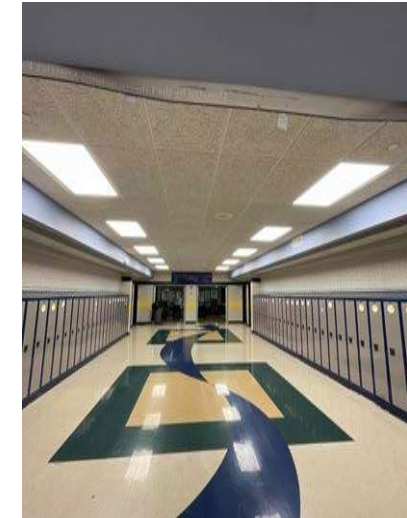

South Valley Middle School



Discovery Middle School



Discovery Middle School

# WEEKLY PROGRESS REPORT



Epic Elementary



Epic Elementary



Liberty North High School




Liberty North High School



## EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother's Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

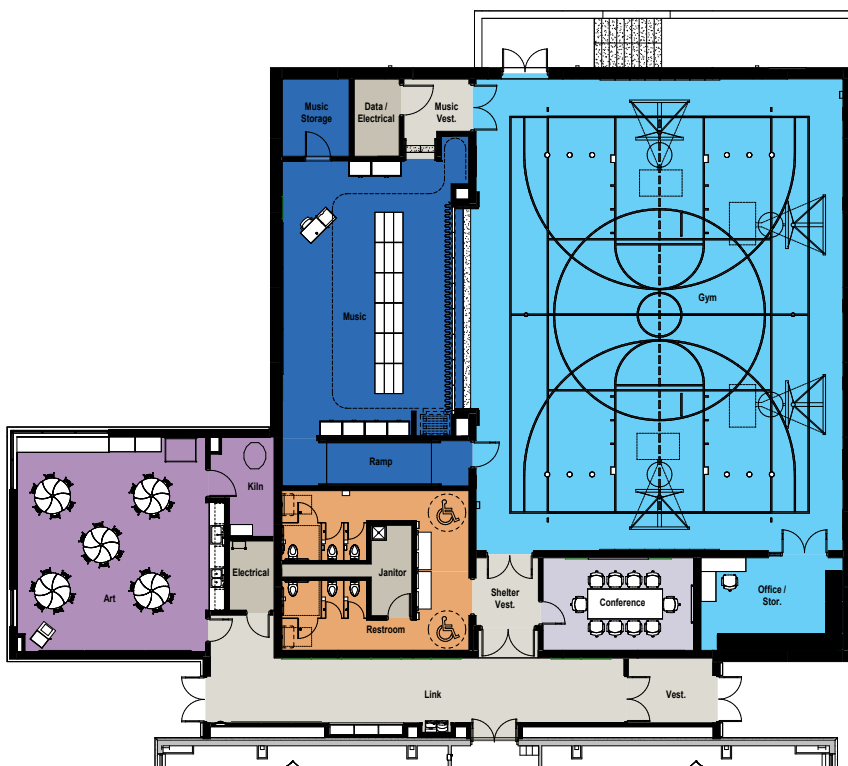

▲ Addition



▲ Renovation Area

## PROJECT STATUS

EPiC Elementary  
- Substantially Complete  
- TCO Issued as of 03/03/2025

## UPCOMING

EPiC Elementary  
- Remaining Punch List Items


Project Completion  
EPiC February 2025



EPiC Elementary - Gym



EPiC Elementary - Link

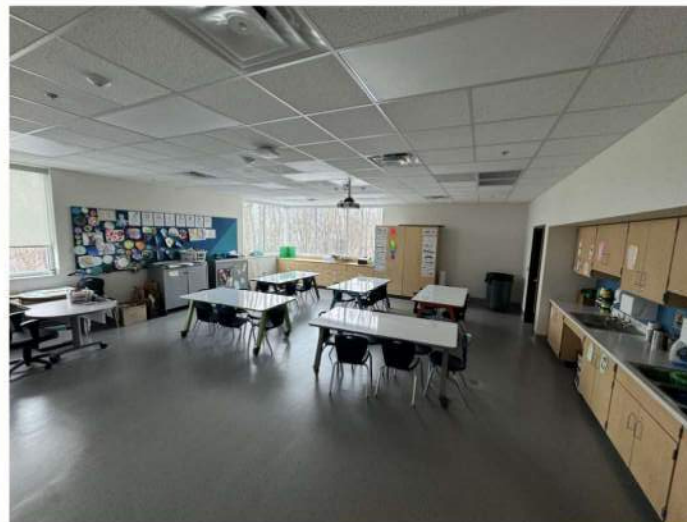

EPiC Elementary - Art Room





EPiC Elementary



## Discovery Middle School

- 11,000 square foot addition
  - ICC 500 rated shelter
  - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
  - Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025

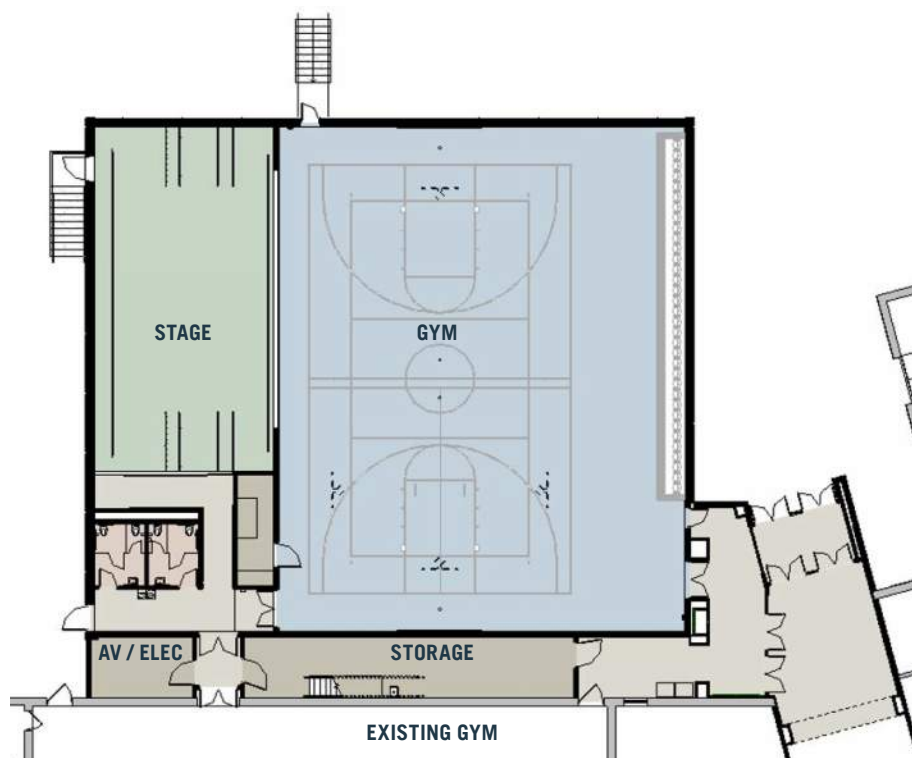

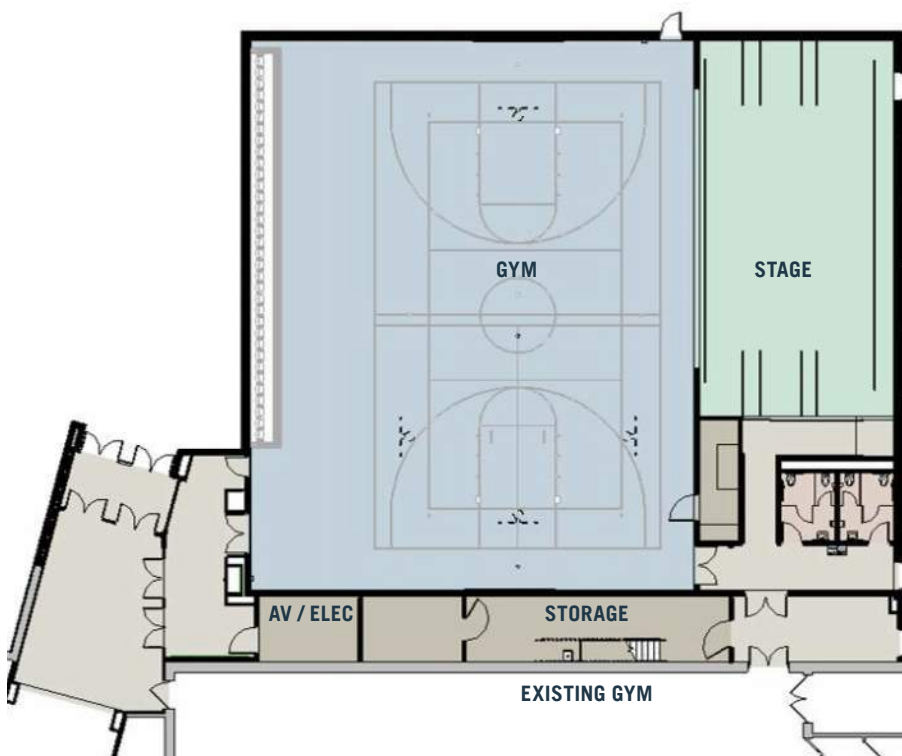

## South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025

WEEKLY  
PROGRESS  
REPORT

# Storm Shelters 09/08/2025

Liberty Public Schools



## PROJECT STATUS

SVMS and DMS  
- Theatrical Equipment & Lighting  
Ongoing  
- Schools have received Final  
Occupancy

## UPCOMING

SVMS and DMS  
- Wall Graphics

Project Completion  
DMS&SVMS August 2025 COMPLETE



DMS Exterior View



SVMS Exterior View



Stage Curtains From Stage




Stage Curtains from Gym



## Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule:  
Fall 2023–Spring 2025

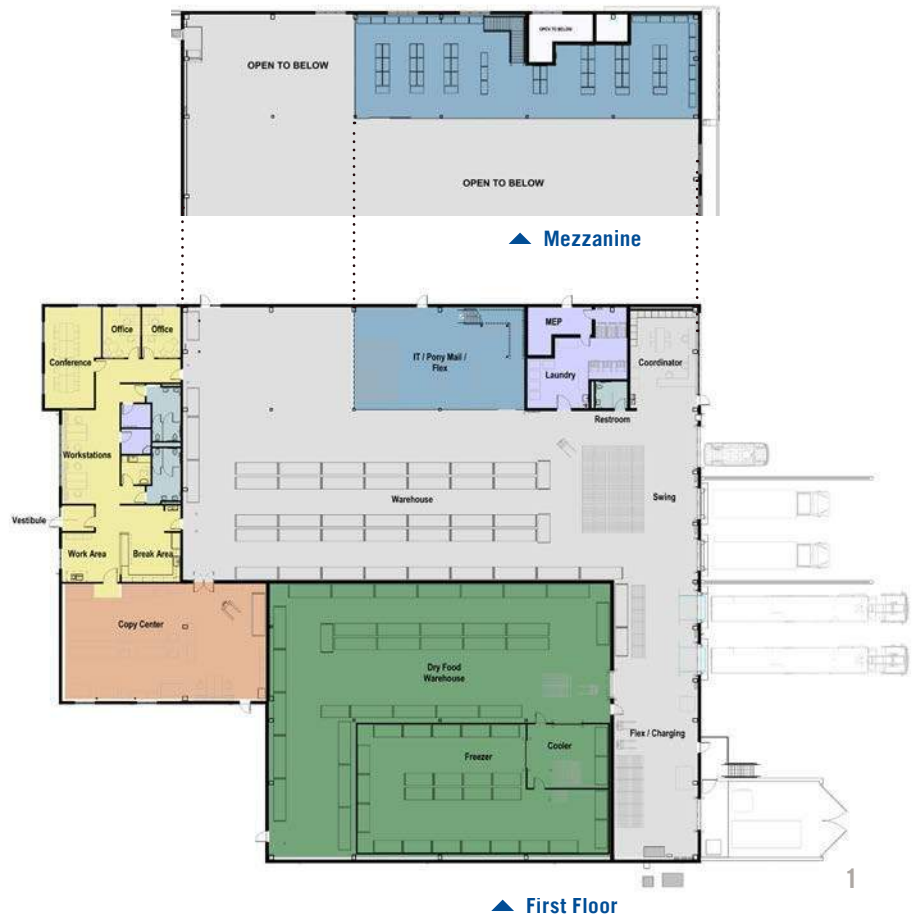

**WEEKLY  
PROGRESS  
REPORT**

# Distribution Center 6/12/25

Liberty Public Schools



**6/12/25**

## PROJECT STATUS

- CO received on 6/6
- Owner moved in 6/6
- Final punch ongoing

## UPCOMING


- Final punch items
- ECB install on south hill side slope
- Closing out open items list



Overall East lot



Warehouse

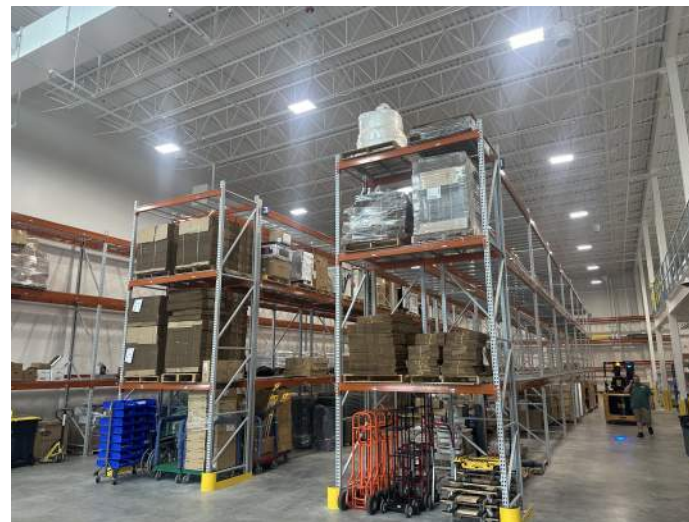

Warehouse



Workstations A102a

# WEEKLY PROGRESS REPORT

6/12/25



Workstations A105



Corridor A111



Overall Site



Overall Site

Fine Arts  
 Kid's Zone  
 Technology  
 Shared Amenities  
 Building Systems  
 Future Phase



## District Technology Center

- Renovated workspace for District's Technology, Fine Arts, and Kid's Zone departments
- Shell space for future growth
- Minor exterior patch + repair improvements
- Projected Construction Schedule:  
Fall 2023 - Summer 2024

**WEEKLY  
PROGRESS  
REPORT**

# District Tech Center 7/12/24

Liberty Public Schools



**7/12/24**

## PROJECT STATUS

District Technology Center:

- Completed Communications Install
- Completed Interior Paint
- Completed All Exterior Paint
- Completed Floor Install
- Completed Data Pod Install
- Completed HVAC Equipment Install
- Completed Landscaping/Fence Install
- Completed Generator Install
- Certificate of Occupancy - Received July 9th

## UPCOMING

District Technology Center:

- Complete Punchlist Work
- Complete Furniture Move In
- Server Switchover July 13th
- Staff Move in July 16th

Project Completion July 2024



IT Reception



Exterior



Kid's Zone Open Office



Fine Arts Open Office



Fine Arts Workshop



Restrooms



Breakroom



Data Pod Install

# WEEKLY PROGRESS REPORT

7/12/24



Exterior



Medium Conference Room



Kid's Zone Storage



IT Open Office



## Heritage Middle School

- 39,000 square feet academic renovation
- Grade level neighborhoods with flex collaboration spaces
  - Integrated SPED resources
- Exterior masonry repair & window replacement
  - Elevator Upgrades
- Projected Construction Schedule:  
Spring 2025–Fall 2025



LEVEL 3



LEVEL 2



LEVEL 1



LEVEL 0

WEEKLY  
PROGRESS  
REPORT

# Heritage Middle School

Liberty Public Schools



1/10/25

## PROJECT STATUS

Heritage Middle School

1964 Wing:

- Completed Floor Install
- Completed MEP Trimout
- Completed Specialty Finish Install
- Completed Owner Move In
- Completed Final Inspections
- Continued Punchlist Work

## UPCOMING

Heritage Middle School

1964 Wing:

- Complete Punchlist Work

Projected Completion: December 2024



1964 (Area A)



1964 (Area A)



1964 (Area A)



1964 (Area A)

# WEEKLY PROGRESS REPORT

1/10/25



1964 (Area A)



1964 (Area A)



1964 (Area A)



1964 (Area A)

**WEEKLY  
PROGRESS  
REPORT** Liberty Public Schools



**PROJECT STATUS**

**UPCOMING**




**WEEKLY  
PROGRESS  
REPORT**   **Liberty Public Schools**



**PROJECT STATUS**

**UPCOMING**



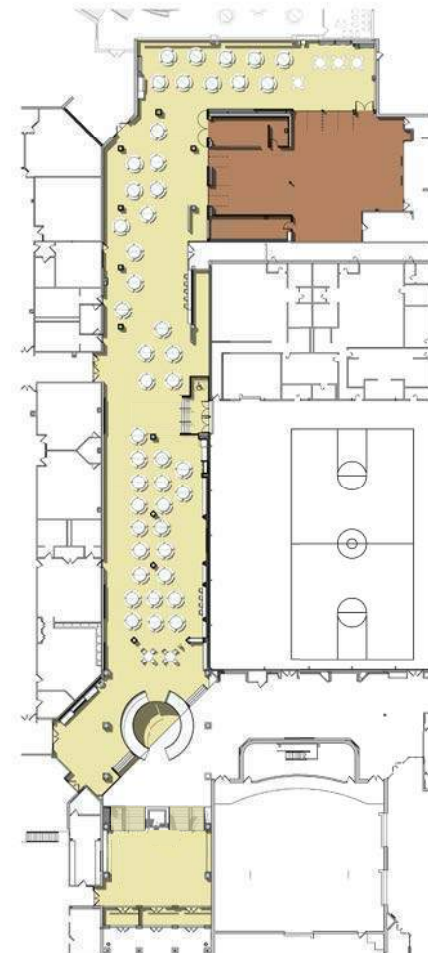

**PHASE 2**

## Liberty High School

- Square footage: 40,800 SF
- Renovation to FACS, SPED and Art classrooms
- Renovated scramble & dining area
- LED lighting replacement
- Project Construction Schedule:  
Summer – Fall 2024 & 2025



**PHASE 1**

WEEKLY  
PROGRESS  
REPORT

# Liberty High School

Liberty Public Schools



1/10/25

## PROJECT STATUS

Liberty High School:

- Continued Punchlist
- Completed Owner Move In
- Completed FACS Room Inspections

## UPCOMING

Liberty High School:

- Complete Punchlist

Project Completion: December 2024



LHS 100's Wing



LHS 100's Wing



LHS 100's Wing



LHS 100's Wing

# WEEKLY PROGRESS REPORT

1/10/25



LHS 100's Wing



LHS 100's Wing



LHS 100's Wing



LHS 100's Wing

**WEEKLY  
PROGRESS  
REPORT** Liberty Public Schools



**PROJECT STATUS**


**UPCOMING**





## Shop Building

- 1,800 Square Foot New Building
- Flexible Open Plan
- Patio & Secure Breezeway
- Woodworking Area
- Metalworking Area
- Flex-space for Lectures or Large Projects
- Projected Construction Schedule: Spring 2024–Spring 2025

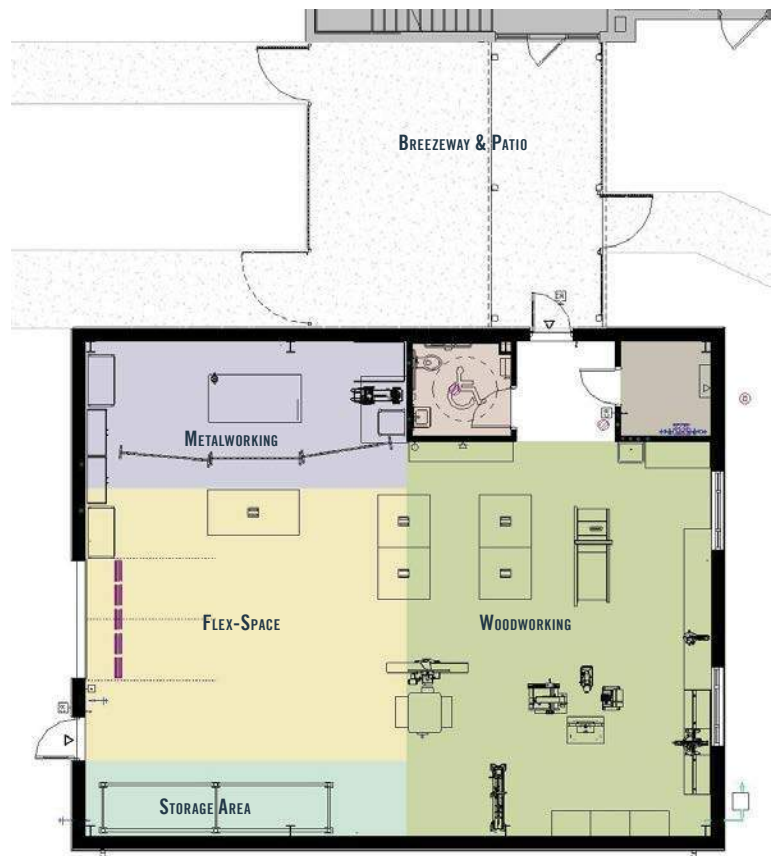

▲ Floor Plan

**WEEKLY  
PROGRESS  
REPORT** Liberty Public Schools



**PROJECT STATUS**

**UPCOMING**






# WEEKLY PROGRESS REPORT




## Recreation Court

- 3,531 Square Foot New Court
- Court Lines for Basketball & Pickleball
- Additional Area for Temporary Bleachers
- Projected Construction Schedule:  
Spring 2024–Spring 2025

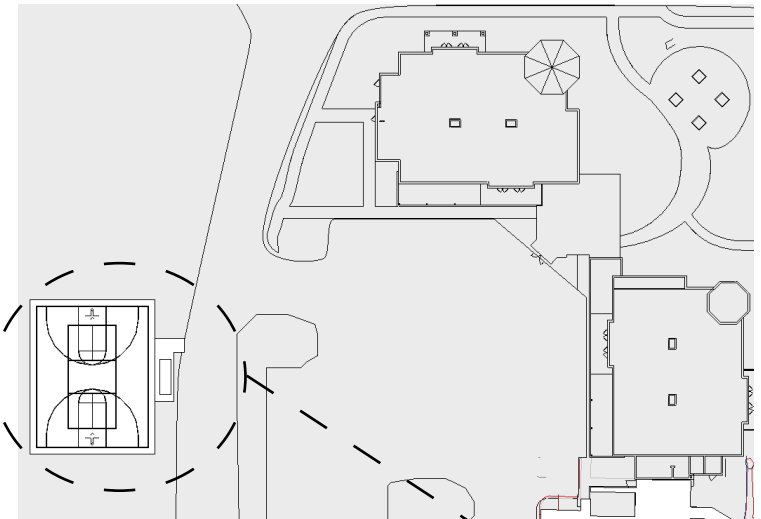

Overall Site Plan

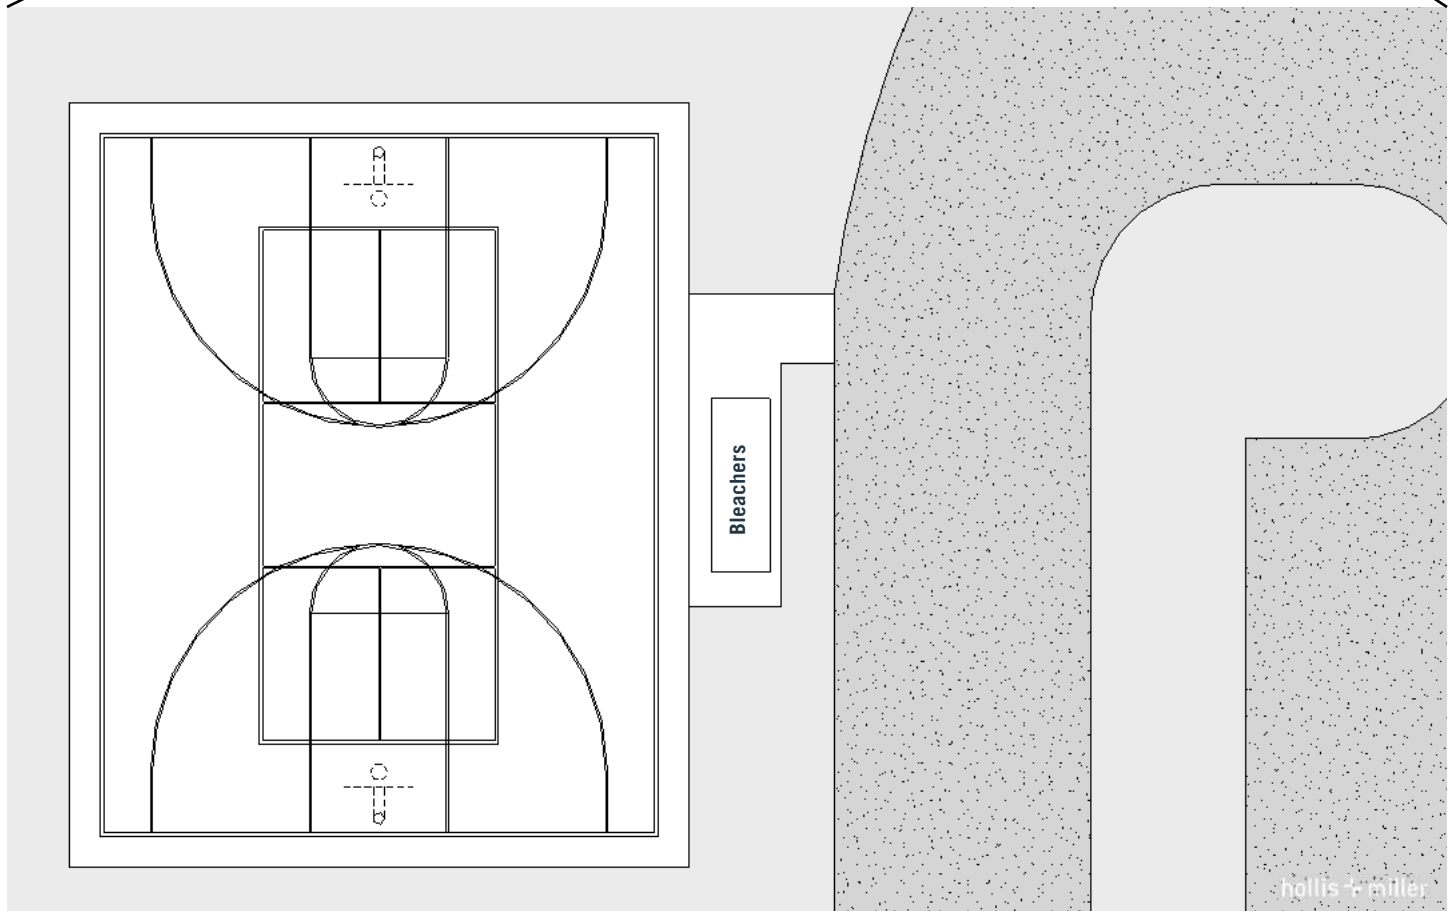

Enlarged Site Plan

## Interior Renovation

- Nurse Room Relocation
- Renovated Teacher Workroom
- SPED Classroom Toilet Renovation
- New Admin Reception Entry Door & Counter
- Staff Restroom Renovation
- Lactation Room
- LED Lighting Replacement
- HVAC Replacement
- Roof Repairs
- Projected Construction Schedule:  
May 2024 - August 2025



▲ Enlarged Floor Plan




▲ Overall Floor Plan

## Interior Renovation


- Nurse Room Renovation
- Administration Office Renovation
- New Admin Reception Desk & Entry Door
- Lactation Room
- Group & Staff Restroom Renovation
- LED Lighting Replacement
- HVAC Replacement
- Projected Construction Schedule:  
May 2024 - August 2025



Administration

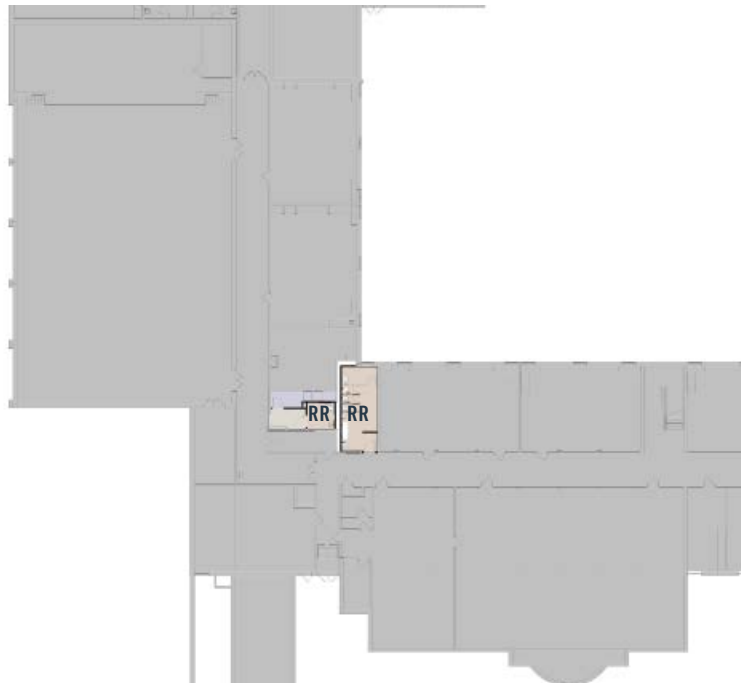

Partial First Level Floor Plan

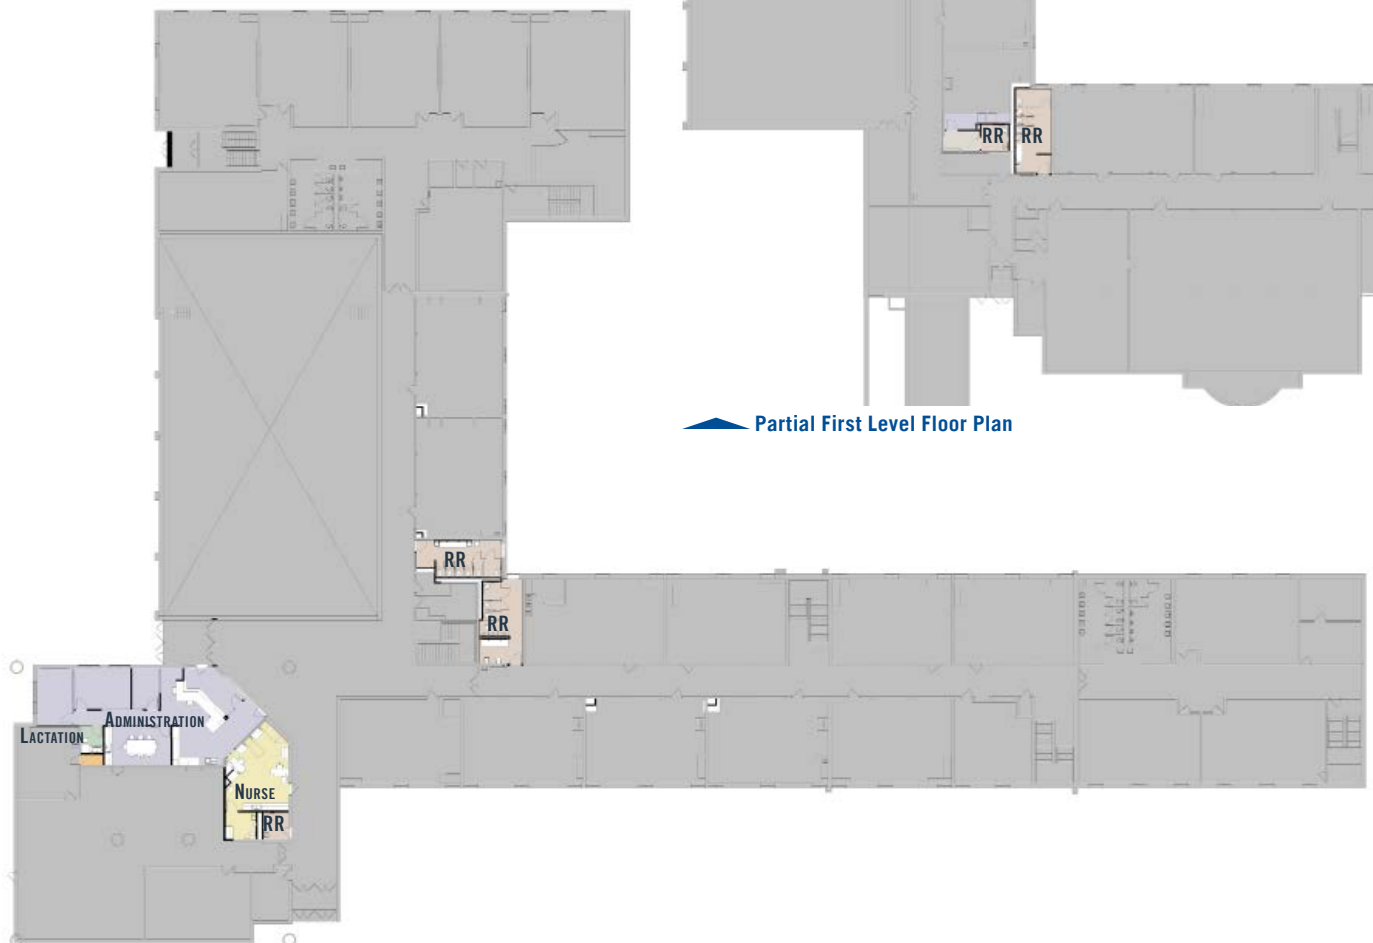


Overall Second Level Floor Plan

## Interior Renovation

- Nurse Room Relocation
- Group & Staff Restroom Renovation
- New Admin Reception Desk & Entry Door
- Gym Stage Renovation into Staff Offices & PE Storage
- Lactation Room
- Media Center Wing LED Lighting
- Projected Construction Schedule:  
May 2024 - August 2025



Administration

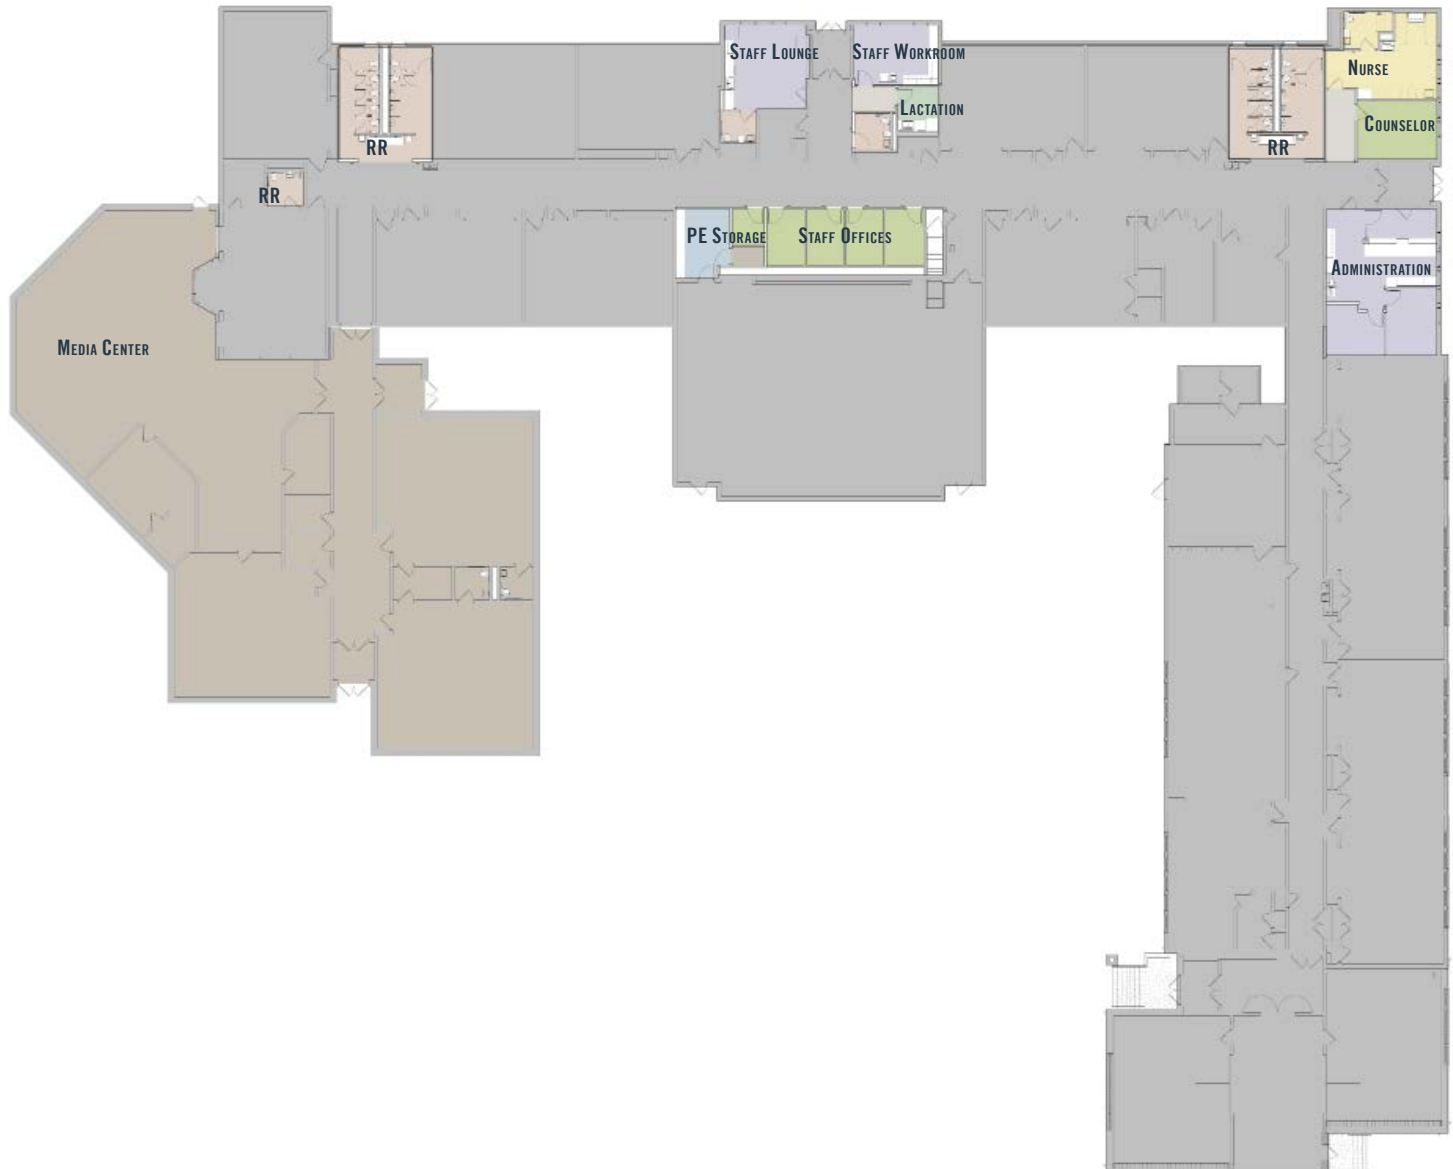

Overall Floor Plan

**WEEKLY  
PROGRESS  
REPORT**

**Doniphan, Franklin, and Ridgeview  
Summer Renovation Projects  
Liberty Public Schools**



**8/9/24**

**PROJECT STATUS**

Doniphan, Franklin, and Ridgeview:

- Completed MEP Install
- Completed Drywall Install
- Completed Ceiling Grid Install
- Completed Paint
- Completed Tile
- Completed Casework Install
- Completed Flooring Install
- Completed Epoxy Install
- Completed Specialties Install
- Began Punch List Work

**UPCOMING**


Doniphan, Franklin, and Ridgeview:

- Complete Punch List Work
- Complete Final Inspections
- Furniture Move-In

Project Completion: August 2024




Franklin - Main Office

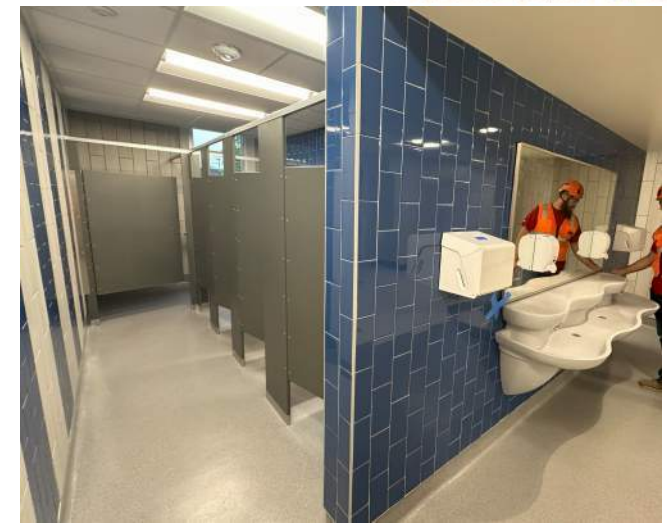

Franklin - Restrooms



Franklin - Workroom

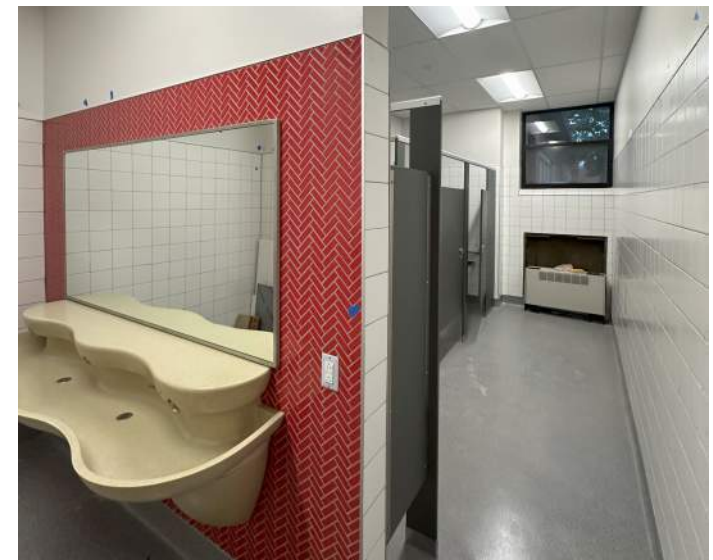

Ridgeview - Level 2 Restroom

# WEEKLY PROGRESS REPORT

8/9/24



Ridgeview - Main Office



Doniphan - Main Office



Doniphan - Assistant Principal Office



Doniphan - Teacher's Lounge

**WEEKLY  
PROGRESS  
REPORT**

# ADES and RES Phase 2

Liberty Public Schools



**9/10/25**

## PROJECT STATUS

Alexander Doniphan:

- Continue Roof Demo and Installation
- Owner Move In
- Punchlist
- Final Cleaning

Ridgeview:

- Install New Stage Platforms
- Owner Move in
- Punchlist
- Final Cleaning

## UPCOMING

Alexander Doniphan

- Complete Roof Installation
- Complete Punchlist

Ridgeview

- Complete Punchlist



Alexander Doniphan



Alexander Doniphan



Ridgeview



Ridgeview



## Liberty Middle School - Track & Field

- 6-lane track
- 195' x 360' natural turf soccer field
- Field events including high jump, long jump, shot put, and discus
- Updated lighting
- Concessions and restroom refresh
- New onsite storage

WEEKLY  
PROGRESS  
REPORT

# LMS Track & Field

Liberty Public Schools



## PROJECT STATUS


Project Complete

## UPCOMING



## LIBERTY MIDDLE SCHOOL SPED

- Classroom connection & finish upgrades
- SPED restroom renovation
- Changing room addition
- SPED swing installation

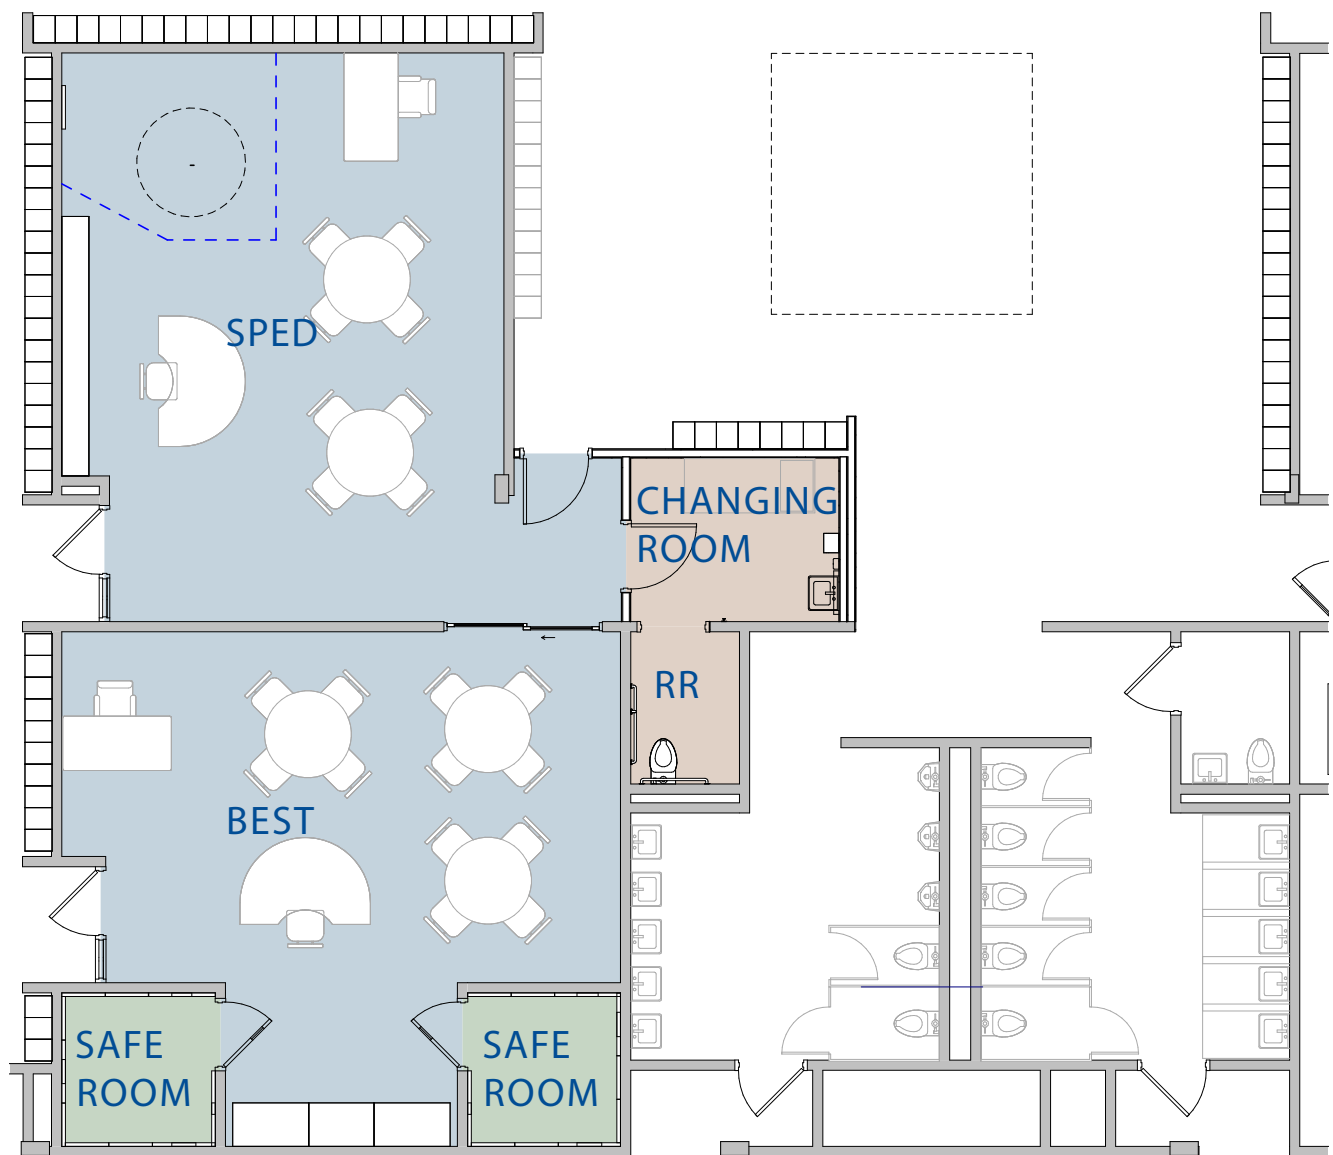

**WEEKLY  
PROGRESS  
REPORT**

**Liberty Public Schools**



**PROJECT STATUS**

**UPCOMING**





**WEEKLY  
PROGRESS  
REPORT** Liberty Public Schools



**PROJECT STATUS**

**UPCOMING**





## Playground Upgrades - Locations

- EpiC Elementary School
- Alexander Doniphan Elementary School
- Lillian Schumacher Elementary School
- Manor Hill Elementary School
- Ridgeview Elementary School
- Lewis & Clark Elementary School
- Liberty Oaks Elementary School
- Shoal Creek Elementary School
- Franklin Elementary School
- Warren Hills Elementary School
- Kellybrook Elementary School
- Early Childhood Center
