

BOND ADVISORY TEAM MEETING #15

August 3, 2026



Welcome Back!



Introductions

Please introduce yourself including your name and role (e.g. parent representative, student representative, school board member, etc.)


Bond Advisory Team (BAT) Feedback



Members are invited to share feedback that they have regarding the Bond Program and feedback that they have received/heard from the community

- What is going well?
- What are your current concerns?
- What have feedback have you received from the community whether hearing feedback first-hand or reading comments on social media platforms?
- Any general questions?

Update From Construction Management Team



Overview of
Construction Timeline



Current Progress and
Upcoming Milestones




Budget and Resource
Allocation



Key Considerations
and Challenges

Overview of Construction Timeline



New Craig Road Elementary School – **2025-2027** – **Early Site Grading Complete, Construction in Spring 2026**

Windsor and Salnave Bus Loops – **Completed Summer 2025**

Cheney HS Stadium Upgrades, Plus Varsity Lockers – **Completed Summer 2025**

Salnave Elementary – Boiler, Pumps, Switchgear – **Boiler, Pumps Completed 2025; Switchgear Summer 2026**

Windsor, Salnave and Betz – Chillers – **Completed Summer 2025**

2N at Snowdon, CMS, and WMS – **Completed Summer 2025**

Laminated Glass Film at Vestibules District-Wide – **2025-2026** – **Completed Fall 2025**

CHS, Elementary School Interior LED Lighting – **2026-2027** – **Start Summer 2026 – Summer 2027**

CHS, Betz, Sunset, and Windsor New Controllers and Cabling – **2026-2027** - **Summer 2026**

New Hot Water Heaters and Water Softeners District-Wide – **2025-2027** – **Summer 2026**

Expand Kitchens at Windsor and Salnave – **2026** – **Construction at Salnave March 2026; Windsor June 2026**

Tie Old-to-New District Wide – **Sunset, Windsor Completed 2025; CHS and Betz Summer 2026 - Summer 2027**

Project Update



New Skyway Elementary School

- Masonry at the gymnasium final lift has been completed and fully grouted.
- Currently installing masonry veneer at the gymnasium
- Installing vapor barrier at slab – working to start pouring slabs within the next few weeks
- Structural steel currently going up around the building



Project Update



New Skyway Elementary School



Current Progress And Upcoming Milestones




Expand Kitchen at Salnave Elementary School

- Construction efforts have been steadily progressing.
- \$47,000 in change orders to-date primarily due to existing conditions uncovered during the demolition phase. Change orders are charged to the project contingency. Project is still currently tracking within budget.
- Salnave construction March 1st, 2026 – **September 2026**. Construction efforts are currently running behind schedule due to supply chain issues – specifically with the kitchen equipment. Meals will be delivered to students as they were during the previous school year. Will utilize the newly expanded breakfast areas to serve meals to students.

Current Progress And Upcoming Milestones



Expand Kitchen at Salnave Elementary School

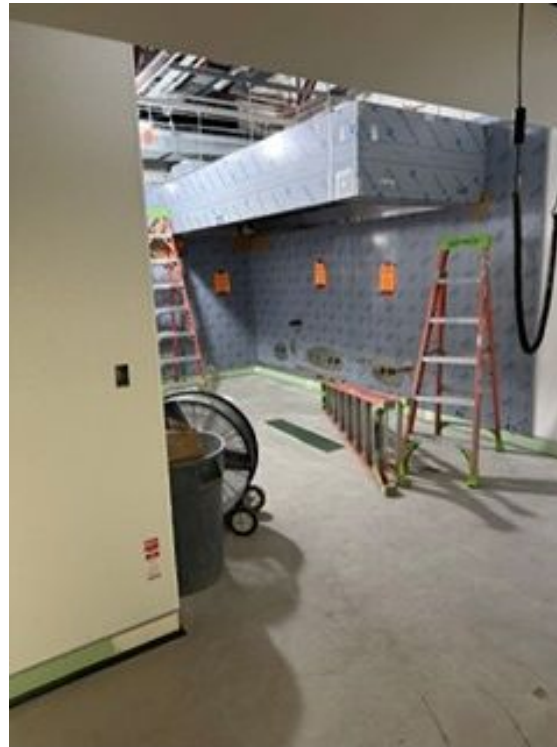


Current Progress And Upcoming Milestones



Expand Kitchen at Windsor Elementary School

- Windsor construction –June – December 18th, 2026
- Construction efforts are currently under way with switchgear installation substantially complete and selective demolition substantially complete.

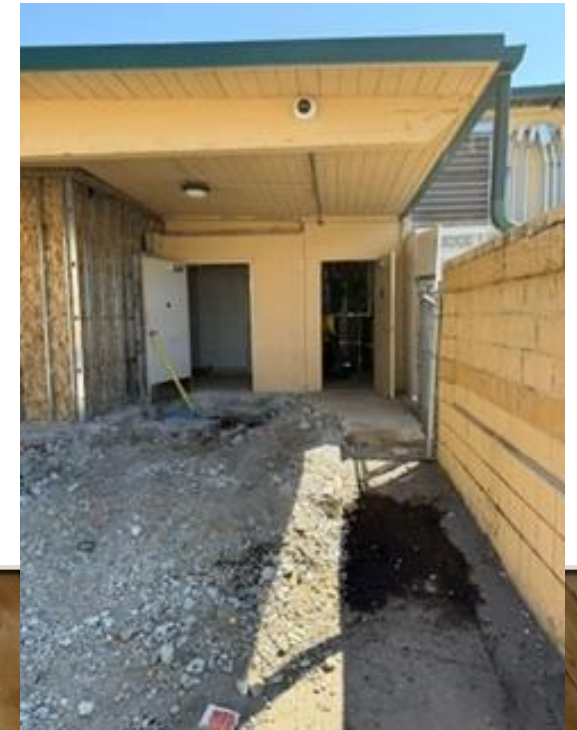

Current Progress And Upcoming Milestones



Salnave Switchgear Upgrades

- Switchgear installation is substantially complete and power is back on to the building.



Current Progress And Upcoming Milestones



Tie Old-to-New - District-Wide

Betz Elementary School

- Painting is substantially complete with punch work currently under way.
- Flooring installation is currently in progress.





Current Progress And Upcoming Milestones



Tie Old-to-New - District-Wide

Cheney High School

- Painting has been completed at the corridors.
- Flooring is currently underway. Rubber base and rubber floor treads at little theater are forthcoming.

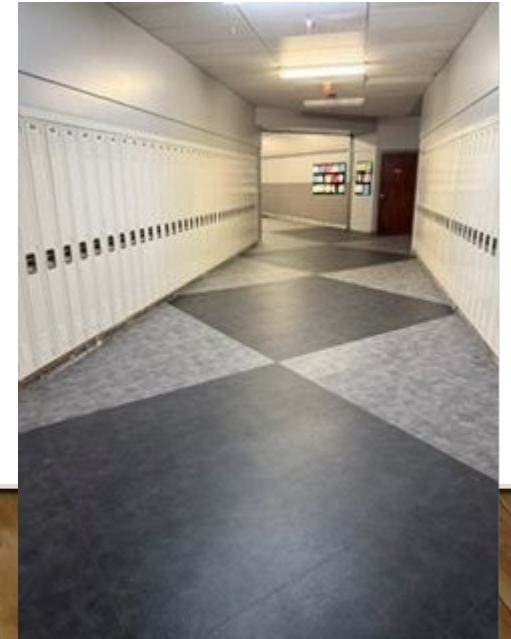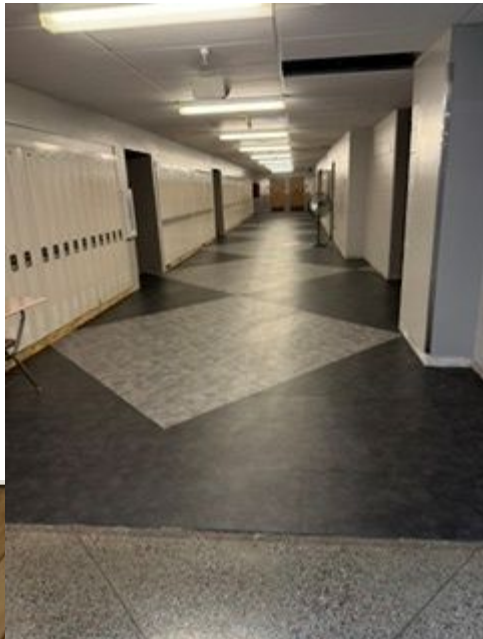

Current Progress And Upcoming Milestones



LED Lighting

- Issued purchase orders for Salnave ES, Windsor ES, and Sunset ES. Lights are currently on order. LED lighting is currently underway at Salnave. Windsor and Sunset ES lighting will take place during swing shifts.
- Cheney HS and Betz ES LED lighting will take place next summer.
- Lighting controls were upgraded as a part of this project to provide additional energy savings for the long term. Currently pursuing rebates for the LED lighting upgrades.

Current Progress And Upcoming Milestones



CHS, Betz and Sunset New Controllers and Cabling

- Controllers and cabling currently underway at CHS, Betz, and Sunset.

New Hot Water Heaters and Water Softeners – District-Wide

- Installation of the new hot water heaters and softeners is substantially complete throughout the District.
- The water heater replacement at CHS was completed this past summer under separate contract.

Budget and Resource Allocation



Program Cost Summary

Cheney School District

2024 Bond Program

	Original Budget	Budget Transfer	Current Budget	Original Commitment	Approved Modifications	Current Commitment	Charged to Date	Forecast at Completion (FAC)	Balance
Access Control - SNO/CMS/W	\$35,000	-\$16,984	\$18,016	\$18,016		\$18,016	\$18,016	\$18,016	\$0
Boiler/Chiller/Switchgear - SAL	\$630,000		\$630,000	\$513,179	\$5,726	\$518,905	\$450,263	\$630,000	\$0
Bus Loops - WES & SAL	\$2,100,000	-\$986,585	\$1,113,415	\$1,023,489	\$61,328	\$1,084,817	\$1,103,324	\$1,113,415	\$0
Chillers - WES & BES	\$425,000		\$425,000	\$299,789	\$23,924	\$323,713	\$327,848	\$425,000	\$0
CHS Stadium & Lockers	\$2,220,000	\$67,494	\$2,287,494	\$2,188,951	\$99,479	\$2,288,430	\$2,232,156	\$2,287,494	\$0
Controllers & Cabling - CHS/	\$1,500,000		\$1,500,000	\$278,602		\$278,602	\$0	\$1,500,000	\$0
Craig Rd Elementary	\$47,500,000		\$47,500,000	\$2,573,928	\$40,291,246	\$42,865,174	\$7,647,678	\$47,500,000	\$0
Kitchen Expansion - WES & SAL	\$1,500,000	\$1,447,240	\$2,947,240	\$2,796,388	-\$26,511	\$2,769,877	\$889,700	\$2,947,240	\$0
Laminated Glass/Vestibules	\$225,000	\$11,652	\$236,652	\$236,652		\$236,652	\$236,652	\$236,652	\$0
LED Lighting - CHS & 3 ES	\$2,400,000		\$2,400,000	\$1,032,081		\$1,032,081	\$0	\$2,400,000	\$0
OLD to NEW Refresh - CHS/W	\$800,000		\$800,000	\$726,078	\$6,989	\$733,067	\$426,529	\$800,000	\$0
Water Heaters/Softeners - DW	\$350,000		\$350,000	\$261,754	\$1,310	\$263,064	\$18,887	\$350,000	\$0
Total	\$59,685,000	\$522,817	\$60,207,817	\$11,948,907	\$40,463,491	\$52,412,398	\$13,351,053	\$60,207,817	\$0
2025 Land Purchase	\$10,500,000		\$10,500,000			\$0	\$2,355	\$10,500,000	\$0
Bond Issuance Costs	\$0	\$246,721	\$246,721			\$0	\$246,761	\$501,721	(\$255,000)
Program Reserve	\$1,815,000	-\$769,538	\$1,045,462			\$0	\$0	\$790,462	\$255,000
Total	\$12,315,000	-\$522,817	\$11,792,183	\$0	\$0	\$0	\$249,116	\$11,792,183	\$0
Program Total	\$72,000,000	\$0	\$72,000,000	\$11,948,907	\$40,463,491	\$52,412,398	\$13,600,169	\$72,000,000	\$0

Budget and Resource Allocation



The number one priority is to build and upgrade all items budgeted on the previous slide, as those are what were approved by the voters when this bond passed in November of 2024.

If there are funds left over in contingency at end of the bond program - *a few potential projects are:*

New Stadium Lighting at Cheney High School.....\$260,000 EST* *based on 2025 pricing*

New RTU at Salnave Elementary School.....\$110,000 EST* *based on 2025 pricing*

Windsor Window Shade Removal.....TBD

Lighting Controls at the Middle Schools.....TBD

- Costs will increase annually

Betz Roof\$275,000 EST

Ceiling Tiles at Elementary Schools and CHSTBD

CHS Bathrooms refresh.....TBD

Little Theater at CHS cleanup to make more functionalTBD

CHS Library paint, flooring and updated techTBD


Skyway Elementary School




With a new school, comes a new mascot!

Cheney Public Schools is currently seeking input on what the new mascot for Skyway Elementary school will be.

Please take a flashcard and write down your mascot suggestions for consideration.





SKYWAY MASCOT FEEDBACK

PROJECT OVERVIEW


PLAN:

To get input for a mascot for our new elementary school, Skyway!

GOALS:

- Tying the mascot to our mission/vision/values
 - BELONG. GROW. LEAD. ACHIEVE
 - Every child is known, valued, challenged, and inspired
 - We cultivate belonging, inspire learning, and empower every child to thrive

CONSIDERATIONS



Grounding Ourselves

How do we ground ourselves while also honoring the design of 'flight'?

- Incorporating that the mascot grounds us and the experiences students, staff, families, and community feel daily in the building are what allow us to take flight

Relatability

Students understand and relate to the mascot. What are they able to identify with?

Branding

Consideration:

The brand around it/sense of community that can be built (lifecycle and growth of the mascot. For example - eaglet→eagle and understanding PK-5th)

Identity

Creating an identity separate from Sunset (their mascot is a bird, SOAR-PBIS acronym)

MASCOT IDEAS

COYOTES

STARS

OSPREY

OWLS

EXPLORERS

PILOTS

JETS

AVIATORS



PLEASE GIVE YOUR INPUT ON THE
PROVIDED CARD



Three teal semi-circles are arranged horizontally, increasing in size from left to right. The word "QUESTIONS?" is written in white, bold, sans-serif capital letters across the middle of the largest semi-circle.

QUESTIONS?

THANK YOU!

Conclusion & Next Steps



Review key takeaways
from today's meeting



Next meeting date and
focus areas



Questions or final
thoughts



Thank you for your
time and commitment!
