



Monthly Progress Report

July 2026

Hempstead Union Free School District (ABGS MS)



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress July 2026

Section III – Work Projected for August 2026

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

July 2026

- **Hempstead UFSD – ABGS MS**
 - New addition to the existing building.
 - Abatement work throughout the existing building.
 - Classroom upgrades in the existing building.
 - New boilers installation in the existing building.
 - MEP upgrades throughout the existing building.



Section II - Work Progress

July 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continued steel roof decking, bolt installation, and welding.
 - Continued CMU walls throughout the new extension, and the elevator shaft.
 - Started exterior wall insulation, and brick work.
 - Progressive demo of girls' locker room, rooms L2, L4, 207, and 209.
 - Progressed from RCA grading/compaction → vapor barrier/rebar placement → first-floor slab pours (main stairs area) → steps/landing pour → forming and pouring 12 stairwell piers on the N side.
 - Started laying out and constructing metal stud walls (rooms L2, L4, 207, 209).
- **Relle:**
 - Continued the rough-in for existing classrooms and the boiler room.
 - Installed risers and sleeves as needed for addition.
 - Temp lighting was installed in new addition as needed.
 - Roughing installed in CMU walls and ceilings.
 - Roughed out for L2, L4, 207, 209, and girl's locker room.
- **Hirsch:**
 - Continued roughing for new addition.
 - Roughed in girl's locker room.
- **RMS**
 - Continued installing piping for new boilers.
 - Continued installing refrigerant piping.
 - Removal of plaster ceiling in corridor to make access for HW piping route.
 - Continued installing duct work as needed in addition, girl's locker room, L2, L4, 207, and 209.



Section III - Work Planned

August 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continue preparing floors for concrete and pour concrete.
 - Continue CMU block installation.
 - Continue exterior insulation and brick work.
 - Continue metal stud framing as needed.
 - Complete girl's locker room, L2, L4, 207, 209, and fire escape stairs.
- **Relle:**
 - Complete lighting in girl's locker room, 207/209, and L2/L4.
 - Continue roughing as needed for new addition.
- **Hirsch:**
 - Install fixtures in girl's locker room, 207/209, and L2/L4.
- **RMS:**
 - Continue installing piping in boiler room.
 - Continue refrigerant piping installation.
 - Continue with duct work installation.



Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos




Hempstead ABGS MS



Section V – Workforce Summary – Company/Hours

July 2026

▼ MANPOWER GRAPH

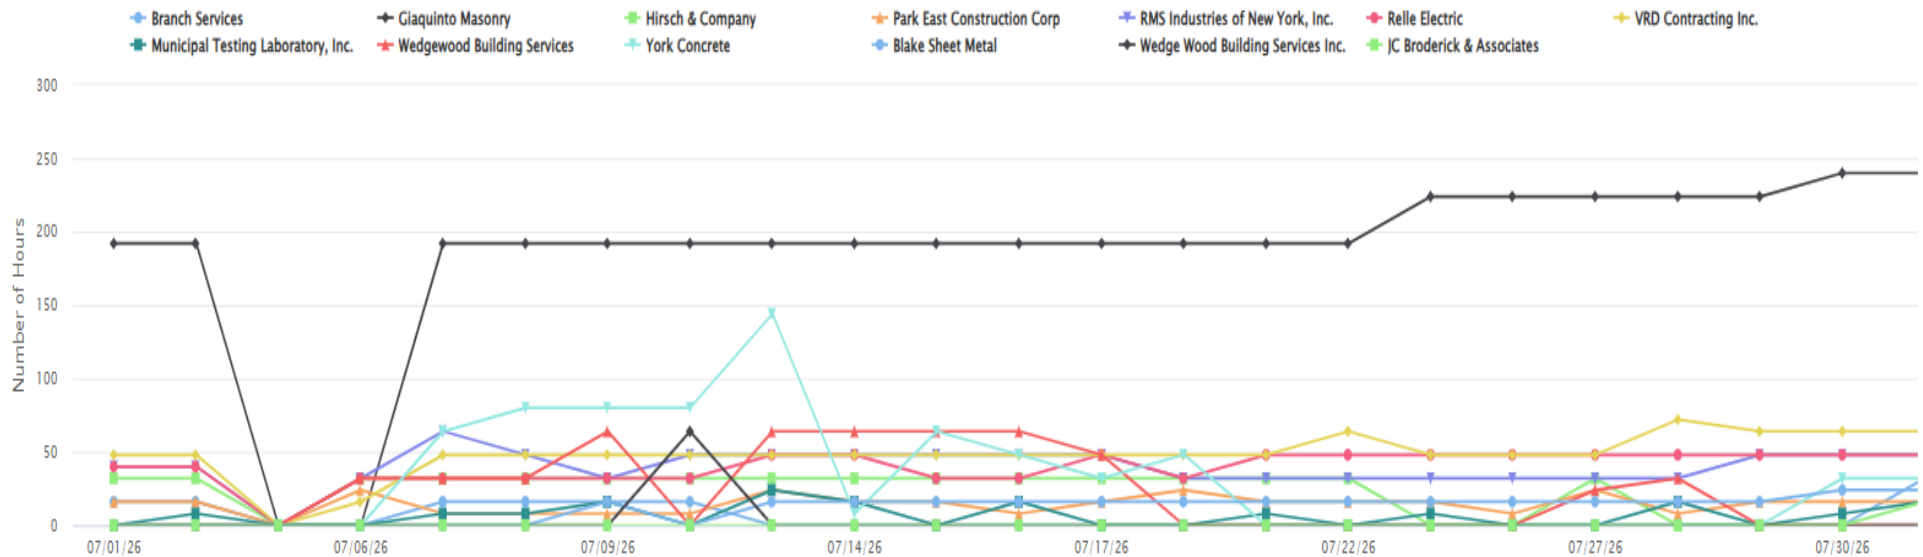

Hempstead ABGS MS



Hempstead Union Free School District (ABGS MS)

July 2026

End of Progress Report
