


FACILITIES, PLANNING & CONSTRUCTION UPDATE


August 24,
2026




The 2026-2027 Delivery Roadmap

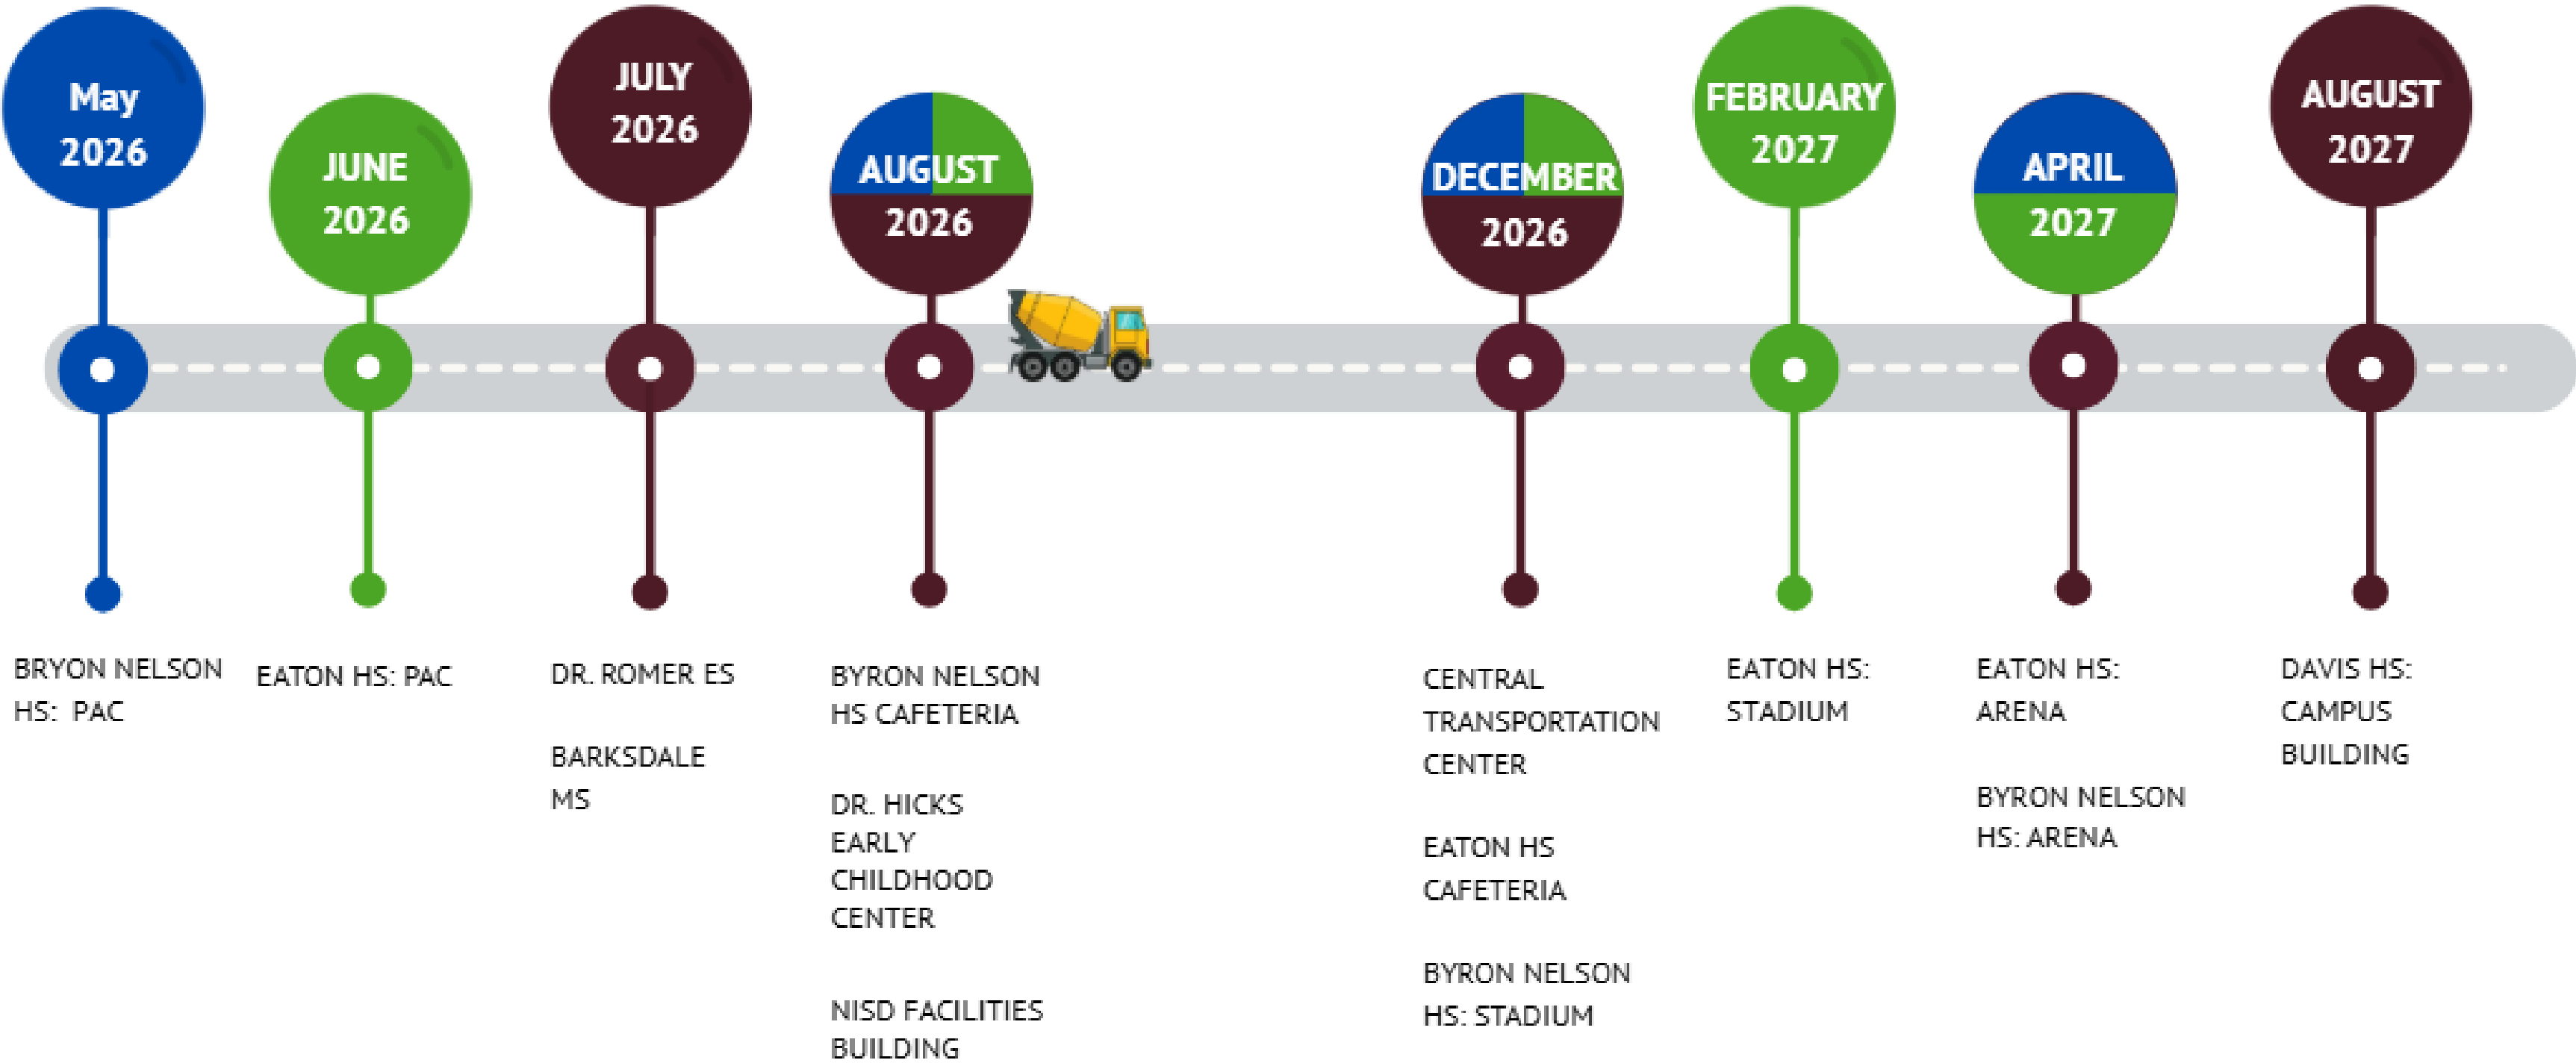


District Portfolio Status Dashboard

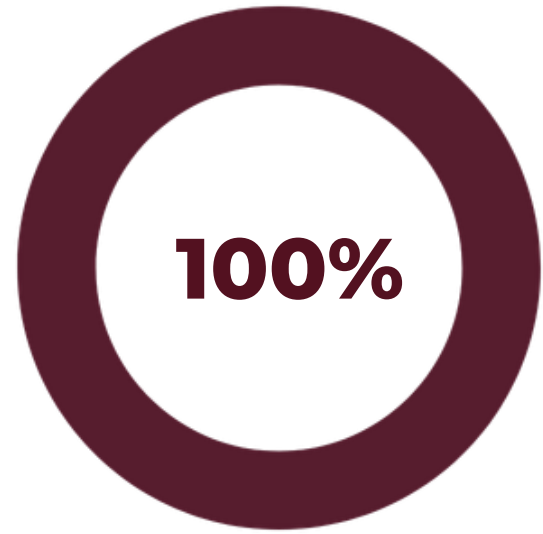


Barksdale Middle School

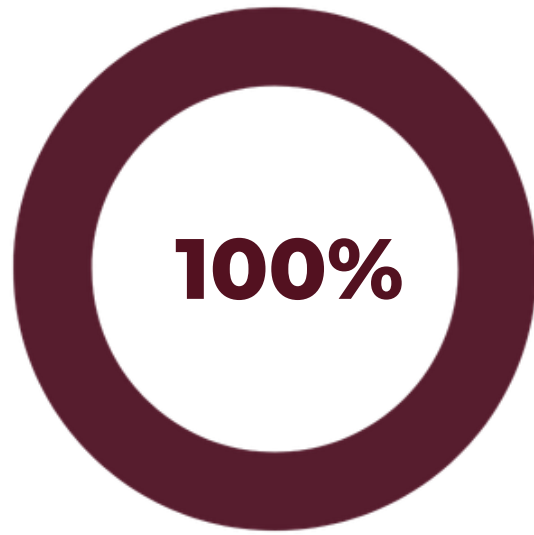


Dr. Romer Elementary School

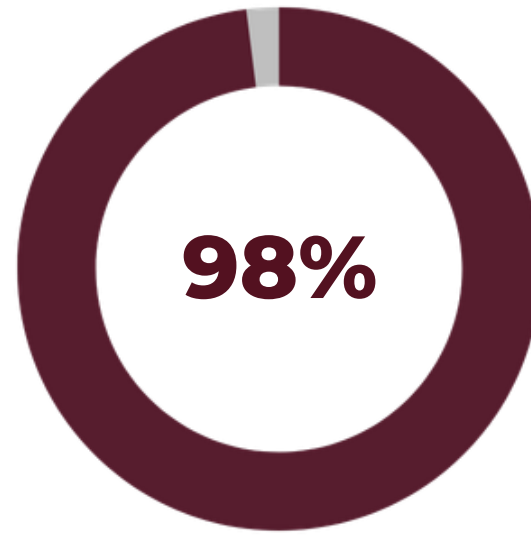


Dr. Hicks Early Childhood Center

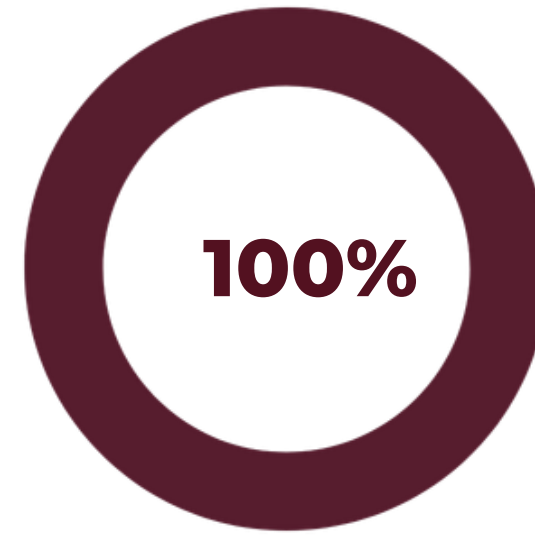


NISD Facilities

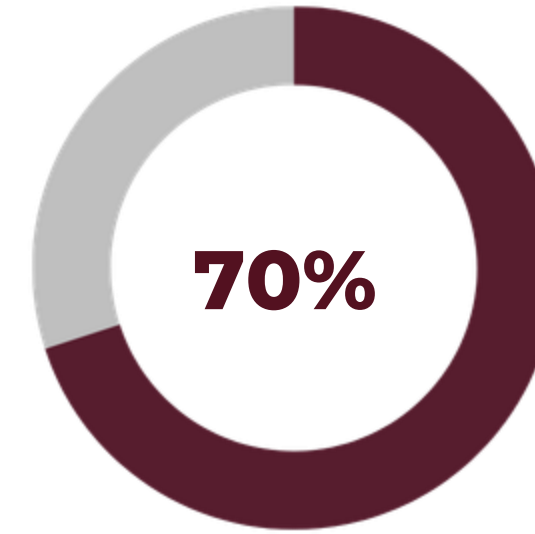


Central Transportation Relocation

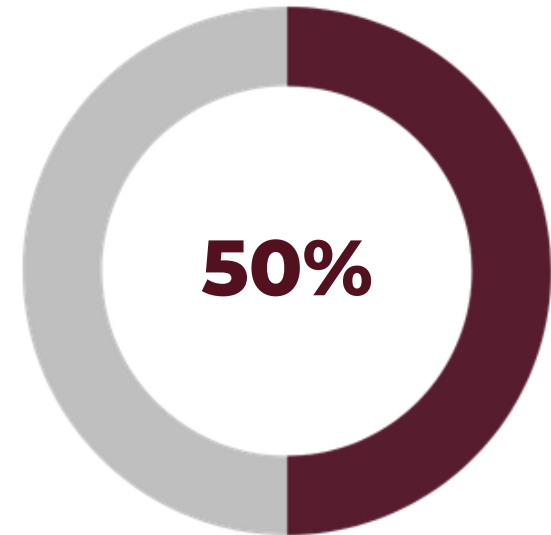


Davis High School

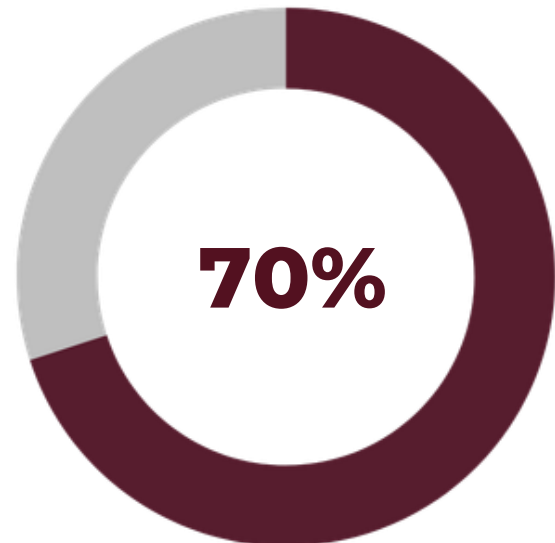


Byron Nelson HS Stadium

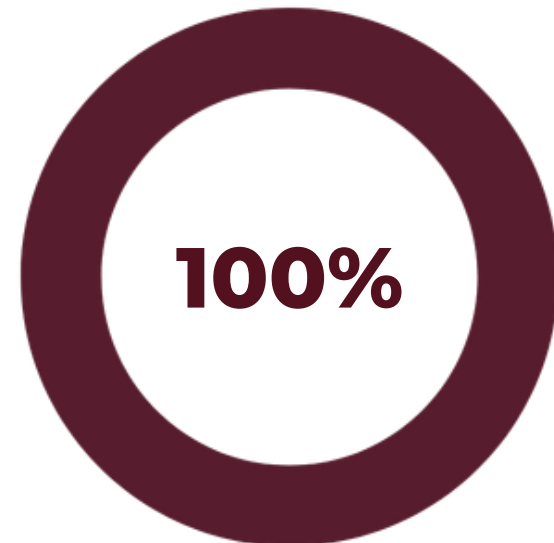


Byron Nelson HS Cafeteria

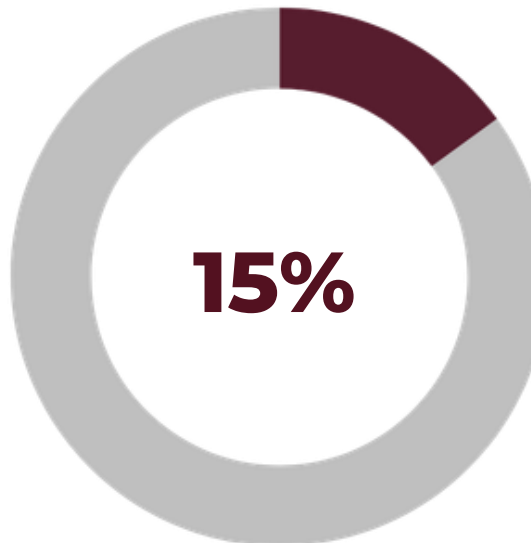


Byron Nelson HS Arena



Eaton HS PAC

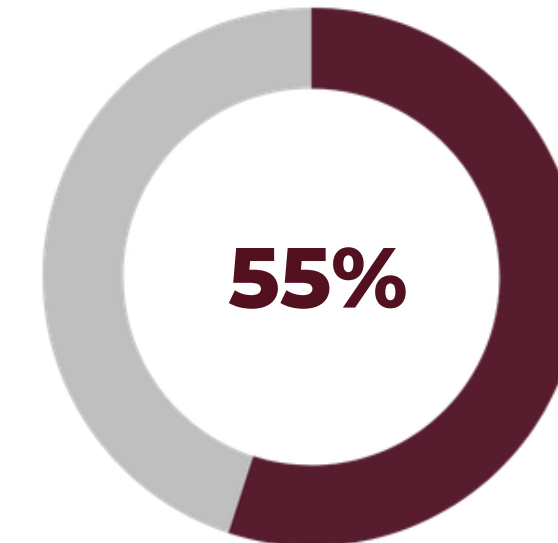

Eaton HS Stadium

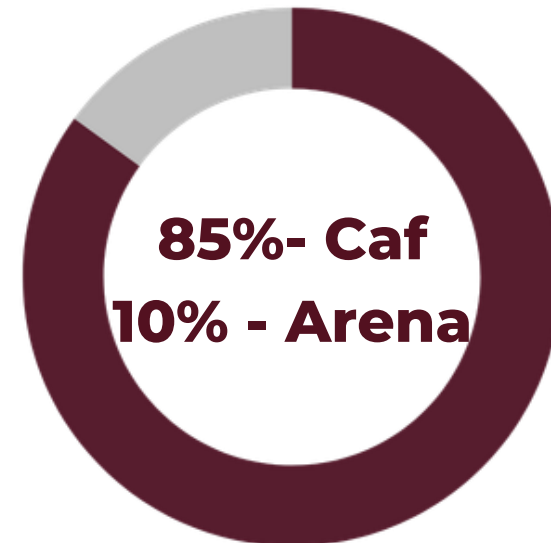

Eaton HS Cafeteria/Arena

Barksdale Middle School

100% Complete



Barksdale Middle School

100% Complete



Dr. Romer Elementary School

100% Complete




Dr. Romer Elementary School

100% Complete



Dr. Romer Elementary School

100% Complete

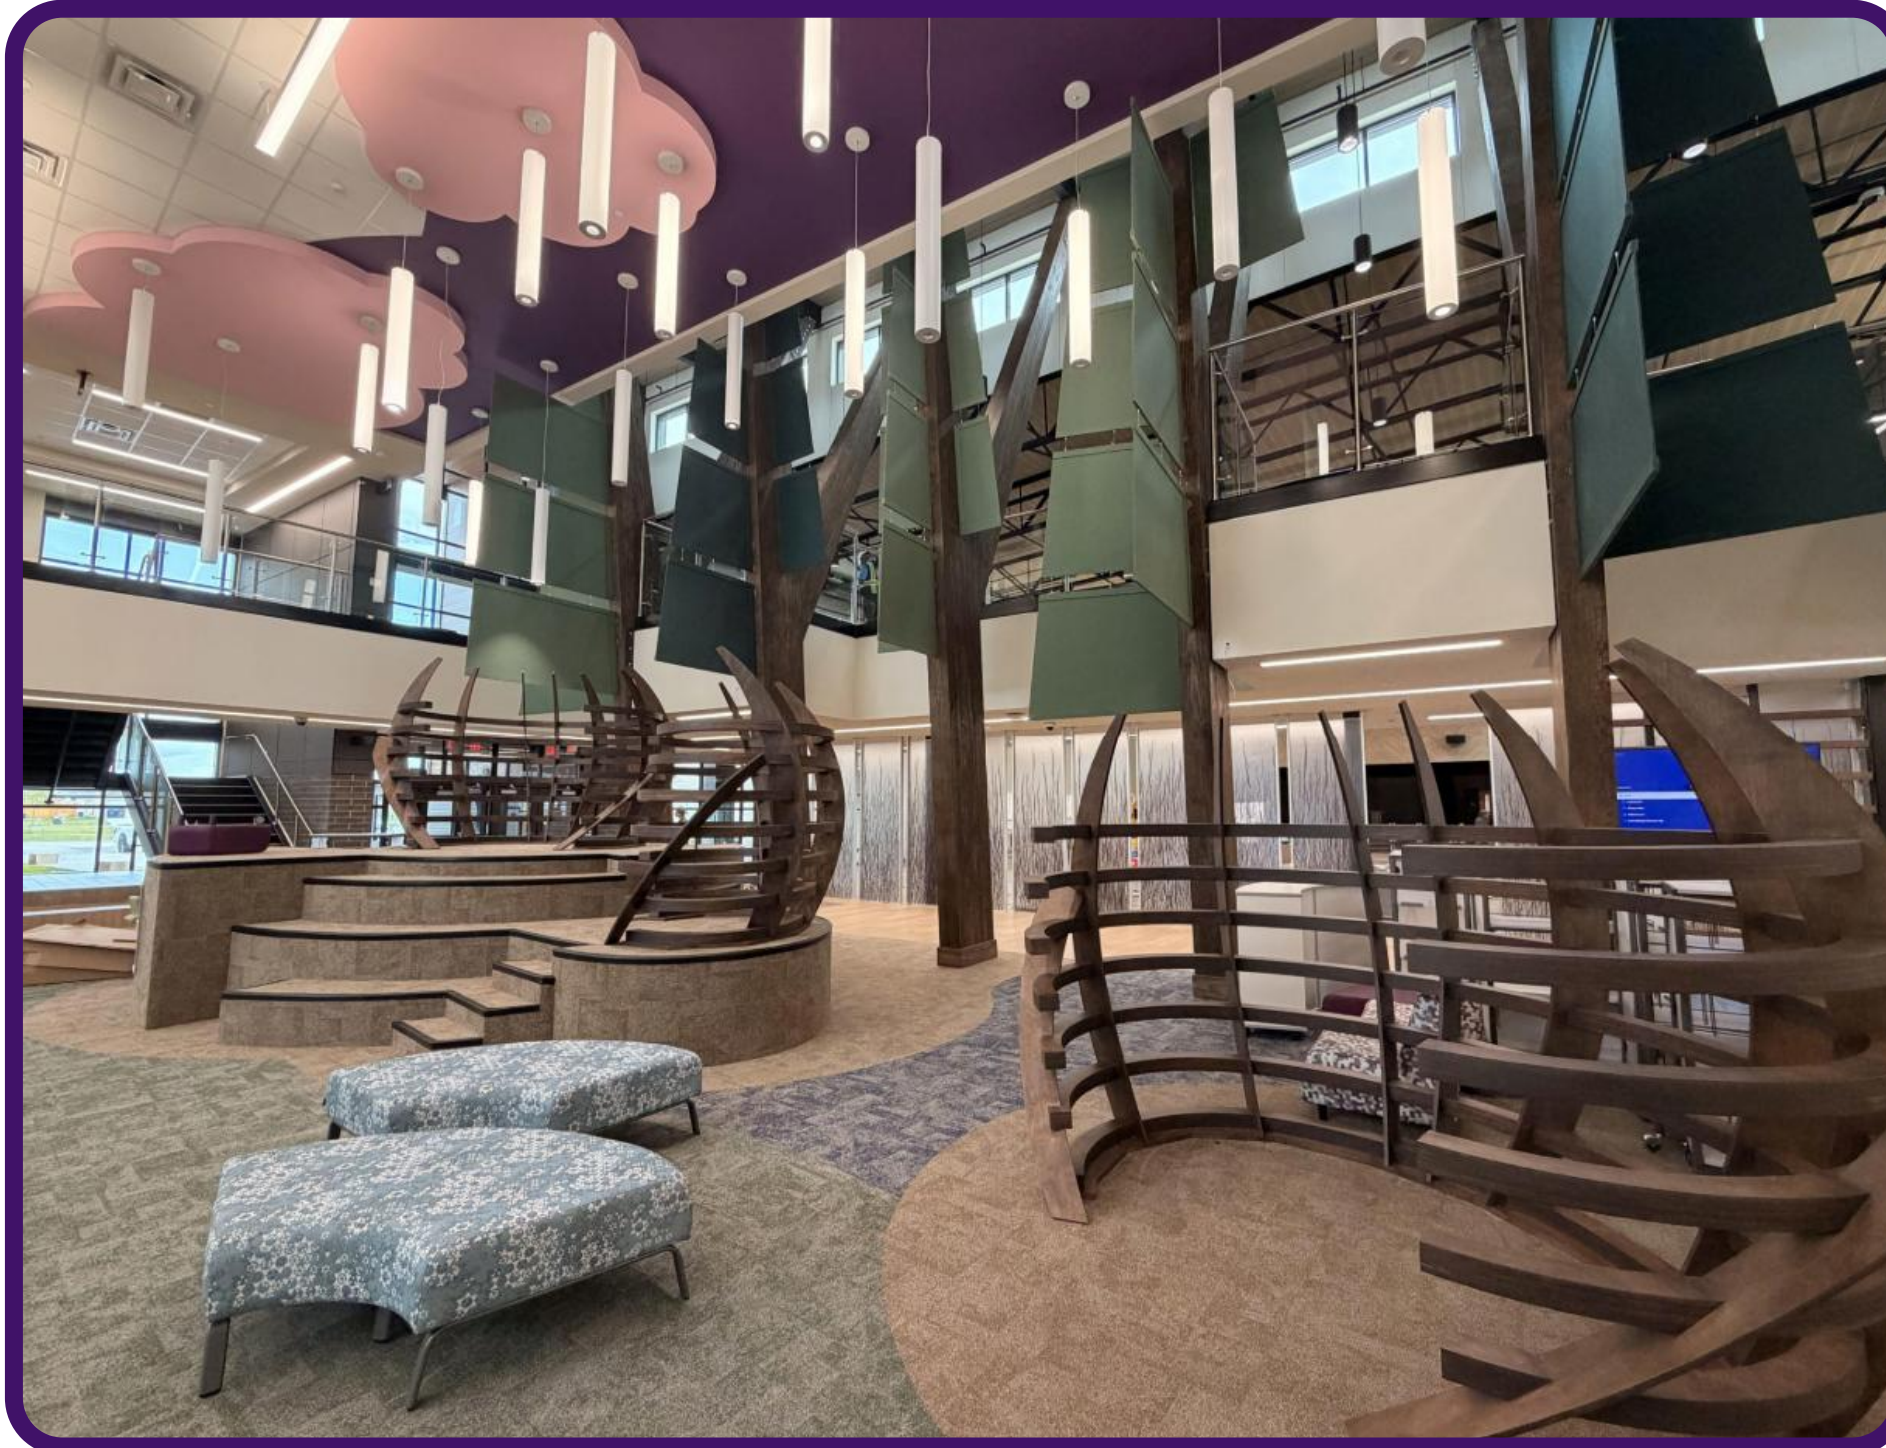

Dr. Hicks Early Childhood Center

98% Progressing



Dr. Hicks Early Childhood Center

98% Progressing



Dr. Hicks Early Childhood Center

98% Progressing



Dr. Hicks Early Childhood Center

98% Progressing



NISD Facilities Building

100% Complete



NISD Facilities Building

100% Complete



Byron Nelson HS: Stadium

70% Complete

Target Delivery:
November 2026



V.R. Eaton High School: Stadium

55% Complete | Target Delivery: February 2027



V.R. Eaton High School: PAC

100% Complete



Central Transportation

70% Complete | Opening: December 2026



Davis High School:

50% Complete | Target Delivery: August 2027



TRACK OUR PROGRESS

www.nisdtxconstruction.org



Northwest Independent School District
Facilities, Planning and Construction

