

Akron Central School District

OACM Meeting Minutes

2023 Capital Improvement Project

August 21, 2026

1. Construction Update

A. K-12 Main Building

- Campus-Wide Wayfinding Signage: All signage has been installed around campus except Athletic Complex parking signs and directionals. Remaining signs will be installed by ASI on Thurs 8/27 or Fri 8/28.
- Outdoor Message Board: Demolition of the old boards is complete; District confirmed they should be disposed of. New boards have been hung, electrical connections today 8/21. Training with Toth's Sports scheduled for next Tues 8/25.
- Weight Room RTU: New unit will be set on Tues 8/25. Start-up the week of 8/31.
- Orch/Band HRU's: New units will be set on Wed 8/26. Start-up the week of 8/31.
- HS H-Wing Additional Graphics: Final approval of design received 7/21. Lead time for material 8–10 weeks. Installation by VSP tentatively mid-September.
- HS H-Wing Railings: Remainder of railings will be installed before the start of school.
 - Prep for flower pot entrance new center railing base is not acceptable. CCMG to address this with TCS.
- HS Cafeteria Doors: Material has been ordered. Still awaiting delivery date from TCS / Builders' Hardware. CCMG will coordinate installation with the District.
- PA System: Installation of added speakers in Faculty Bathrooms is complete. Stark is addressing all outstanding items in-house in lieu of Goodwin.
- Secure Entrance: New security transaction window has been installed and drywall returns are in progress.
 - District stated the exterior storefront active doors have been misfiring. CCMG to review issues onsite with SRO and Stark / TCS.
- Gym Bleachers: Gym #3 bleachers delivery 11/16. Gym #2 bleachers delivery 11/23. Bleachers will be installed immediately upon delivery, approx. 5–6 days install duration for each gym.

B. Athletic Complex

- Turf Field punchlist work and training is complete. Punchlist work for the Grandstand structure will be complete today 8/21.
- Roadway underdrainage and concrete slip-form curbing is complete.
- Asphalt binder is complete in Lot D2, Lot D3, and the Roadway.
- Concrete flatwork remainder will be completed today 8/21 or tomorrow 8/22.
- Main Entrance and Front Sign finishes throughout the week of 8/24.
- Perimeter 6'H chain link and aluminum fencing completion anticipated by 8/31.
- Windscreens installation underneath and on the back of Grandstand mid-September.
- Musco sports lighting is functional and has been tested.
- Scoreboard system commissioning next Tues 8/25. Training needs to be scheduled.

- District stated BOCES will be onsite Fri 8/28 for network switches in the new Press Box and Concession Building data racks.
- Crafcro track surfacing installation is in progress. Base mat is complete. Seal coat, drainage testing, and topcoat broadcasting is in progress. Completion currently tracking for Thurs 8/27, weather dependent.
- Discuss plan for asphalt completion incorporating 9/2 games, 9/8 back to school, and entrance widening.
- District requested additional ADA parking spaces in Lot D2. See attached sketch.
- Fire Hydrant: Installation starting next week 8/24. CCMG to let Town know when line is charged and send test results.
- Visitor bleacher system is in fabrication. Installation start date tentatively 9/8.
- Area of Reflection:
 - Granite Monument – NCI subcontracting process with Woodside Granite is complete. Order has been placed, awaiting official lead time. Installation in Spring 2027.
 - Temp. Project Sign – Sign type switched to heavy-duty snap edge in lieu of two-post. Final rendering approved 8/17. ASI released job into production, awaiting lead time.
 - Permanent Project Sign – Lectern-style sign w/ black finish; District requested that ASI provide design services (est. \$6,000). District needs to gather content.
 - Custom Landscaping – Lavocat's Nursery quote \$2,295. Donnie Jr. is working on meeting public work requirements & prevailing wage.

2. Project Budget Summary

A. Project Budget Summary dated 8/20/26 attached.

- Total Construction Contingency Utilized = \$1,509,396 (97%)
 - This includes estimate for Entrance Widening.
- Total Construction Contingency Remaining = \$36,830
- Total Allowances Remaining = \$11,174

B. Considerations not currently carried in Contingency executed/pending values:

- ~~HS H Wing Scholar Athlete Wall Graphics – est. \$10,000 – \$20,000~~
 - Item removed from wishlist per discussion in 8/21/26 OACM Meeting.
- WeatherScape 24'L Team Shelters – est. \$47,500 (2 QTY)
- Main Entrance Security Enhancements – est. \$25,000
- Weight Room Flooring – proposal received \$62,573
 - Moisture mitigation scope alone exceeds \$35K CO threshold.

C. Incidental Budget spreadsheet dated 6/10/26 attached.


- Incidental Reserves = \$99,124
- Yellow highlighted items shall be reviewed for accuracy.
 - CCMG to update CPL line items to incorporate additional design fees.
 - Furniture, Fixtures, & Equipment
 - Interactive board for Walk of Fame – District bought board, need to code
 - HUDL Camera – not an additional expense, already included in District's package
 - Picnic tables for Concessions Plaza – est. \$1,400 per picnic table
- District to provide updated expenditures workbook.

3. General Items / New Business

- A. Surveying work for Airport parcel and JV Baseball Field were completed.
 - CPL provided surveying documents from Wendel on 8/21/26 (attached).
 - OACM Team to review jetting vs scoping the existing JV Baseball Field underdrain.

4. Next Meetings

- A. OACM Meeting – Friday, September 18th, 2026 @ 9:00 AM

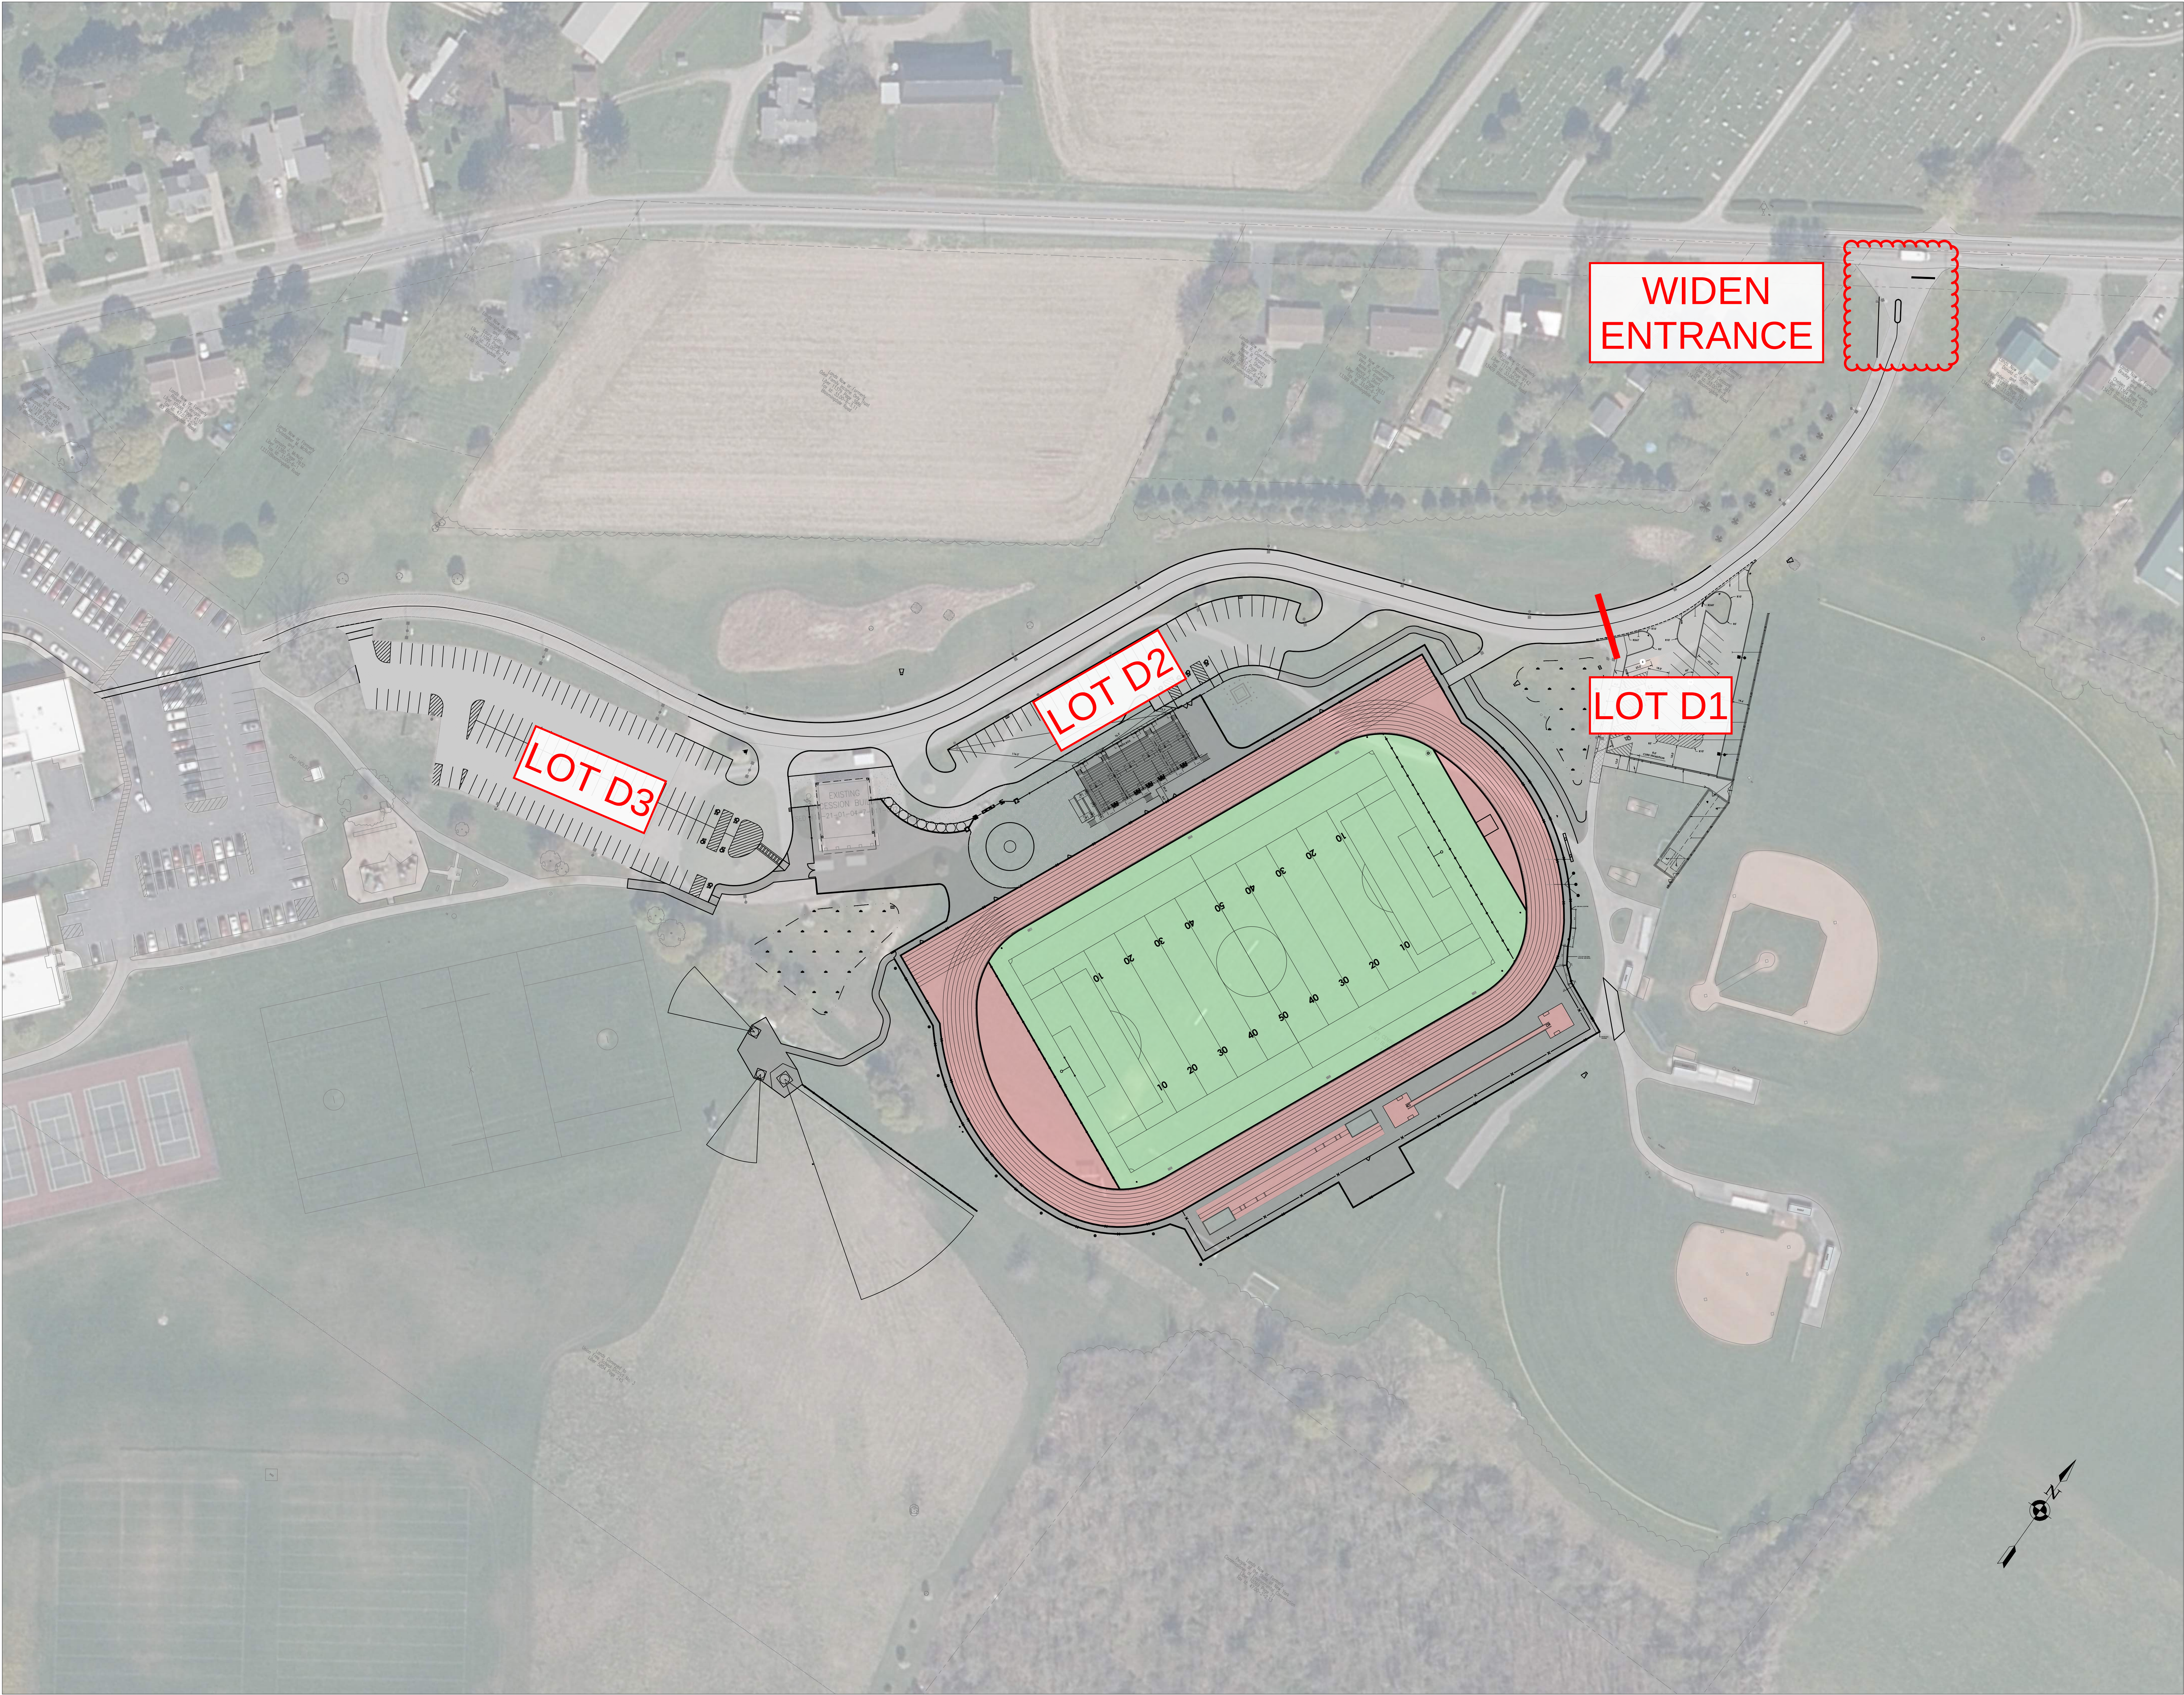

PROJECT INFORMATION

Project Number: 821.13091.12
Client Name: AKRON CENTRAL SCHOOL DISTRICT
Project Name: 2023 CAPITAL IMPROVEMENT PROJECT - PHASE II
MAIN BUILDING
District Office Address: 47 BLOOMINGDALE AVE AKRON, NY 14001

AKRON CENTRAL SCHOOL DISTRICT

MAN BUILDING: 1470-01-04-02-01-02
CONCRETE BUILDING: 1470-01-04-01-01-02
Paved Area: 1470-01-04-01-01-01

PROJECT ISSUE & REVISION SCHEDULE

No. Date Description

PROFESSIONAL STAMPS



NEW YORK STATE PROFESSIONAL ENGINEER
ALAN BENOIT, P.E.
11392/022
LICENSED PROFESSIONAL ENGINEER
LICENSED EXP. DATE 11/30/2027

SHEET INFORMATION

Scale: 1" = 50'
Date: 03/10/2025
Project Status: BID DOCUMENTS
Drawn By: JMB
Checked By: NG
Drawing Title: OVERALL SITE PLAN

Drawing Number: MB
Revision Number: C001



201 W. Third Street, Suite 320
Jamestown, NY 14701

CPLteam.com

NY ENGINEERING FIRM CERTIFICATE #0021419

PROJECT INFORMATION

Project Number
R21.13091.12

Client Name

AKRON CSD

Project Name

2023 CIP - PHASE II

Project Address

47 BLOOMINGDALE AVE
AKRON, NY

SHEET INFORMATION


Issued	Scale
08/19/2026	1" = 20'
Drawn By	Checked By
JMB	JG
Drawing Title	

ENTRANCE WIDENING

Drawing Number

IB-SC-19



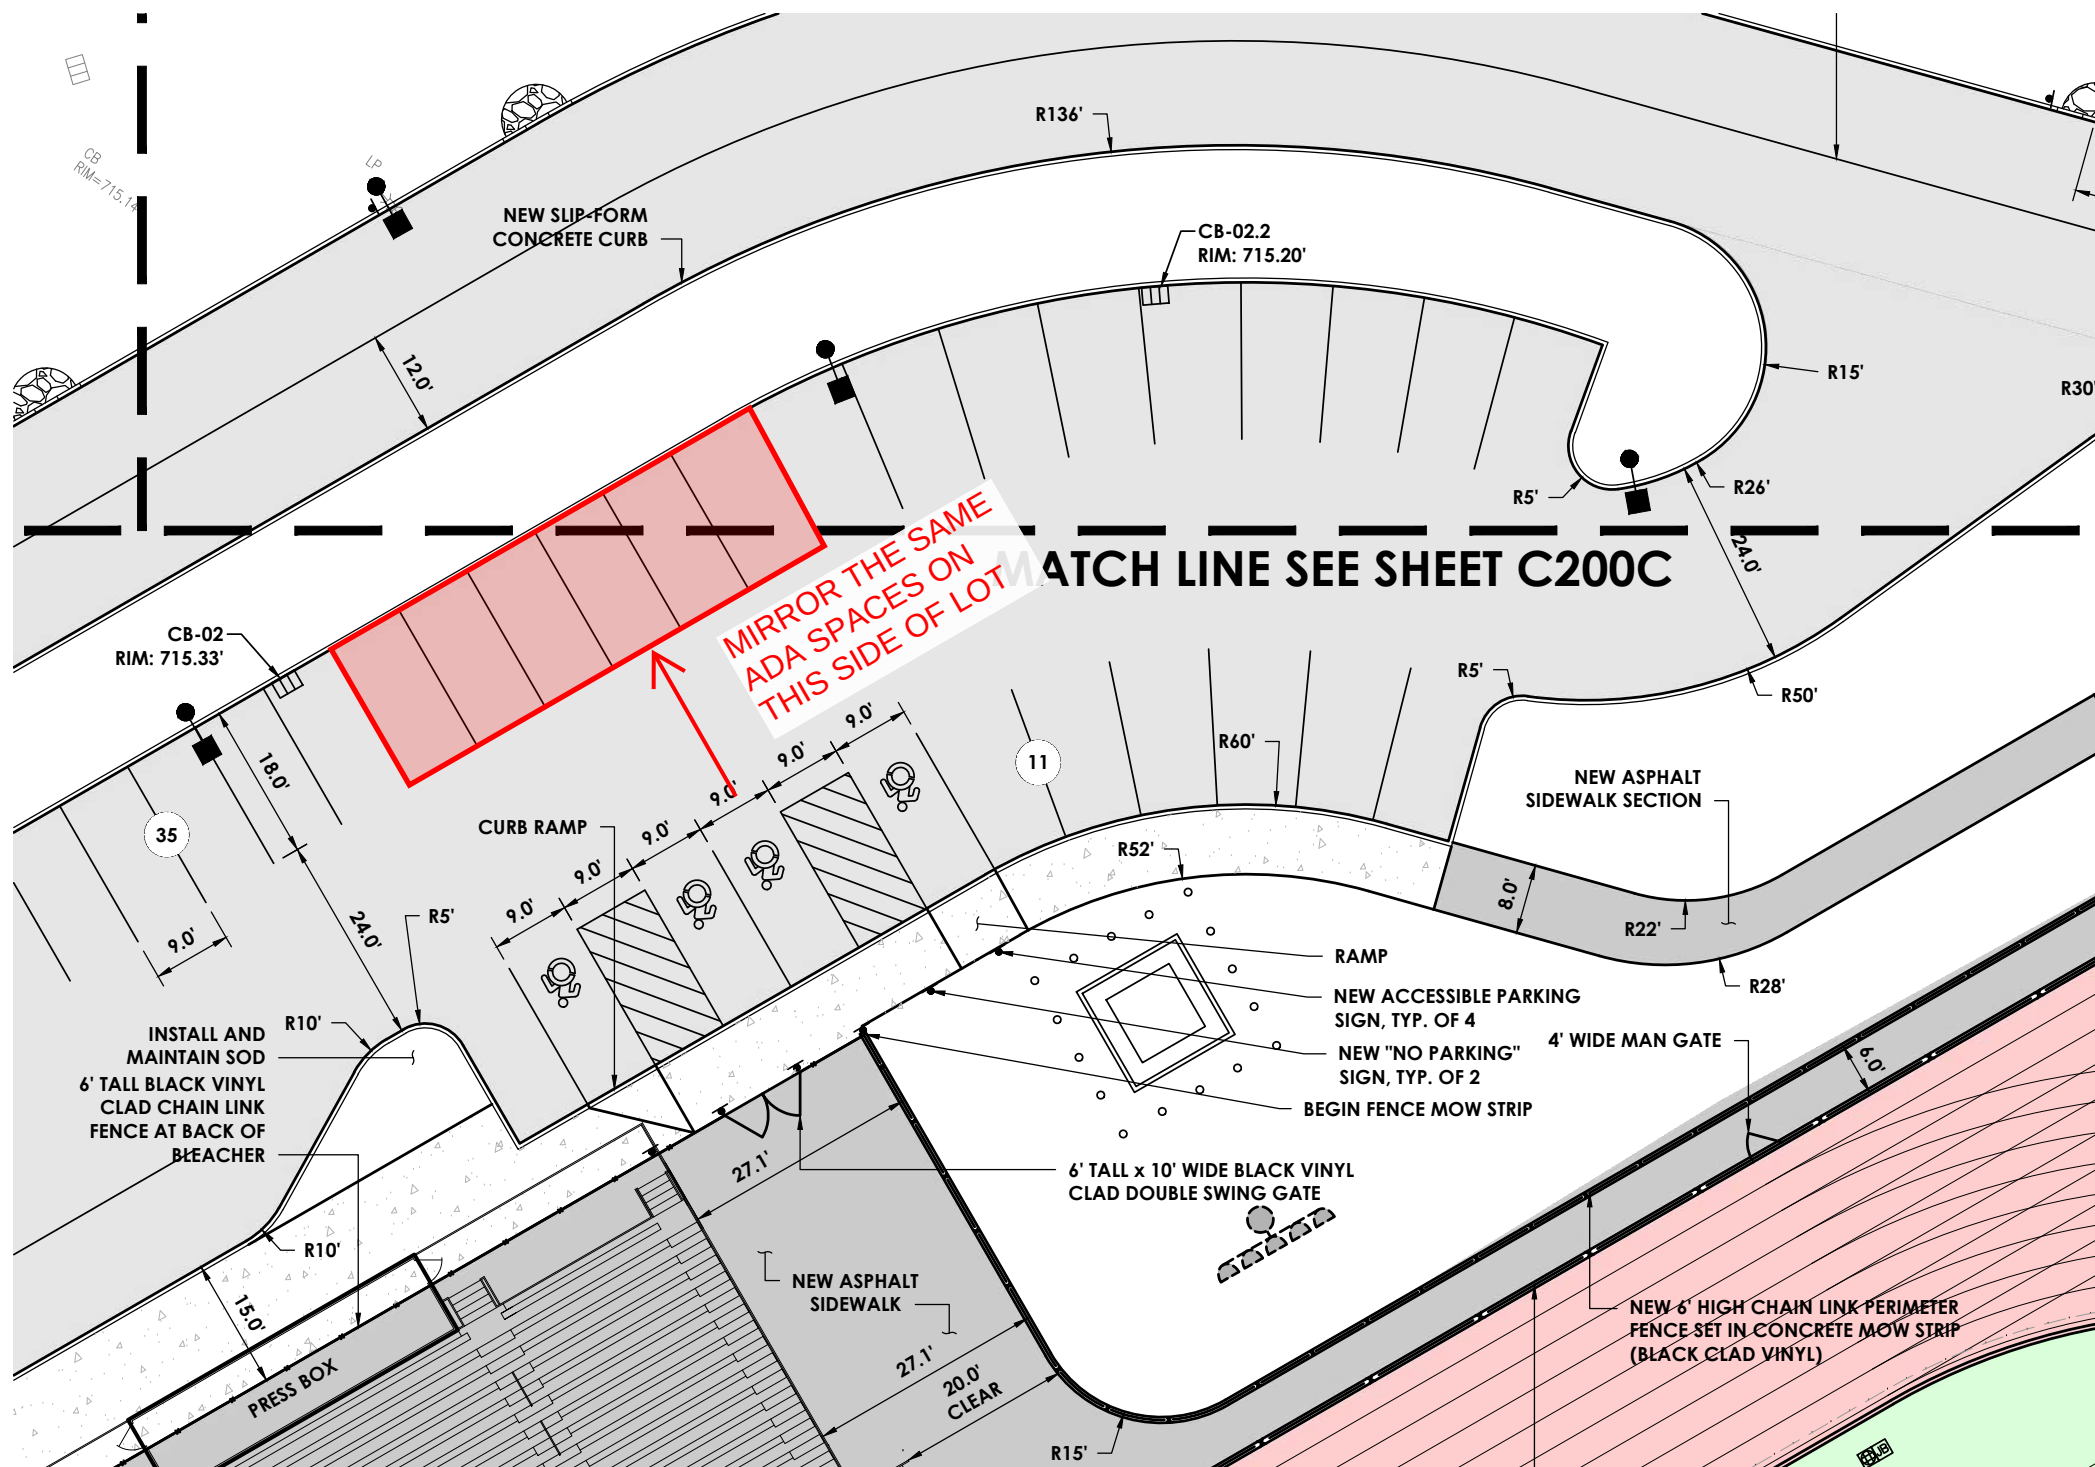



Project Budget Summary

2023 Capital Improvement Project

August 20, 2026

Akron Central School District

Referendum Authorization	\$	29,829,634
Incidental Budget¹	\$	4,410,235
Construction Contracts		
<u>Phase I</u>	\$	12,281,766
Contract #101 - General Trades	[Transit Construction Services]	\$ 5,381,000
Contract #102 - Plumbing	[Numarco]	\$ 531,900
Contract #103 - Mechanical	[Mollenberg-Betz]	\$ 2,720,700
Contract #104 - Electrical	[Goodwin Electric]	\$ 1,721,000
Contract #105 - Theatrical	[Syracuse Scenery & Stage Lighting]	\$ 662,830
Contract #106 - PA & Security	[Stark Tech - Co-Op]	\$ 898,700
Contract #107 - Vehicle Lifts	[Vehicle Service Group - Co-Op]	\$ 265,469
Contract #109 - Signage	[Takeform - Co-Op]	\$ 100,167
<u>Phase II</u>	\$	9,957,732
Contract #200 - Site Work	[Northeast Diversification]	\$ 5,360,600
Contract #201 - General Trades	[NCI Construction]	\$ 438,200
Contract #203 - Mechanical	[John W. Danforth]	\$ 785,300
Contract #204 - Electrical	[CIR Electrical]	\$ 2,647,800
Contract #205 - Track Surfacing	[FieldTurf - Co-Op]	\$ 725,832
<u>Phase III</u>	\$	1,633,675
Contract #300 - Site Work	[Northeast Diversification]	\$ 532,800
Contract #301 - General Trades	[NCI Construction]	\$ 838,300
Contract #304 - Electrical	[Frey Electric]	\$ 199,900
Contract #306 - Electronic Signage	[Daktronics - Co-Op]	\$ 62,675
Total Construction Dollars (All Phases)	\$	23,873,173
Balance²	\$	1,546,226
Total Phase I Construction Contingency	\$	864,708
Total Phase I Change Orders Executed	\$	864,708
Total Phase I Change Orders Pending	\$	-
Total Phase I Construction Contingency Remaining	\$	-
Total Phase I Allowances Available	\$	15,000
Total Phase I Allowances Used	\$	15,000
Total Phase I Allowances Remaining	\$	-
Total Phase II Construction Contingency	\$	667,327
Total Phase II Change Orders Executed	\$	540,307
Total Phase II Change Orders Pending	\$	111,872
Total Phase II Construction Contingency Remaining	\$	15,148
Total Phase II Allowances Available	\$	45,500
Total Phase II Allowances Used	\$	34,327
Total Phase II Allowances Remaining	\$	11,174
Total Phase III Construction Contingency	\$	14,191
Total Phase III Change Orders Executed	\$	(23,841)
Total Phase III Change Orders Pending	\$	16,350
Total Phase III Construction Contingency Remaining	\$	21,682
Total Phase III Allowances Available	\$	45,000
Total Phase III Allowances Used	\$	45,000
Total Phase III Allowances Remaining	\$	-

- Incidentals are budgeted costs for all soft costs within the project: A/E, CM, Surveying, Testing, Legal, Finance, FF&E, etc.

- Change orders executed includes cost of all change orders currently written and in process of execution.

1. Incidental Budget reduced by \$375,000 on 1/17/25 and \$186,371 on 3/31/26 after review of expenditures to date.

2. Construction Contingency Budget reduced by \$80,000 after accepting Phase III bids to balance the construction budget.

Akron CSD
2023 Capital Improvement Project



**INCIDENTAL
BUDGET**

	Original	Revised 1/17/25	Revised 3/31/26
Building Construction	\$14,293,149	\$14,293,149	\$14,293,149
Site Work	\$10,564,879	\$10,939,879	\$11,126,250
District Incidental	\$4,971,606	\$4,596,606	\$4,410,235
Total Project (Referendum)	\$29,829,634	\$29,829,634	\$29,829,634

PROPOSED INCIDENTALS

Expenditures Updated: 6/10/2026

			% of Project	Expenditures to Date:	Remaining Balance:
PROFESSIONAL FEES		\$3,879,990			
Architect and Engineer		\$1,965,740	6.59%		
Contract	\$1,737,740			\$1,700,885.22	\$36,854.78
Specialty Design Services	\$83,000			\$50,000.00	\$33,000.00
Reimbursables	\$20,000				\$20,000.00
Contingent Additional Services	\$125,000			\$58,410.00	\$66,590.00
Construction Manager		\$1,704,500	5.71%		
Contract	\$1,699,500			\$1,527,960.00	\$171,540.00
Reimbursables	\$5,000			\$3,054.90	\$1,945.10
Contingent Additional Services	\$0				\$0.00
Legal/Financial		\$175,000	0.59%		
Legal Council	\$100,000			\$63,747.20	\$36,252.80
Bond Council	\$25,000				\$25,000.00
Financial Advisor	\$50,000			\$18,205.51	\$31,794.49
Other		\$34,750	0.12%		
CITI Boces - 3rd Party Review	\$34,750			\$34,750.00	\$0.00
Additional Consultants	\$0				\$0.00
GENERAL ADMINISTRATION		\$154,121			
Surveys		\$26,887	0.09%		
Site Survey - PH I (billed above)	\$0				\$0.00
Site Survey - PH II (billed above)	\$0				\$0.00
Soil Borings - PH I (billed above)	\$0				\$0.00
Soil Borings - PH II (billed above)	\$0				\$0.00
Subsurface Testing (billed above)	\$0				\$0.00
Asbestos/Lead Survey	\$26,887			\$26,887.00	\$0.00
Roofing Survey (billed above)	\$0				\$0.00
SWPPP Preparation	\$0				\$0.00
Underground Utility Inspection	\$0				\$0.00
Theatrical Study (billed above)	\$0				\$0.00
EV Transp. Study (moved to reserve)	\$0				\$0.00
Other	\$0				\$0.00
Construction Testing		\$101,426	0.34%		
Construction Testing (Whitestone) - PH I	\$26,389			\$26,388.75	\$0.00
Construction Testing (Whitestone) - PH II	\$60,000			\$23,096.25	\$36,903.75
Asbestos Monitoring (Stohl) - PH I	\$15,037			\$15,037.00	\$0.00
SWPPP Inspections (billed above)	\$0				\$0.00
Other	\$0				\$0.00
Printing, Advertising		\$9,808	0.03%		
Construction Plans & Specs	\$9,608			\$9,607.96	\$0.00
Marketing & Advertising	\$200			\$86.12	\$113.88
Other		\$16,000	0.05%		
Additional Admin/Custodial Support	\$0				\$0.00
Cleaning	\$0				\$0.00
Moving and Storage	\$0				\$0.00
HVAC Commissioning	\$16,000			\$12,000.00	\$4,000.00

Field Office Equipment	\$0					\$0.00
Miscellaneous	\$0					\$0.00

INSURANCE DURING CONSTRUCTION			\$65,000	0.22%		
Builder's Risk	\$65,000				\$59,644.00	\$5,356.00
Other	\$0					\$0.00

UTILITIES & SERVICE FEES			\$0	0.00%		
Sewage	\$0					\$0.00
Water Service	\$0					\$0.00
Gas Service	\$0					\$0.00
Electric Service	\$0					\$0.00
Telephone Service	\$0					\$0.00
Data/Security	\$0					\$0.00
Fire Alarm	\$0					\$0.00

TEMPORARY UTILITIES			\$0	0.00%		
Water Service	\$0					\$0.00
Sewage Service	\$0					\$0.00
Electric/Gas Service	\$0					\$0.00
Tel/Data Service	\$0					\$0.00
Temp District Office	\$0					\$0.00
Temp Field Office	\$0					\$0.00

FURNITURE & EQUIPMENT			\$212,000	0.71%		
Furniture, Fixtures & Equipment	\$112,000				\$111,318.36	\$681.64
IT - Cameras, Switches, WAPs - PH II	\$50,000					\$50,000.00
Other District Purchases	\$50,000					\$50,000.00

SITE			\$0	0.00%		\$0.00
Site Acquisition	\$0					\$0.00
Fees/Expenses	\$0					\$0.00

FINANCING			\$0	0.00%		
Capitalized Interest	\$0					\$0.00

INCIDENTAL RESERVE	\$99,124		\$99,124	0.33%		\$99,124.00
---------------------------	----------	--	-----------------	--------------	--	-------------

SUBTOTALS	\$4,410,235		\$4,410,235	14.78%	\$3,741,078.27	\$669,156.44
------------------	-------------	--	--------------------	---------------	-----------------------	---------------------

TOTAL INCIDENTAL / FINANCING COSTS			\$4,410,235	14.78%		
---	--	--	--------------------	---------------	--	--

TOTAL PROJECT (Referendum)	\$29,829,634
-----------------------------------	---------------------

Notes:

1) North as Shown on this Map is True North at 78°35' Meridian of West Longitude, as established by GPS Static Survey:


- Control Point 1 Set Pin N. 1103098.46, E. 1174724.57
- JAVAD GPS Receiver 944
- Static GPS Observations March 5, 2024
- New York State Plane Coordinates West Zone (3103)
- NAD_83 (2011)(EPOCH:2010.0000)

Base Stations used:

PID	DESIGNATION	LATITUDE	LONGITUDE	DISTANCE (m)
NONE	BFNY	N 42° 52' 39.17322" W 78° 53' 25.58441"		37079.485
NONE	NYBT	N 42° 59' 17.96015" W 78° 07' 20.37552"		29845.792
NONE	NYHB	N 42° 43' 02.66341" W 78° 50' 47.27351"		45401.937
NONE	NYLP	N 43° 09' 54.85476" W 78° 45' 13.35709"		26735.309
NONE	PWEL	N 43° 14' 12.20239" W 79° 13' 10.77712"		64178.555

Linear Unit - U.S. Survey Foot. Combined scale factor: 0.99990967. All dimensions shown are Ground.

2) Map Reference: Map filed in the Erie County Clerk's Office under Cover 803.

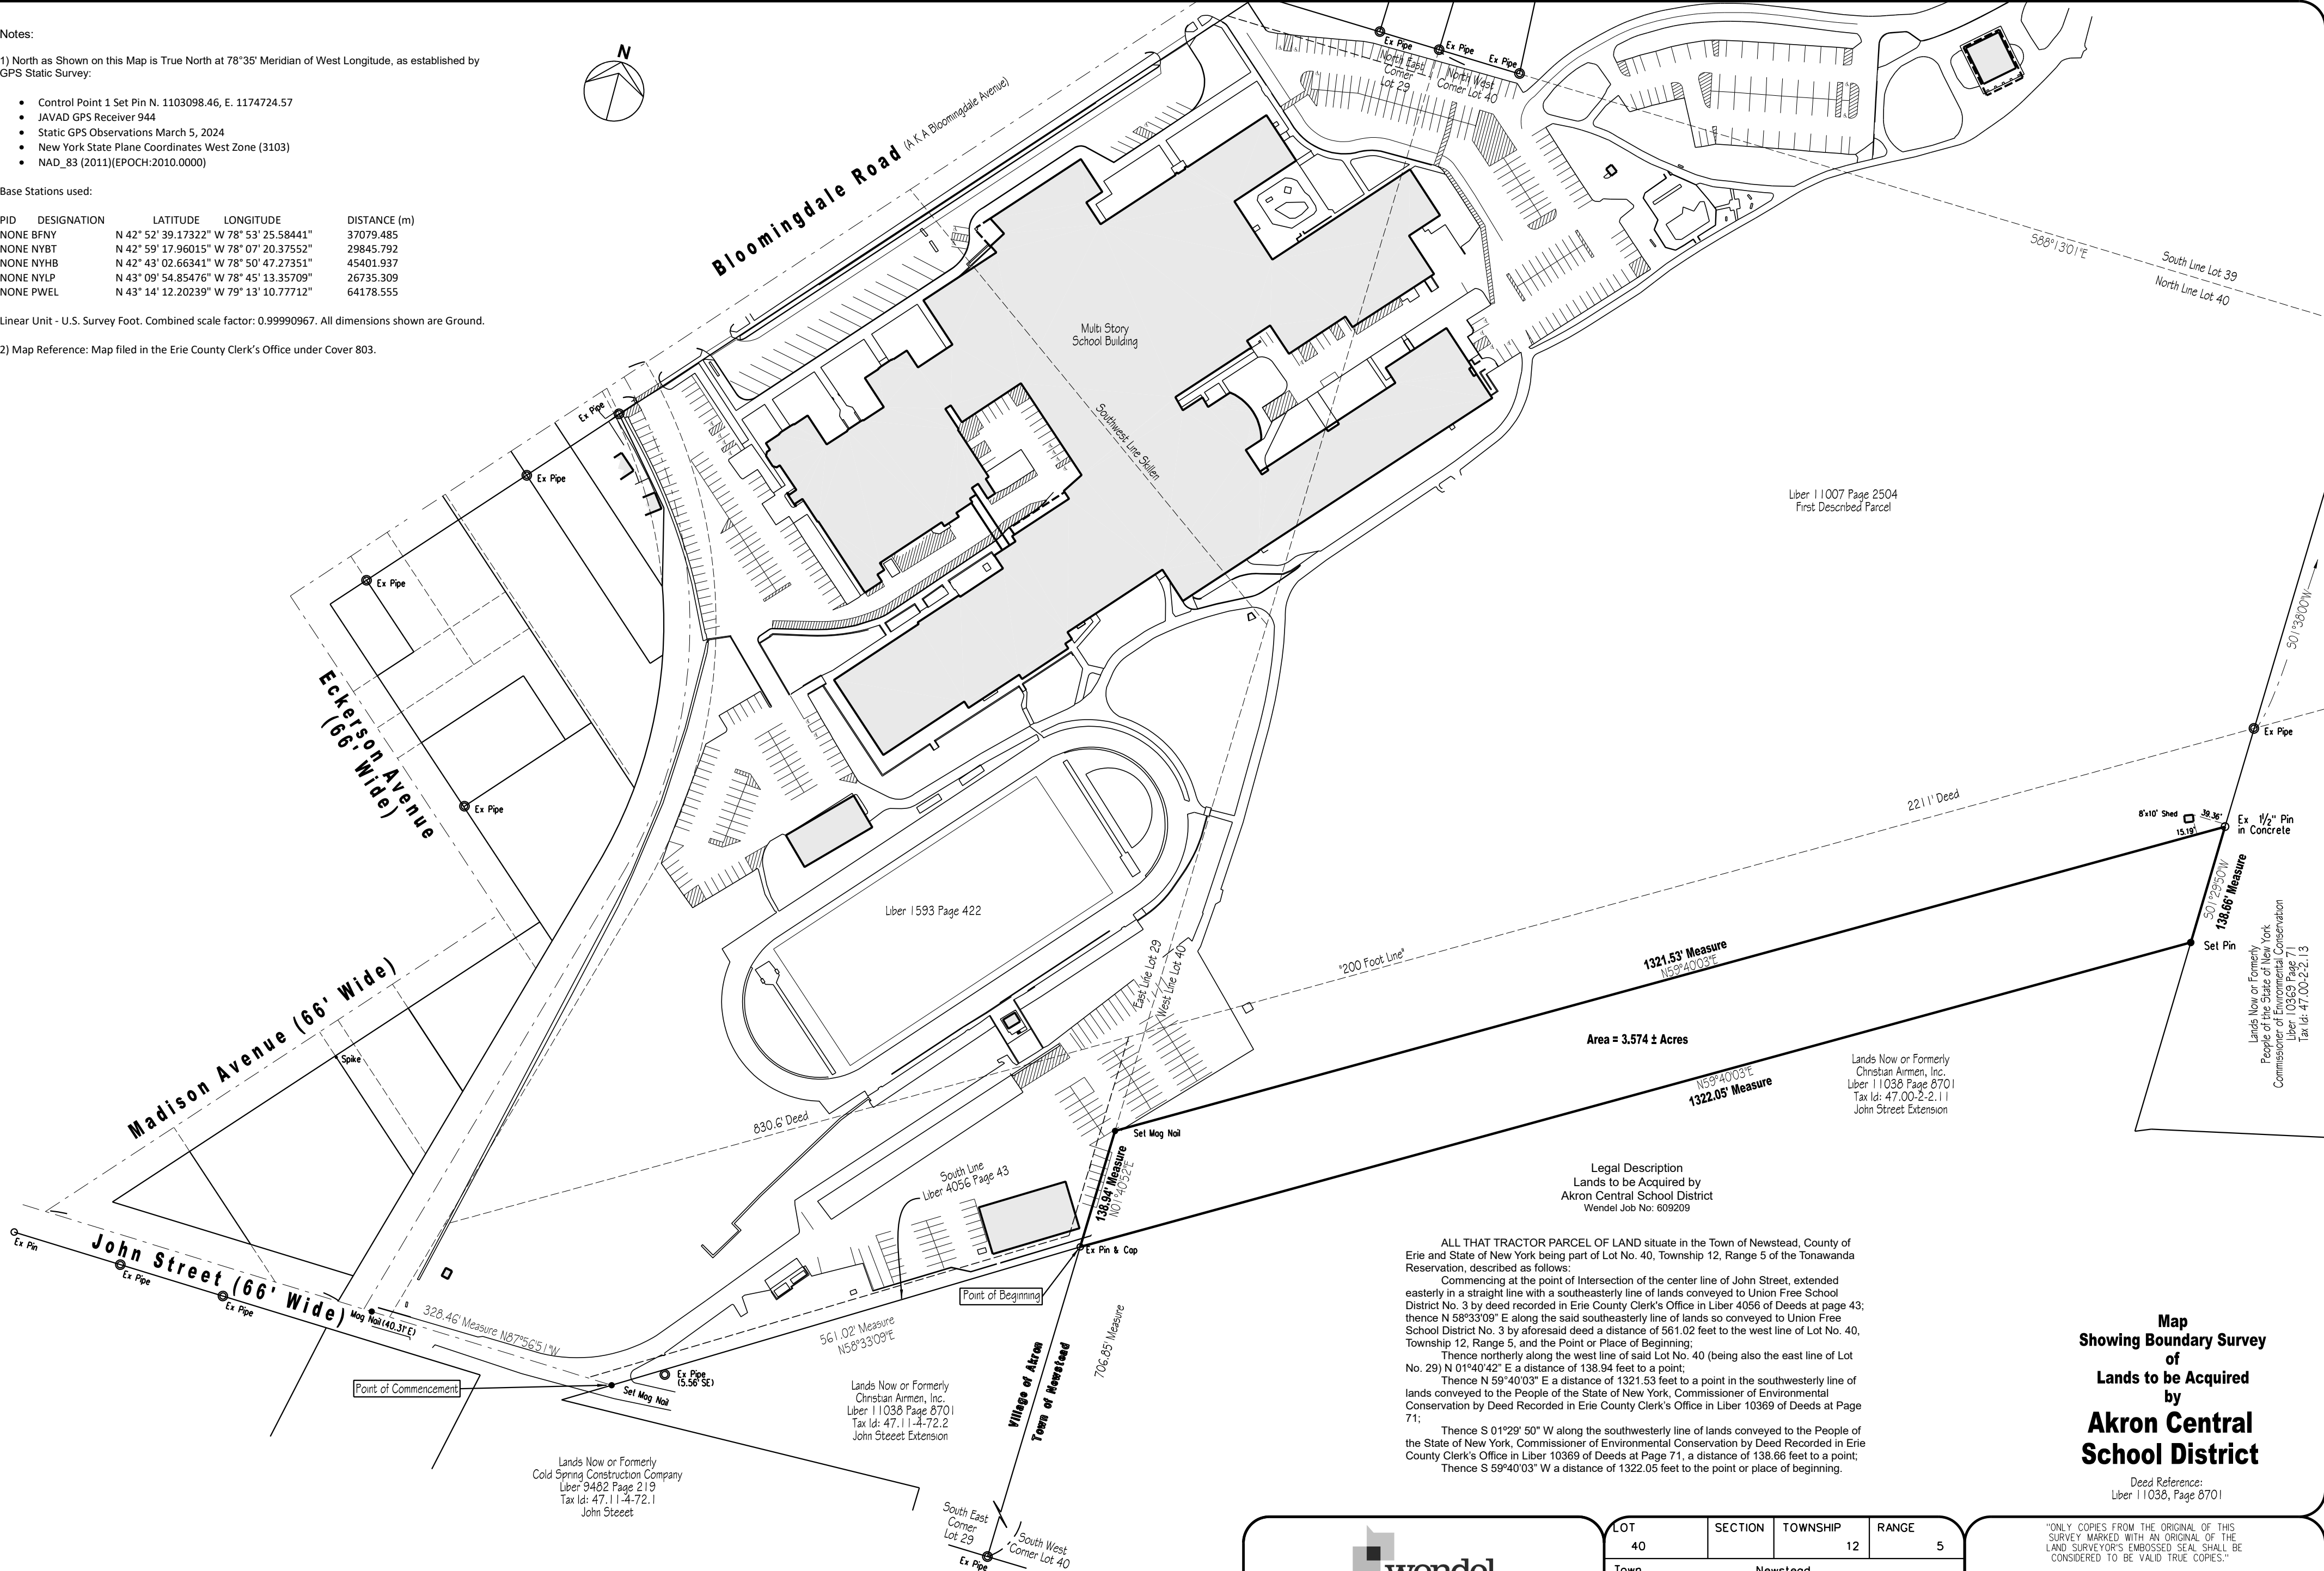

ALL THAT TRACTOR PARCEL OF LAND situate in the Town of Newstead, County of Erie and State of New York being part of Lot No. 40, Township 12, Range 5 of the Tonawanda Reservation, described as follows:

Commencing at the point of Intersection of the center line of John Street, extended easterly in a straight line with a southeasterly line of lands conveyed to Union Free School District No. 3 by deed recorded in Erie County Clerk's Office in Liber 4056 of Deeds at page 43; thence N 58°33'09" E along the said southeasterly line of lands so conveyed to Union Free School District No. 3 by aforesaid deed a distance of 561.02 feet to the west line of Lot No. 40, Township 12, Range 5, and the Point or Place of Beginning;

Thence northerly along the west line of said Lot No. 40 (being also the east line of Lot No. 29) N 01°40'42" E a distance of 138.94 feet to a point;

Thence N 59°40'03" E a distance of 1321.53 feet to a point in the southwesterly line of lands conveyed to the People of the State of New York, Commissioner of Environmental Conservation by Deed Recorded in Erie County Clerk's Office in Liber 10369 of Deeds at Page 71;

Thence S 01°29' 50" W along the southwesterly line of lands conveyed to the People of the State of New York, Commissioner of Environmental Conservation by Deed Recorded in Erie County Clerk's Office in Liber 10369 of Deeds at Page 71, a distance of 138.66 feet to a point;

Thence S 59°40'03" W a distance of 1322.05 feet to the point or place of beginning.

Map
Showing Boundary Survey
of
Lands to be Acquired
by
**Akron Central
School District**

Deed Reference:
Liber 11036, Page 8701



Centerpointe Corporate Park • 375 Essjay Road, Suite 200
Williamsville, New York 14221
PHONE: 716.688.0766 FAX: 716.625.6825
WEBSITE: www.wendelcompanies.com
Wendel WD Architecture, Engineering,
Surveying and Landscape Architecture P.C.

UNAUTHORIZED ALTERATION OR ADDITION TO THIS SURVEY
MAP IS A VIOLATION OF SECTION 7209, PROVISION 2 OF THE
NEW YORK STATE EDUCATION LAW.

THIS SURVEY WAS PREPARED WITHOUT THE BENEFIT OF AN
ABSTRACT OF TITLE AND IS SUBJECT TO ANY STATE OF FACTS
THAT MAY BE REVEALED BY AN EXAMINATION OF SUCH.

LOT	SECTION	TOWNSHIP	RANGE
40		12	5
Town		Newstead	
COUNTY		Erie	
STATE		New York	
DATE		July 30, 2026	
SCALE		1" = 120'	
JOB NO.		609209	
REVISIONS			

"ONLY COPIES FROM THE ORIGINAL OF THIS
SURVEY MARKED WITH AN ORIGINAL OF THE
LAND SURVEYOR'S EMBOSSED SEAL SHALL BE
CONSIDERED TO BE VALID TRUE COPIES."


THIS SURVEY WAS PREPARED FOR THE PARTIES
AND PURPOSE INDICATED HEREON. ANY EXTENSION
OF THE USE BEYOND THE PARTIES OR PURPOSE
INDICATED IS EXPRESSLY FORBIDDEN WITHOUT
WRITTEN RELEASE OR PERMISSION OF THE UNDERSIGNED.

USE OF THIS SURVEY IN CONJUNCTION
WITH AN AFFIDAVIT OF NO CHANGE IS FORBIDDEN

Kenneth L. Slausenhaupt Lic. No. 50349

© Copyright NIAGARA BOUNDARY AND MAPPING SERVICES L.S.P.C.

Reproduction or copying of this document may be a violation of copyright law unless permission of the author and / or copyright holder is obtained.



Legend

Abbreviations

Ex = Existing HT = Height
E = East
N = North
W = West
S = South
R.O.W. = Right of Way
A.K.A. = also known as
OH = Overhead Piping
EM = Electric Meter
Well = Monitoring Well
ELMH = Electric Hand Hole
Deciduous Tree
Bush
Coniferous Tree
Signal Pole
Electric Manhole
Signal Pole
Communication Manhole
Water Manhole
Traffic Manhole
Large Rock
Signal Pole

Symbols

Sanitary Manhole
Catchout
Catch Basin
Drain Inlet
Storm Manhole
Yard Drain
Cable TV
Electric Riser
Power Pole
Guy Wire Anchor
Telephone Riser
Fire Hydrant
Water Valve
Water Service Valve
Gas Line Marker
Gas Valve
Gas Service Valve
Sign
Mailbox
Metal Post
Concrete R.O.W. Monument
Light Standard
Telephone Manhole
Bollard
Irrigation Control Valve
Traffic Control Box

Line Styles

SA = Sanitary Sewer
ST = Storm Sewer
W = Water Line
C = Gas Line
UT = Telephone Wires or Cables
E = Electric Wires or Cables
OH = Overhead Wires
100 = Contour Line
01 = Centerline of Ditch
02 = Crown of Pavement
03 = Right of Way Line
04 = Centerline of Road
05 = Building Setback Line
06 = Easement Line
07 = Property Line
UE = Underground Electric
Point Stripe
Former Boundary Parcel Line
Underground Cable TV
UFO = Underground Fiber Optic



Notes:

1) North as Shown on this Map is True North at 78°35' Meridian of West Longitude, as established by GPS Static Survey.

- Control Point 1 Set Pin N. 1103098.46, E. 1174724.57
- JAVAD GPS Receiver 944
- Static GPS Observations March 5, 2024
- New York State Plane Coordinates West Zone (3103)
- NAD_83 (2011)(EPOCH:2010.0000)

Base Stations used:

PID	DESIGNATION	LATITUDE	LONGITUDE	DISTANCE (m)
NONE	BFNY	N 42° 52' 39.17322" W 78° 53' 25.58441"		37079.485
NONE	NYBT	N 42° 59' 17.96015" W 78° 07' 20.37552"		29845.792
NONE	NYHB	N 42° 43' 02.66341" W 78° 50' 47.27351"		45401.937
NONE	NYLP	N 43° 09' 54.85476" W 78° 45' 13.35709"		26735.309
NONE	PWEL	N 43° 14' 12.20239" W 79° 13' 10.77712"		64178.555

Linear Unit - U.S. Survey Foot. Combined scale factor: 0.99990967. All dimensions shown are Ground.

2) Elevations as shown on this Map are based on NAVD88 Datum. Site Benchmark: as observed by static GPS observation on Pin 1 is 714.05 (NAVD88 (Computed using Geoid128)).

3) Utilities as shown on this map are plotted from field locations of visible structures and information provided by others. Wendel Survey, along with the undersigned Land Surveyor assumes no responsibility as to the accuracy of underground utilities. Contractor must call UFPO three working days prior to any excavation construction activities.

4) Contour interval is 1.0' Foot



Map Showing Topographic Survey of a portion of Property Owned by Akron Central School District

AKRON CENTRAL SCHOOL DISTRICT



Centerpointe Corporate Park • 375 Essay Road, Suite 200
Williamsville, New York 14221
PHONE: 716.698.0768 FAX: 716.625.6825
WEBSITE: www.wendelcompanies.com
Wendel VMD Architecture, Engineering,
Surveying and Landscape Architecture P.C.


UNAUTHORIZED ALTERATION OR ADDITION TO THIS SURVEY MAP IS A VIOLATION OF SECTION 7209, PROVISION 2 OF THE NEW YORK STATE EMBROIDERED SEAL ACT.
THIS SURVEY WAS PREPARED WITHOUT THE BENEFIT OF AN ABSTRACT OF TITLE AND IS SUBJECT TO ANY STATE OF FACTS THAT MAY BE REVEALED BY AN EXAMINATION OF SUCH.

LOT	SECTION	TOWNSHIP	RANGE
Village	Akron		
COUNTY	Erie		
STATE	New York		
DATE	July 30, 2026		
SCALE	1" = 20'		
JOB NO.	609209		
REVISIONS			

ONLY COPIES FROM THE ORIGINAL OF THIS SURVEY MARKED WITH AN ORIGINAL OF THE LAND SURVEYOR'S EMBROIDERED SEAL SHALL BE CONSIDERED TO BE VALID TRUE COPIES.
THIS SURVEY WAS PREPARED FOR THE PARTIES AND PURPOSE INDICATED HEREON. ANY EXTENSION OF THE USE BEYOND THE PARTIES OR PURPOSE INDICATED IS EXPRESSLY FORBIDDEN WITHOUT WRITTEN RELEASE OR PERMISSION OF THE UNDERSIGNED.
USE OF THIS SURVEY IN CONJUNCTION WITH AN AFFIDAVIT OF NO CHANGE IS FORBIDDEN

Kenneth L. Slougenhoup Lic. No. 50349

20' 0 20' 40'
SCALE BAR
IN FEET



Akron Central School District
2023 Capital Improvement Project
OACM Meeting
August 21, 2026

	NAME	COMPANY	PHONE	E-MAIL
1	Adam Klose	Akron	545-5045	AKlose@akronk12.org
2	BRIAN MURRAY			
3	Mark Alexander	ACS	716 542 5012	maalexandereakronk12.org
4	Vaughn Marade	CCMG		
5	Paul Kowalski	ACS	716 542 5015	PKowalski@Akronk12.org
6	Chris Conrath	C/S		christopher.l.conrath@gmail.com
7	JASON BENNETT	CPL	585 750 1106	JBENNETT@CPLTEAM.COM
8	Steve Dinitz	ACS		
9	Peter Forrestel	VOA	716-863-6688	pforrestel2@gmail.com
10	John Marello	ACS	716 542 5088	jmarello@akronk12.org
11	Marc A. Gruff	Compass CMG	(716) 225-2887	mgruff@compasscmg.com
12				
13	Online			
14	Erik Polkowski	ACS BOE		
15	Austin Garbary	CPL		
16	John Gimfeno	CPL		
17	Norm Gardner	CPL		
18	Jason Mark	B-Fl. Eng.		
