

Helen Caise Wade Elementary School



☐ **Completed Work:**

- ☐ Installation of ceramic wall and floor tile has begun in the restrooms.
- ☐ Installation of metal stud framing has started at the second floor at the "EX" walls.
- ☐ Installation of roofing top sheets appear to be nearing completion.
- ☐ ICF forms at the Gymnasium appear to be full height. Roof trusses are staged on site for installation.
- ☐ The floor of Corridor C01 has been cleaned and closed off in preparation of placing terrazzo.
- ☐ Application Installation of the Geofoam under Stair A was in progress.
- ☐ Laying of brick masonry continues to the north face of the building.

☐ **Upcoming Work / Look Ahead:**

- ☐ Installation of the ceramic tile to continue.
- ☐ Hanging of the gypsum board throughout the building to begin.
- ☐ Placing of asphalt at the north side of the building to be completed.
- ☐ Continue the installation of MEP.
- ☐ Roofing to be complete and interior finishes to begin once the building dried-in.

Helen Caise Wade Elementary School



North Face of the Building



Week Ending August 28, 2026

Helen Caise Wade Elementary School



ICF Exterior Walls at the Gymnasium



Week Ending August 28, 2026

Helen Caise Wade Elementary School



Laying of Brick Masonry at the North End of the Building



Week Ending August 28, 2026

Helen Caise Wade Elementary School



Installed Top Sheet of Roofing



Week Ending August 28, 2026

Helen Caise Wade Elementary School



Corridor C01 Preparation of Slab for Installation of the Terrazzo Installation




Week Ending August 28, 2026

Helen Caise Wade Elementary School



Laying of Ceramic Floor Tile

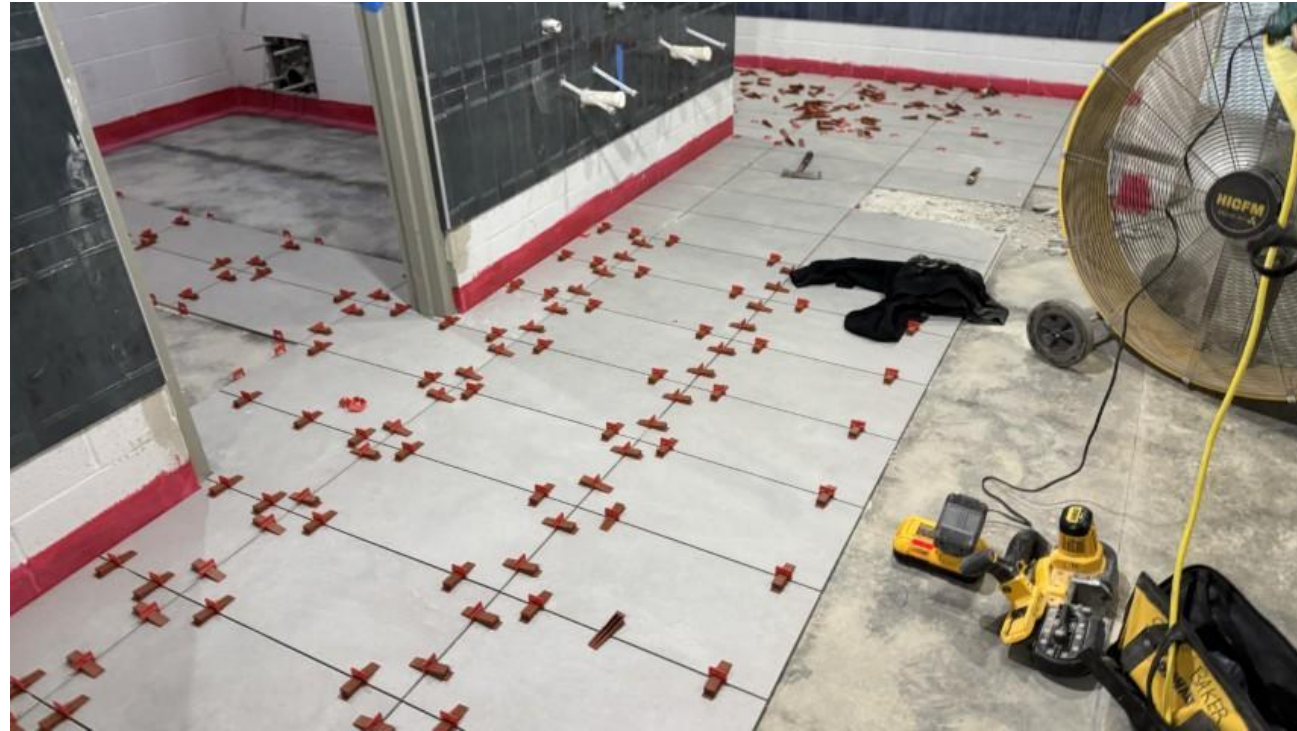

Week Ending August 28, 2026

Helen Caise Wade Elementary School



Metal Stud Framing at the Top of the “EX” Walls



Week Ending August 28, 2026

Helen Caise Wade Elementary School



Geofoam under Stair A



Week Ending August 28, 2026
