



Monthly Progress Report

August 2026

Hempstead Union Free School District (ABGS MS)



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress August 2026

Section III – Work Projected for September 2026

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

August 2026

- **Hempstead UFSD – ABGS MS**
 - New addition to the existing building.
 - Abatement work throughout the existing building.
 - Classroom upgrades in the existing building.
 - New boilers installation in the existing building.
 - MEP upgrades throughout the existing building.



Section II - Work Progress

August 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continued CMU walls throughout the new extension.
 - Continued exterior wall insulation, and brick work.
 - Completed elevator replacement.
 - Flashed in new roof curbs on existing building.
 - Completed rooms L2/L4, 207/209, and girl's locker room.
 - Abated 1/3 of the cafeteria and installed temp tiles.
 - Completed boy's gym fire escape stairs.
 - Completed cleaning of all areas in the existing building.
 - Readjusted fencing for emergency egress from the existing building.
- **Relle:**
 - Continued installing risers and sleeves as needed for addition.
 - Roughing installed in CMU walls and ceilings.
 - Completed rooms L2/L4, 207/209, and girl's locker room.
- **Hirsch:**
 - Continued roughing for new addition.
 - Completed all roughing for rooms L2/L4, 207/209, and girl's locker room.
 - Installed all fixtures in rooms L2/L4, 207/209, and girl's locker room.
- **RMS**
 - Installed new HW piping on first and second floors ceilings.
 - Reinstalled ceiling tiles and grid in corridors.
 - Completed duct work in girl's locker room, L2, L4, 207, and 209.
 - Installed new ceiling cassettes in 207a/b and girls locker room.



Section III - Work Planned September 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continue CMU block installation.
 - Continue exterior insulation and brick work.
 - Continue metal stud framing as needed in new addition.
 - Complete stair installation in new addition.
 - Start installing roof insulation as needed.
- **Relle:**
 - Continue roughing as needed for new addition.
- **Hirsch:**
 - Continue roughing as needed for new addition.
- **RMS:**
 - Continue installing piping in boiler room.
 - Continue refrigerant piping installation in new addition.
 - Continue with duct work installation in new addition.



Section IV – Progress Photos



Hempstead ABGS MS





Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos

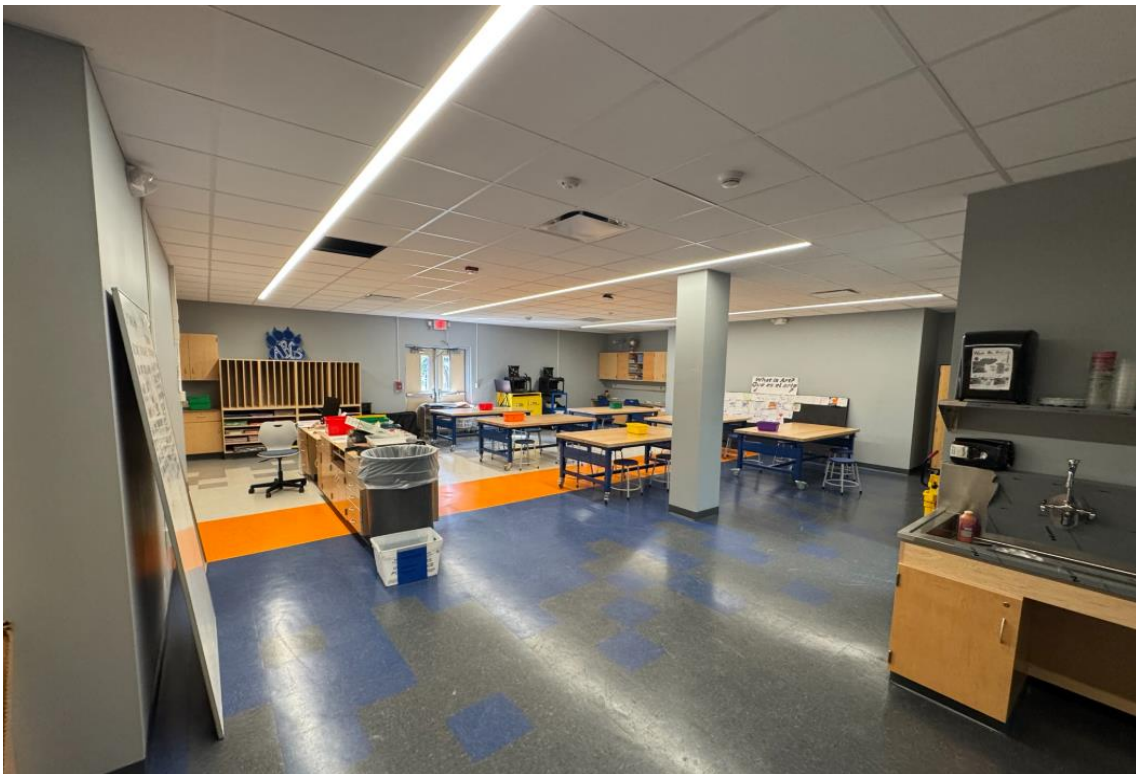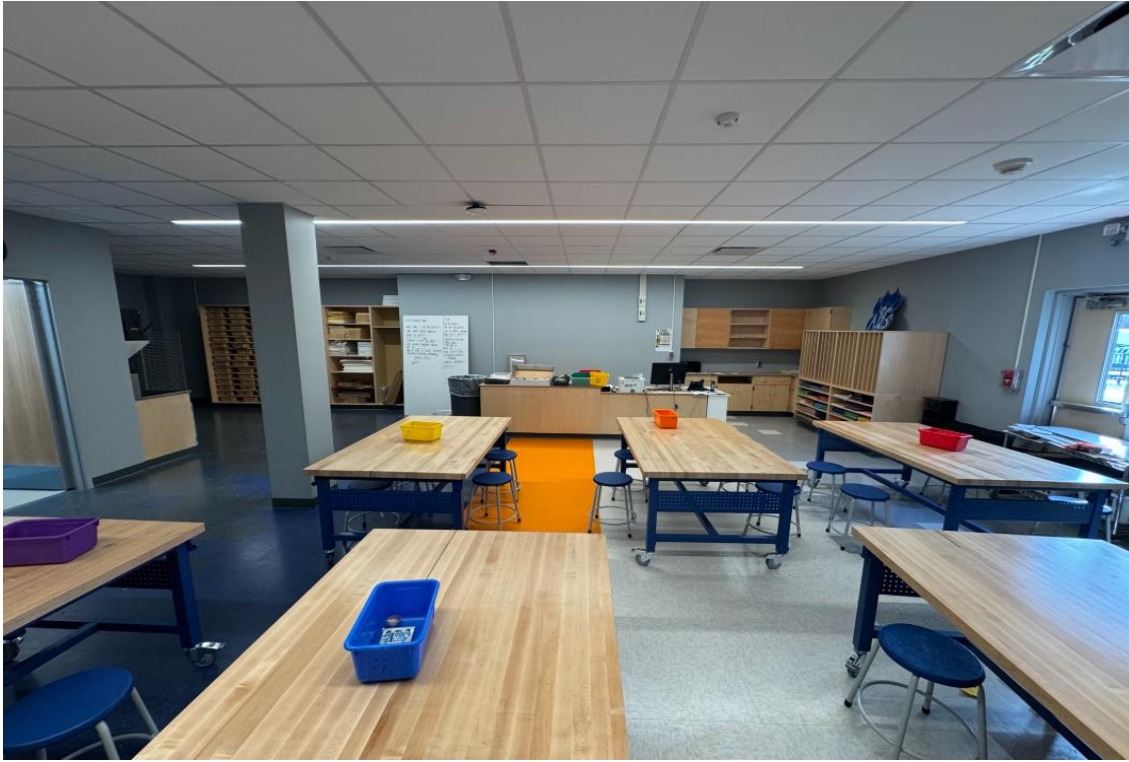

Hempstead ABGS MS




Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos

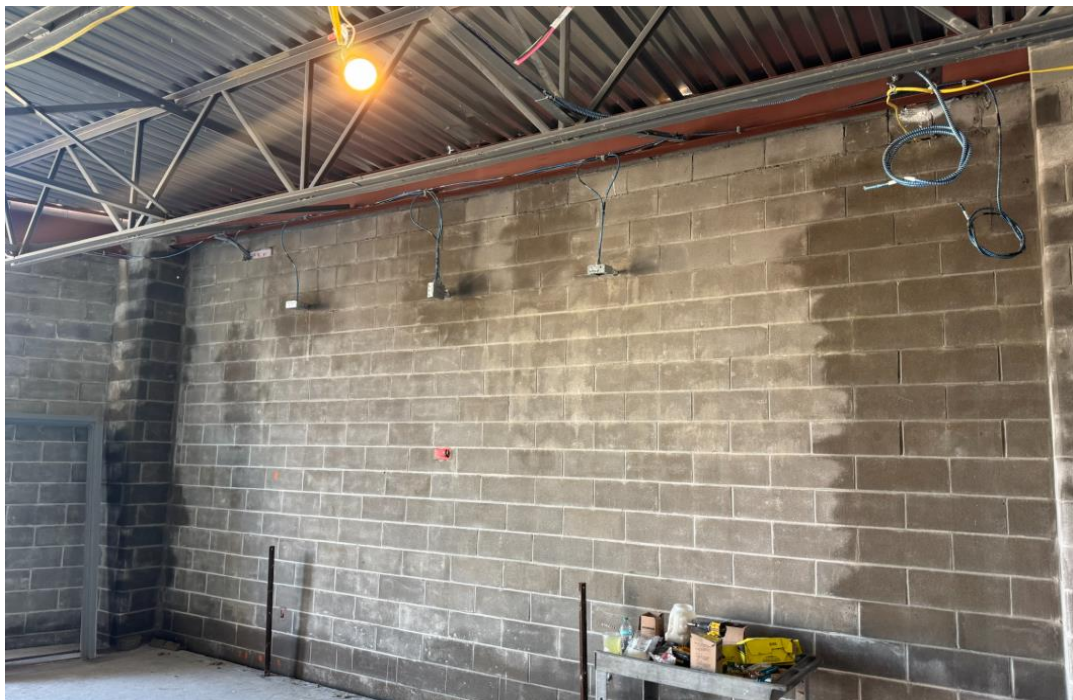

Hempstead ABGS MS



Section IV – Progress Photos




Hempstead ABGS MS



Section V – Workforce Summary – Company/Hours

August 2026

MANPOWER GRAPH

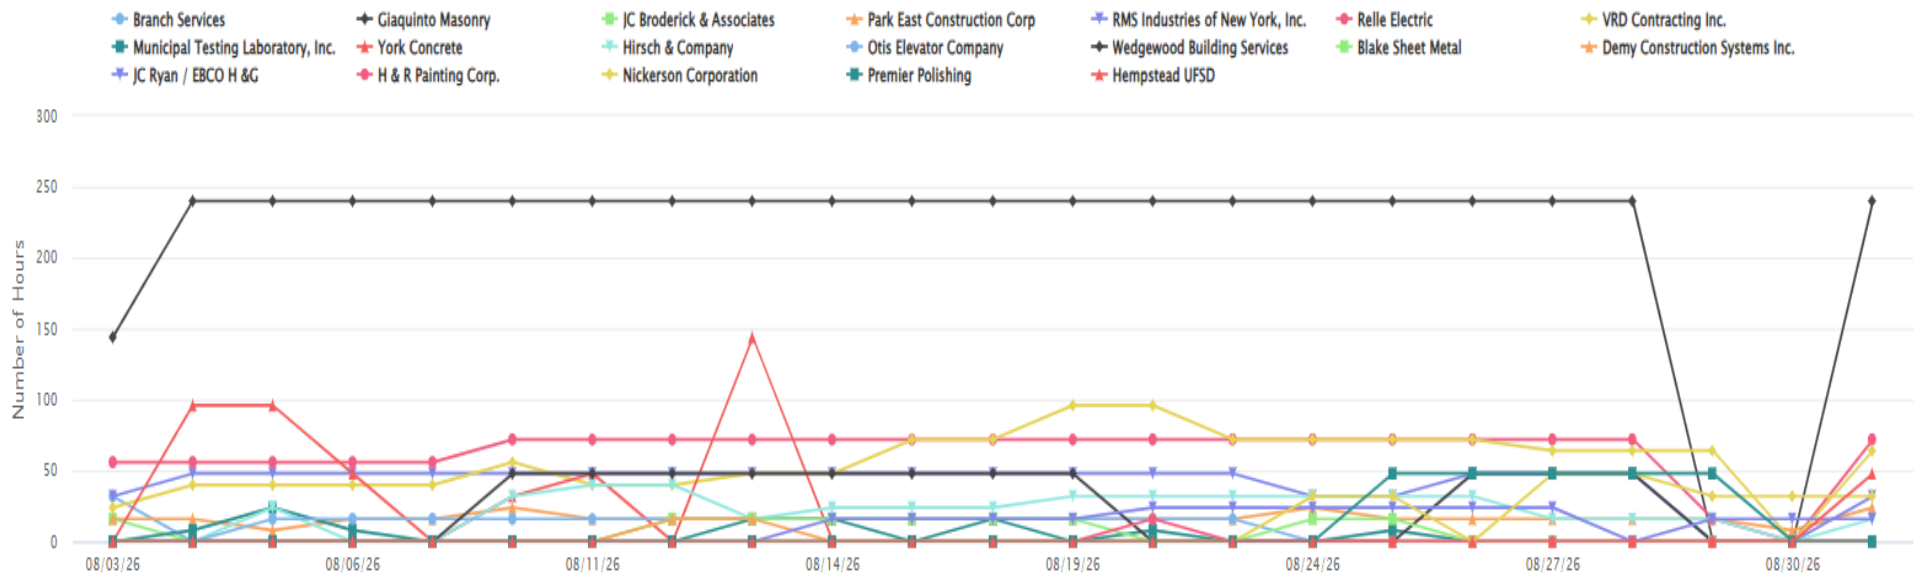

Hempstead ABGS MS



Hempstead Union Free School District (ABGS MS)

August 2026

End of Progress Report
