




Monthly Progress Report

August 2026

Hempstead Union Free School District



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress August 2026

Section III – Work Projected for September 2026

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

August 2026

Project List

- **Hempstead UFSD – IAQ at Various School – Completed**
 - Indoor air quality and mechanical upgrades.
 - Electrical upgrades.
- **Hempstead UFSD – 2022 Bond Phase 3 – In Progress**
 - Infrastructure upgrades throughout all schools.
- **Hempstead UFSD – Boiler replacement at Prospect Elementary School – In Progress**
 - Boiler and piping replacement.
- **Hempstead UFSD – 2022 Bond Phase 4 – In Progress**
 - Infrastructure upgrades throughout all schools.
- **Hempstead UFSD – 2024 Bond Phase 2 – In Progress**
 - Infrastructure upgrades throughout all schools.



Section II - Work Progress

August 2026

Hempstead UFSD – IAQ at Various Schools

- **Eldor & RMS:**
 - Punch list and closeout documentation.

Hempstead UFSD – 2022 Bond Phase 3

- **J Cole:**
 - Restored area around grease trap. Poured sidewalk and asphalt.
 - Completed the kitchen and public elevators at the HS.
 - Completed power washing at the HS.
 - Completed openings for lintels and louvers for the HVAC upgrades.
 - Completed various openings for the HVAC upgrade.
- **Eldor:**
 - completed wire pulls for fans at all schools.
 - Programmed new fire alarm equipment at Paterson.
 - completed electrical work elevators at the HS.
- **RMS:**
 - Started duct installation at various schools.
 - Started installing roof fans installation at various schools.
 - Klima started roughing controls for all new fans.
- **IPS:**
 - Completed 75% of new waste piping in the HS.

Hempstead UFSD – Boiler replacement at Prospect Elementary School

- **KG Mechanical**
 - Set boilers on pads. .
 - Started fabricating and installing pipe.
 - Cut into buildings water tap for boiler water feed.



Section II - Work Progress

August 2026

Hempstead UFSD – 2022 Bond Phase 4

- In process of submittal approvals.
- GC to be rebid.
- Preparation of work to start over school year and next summer.

Hempstead UFSD – 2024 Bond Phase 2

- **J Cole:**
 - Completed bathroom renovations at the HS.
 - Completed new ADA ramp and stairs at the MS.
 - Formed and poured footings for elevator extension.
 - Formed and poured foundation walls for elevator extension.
 - Installed new railings for basement exterior entrance at Paterson ES.
- **Hirsch:**
 - Roughed in for all bathrooms at the HS.
 - Completed fixture install for bathrooms at the HS.
- **Cooper Electric:**
 - Completed roughing for the bathrooms at the HS.
 - Installed all new accessories in bathrooms at the HS.
- **RMS:**
 - Installed new diffusers in the bathrooms at the HS.



Section III - Work Planned September 2026

Hempstead UFSD – IAQ at Various Schools

- **Eldor:**
 - Punchlist and closeout.
- **RMS:**
 - Punchlist and closeout.

Hempstead UFSD – 2022 Bond Phase 3

- **J Cole:**
 - Complete openings for HVAC upgrades
 - Start custodial elevator replacement.
- **IPS:**
 - Complete kitchen waste lines.
- **RMS:**
 - Complete duct work.
 - Install exhaust fans.
 - Start-up fans.
- **Eldor:**
 - Complete start up along side RMS.

Hempstead UFSD – Boiler replacement at Prospect Elementary School

- **KG Mechanical**
 - Complete piping for new boilers.
 - Complete flue and duct installation.
 - Complete electric for new boilers.

Hempstead UFSD – 2022 Bond Phase 4

- Start exterior electric work for various schools.
- Start security work in various schools.
- GC Rebid to take place.
- Start roof work at various schools.



Section III - Work Planned September 2026

Hempstead UFSD – 2024 Bond Phase 2

- McNeil elevator footing/foundation continuation.
 - Start structural for elevator shaft.
- Start mechanical upgrades at various schools.
- Start electrical upgrades at various schools.
- Continue new waste piping installation in MS crawl space.



Section IV – Progress Photos



Hempstead McNeil ES – Ramp and Asphalt




Section IV – Progress Photos



Hempstead HS – Sidewalk Restoration


Section IV – Progress Photos

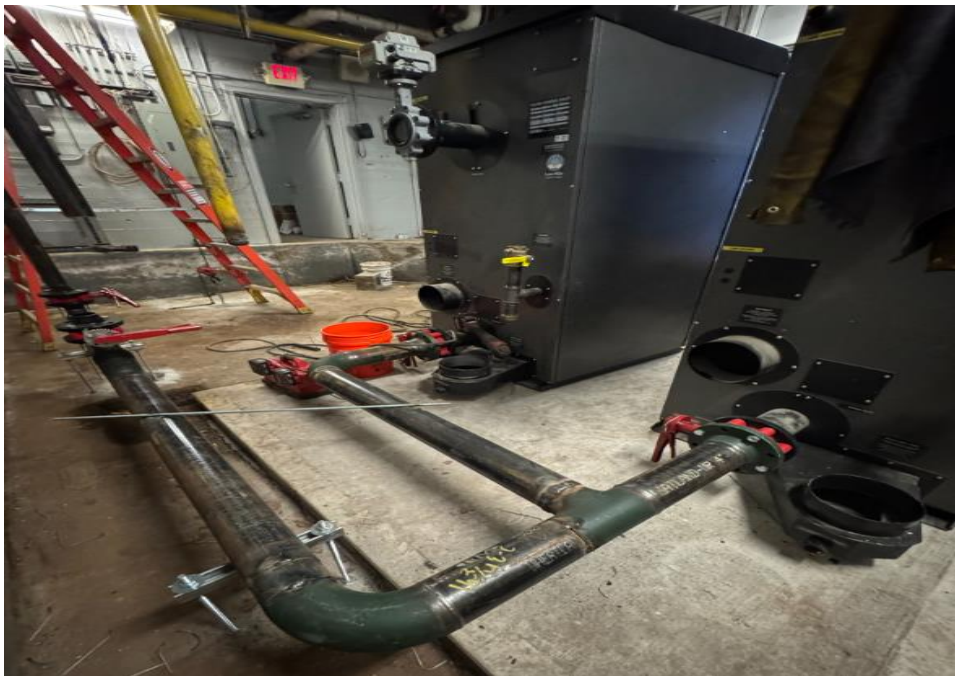

Hempstead Paterson ES – Boiler Replacement



Section IV – Progress Photos

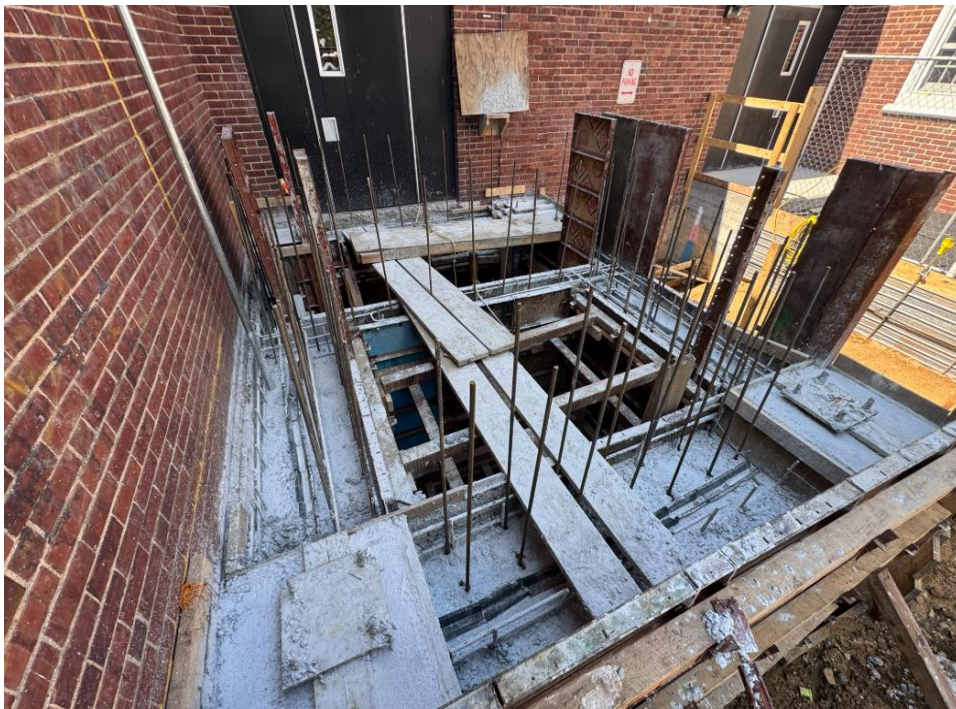

Hempstead McNeil ES – Elevator Extension



Section IV – Progress Photos



Hempstead UFSD – New Railings



Section IV – Progress Photos




Hempstead HS – Bathroom Renovation



Section V – Workforce Summary – Company/Hours

August 2026

▼ MANPOWER GRAPH

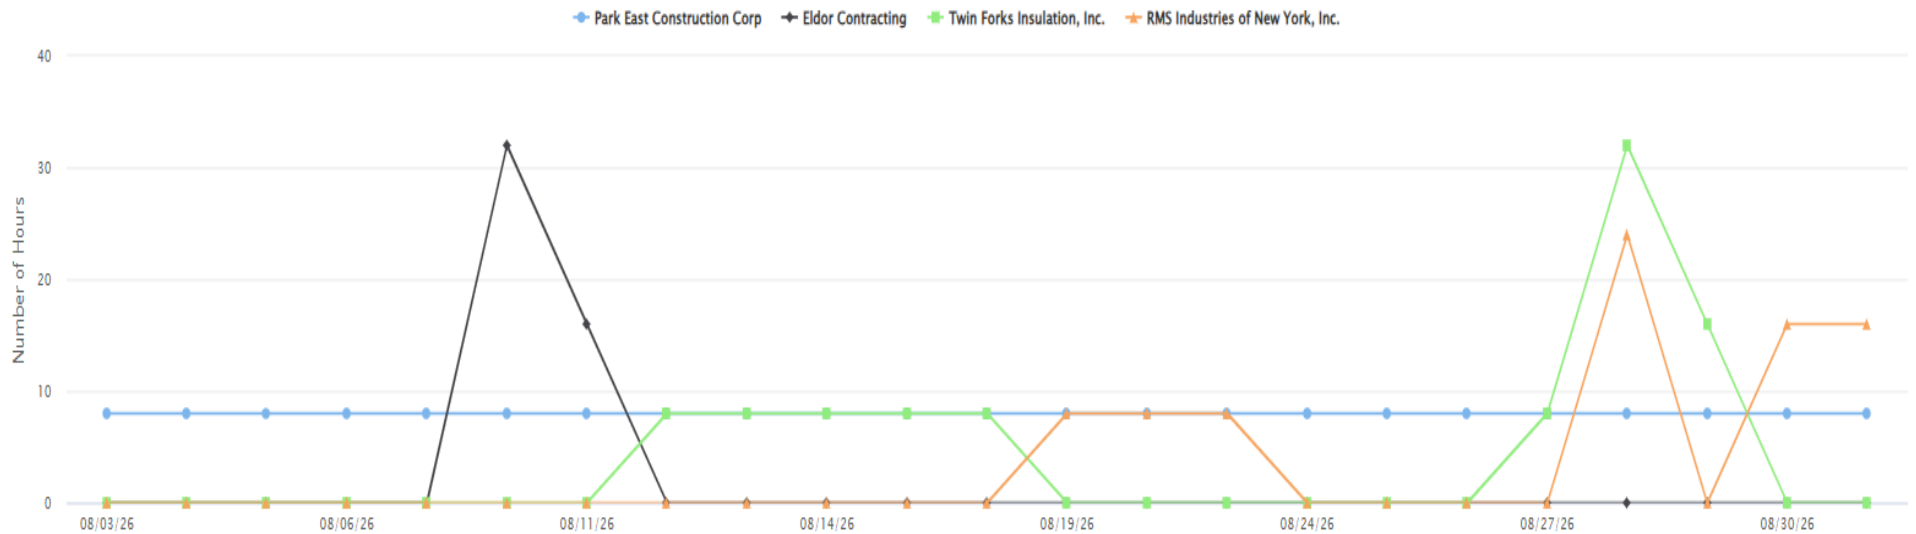


Hempstead UFSD – IAQ at Various Schools



Section V – Workforce Summary – Company/Hours

August 2026

▼ MANPOWER GRAPH

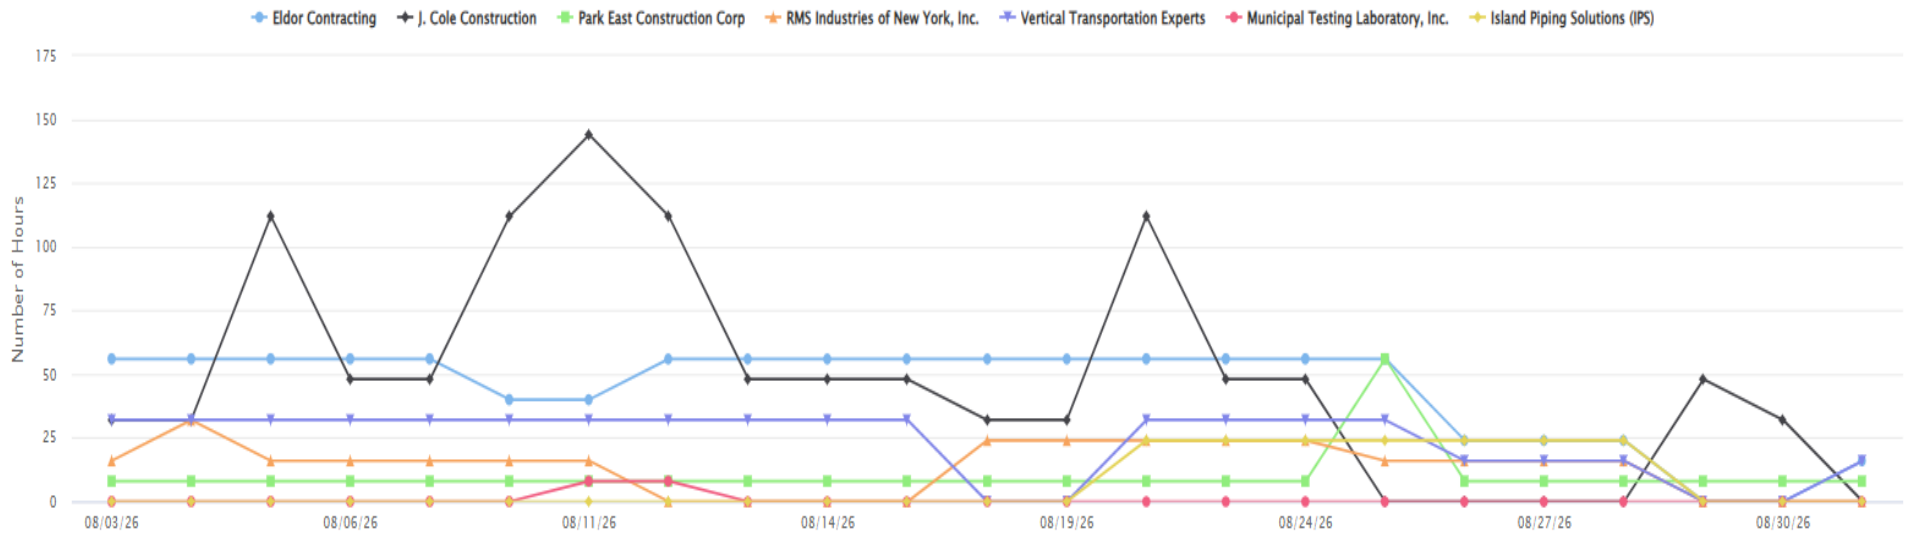


Hempstead UFSD – 2022 Bond Phase 3



Section V – Workforce Summary – Company/Hours

August 2026

▼ MANPOWER GRAPH

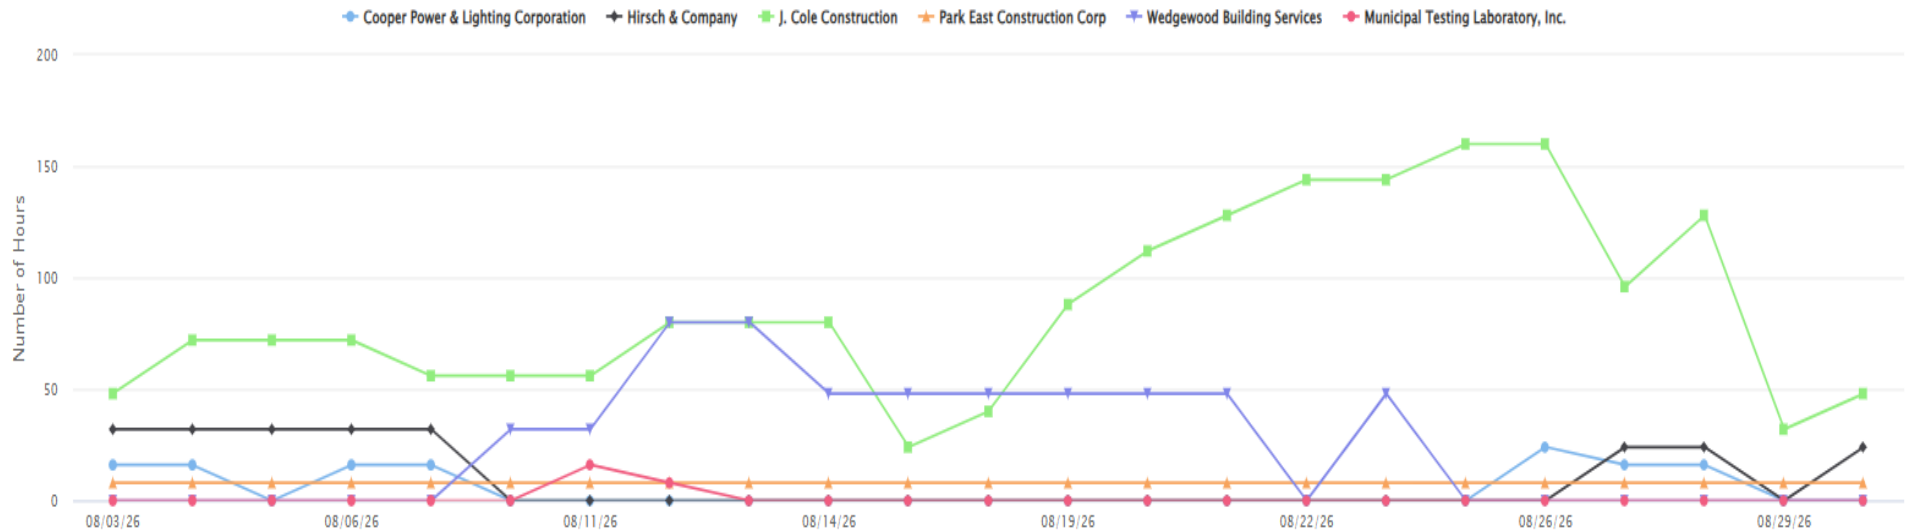


Hempstead UFSD – 2024 Bond Phase 2



Section V – Workforce Summary – Company/Hours

August 2026

MANPOWER GRAPH

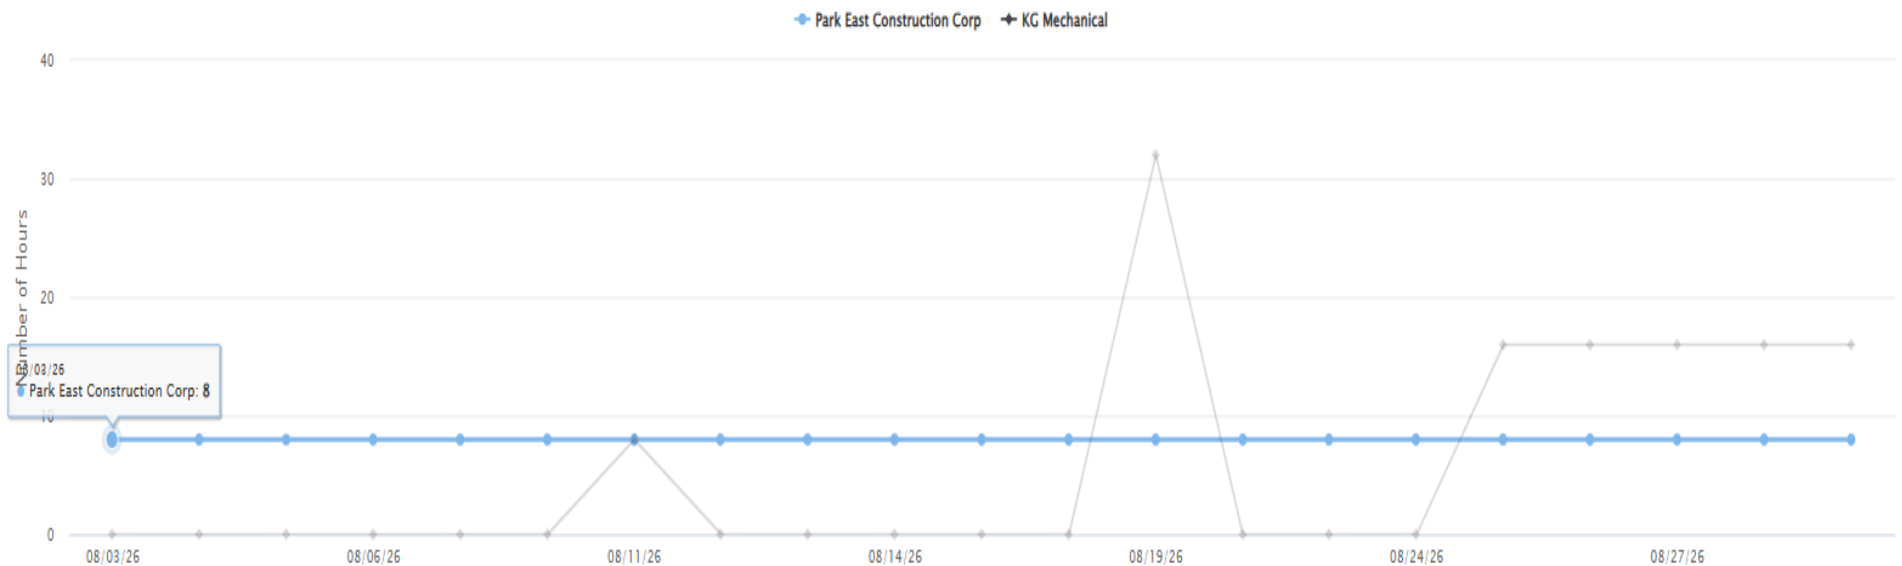

Hempstead UFSD – Paterson Boiler



Hempstead Union Free School District

August 2026

End of Progress Report
