


# FACILITIES, PLANNING & CONSTRUCTION UPDATE


September 28, 2026




# The 2026-2027 Delivery Roadmap

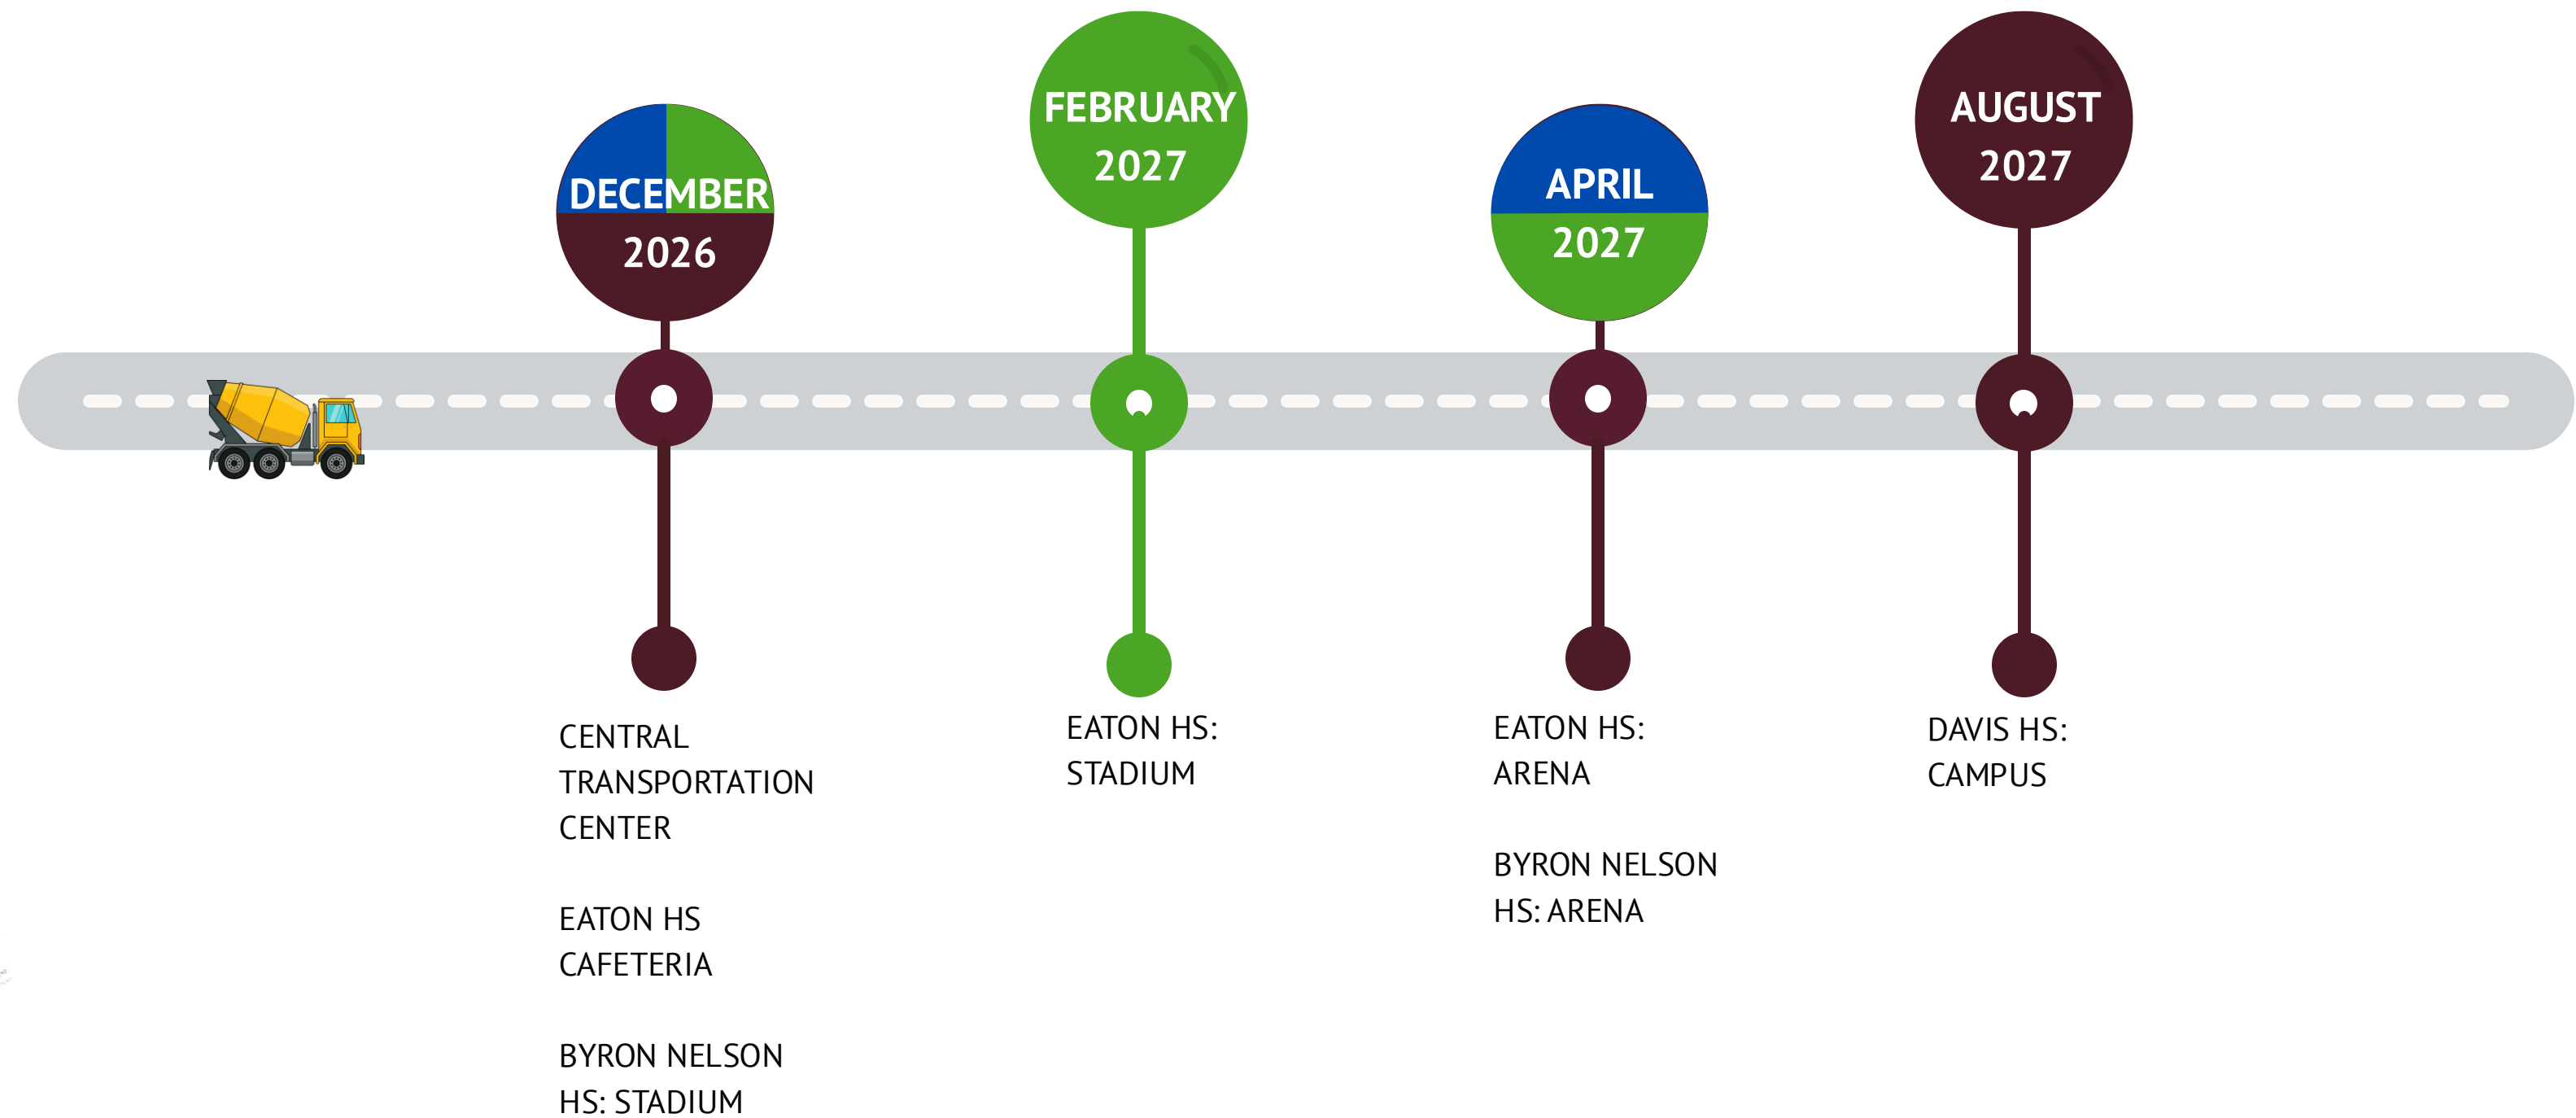


# District Portfolio Status Dashboard

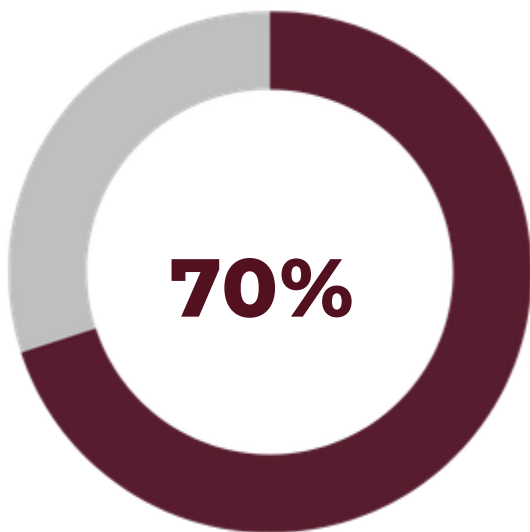


Central Transportation  
Relocation

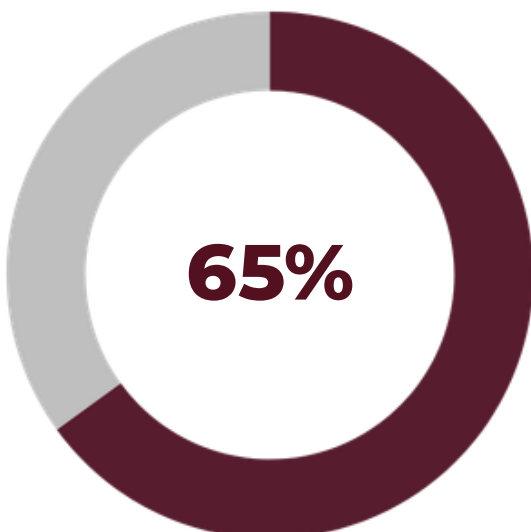


Davis High School

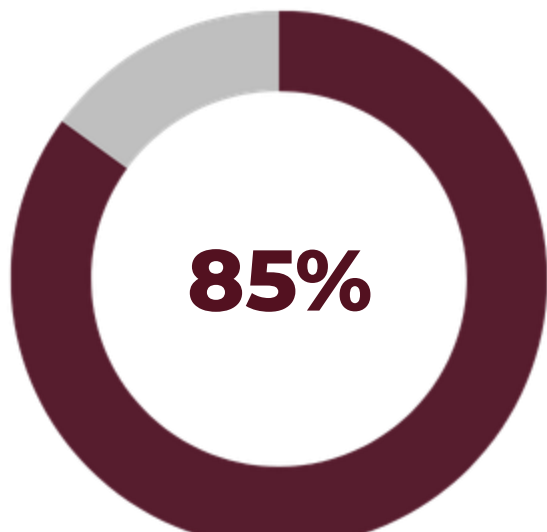


Byron Nelson  
HS  
Stadium

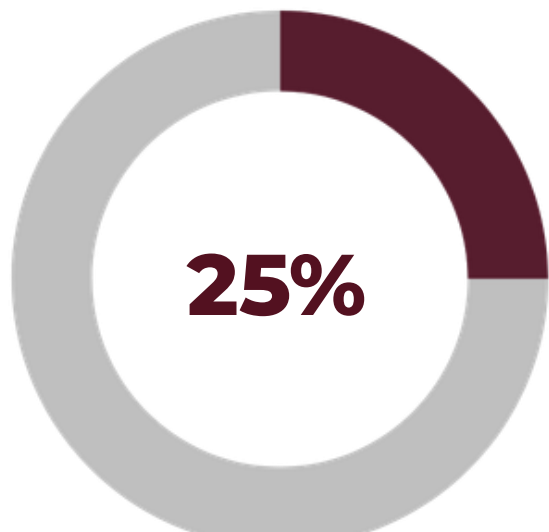


Byron Nelson  
HS Arena

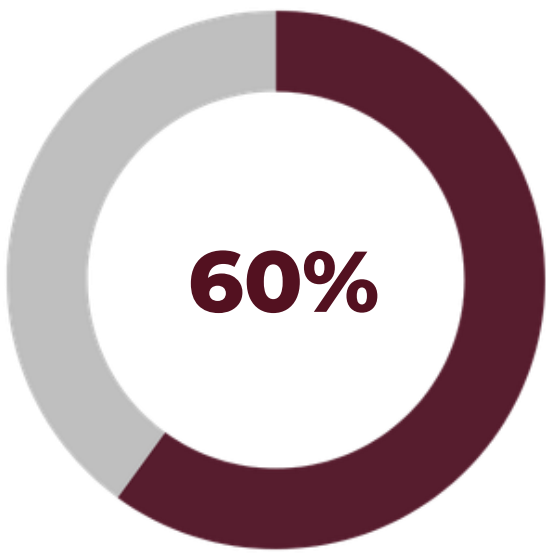

Eaton HS  
Stadium

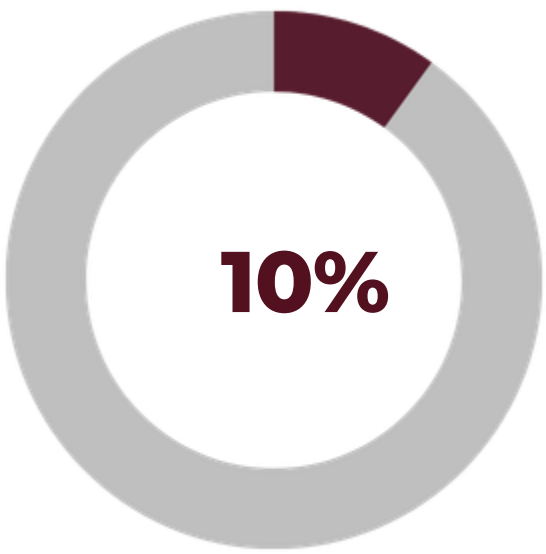

Eaton HS  
Arena

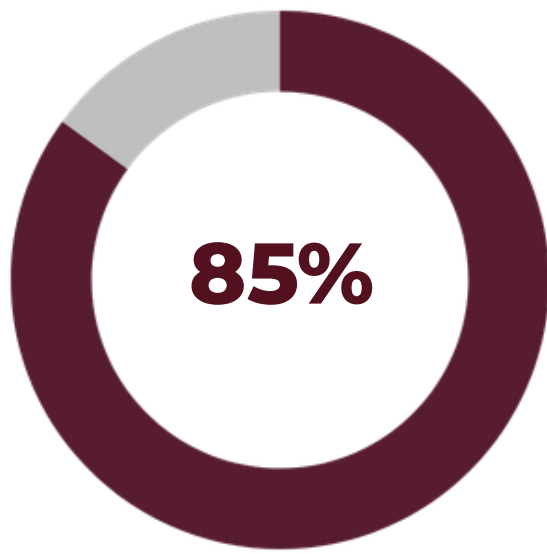

Eaton HS  
Cafeteria


# Byron Nelson HS: Stadium

85% Complete | Target Delivery: December 2026



# Byron Nelson HS: Arena

25% Complete | Target Delivery: April 2027

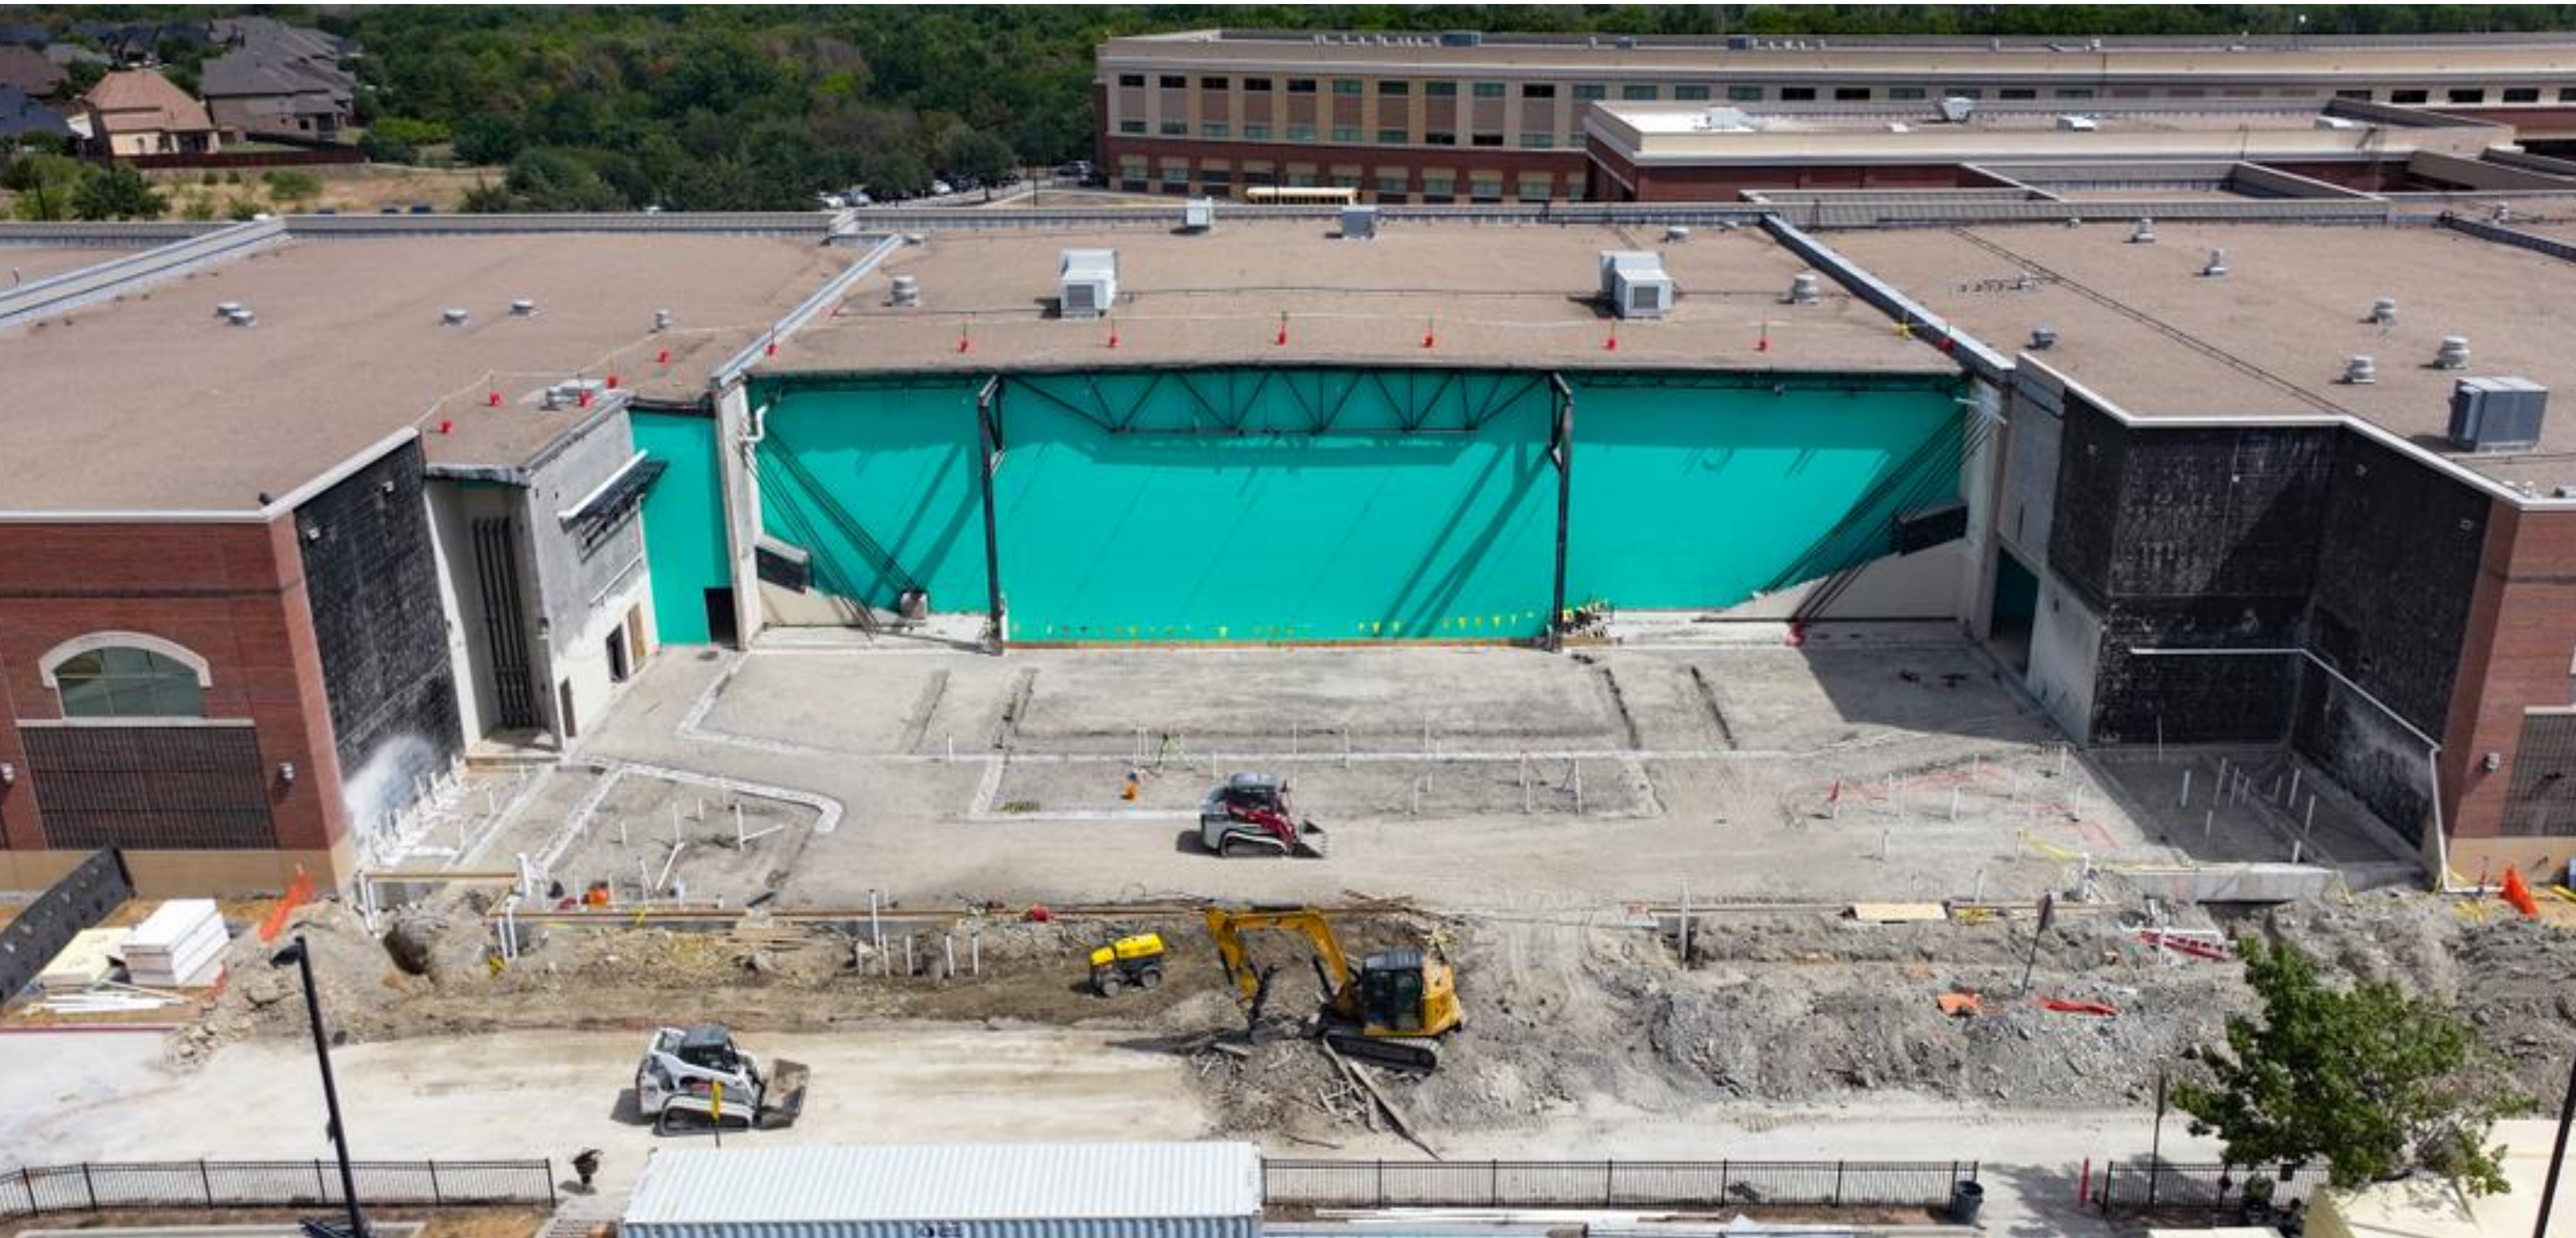


# Eaton HS: Stadium

60% Complete | Target Delivery: February 2027



# V.R. Eaton HS: Arena

10% Complete | Target Delivery: April 2027

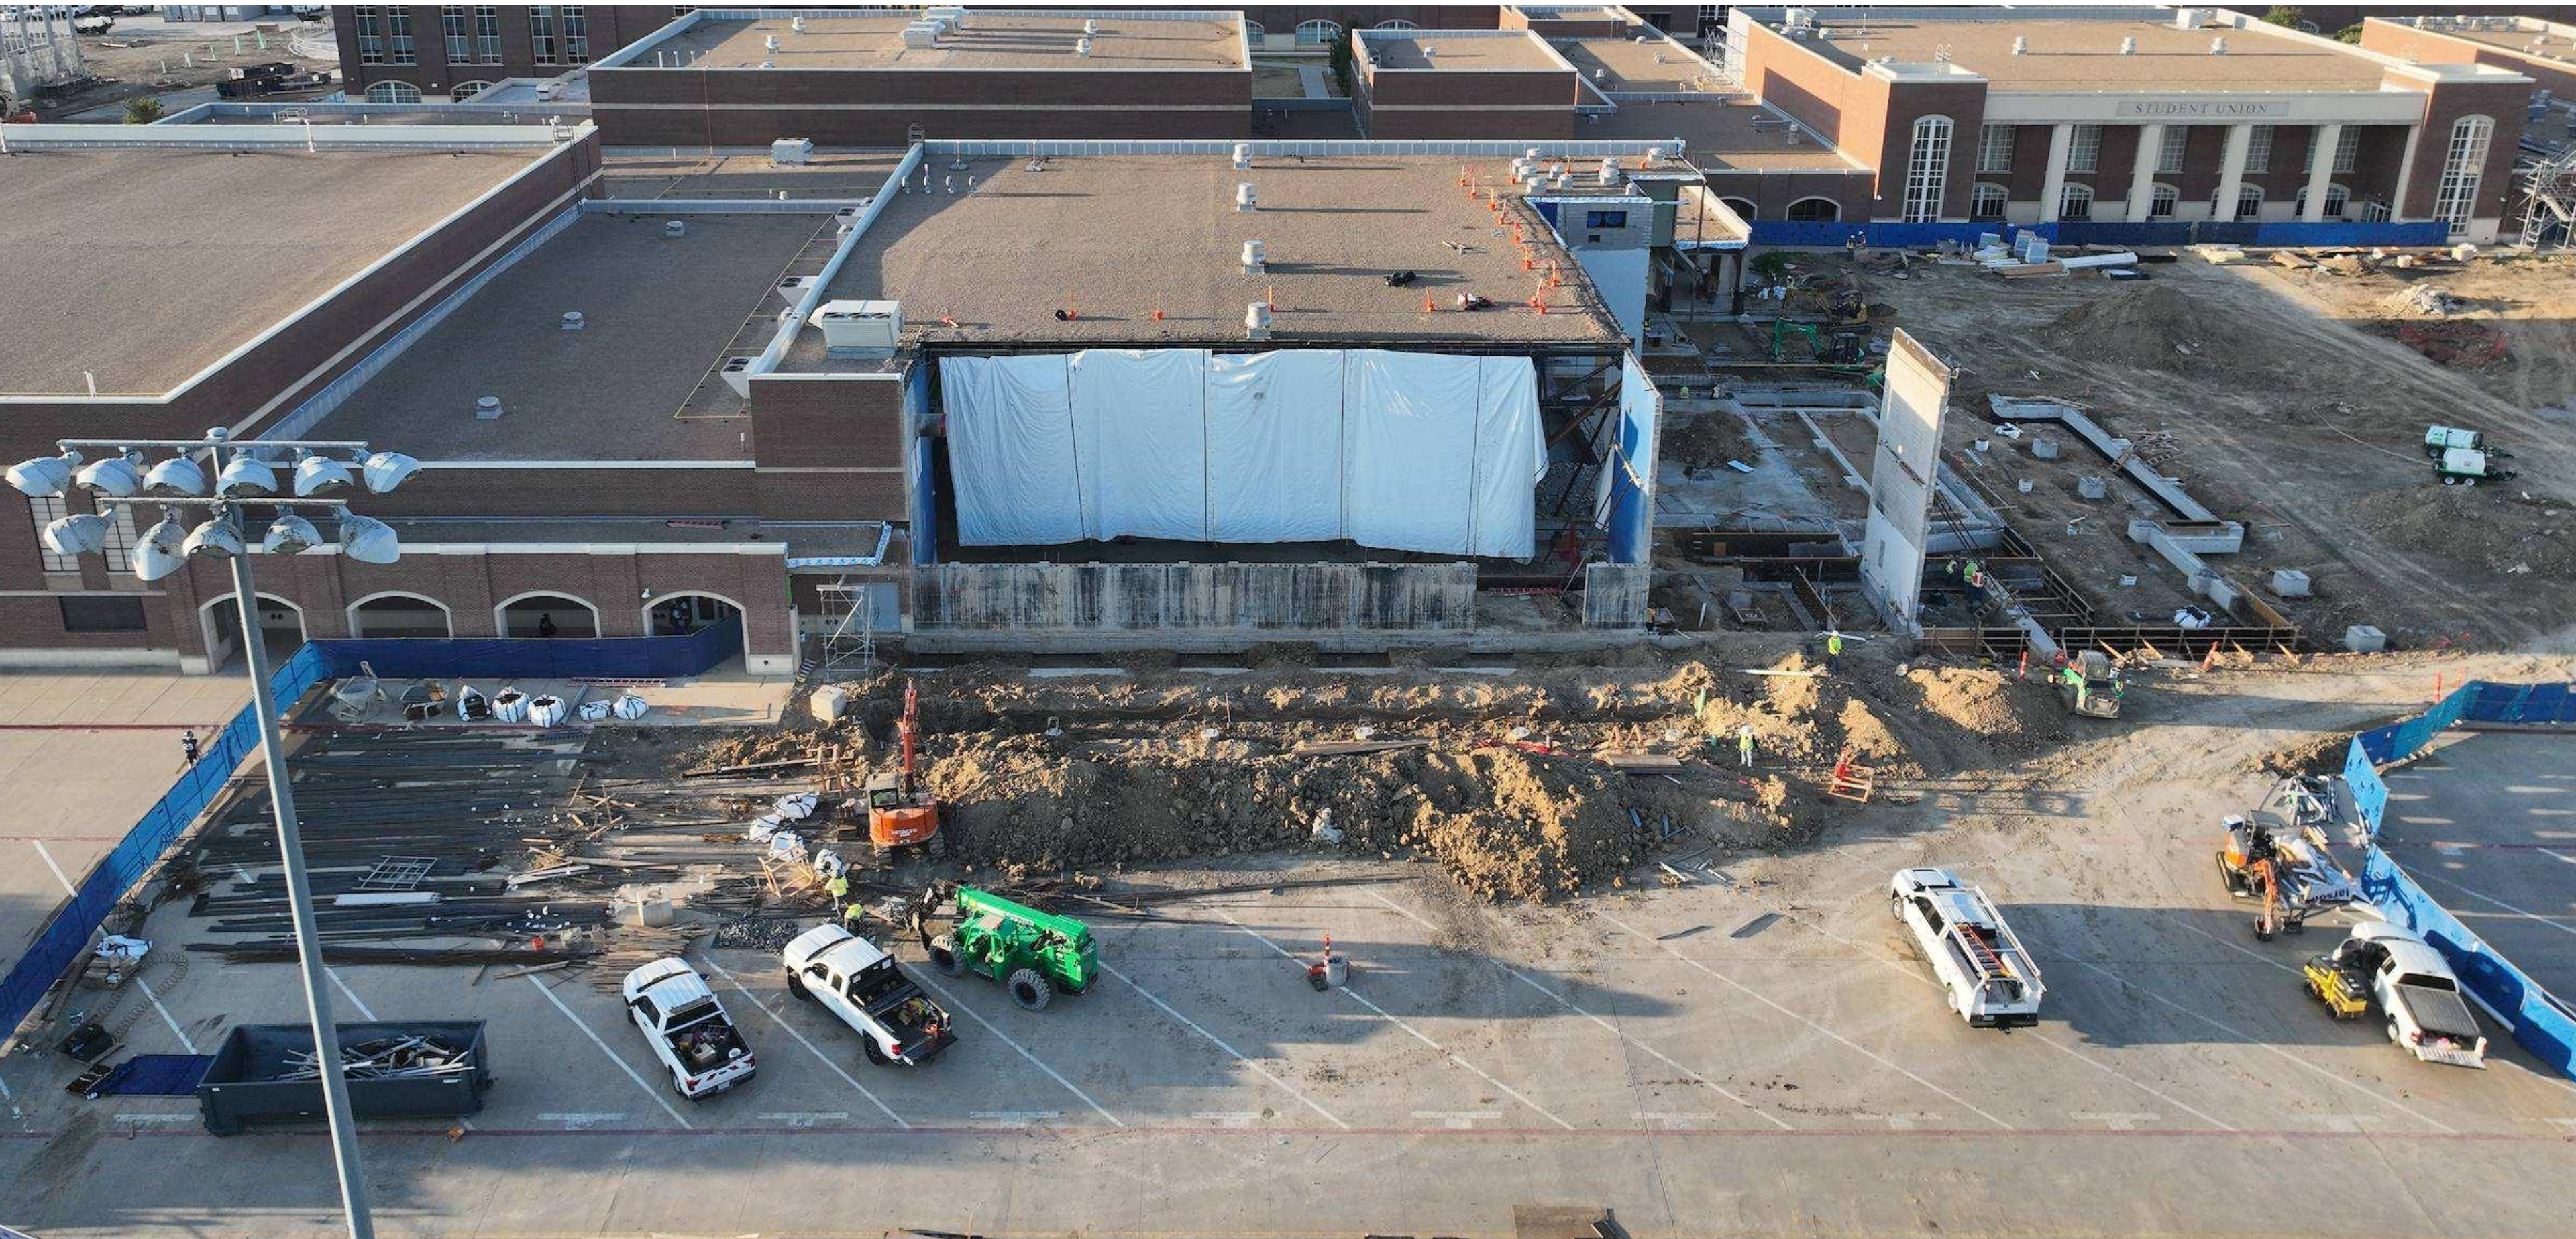

# V.R. Eaton High School: Cafeteria

85% Complete | Target Delivery: December 2026



# Central Transportation

70% Complete | Opening: December 2026



# Davis High School:

65% Complete | Target Delivery: August 2027



# TRACK OUR PROGRESS

[www.nisdtxconstruction.org](http://www.nisdtxconstruction.org)



Northwest Independent School District  
Facilities, Planning and Construction

