



Monthly Progress Report

September 2026

Hempstead Union Free School District (ABGS MS)



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress September 2026

Section III – Work Projected for October 2026

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

September 2026

- **Hempstead UFSD – ABGS MS**
 - New addition to the existing building.
 - Abatement work throughout the existing building.
 - Classroom upgrades in the existing building.
 - New boilers installation in the existing building.
 - MEP upgrades throughout the existing building.



Section II - Work Progress

September 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Completed CMU walls throughout the new extension.
 - Completed exterior wall insulation, and brick work.
 - York poured footings for the fire escape stairs.
 - York poured stairs for boy's locker room exit. Installed railings.
 - York poured the ramp from existing cafeteria out to parking lot.
 - Received roofing material and stored on roof.
 - Started framing soffits throughout extension.
 - Readjusted fencing for emergency egress from the existing building.
 - Started installing blocking for roof curbs and blocking for roof edge.
- **Relle:**
 - Continued installing risers and sleeves as needed for addition.
 - Continued roughing in ceilings and walls.
- **Hirsch:**
 - Continued roughing for new addition in walls and ceilings.
- **RMS**
 - Continued installing new HW piping on first and second floors ceilings.
 - Continued duct installation throughout new addition.



Section III - Work Planned October 2026

Hempstead UFSD – ABGS MS

- **VRD:**
 - Continue installing soffits.
 - Continue exterior blocking around addition.
 - Continue metal stud framing as needed in new addition.
 - Complete stair installation in new addition.
 - Start installing roofing.
 - Pour concrete in the stairs.
- **Relle:**
 - Continue roughing as needed for new addition.
- **Hirsch:**
 - Continue roughing as needed for new addition.
- **RMS:**
 - Continue installing piping in boiler room.
 - Continue refrigerant piping and HW piping installation in new addition.
 - Continue with duct work installation in new addition.



Section IV – Progress Photos



Hempstead ABGS MS




Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos

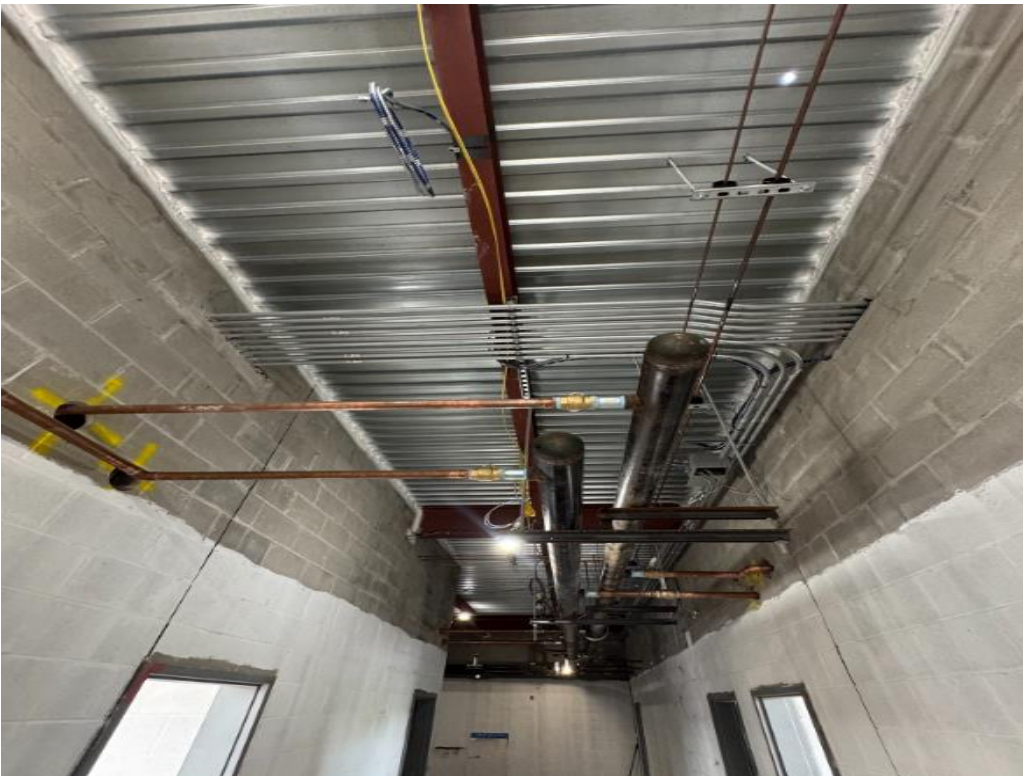

Hempstead ABGS MS



Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos



Hempstead ABGS MS



Section IV – Progress Photos




Hempstead ABGS MS



Section V – Workforce Summary – Company/Hours

September 2026

MANPOWER GRAPH

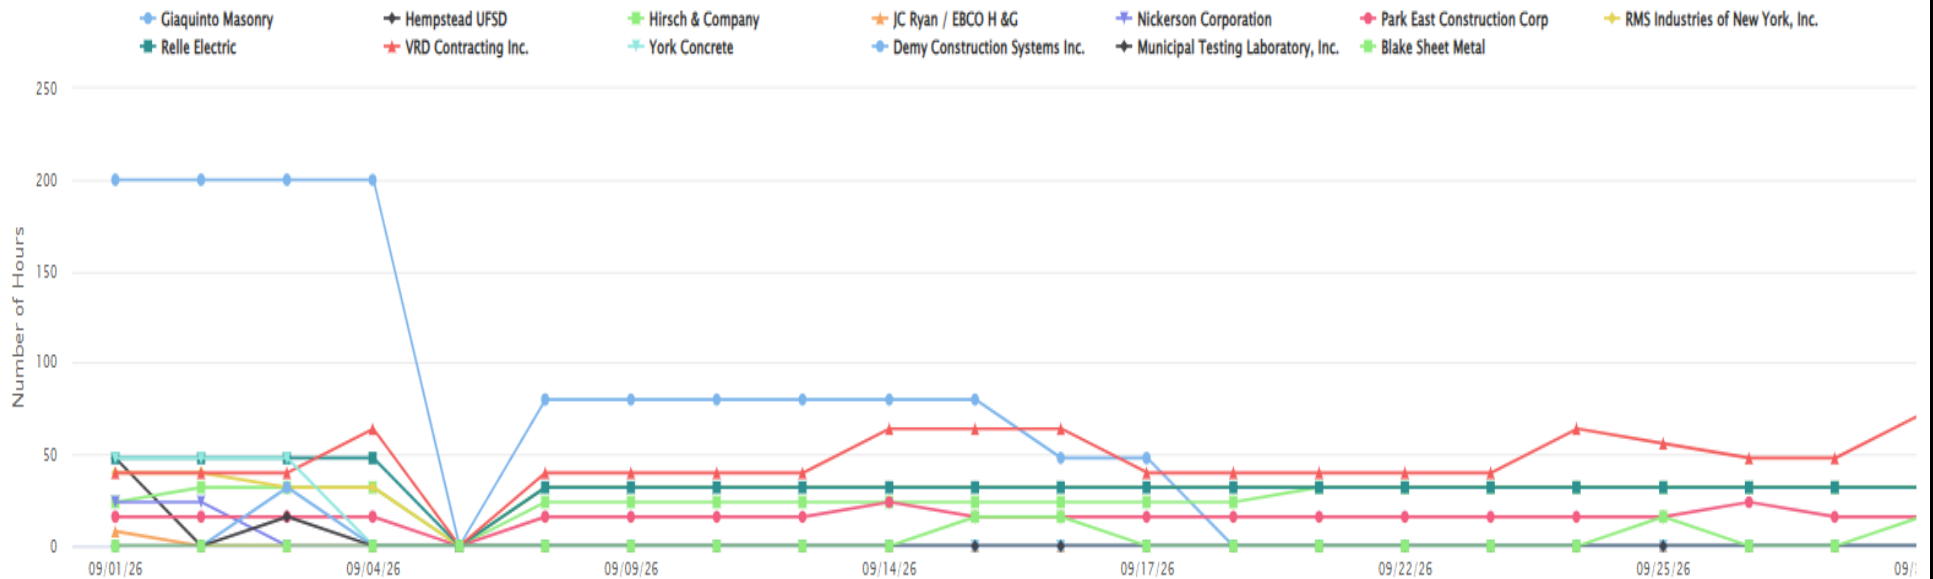

Hempstead ABGS MS



Hempstead Union Free School District (ABGS MS)

September 2026

End of Progress Report
