

INTERMEDIATE HIGH SCHOOL & PERFORMING ARTS CENTER ADDITIONS

UPDATE

- **GC-Massaro Corp.:** Worked on demo at the canopy near the existing computer lab and storage room at the district office entrance. Cut concrete slabs for braced beam connections. Installed student walkway modifications and overhead protection/scaffolding between the SHS and IHS.
 - **R&S Concrete:** Formed and poured the new SHS parking area footers and retaining walls. Excavated and installed footers and formed and poured foundation walls for area AC. Backfilled in area AC and constructed rebar mats for area AC floor slabs.
 - **Century Steel:** Erected steel and installed decking for areas AA and AB
- **EC – Blackhawk Neff:** Installed conduit for the new electrical room in the basement of the existing IHS. Installed conduit and light pole foundations for the new SHS parking area. Installed underground conduits through area AC.
- **PC – Vrabel Plumbing:** Installed sleeves in footers and underground drainage piping for area AC.
- **MC – First American:** Installed piping through the crawl space beneath the existing IHS and demo/prep in the existing boiler room for new layouts.

SCHEDULE

- Substantial Completion for the Classroom Addition: 7/14/2028
- Substantial Completion for the Performing Arts Center Addition: 7/12/2030

REFER TO THE ATTACHED DETAILED SCHEDULE UPDATE FOR SEPTEMBER 2026.

PROGRESS PHOTOS











Seneca Valley IHS Performing Arts Center		All Activities		2026												2027												2028																										
Activity ID	Activity Name	Activity % Complete	OO	RD	Start	Finish	Total Float																																															
Seneca Valley IHS & Performing Arts Center																																																						
Preconstruction																																																						
Massaro																																																						
Submittals & Permits																																																						
G3.1 - Concrete																																																						
A6870	REINFORCING - SUBMIT TO GC	100%	30	0	14-Nov-25A	15-Apr-26	0																																															
A6880	REINFORCING - DESIGN TEAM REVIEW & APPROVAL	100%	15	0	23-Feb-26A	20-Mar-26A	276																																															
A6890	MIX DESIGNS - SUBMIT TO GC	100%	30	0	13-Jan-26A	20-Mar-26A	276																																															
A6700	MIX DESIGNS - DESIGN TEAM REVIEW & APPROVAL	100%	15	0	20-Mar-26A	04-May-26A	455																																															
G4.1 - Masonry																																																						
A9840	MASONRY - PRODUCT DATA - SUBMIT TO GC	100%	30	0	19-Jan-26A	23-Jun-26A	171																																															
A9870	MASONRY - PRODUCT DATA - DESIGN TEAM REVIEW & APPROVAL	100%	15	0	30-Apr-26A	05-May-26A	201																																															
A9850	MASONRY - SAMPLES - SUBMIT TO GC	100%	30	0	19-Jan-26A	18-May-26A	171																																															
A9860	MASONRY - SHOP DRAWINGS - SUBMIT TO GC	100%	30	0	19-Jan-26A	09-Jun-26A	171																																															
A9860	MASONRY - SAMPLES - DESIGN TEAM REVIEW & APPROVAL	100%	15	0	26-May-26A	10-Jun-26A	171																																															
A9890	MASONRY - SHOP DRAWINGS - DESIGN TEAM REVIEW & APPROVAL	100%	15	0	10-Jun-26A	23-Jun-26A	171																																															
G5.1 - Structural Steel																																																						
A3680	STEEL ZONE 101 - SUBMIT TO GC	100%	2	0	23-Dec-25A	17-Apr-26A	40																																															
A3450	STEEL ZONE 101 - DESIGN TEAM REVIEW & APPROVAL	100%	18	0	20-Apr-26A	09-May-26A	40																																															
A3650	STEEL ZONE 102 - SUBMIT TO GC	100%	20	0	23-Dec-25A	18-May-26A	40																																															
A3680	STEEL ZONE 102 - DESIGN TEAM REVIEW & APPROVAL	100%	18	0	21-May-26A	16-Jun-26A	40																																															
A3690	STEEL ZONE 103 - SUBMIT TO GC	100%	20	0	23-Dec-25A	19-Jun-26A	40																																															
A3670	STEEL ZONE 103 - DESIGN TEAM REVIEW & APPROVAL	100%	18	0	24-Jun-26A	10-Jul-26A	40																																															
G7.1 - Roofing																																																						
A9700	ROOFING - PRODUCT DATA - SUBMIT TO GC	100%	30	0	17-Mar-26A	03-Sep-26	40																																															
A9710	ROOFING - SAMPLES - SUBMIT TO GC	100%	30	0	17-Mar-26A	03-Sep-26	40																																															
A9720	ROOFING - SHOP DRAWINGS - SUBMIT TO GC	100%	30	0	17-Mar-26A	03-Sep-26	40																																															
A9730	ROOFING - PRODUCT DATA - DESIGN TEAM REVIEW & APPROVAL	0%	15	15	03-Sep-26	24-Sep-26	40																																															
A9740	ROOFING - SAMPLES - DESIGN TEAM REVIEW & APPROVAL	0%	15	15	03-Sep-26	24-Sep-26	40																																															
A9750	ROOFING - SHOP DRAWINGS - DESIGN TEAM REVIEW & APPROVAL	0%	15	15	03-Sep-26	24-Sep-26	40																																															
G7.2 - Metal Panels																																																						
A9760	METAL PANELS - PRODUCT DATA - SUBMIT TO GC	100%	30	0	29-Jan-26A	17-Jun-26A	171																																															
A9780	METAL PANELS - SHOP DRAWINGS - SUBMIT TO GC	100%	30	0	29-Jan-26A	17-Jun-26A	171																																															
A9790	METAL PANELS - PRODUCT DATA - DESIGN TEAM REVIEW & APPROVAL	100%	15	0	18-Jun-26A	30-Jun-26A	201																																															
A9810	METAL PANELS - SHOP DRAWINGS - DESIGN TEAM REVIEW & APPROVAL	0%	15	15	18-Jun-26A	24-Sep-26	171																																															
A9770	METAL PANELS - SAMPLES - SUBMIT TO GC	0%	30	30	29-Jan-26A	15-Oct-26	171																																															
A9800	METAL PANELS - SAMPLES - DESIGN TEAM REVIEW & APPROVAL	0%	15	15	16-Oct-26	05-Nov-26	171																																															
G7.3 - Waterproofing																																																						
A9820	WATERPROOFING - PRODUCT DATA - SUBMIT TO GC	100%	30	0	30-Apr-26A	05-May-26A	78																																															
A9850	WATERPROOFING - PRODUCT DATA - DESIGN TEAM REVIEW & APPROVAL	100%	15	0	08-May-26A	15-May-26A	78																																															
A9840	WATERPROOFING - SHOP DRAWINGS - SUBMIT TO GC	100%	30	0	30-Apr-26A	09-Jun-26A	78																																															
A9870	WATERPROOFING - SHOP DRAWINGS - DESIGN TEAM REVIEW & APPROVAL	100%	15	0	10-Jun-26A	06-Jul-26A	78																																															
G8.1 - DFM																																																						
A9810	DFM - SUBMIT TO GC	100%	30	0	24-Dec-25A	12-Mar-26A	78																																															
A9820	DFM - DESIGN TEAM REVIEW & APPROVAL	100%	15	0	13-Mar-26A	06-Apr-26A	78																																															
G8.2 - Overhead Doors																																																						
A9880	OHD - PRODUCT DATA - SUBMIT TO GC	0%	30	30	13-Feb-26A	15-Oct-26	78																																															
A9890	OHD - SAMPLES - SUBMIT TO GC	0%	30	30	13-Feb-26A	15-Oct-26	78																																															
Legend																																																						
Actual Work																																																						
Remaining Work																																																						
Critical Remaining Work																																																						
Milestone																																																						
TASK filter: All Activities																																																						
Page 1 of 27																																																						
Oracle Corporation																																																						

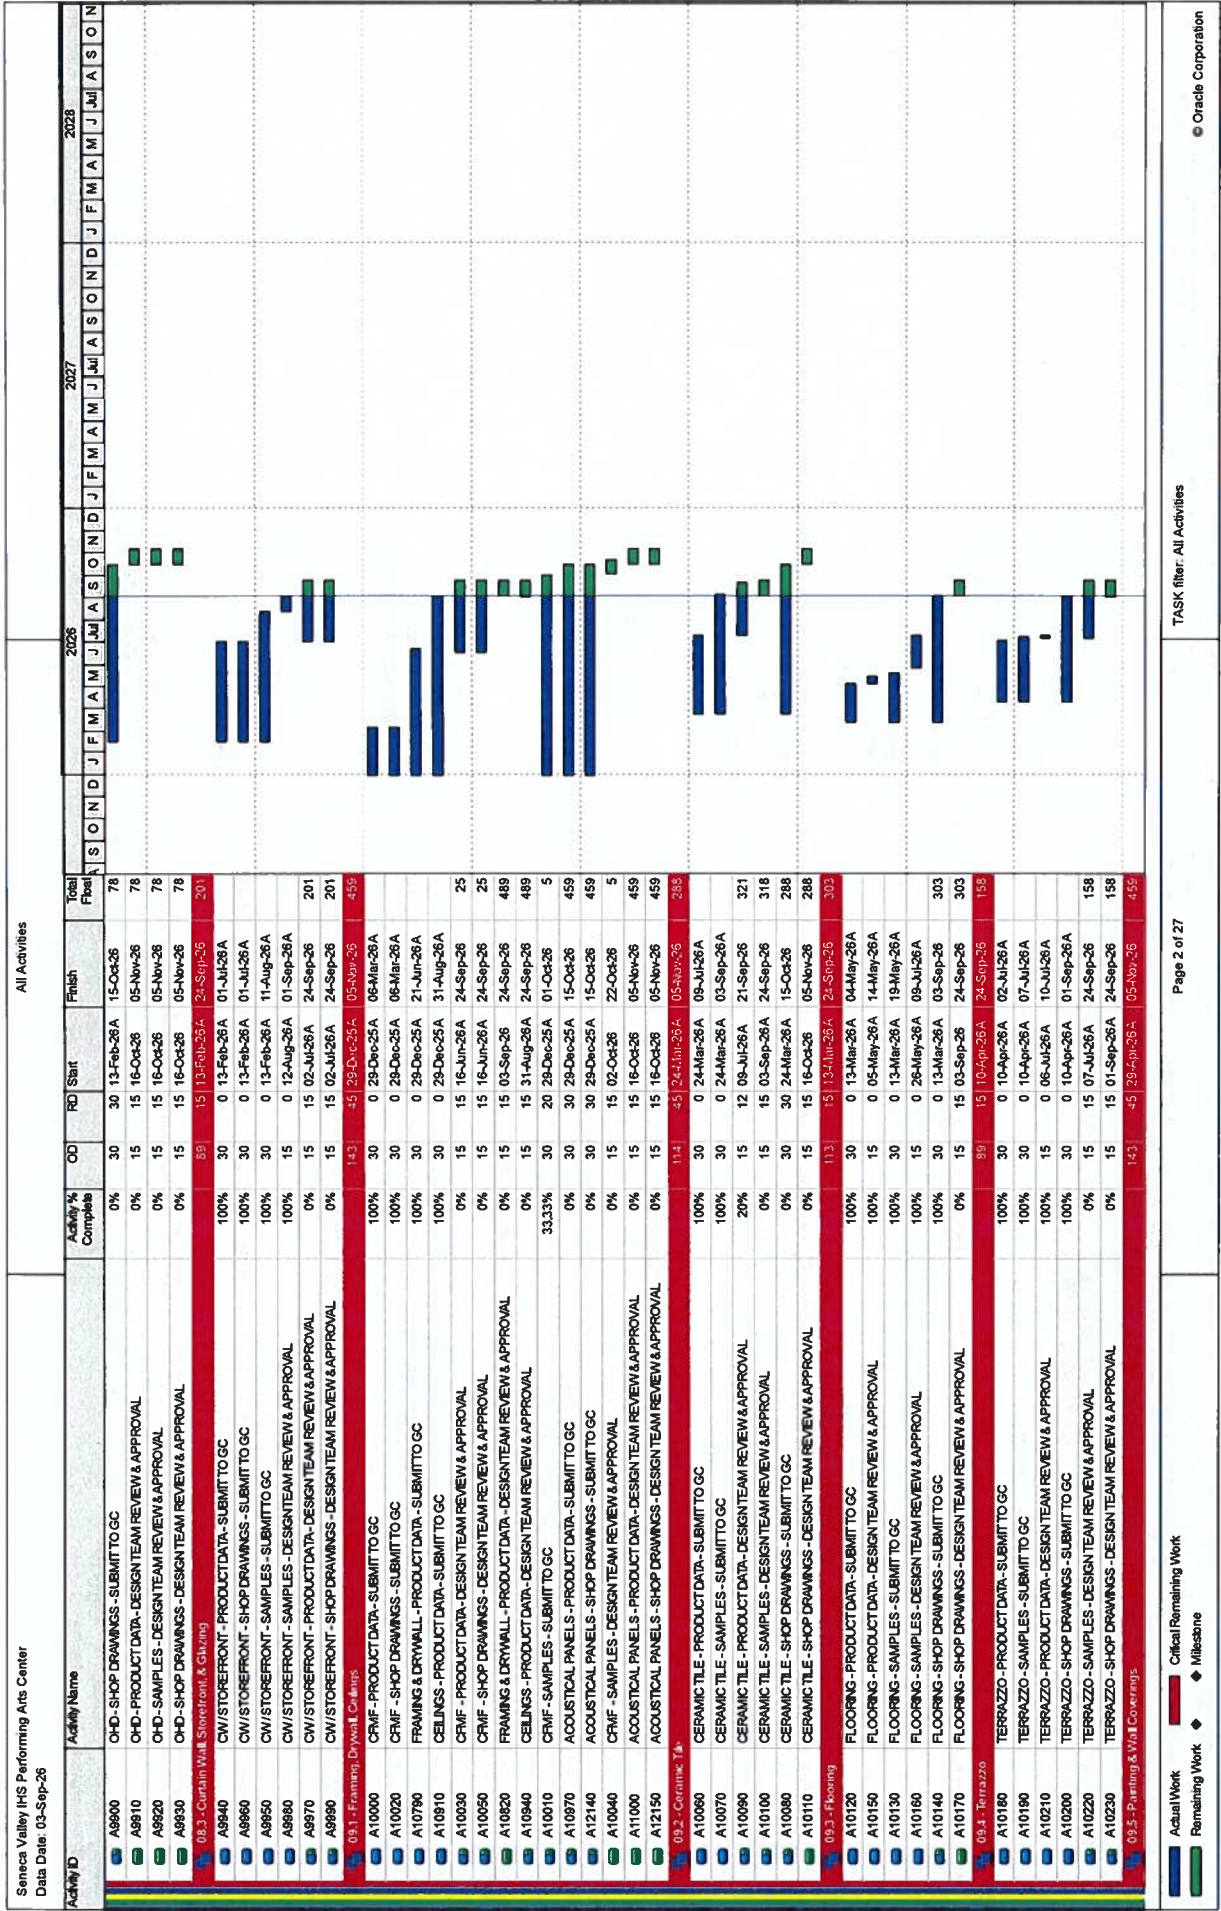



Seneca Valley IHS Performing Arts Center		All Activities																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
Data Date: 03-Sep-26																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
Activity ID	Activity Name	Activity % Complete	OO	RD	Start	Finish	Total Float																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
A10240	PAINING & WC - PRODUCT DATA - SUBMIT TO GC	100%	30	0	28-Apr-26A	27-May-26A																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																</


Activity ID	Activity Name	Activity % Complete	OO	RD	Start	Finish	Total
04.1 - Masonry							
A11020	MASONRY PROCUREMENT	0%	50	50	03-Sep-26	12-Nov-26	258
05.1 - Structural Steel							
A3460	STEEL ZONE 101 FABRICATION	100%	57	0	10-May-26A	31-Jul-26A	17
A3710	STEEL ZONE 102 FABRICATION	100%	40	0	17-Jun-26A	03-Sep-26	12
A3700	STEEL ZONE 103 FABRICATION	83.72%	43	7	13-Jul-26A	14-Sep-26	17
07.1 - Roofing							
A11030	ROOFING PROCUREMENT	0%	60	60	25-Sep-26	21-Dec-26	40
07.2 - Metal Panels							
A11040	METAL PANEL PROCUREMENT	0%	60	60	06-Nov-26	03-Feb-27	171
07.3 - Waterproofing							
A11050	WATERPROOFING PROCUREMENT	65%	20	7	07-Jul-26A	14-Sep-26	44
08.1 - DFW							
A6840	DFW - HM FRAME PROCUREMENT	0%	50	50	03-Sep-26	29-Dec-26	328
A6850	DFW - HARDWARE PROCUREMENT	0%	50	50	03-Sep-26	12-Nov-26	133
A6860	DFW - HM DOOR PROCUREMENT	0%	50	50	03-Sep-26	12-Nov-26	358
A6830	DFW - WOOD DOOR PROCUREMENT	0%	80	80	03-Sep-26	29-Dec-26	328
08.2 - Overhead Doors							
A11060	OHD PROCUREMENT	0%	60	60	06-Nov-26	03-Feb-27	78
08.3 - Curtain Wall Storefront & Glazing							
A11070	STOREFRONT PROCUREMENT	0%	80	80	25-Sep-26	20-Jan-27	233
A11270	CURTAIN WALL PROCUREMENT	0%	80	80	25-Sep-26	20-Jan-27	201
09.1 - Framing, Drywall Ceilings							
A11080	CMF PROCUREMENT	0%	20	20	23-Oct-26	19-Nov-26	5
09.2 - Ceramic Tile							
A11090	CERAMIC TILE PROCUREMENT	0%	50	50	06-Nov-26	20-Jan-27	288
09.3 - Flooring							
A11100	FLOORING PROCUREMENT	0%	50	50	25-Sep-26	07-Dec-26	303
09.4 - Terrazzo							
A11110	TERRAZZO PROCUREMENT	0%	50	50	25-Sep-26	07-Dec-26	158
09.5 - Painting & Wall Coverings							
A11120	WALL COVERING PROCUREMENT	0%	50	50	03-Sep-26	12-Nov-26	153
10.1 - Signage							
A11130	SIGNAGE PROCUREMENT	0%	50	50	06-Nov-26	20-Jan-27	328
10.2 - Misc Dry 10							
A11140	FIRE EXTINGUISHER PROCUREMENT	0%	30	30	06-Nov-26	03-Feb-27	308
A11150	TOILET PARTITION PROCUREMENT	0%	50	50	06-Nov-26	20-Jan-27	318
A11160	TOILET ACCESSORIES PROCUREMENT	0%	50	50	06-Nov-26	20-Jan-27	318
A11170	OPERABLE PARTITION PROCUREMENT	0%	60	60	06-Nov-26	03-Feb-27	308
10.3 - Metal Lockers							
A11180	METAL LOCKER PROCUREMENT	0%	60	60	03-Sep-26	30-Nov-26	444
11.1 - Loading Dock Equipment							
A11190	LOADING DOCK PROCUREMENT	0%	60	60	06-Nov-26	03-Feb-27	399
11.2 - Orchestra Stage Equipment							
A11200	ORCHESTRA STAGE EQUIPMENT PROCUREMENT	0%	60	60	06-Nov-26	03-Feb-27	399
12.1 - Window Coverings							
A11210	WINDOW COVERING PROCUREMENT	0%	40	40	03-Jun-27	29-Jul-27	121
12.2 - Fired Seating							
A11220	FIRE SEATING PROCUREMENT	0%	60	60	06-Nov-26	03-Feb-27	399


Actual Work Remaining Work Critical Remaining Work Milestone

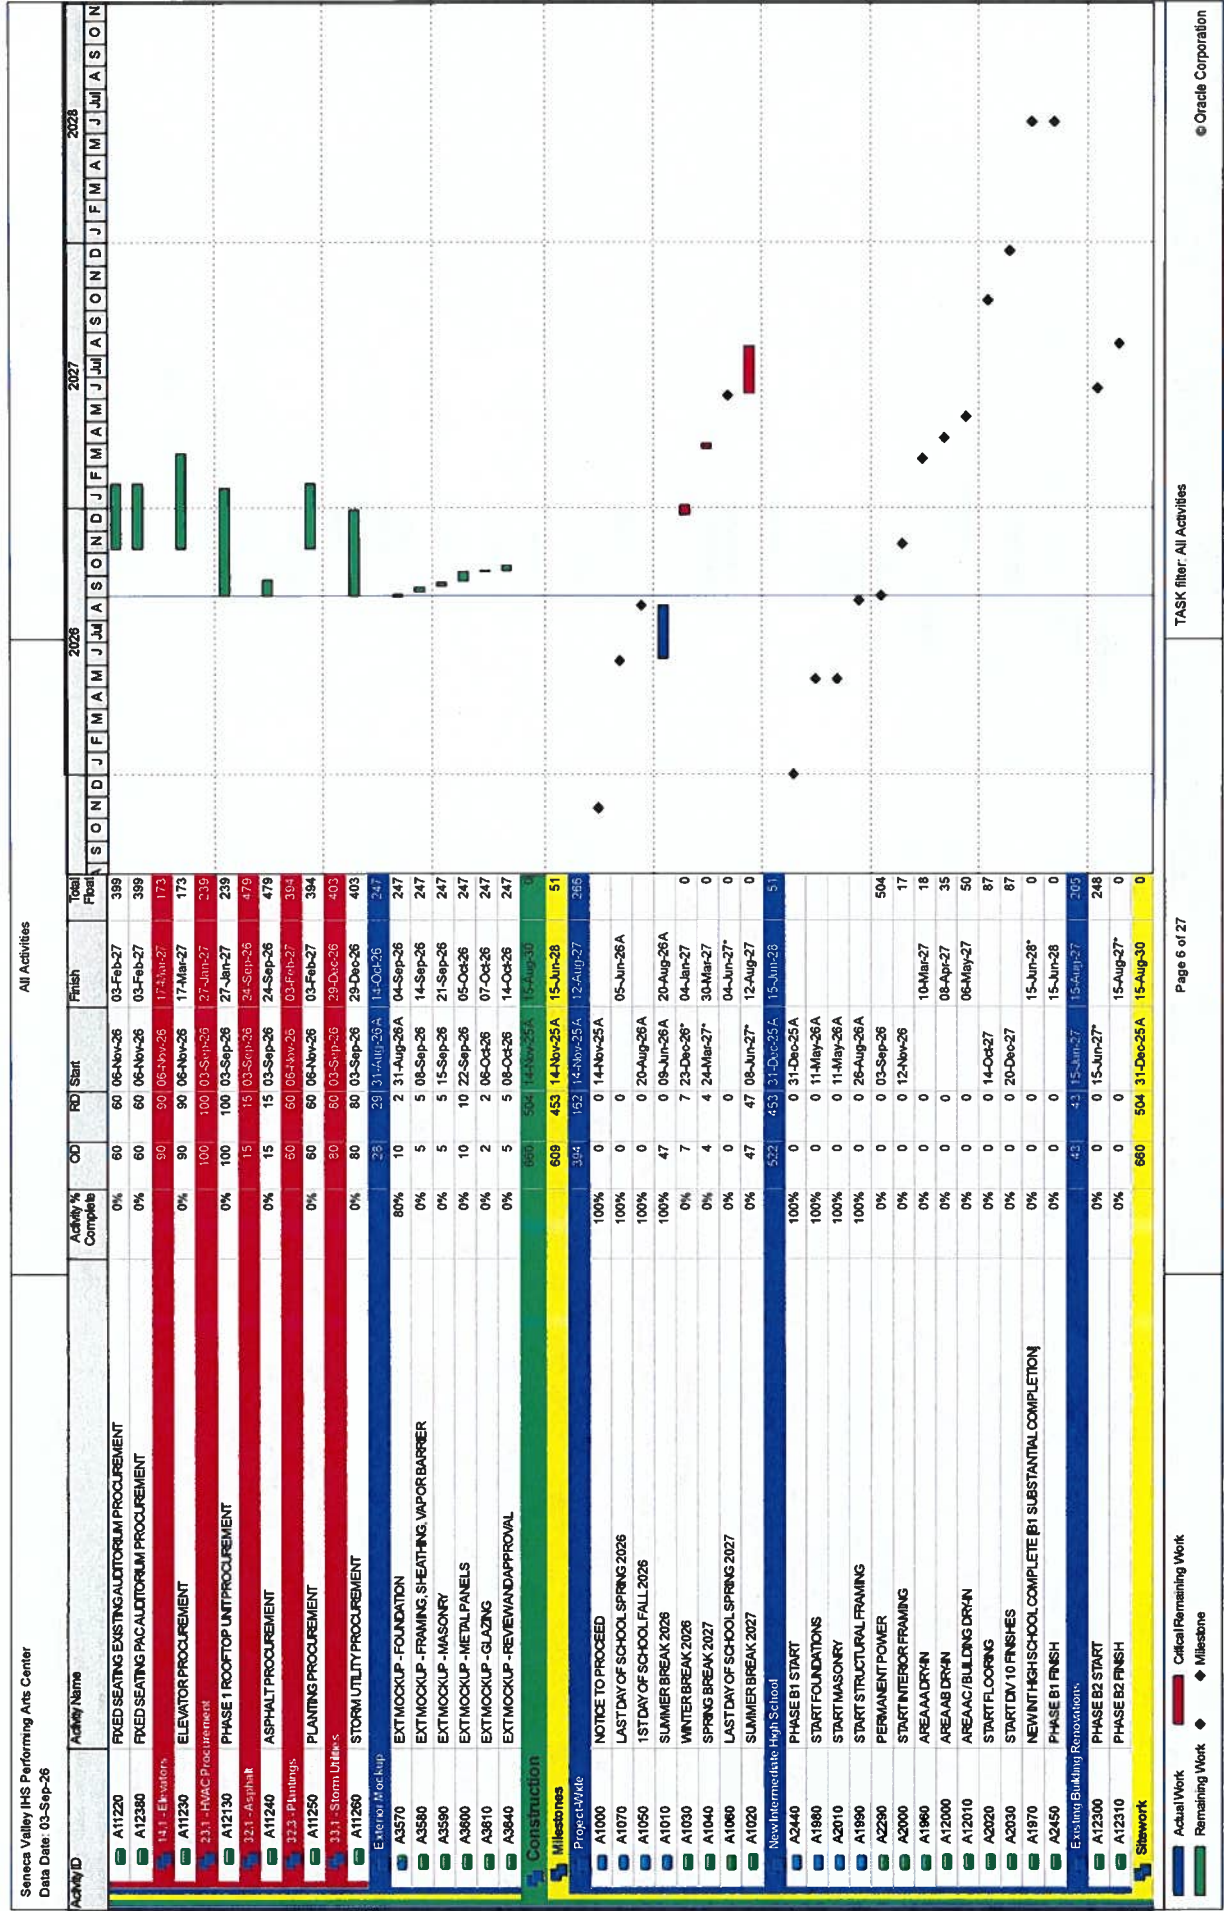


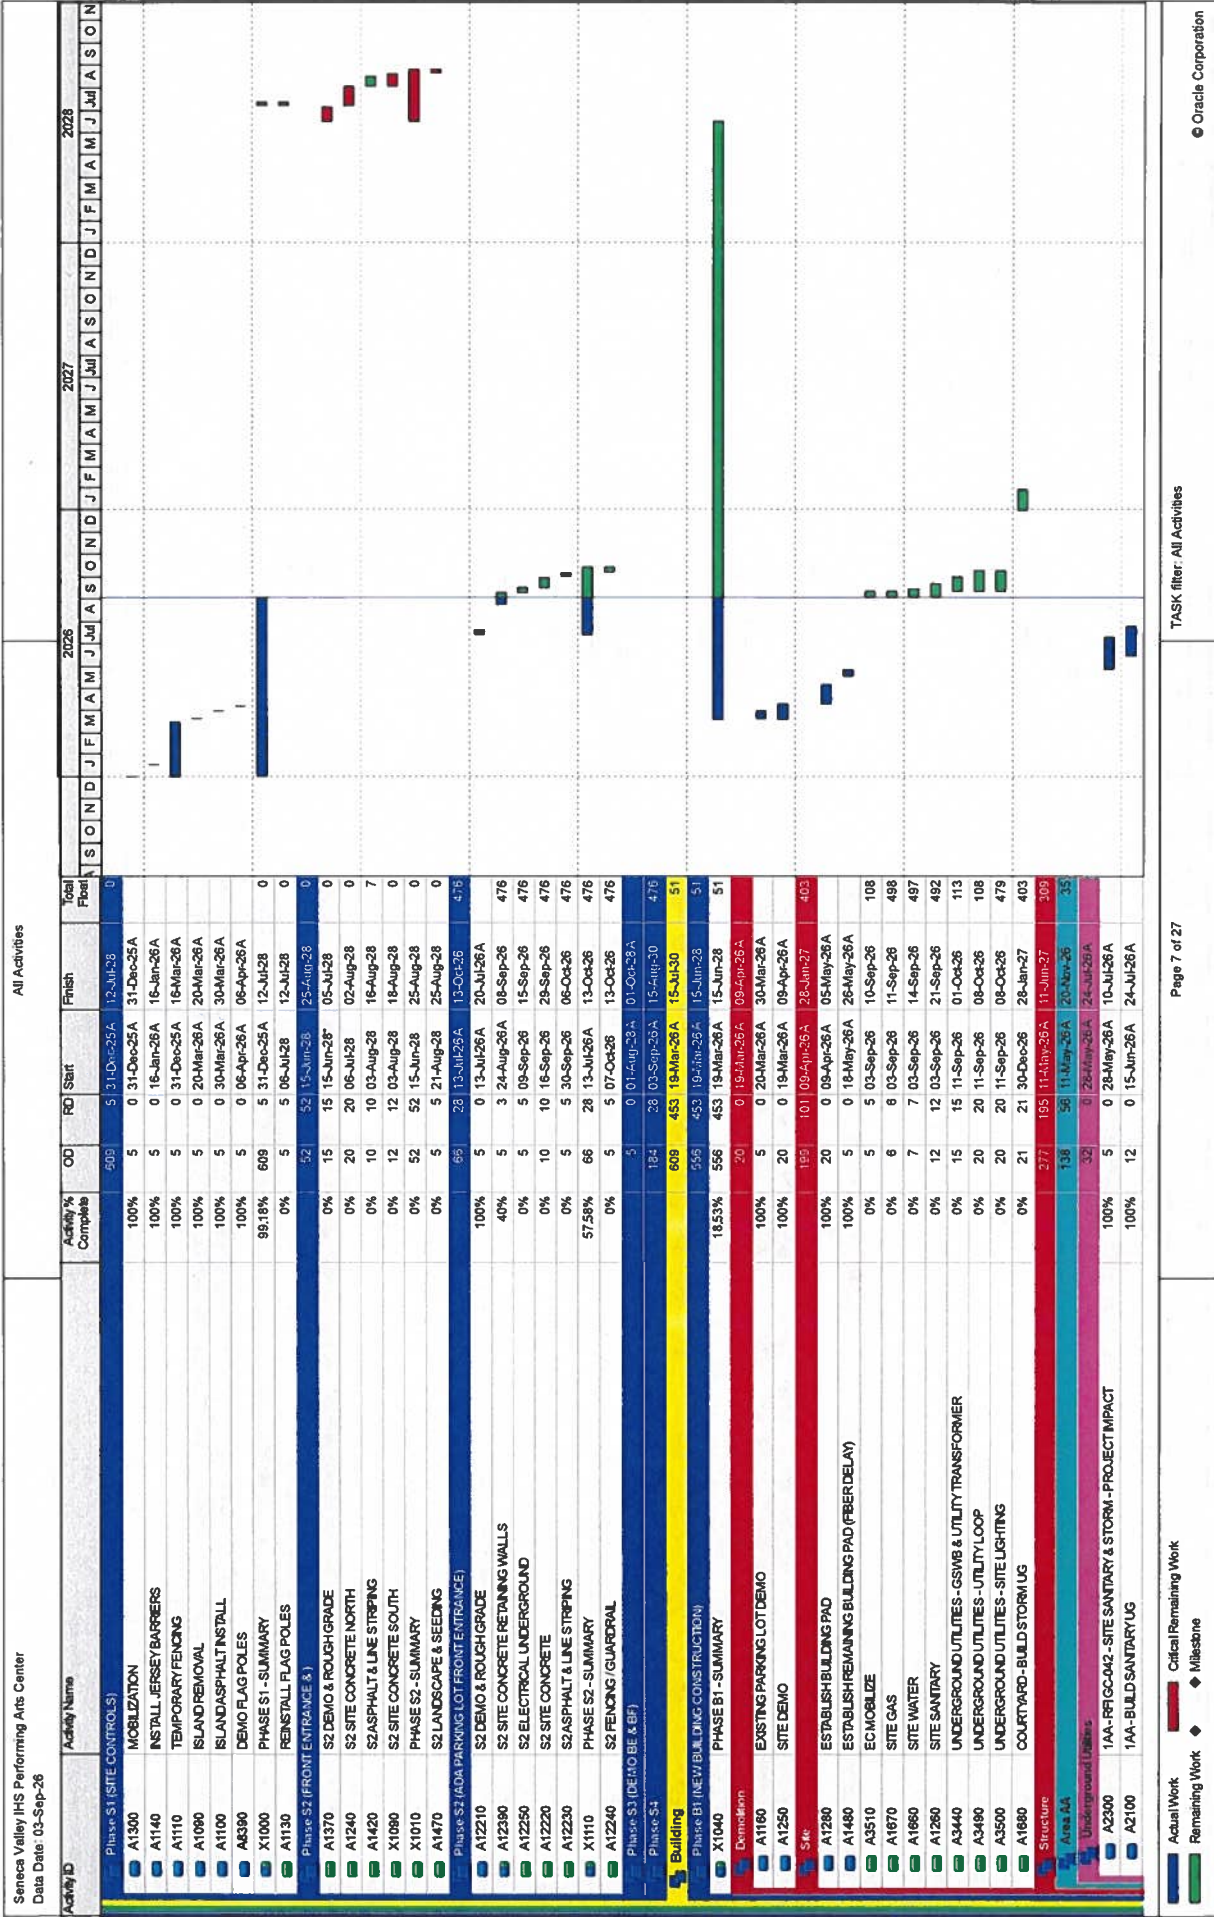


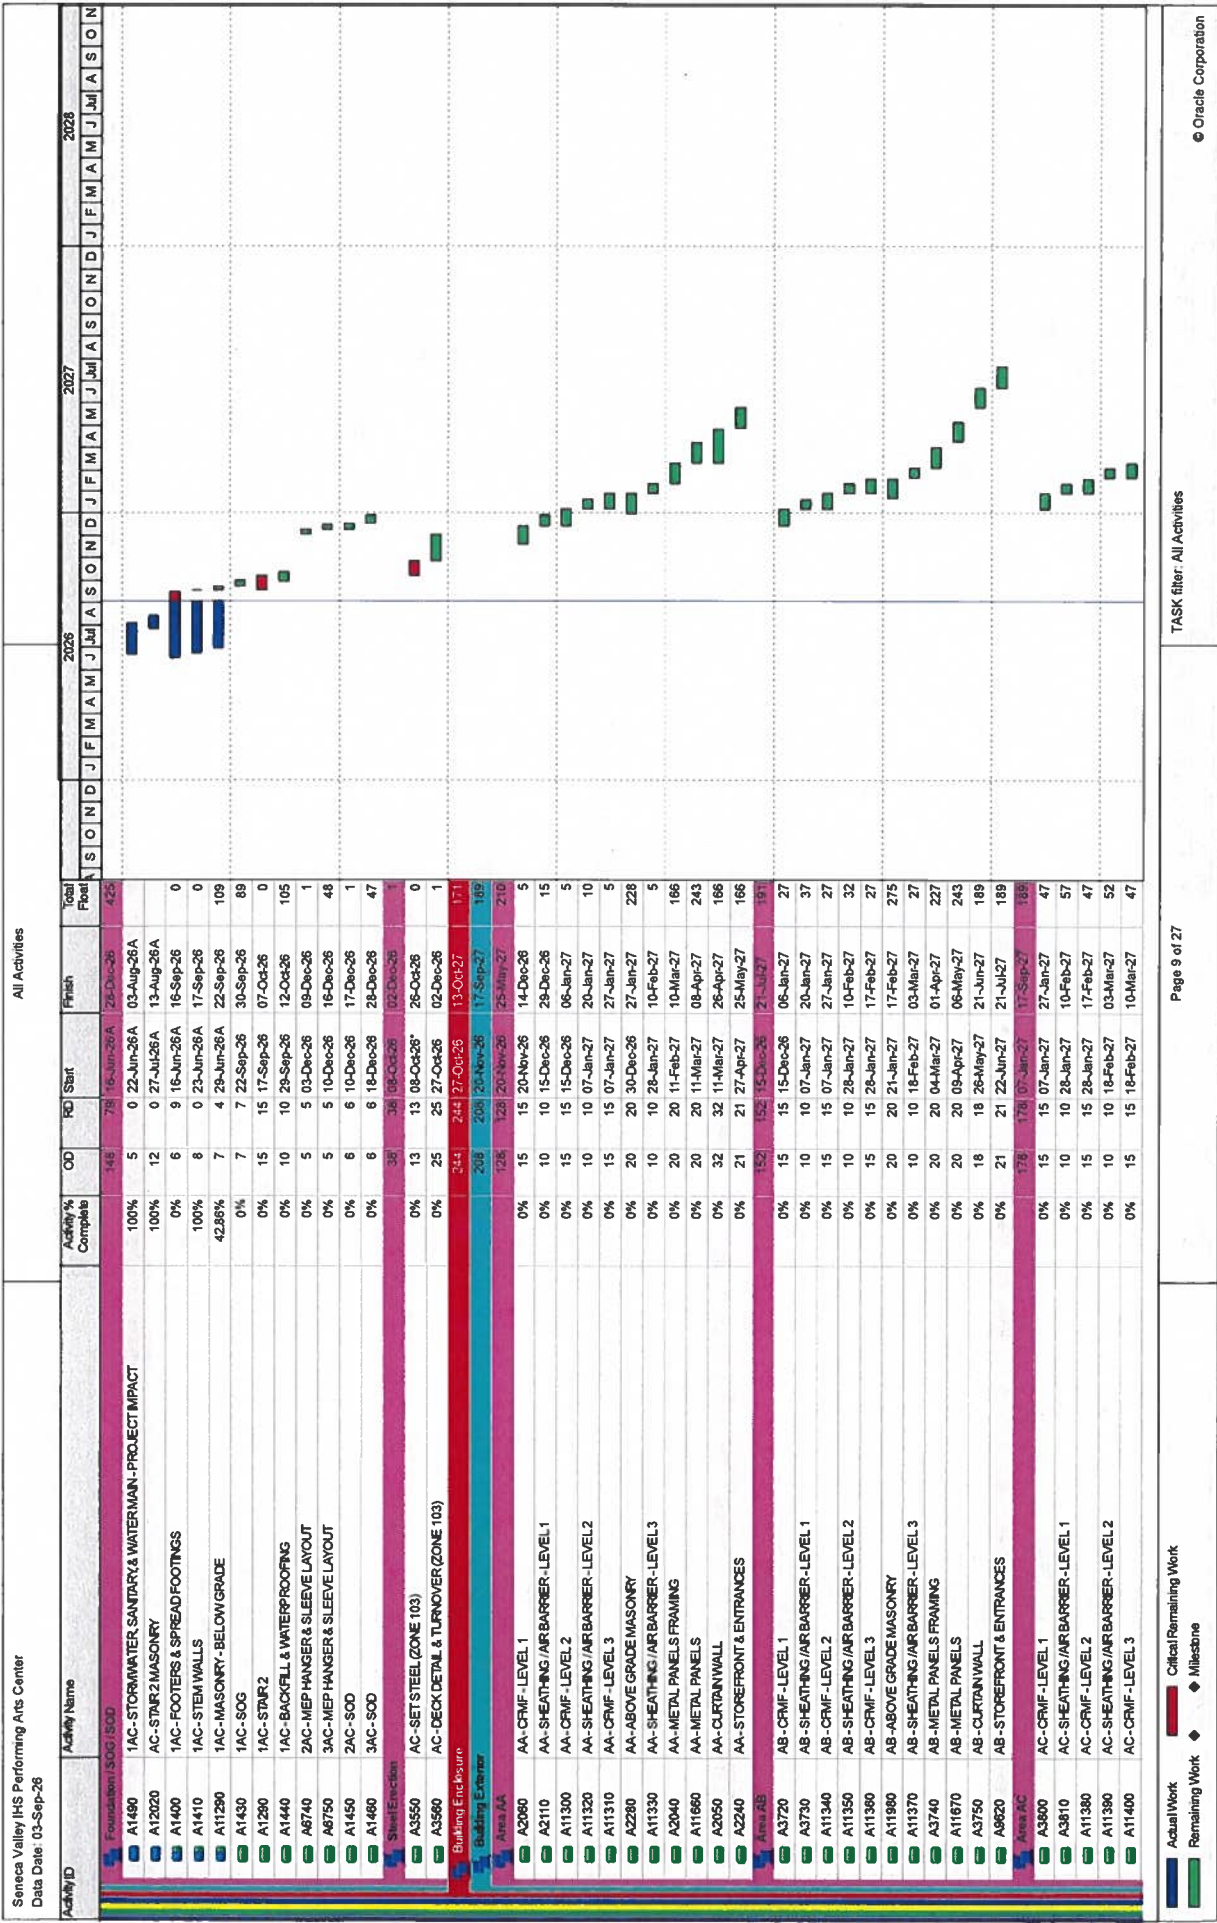

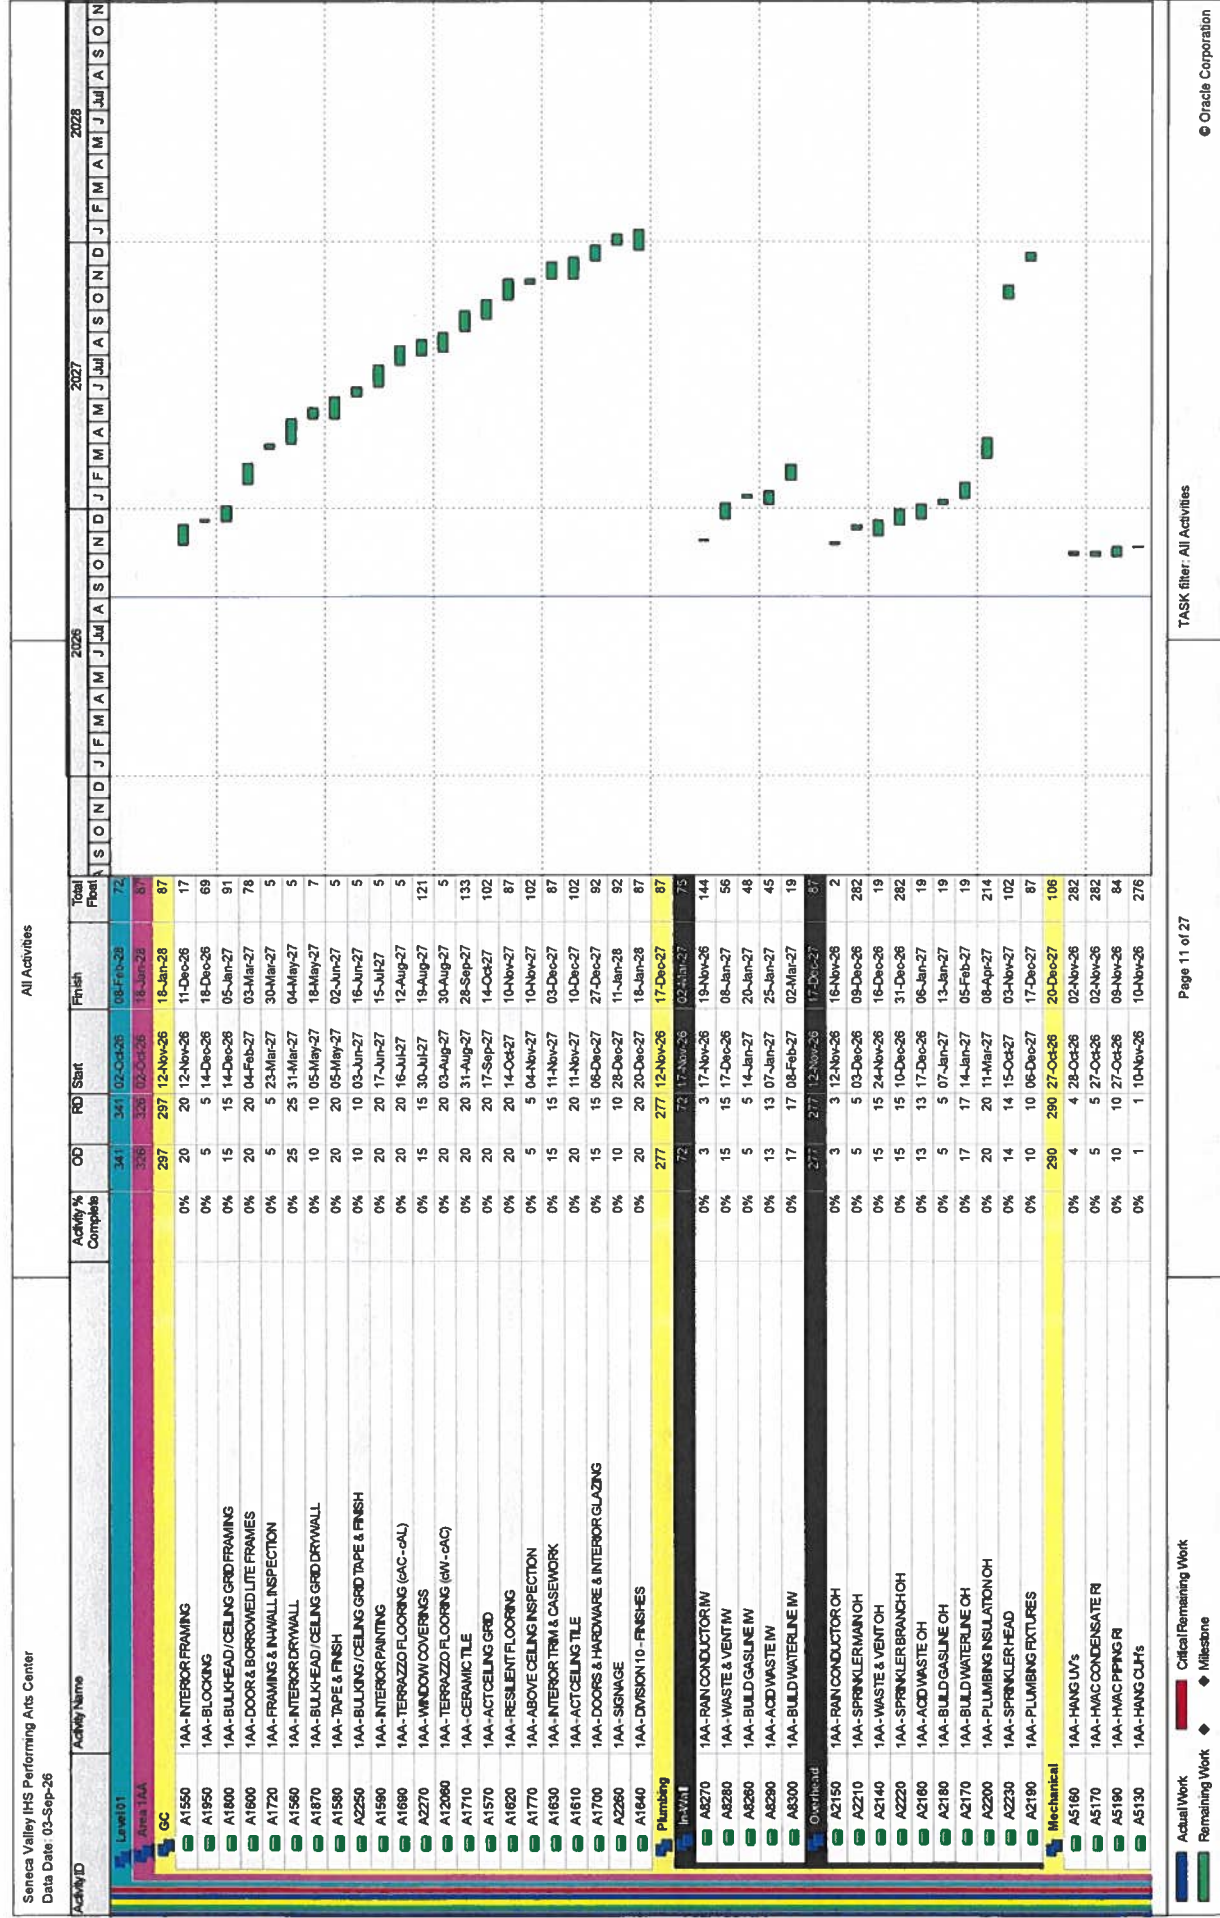


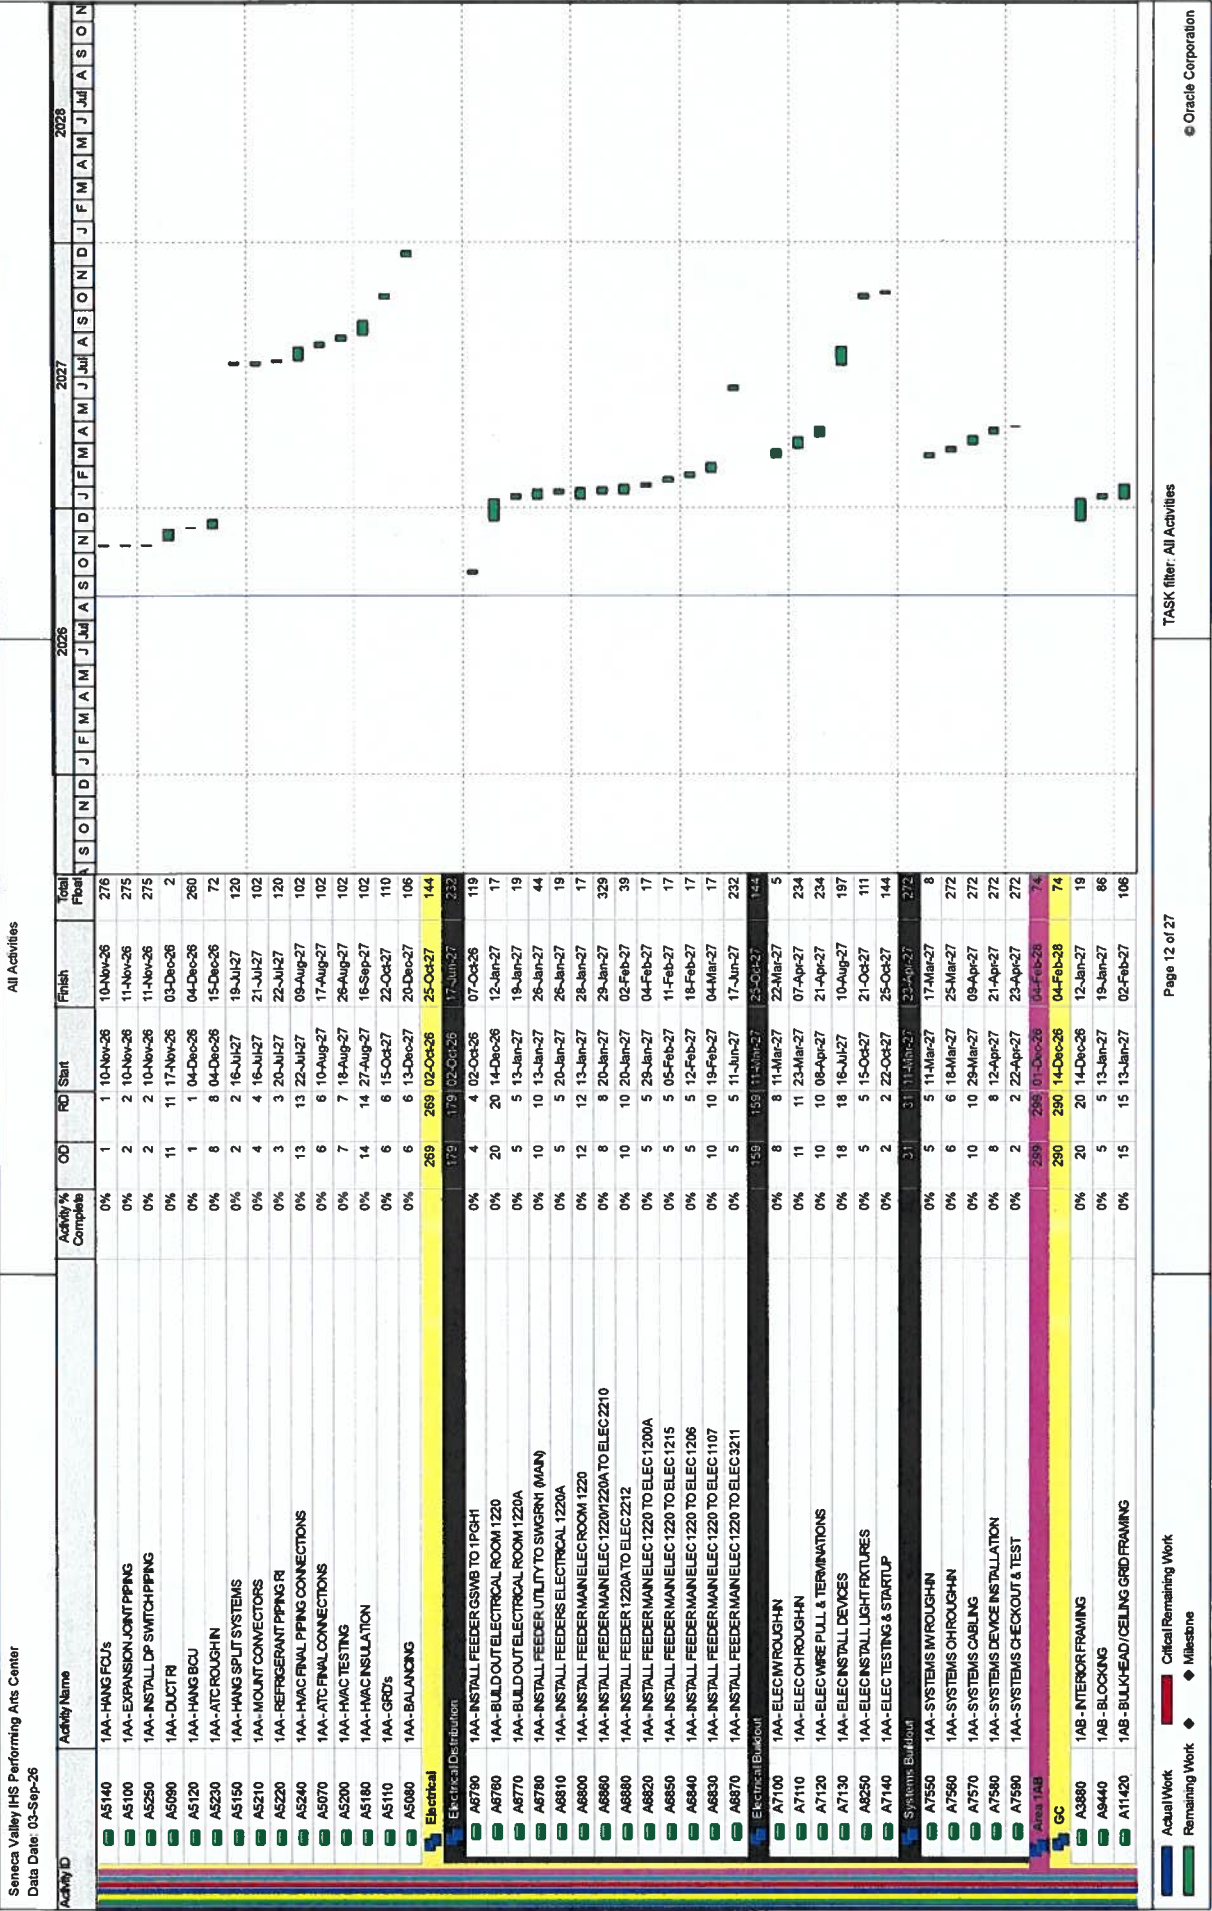


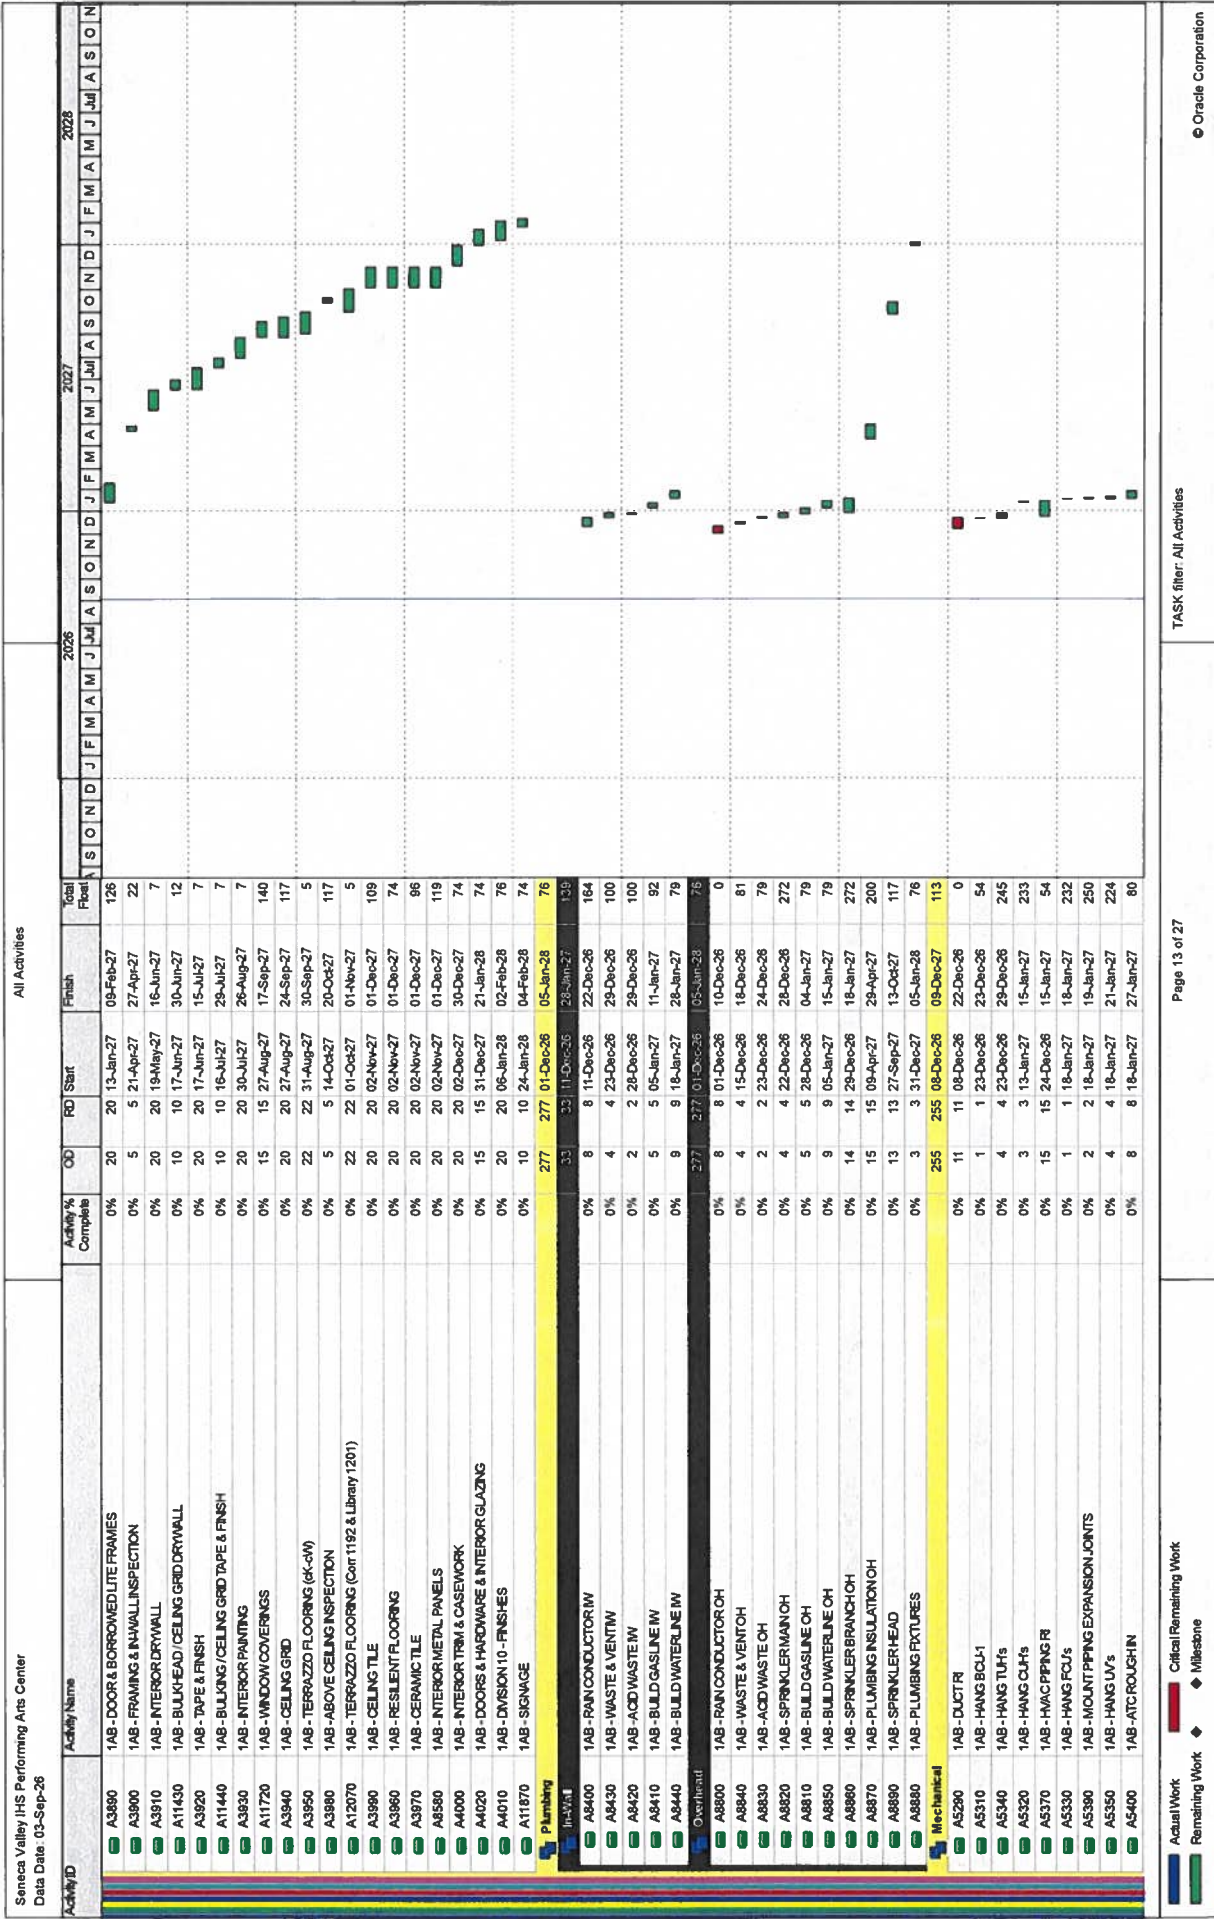


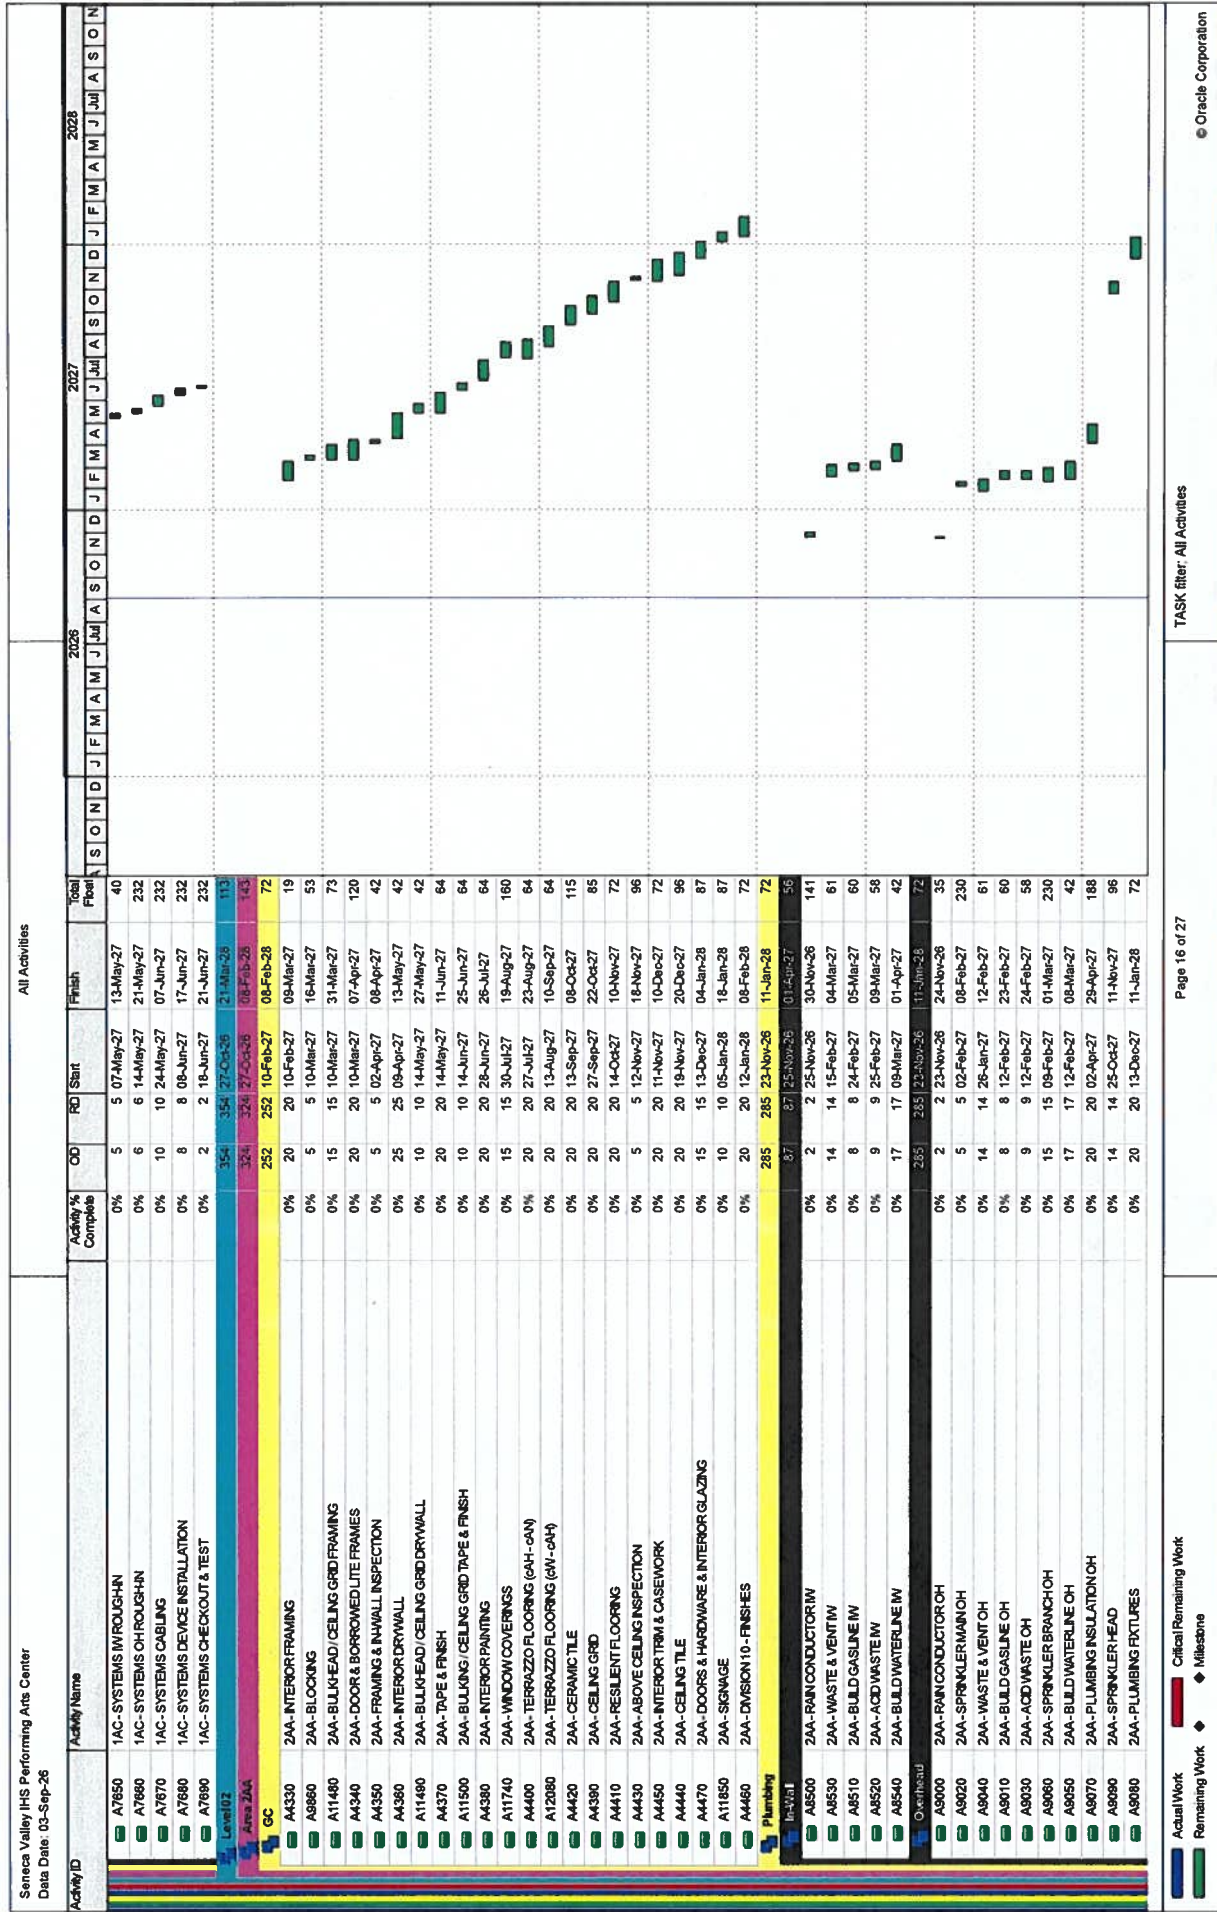


[illegible]

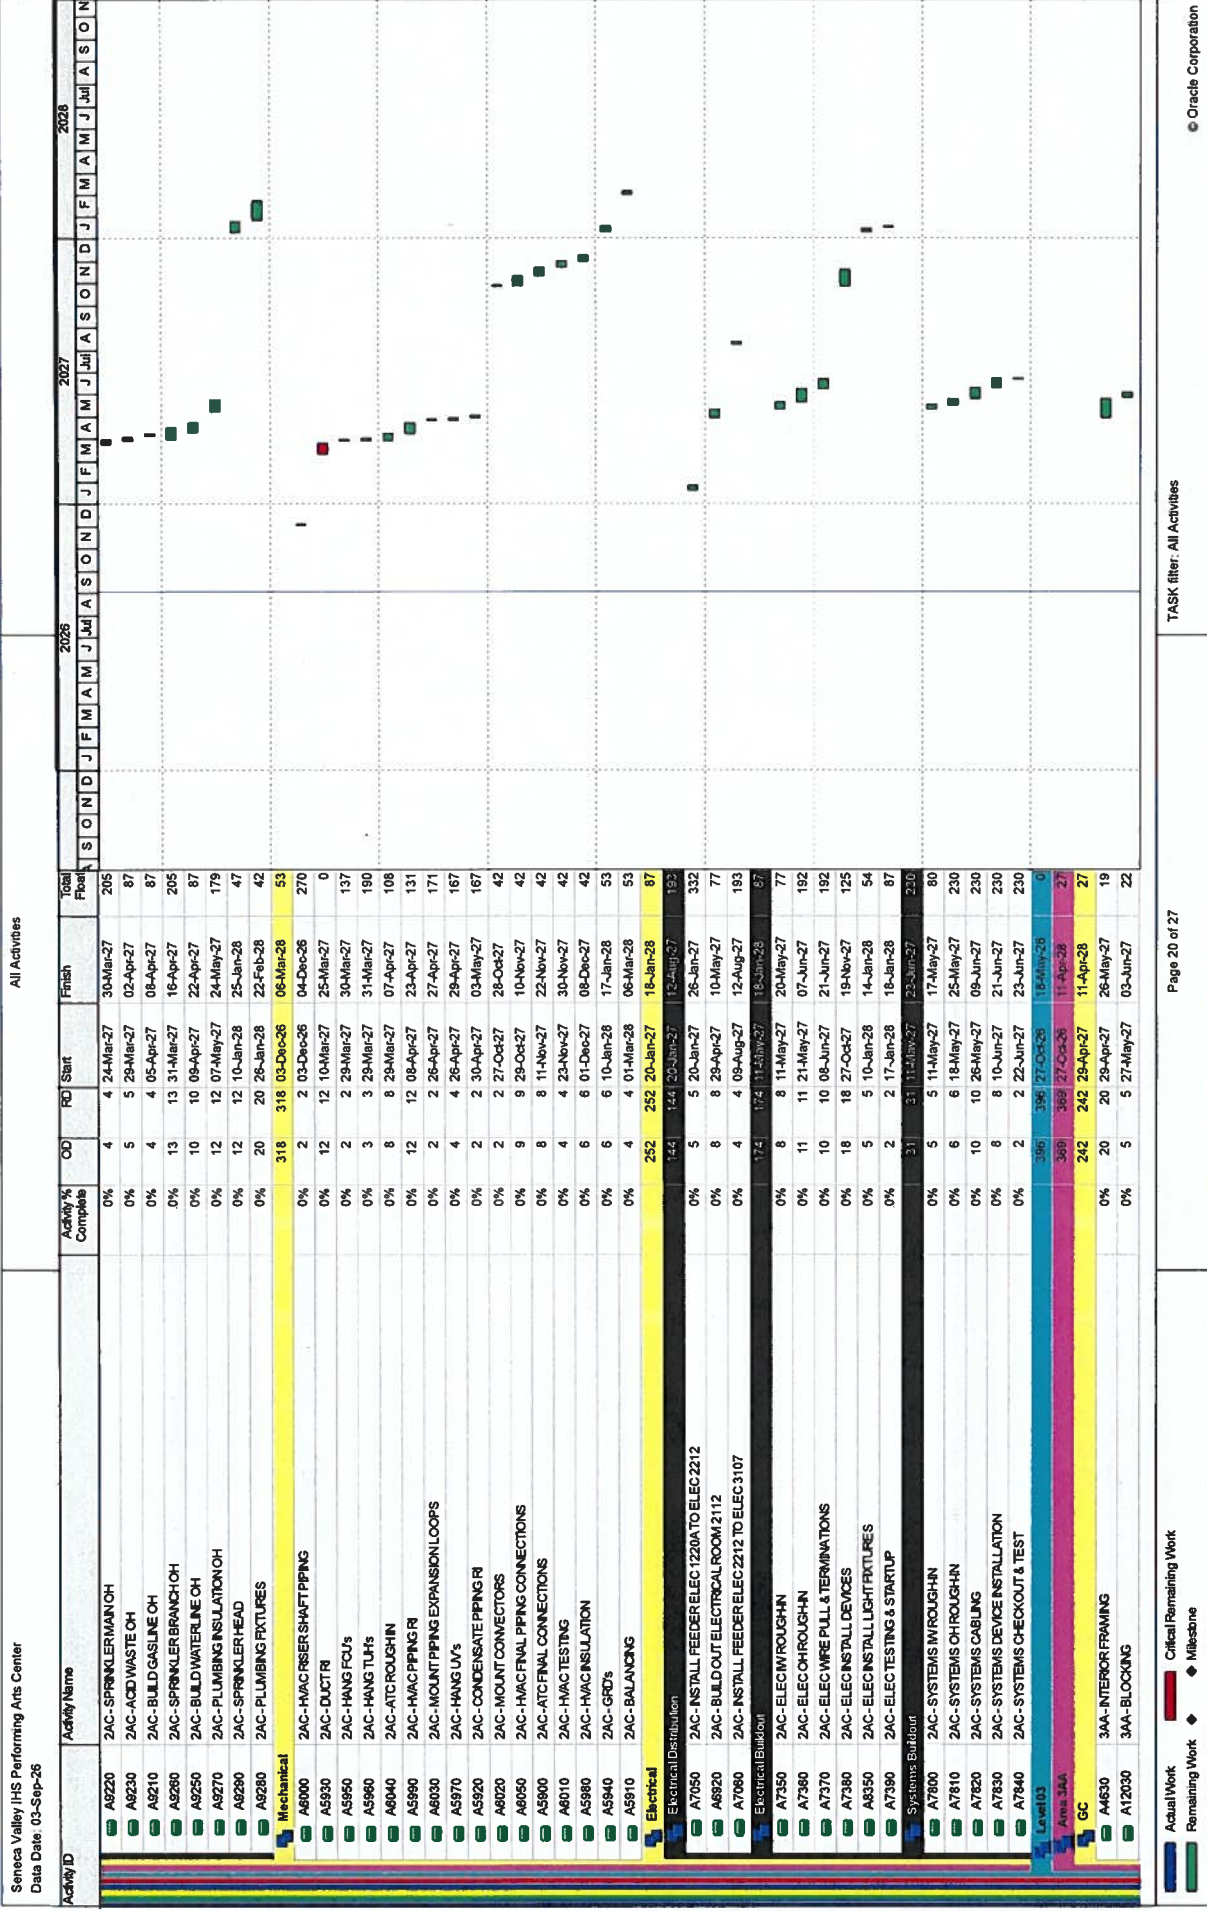

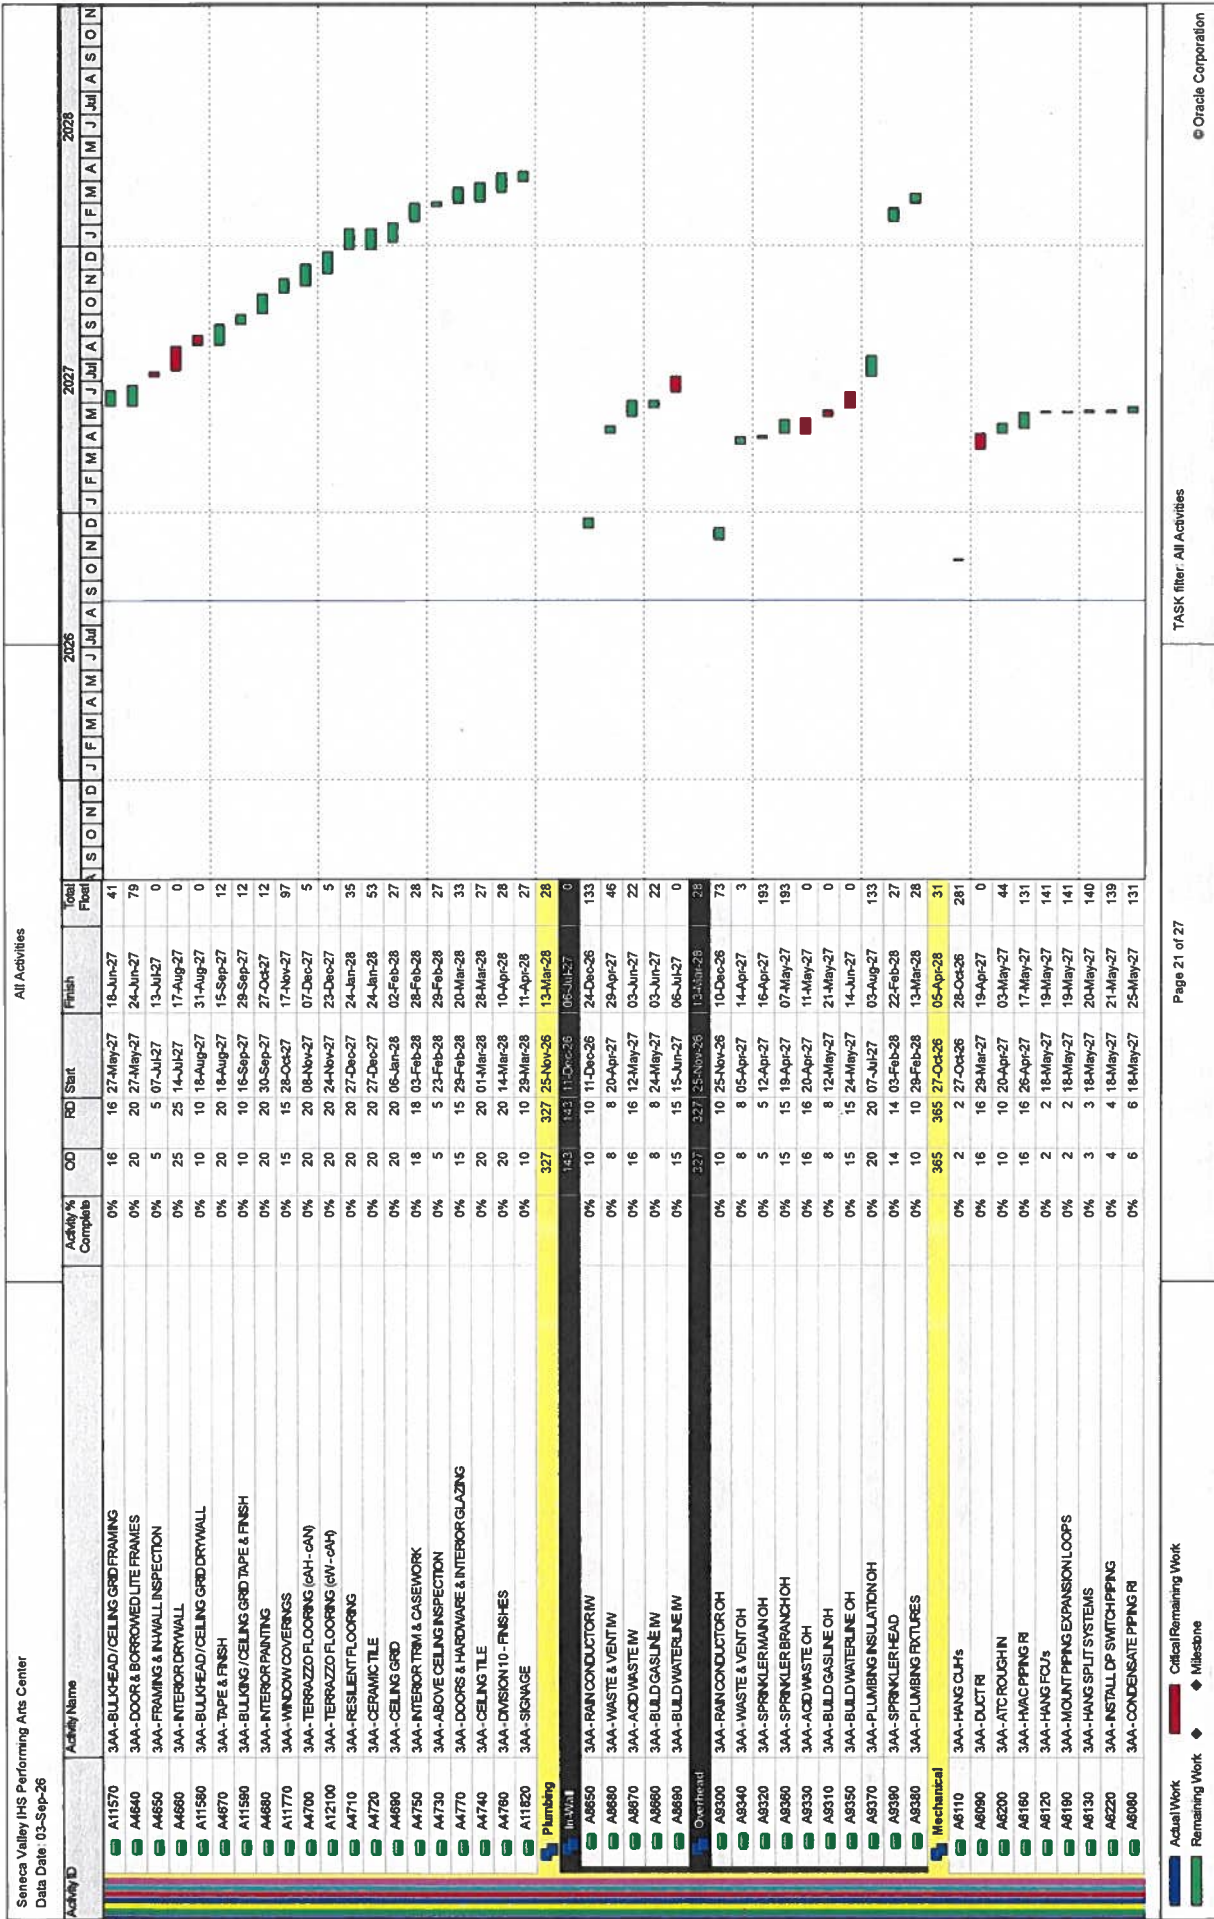

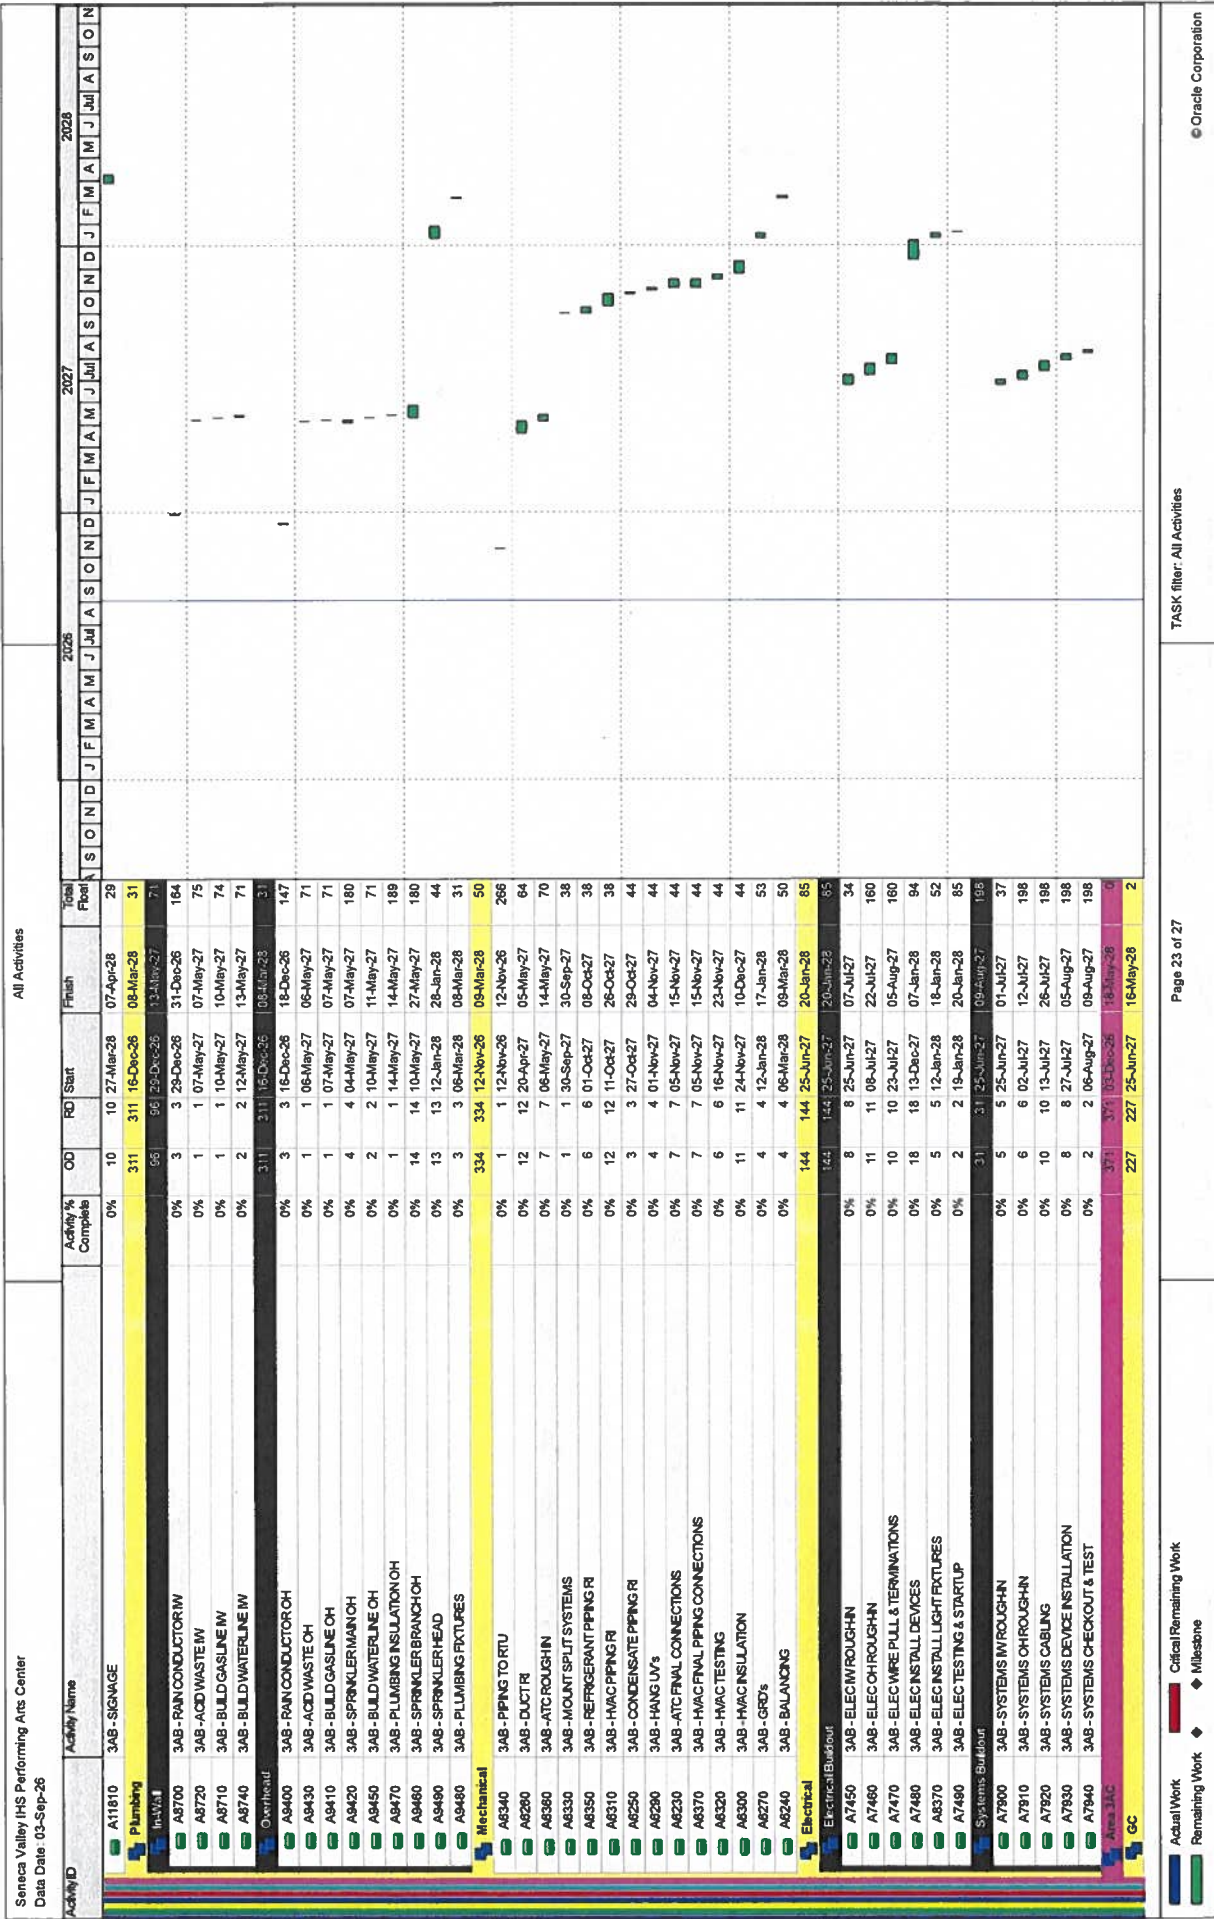

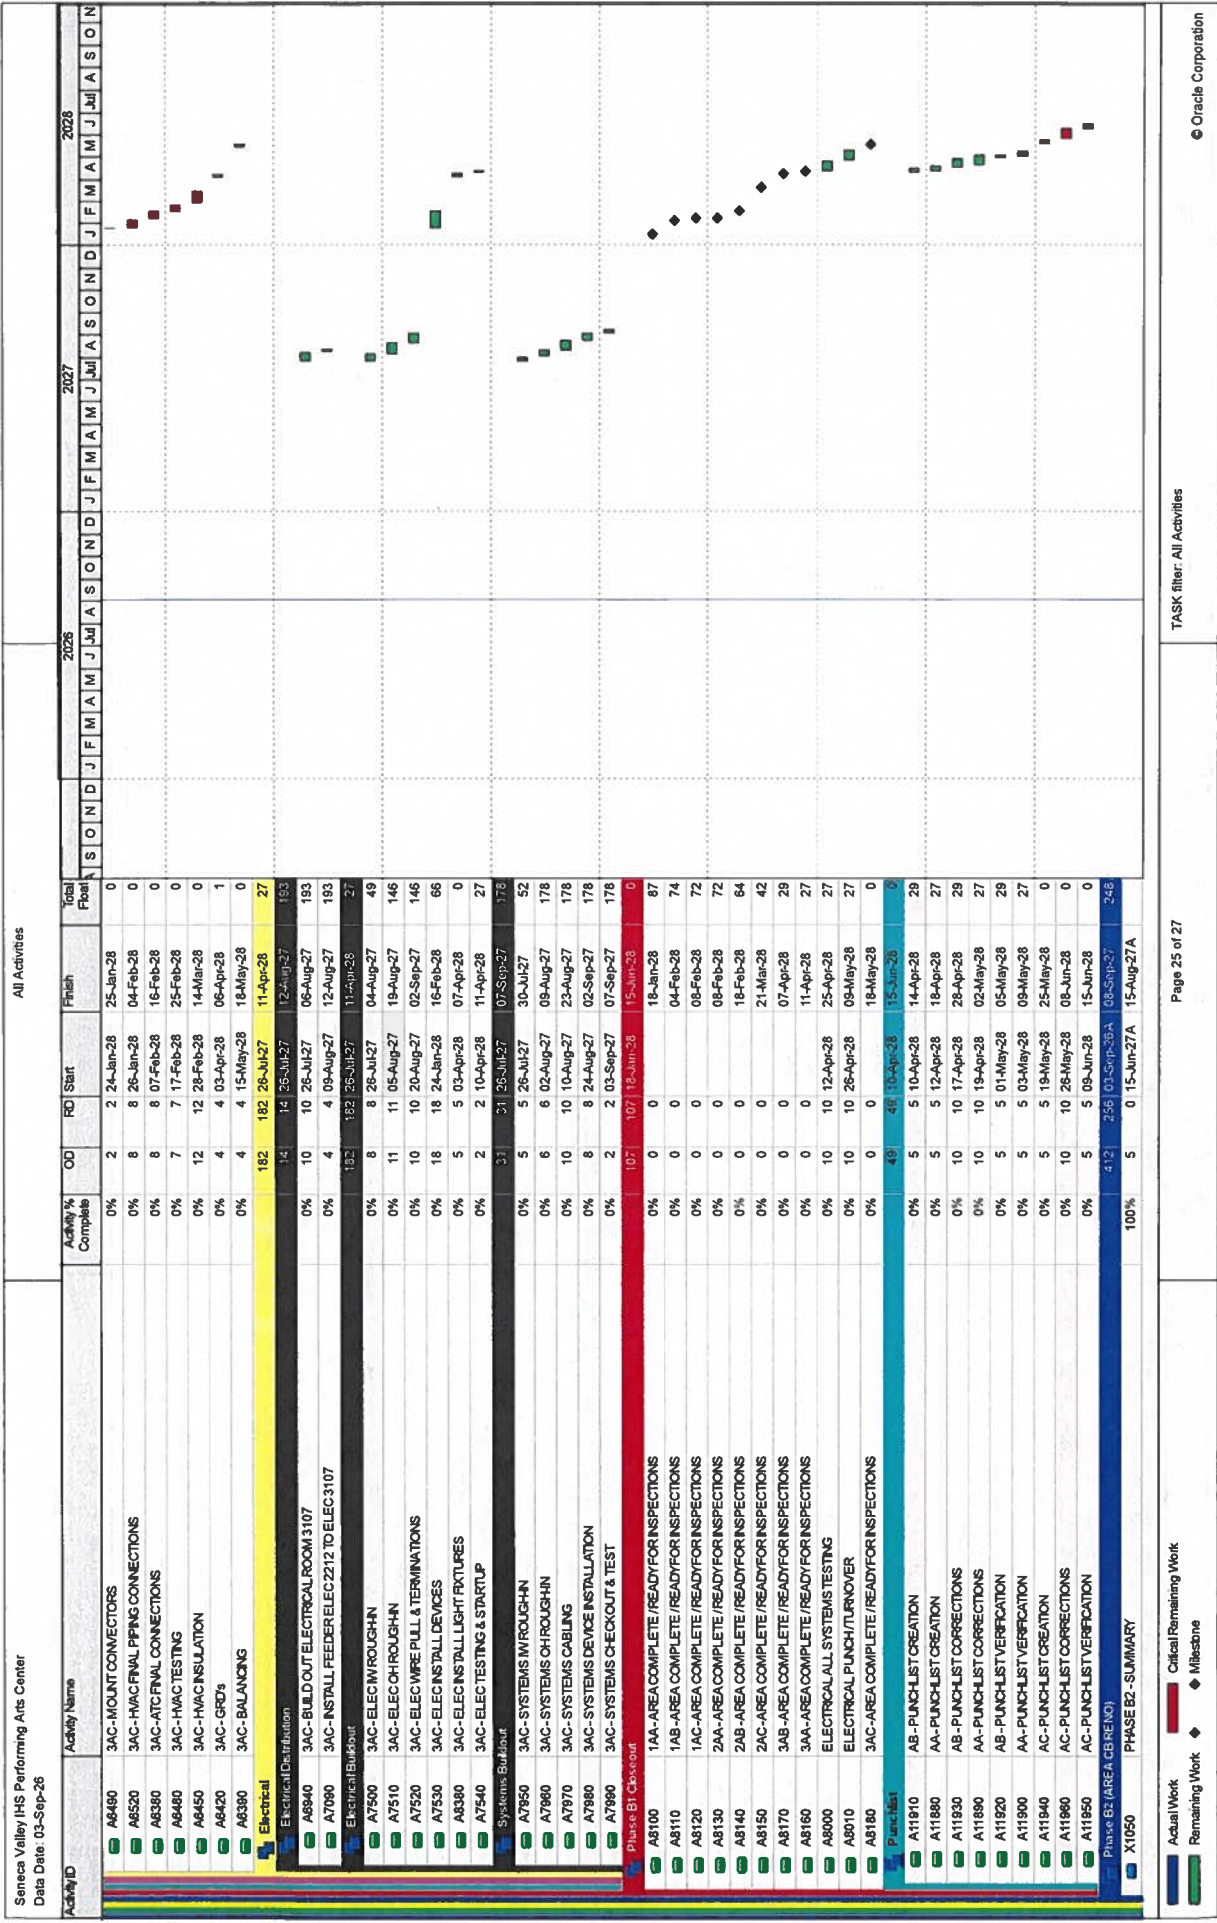

Seneca Valley JHS Performing Arts Center			All Activities		2026												2027												2028																							
Data Date: 03-Sep-26					Activity ID				Activity Name				Activity % Complete				OD				RD				Start				Finish				Total Pkts																			
					Exterior Work																																															
					A12260 SITE DEMO ROUGH GRADE FOR GENERATOR PAD				0%				15				15				15				15-Jun-27				05-Jul-27				293																			
					A12280 PREP PLACE POUR GENERATOR PAD				0%				5				5				5				5				22-Jun-27				28-Jun-27				293															
					A12270 PREP PLACE POUR GENERATOR WALLS				0%				5				5				5				5				29-Jun-27				06-Jul-27				293															
					Demolition																																															
					A12430 1CB-MECH EQUIP DEMO				0%				201				201				03-Sep-26				21-Jun-27				258																							
					A12410 1CB-MECH DUCT DEMO				0%				5				5				5				03-Sep-26				10-Sep-26				457																			
					A12410 1CB-MECH DUCT DEMO				0%				8				8				8				03-Sep-26				15-Sep-26				429																			
					A12420 1CB-MECH PIPING DEMO				0%				8				8				8				03-Sep-26				15-Sep-26				423																			
					A1740 1CB-DEMO AUDITORIUM & LOBBY				0%				5				5				5				15-Jun-27				21-Jun-27				298																			
					A1750 1CB-DEMO CLASSROOMS & HALLWAYS				0%				5				5				5				15-Jun-27				21-Jun-27				273																			
					A12290 1CB-DEMO RESTROOMS				0%				5				5				5				15-Jun-27				21-Jun-27				248																			
					Interior Building																																															
					A12460 1CB-SET EQUIPMENT CURBS (ROOF)				0%				4				4				03-Sep-26				09-Sep-26				497																							
					A12480 1CB-SET ROOFTOP AHUS				0%				3				3				10-Sep-26				14-Sep-26				487																							
					A12510 1CB-SET CONNECTORS				0%				5				5				11-Sep-26				17-Sep-26				457																							
					A12520 1CB-GRDS (DUCT) FINAL CONNECTIONS				0%				5				5				18-Sep-26				24-Sep-26				485																							
					A12440 1CB-DUCT ROUGH IN				0%				20				20				16-Sep-26				13-Oct-26				429																							
					A12450 1CB-PIPING ROUGH IN				0%				30				30				16-Sep-26				27-Oct-26				423																							
					A12470 1CB-ATC ROUGH IN				0%				12				12				14-Oct-26				29-Oct-26				429																							
					A12490 1CB-SET CLHS				0%				2				2				28-Oct-26				29-Oct-26				427																							
					A12500 1CB-SET LVS				0%				6				6				28-Oct-26				04-Nov-26				423																							
					A12540 1CB-ATC FINAL CONNECTIONS				0%				10				10				05-Nov-26				18-Nov-26				425																							
					A12530 1CB-PIPING FINAL CONNECTIONS				0%				12				12				05-Nov-26				20-Nov-26				423																							
					A12550 1CB-MECH TESTING				0%				5				5				23-Nov-26				01-Dec-26				423																							
					A12570 1CB-MECH BALANCING				0%				4				4				02-Dec-26				07-Dec-26				439																							
					A12560 1CB-MECH INSULATION				0%				20				20				02-Dec-26				30-Dec-26				423																							
					Auditorium & Lobby																																															
					A1900 1CB-AUDITORIUM ACOUSTICAL PANEL CEILING TILES				0%				5				5				22-Jun-27				28-Jun-27				298																							
					A1910 1CB-AUDITORIUM SEATING				0%				5				5				22-Jun-27				28-Jun-27				298																							
					A1920 1CB-AUDITORIUM WOOD VENEER				0%				5				5				22-Jun-27				28-Jun-27				298																							
					A1930 1CB-AUDITORIUM GYPSUM WALL SHEATHING				0%				5				5				22-Jun-27				28-Jun-27				298																							
					A2320 1CB-AUDITORIUM INSTALL HPC FLOORING				0%				5				5				22-Jun-27				28-Jun-27				298																							
					A2340 1CB-AUDITORIUM INSTALL CARPET TILE/LINOLEUM				0%				5				5				22-Jun-27				28-Jun-27				298																							
					A2350 1CB-AUDITORIUM PAINTING				0%				5				5				22-Jun-27				28-Jun-27				298																							
					A2360 1CB-AUDITORIUM DIV 10/SIGNAGE				0%				5				5				22-Jun-27				28-Jun-27				298																							
					A2370 1CB-AUDITORIUM INSTALL DOORS				0%				5				5				22-Jun-27				28-Jun-27				298																							
					Classrooms & Hallways																																															
					A1830 1CB-INTERIOR WALL INFILL FRAMING				0%				50				50				22-Jun-27				03-Aug-27				273																							
					A1850 1CB-TAPE & FINISH				0%				5				5				22-Jun-27				28-Jun-27				273																							
					A1790 1CB-DOORS, FRAMES & INT WINDOWS				0%				5				5				28-Jun-27				06-Jul-27				273																							
					A1860 1CB-INTERIOR PAINTING				0%				5				5				07-Jul-27				13-Jul-27				278																							
					A2310 1CB-CEILING GRID				0%				5				5				14-Jul-27				20-Jul-27				273																							
					A1940 1CB-TERRAZZO FLOORING				0%				5				5				14-Jul-27				20-Jul-27				283																							
					A1840 1CB-FLOORING				0%				5				5				21-Jul-27				27-Jul-27				273																							
					A1880 1CB-DIVISION 10 FINISHES				0%				5				5				21-Jul-27				27-Jul-27				278																							
					A2330 1CB-CEILING TILE				0%				5				5				21-Jul-27				27-Jul-27				278																							
					A2380 1CB-CORRIDOR WALL CERAMIC TILE				0%				15				15				07-Jul-27				27-Jul-27				278																							
					A1780 1CB-INSTALL RAILINGS				0%				5				5				28-Jul-27				03-Aug-27				273																							

Actual Work

Remaining Work

Critical/Remaining Work

Milestone

Page 26 of 27

TASK filter: All Activities

© Oracle Corporation

Seneca Valley IHS Performing Arts Center										All Activities																								
Data Date: 03-Sep-26																																		
Activity ID	Activity Name	Activity % Complete	OO	RD	Start	Finish	Total Float	202620272028																										
								S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N
Restrooms																																		
A1820	1CB - INTERIOR FRAMING	0%	5	5	22-Jun-27	08-Sep-27	248																											
A2390	1CB - DRYWALL, TAPE & FINISH	0%	5	5	22-Jun-27	28-Jun-27	248																											
A2410	1CB - CEILING FRAMING / BOARD / FINISH	0%	5	5	23-Jun-27	06-Jul-27	248																											
A2430	1CB - RESTROOM FLOOR CERAMIC TILE	0%	15	15	07-Jul-27	13-Jul-27	248																											
A1810	1CB - REINSTALL CASEWORK & COUNTERTOPS	0%	5	5	14-Jul-27	03-Aug-27	248																											
A2400	1CB - RESTROOM WALL CERAMIC TILE	0%	15	15	04-Aug-27	10-Aug-27	248																											
A1890	1CB - TOILET PARTITIONS	0%	5	5	25-Aug-27	31-Aug-27	248																											
A2420	1CB - TOILET ACCESSORIES	0%	5	5	01-Sep-27	08-Sep-27	248																											
Area CC Chiller Damage																																		
A12400	INSTALL SUPPLEMENTAL STEEL	0%	5	5	03-Sep-28	10-Sep-28	499																											
Phase B3 (AREA CB ORCHESTRA / ART ROOMS & TEMP CORRIDOR)																																		
Phase B4 (AREA BD BE BF & EXT COURTYARD)																																		
Phase B5 (AREA CC RENOV)																																		

</

