

Cook Elementary

Modernization & Interim-Housing
Update Meeting
October 8, 2026




Agenda

- Design Updates
- Planning Updates
- Phasing Plan
- School Safety
- Next Steps
- Feedback & Questions

Site Modernization

- New exterior paint and wayfinding
- New kinder/preschool complex perimeter wall
- New lunch shelter secure perimeter
- New play equipment, play surfaces, and shade structures
- Hardscape path of travel improvements
- New accessible parking and student drop-off

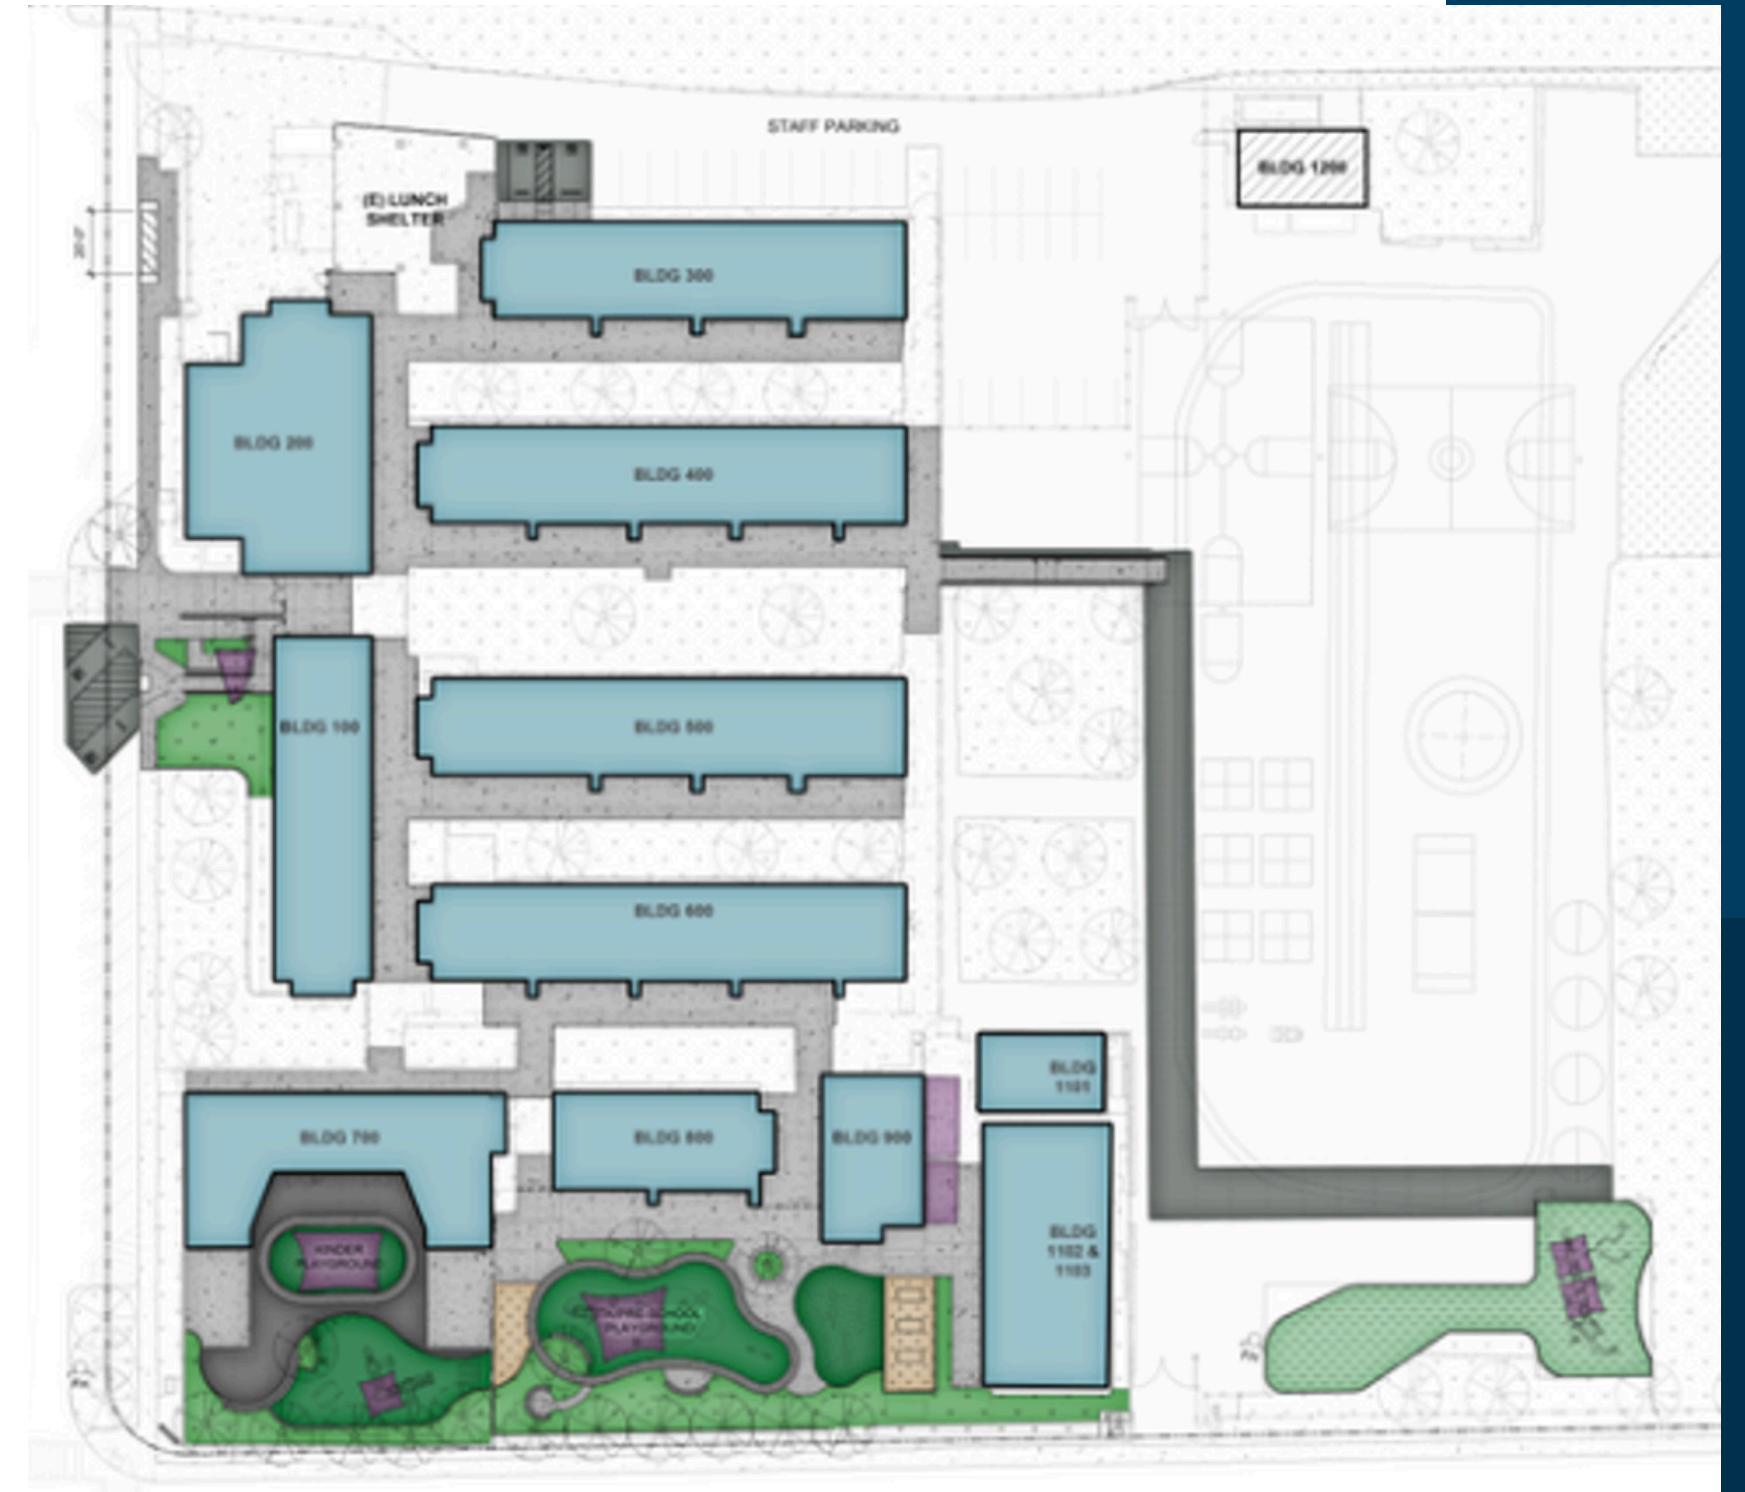

Building Modernizations

- New interior finishes including wall and ceiling paint, new flooring and wall base
- New whiteboards, tackboards, sinks, and furniture in classrooms
- Restroom remodel including new fixtures and finishes and the addition of (2) single user student restrooms in the MPR building
- Administration building main entry remodel and new workroom casework
- New roofing and select window replacement
- Network upgrades (New MDF/IDF, CAT6A) and new intercom system



Site Modernization



Campus Entry

Lunch Shelter



Furniture Upgrades



Furniture Upgrades



Furniture Upgrades



Planning Updates

Modernization Project


Activity	Estimated Start	Estimated Finish
DSA Document Review and Approval	7/25/2026	12/1/2026
Project Bid Phase	1/8/2027	2/25/2027
Board Meeting/ Approval		3/10/2027
Construction Preparation Phase	3/11/2027	6/4/2027
Modernization Project Construction	6/7/2027	12/15/2028

Interim Housing Project

Activity	Estimated Start	Estimated Finish
Portable Contractor Bid Phase	9/15/2026	9/28/2026
Board Meeting/Approval - Portable		10/14/2026
DSA Document Review and Approval	10/30/2026	1/22/2027
Project Bid Phase	1/29/2027	2/16/2027
Board Meeting/Approval		3/10/2027
Interim Housing Construction	3/22/2027	7/16/2027

LEGEND

	24' X 40' RSLD CLASSROOM
	12' X 40' RSLD RESTROOM
	STANDARD RAMP 11' X 4' RAMP W/ 7' X 5' LANDING
	PATH OF TRAVEL (MODERNIZATION)
	PATH OF TRAVEL (INTERIM HOUSING)

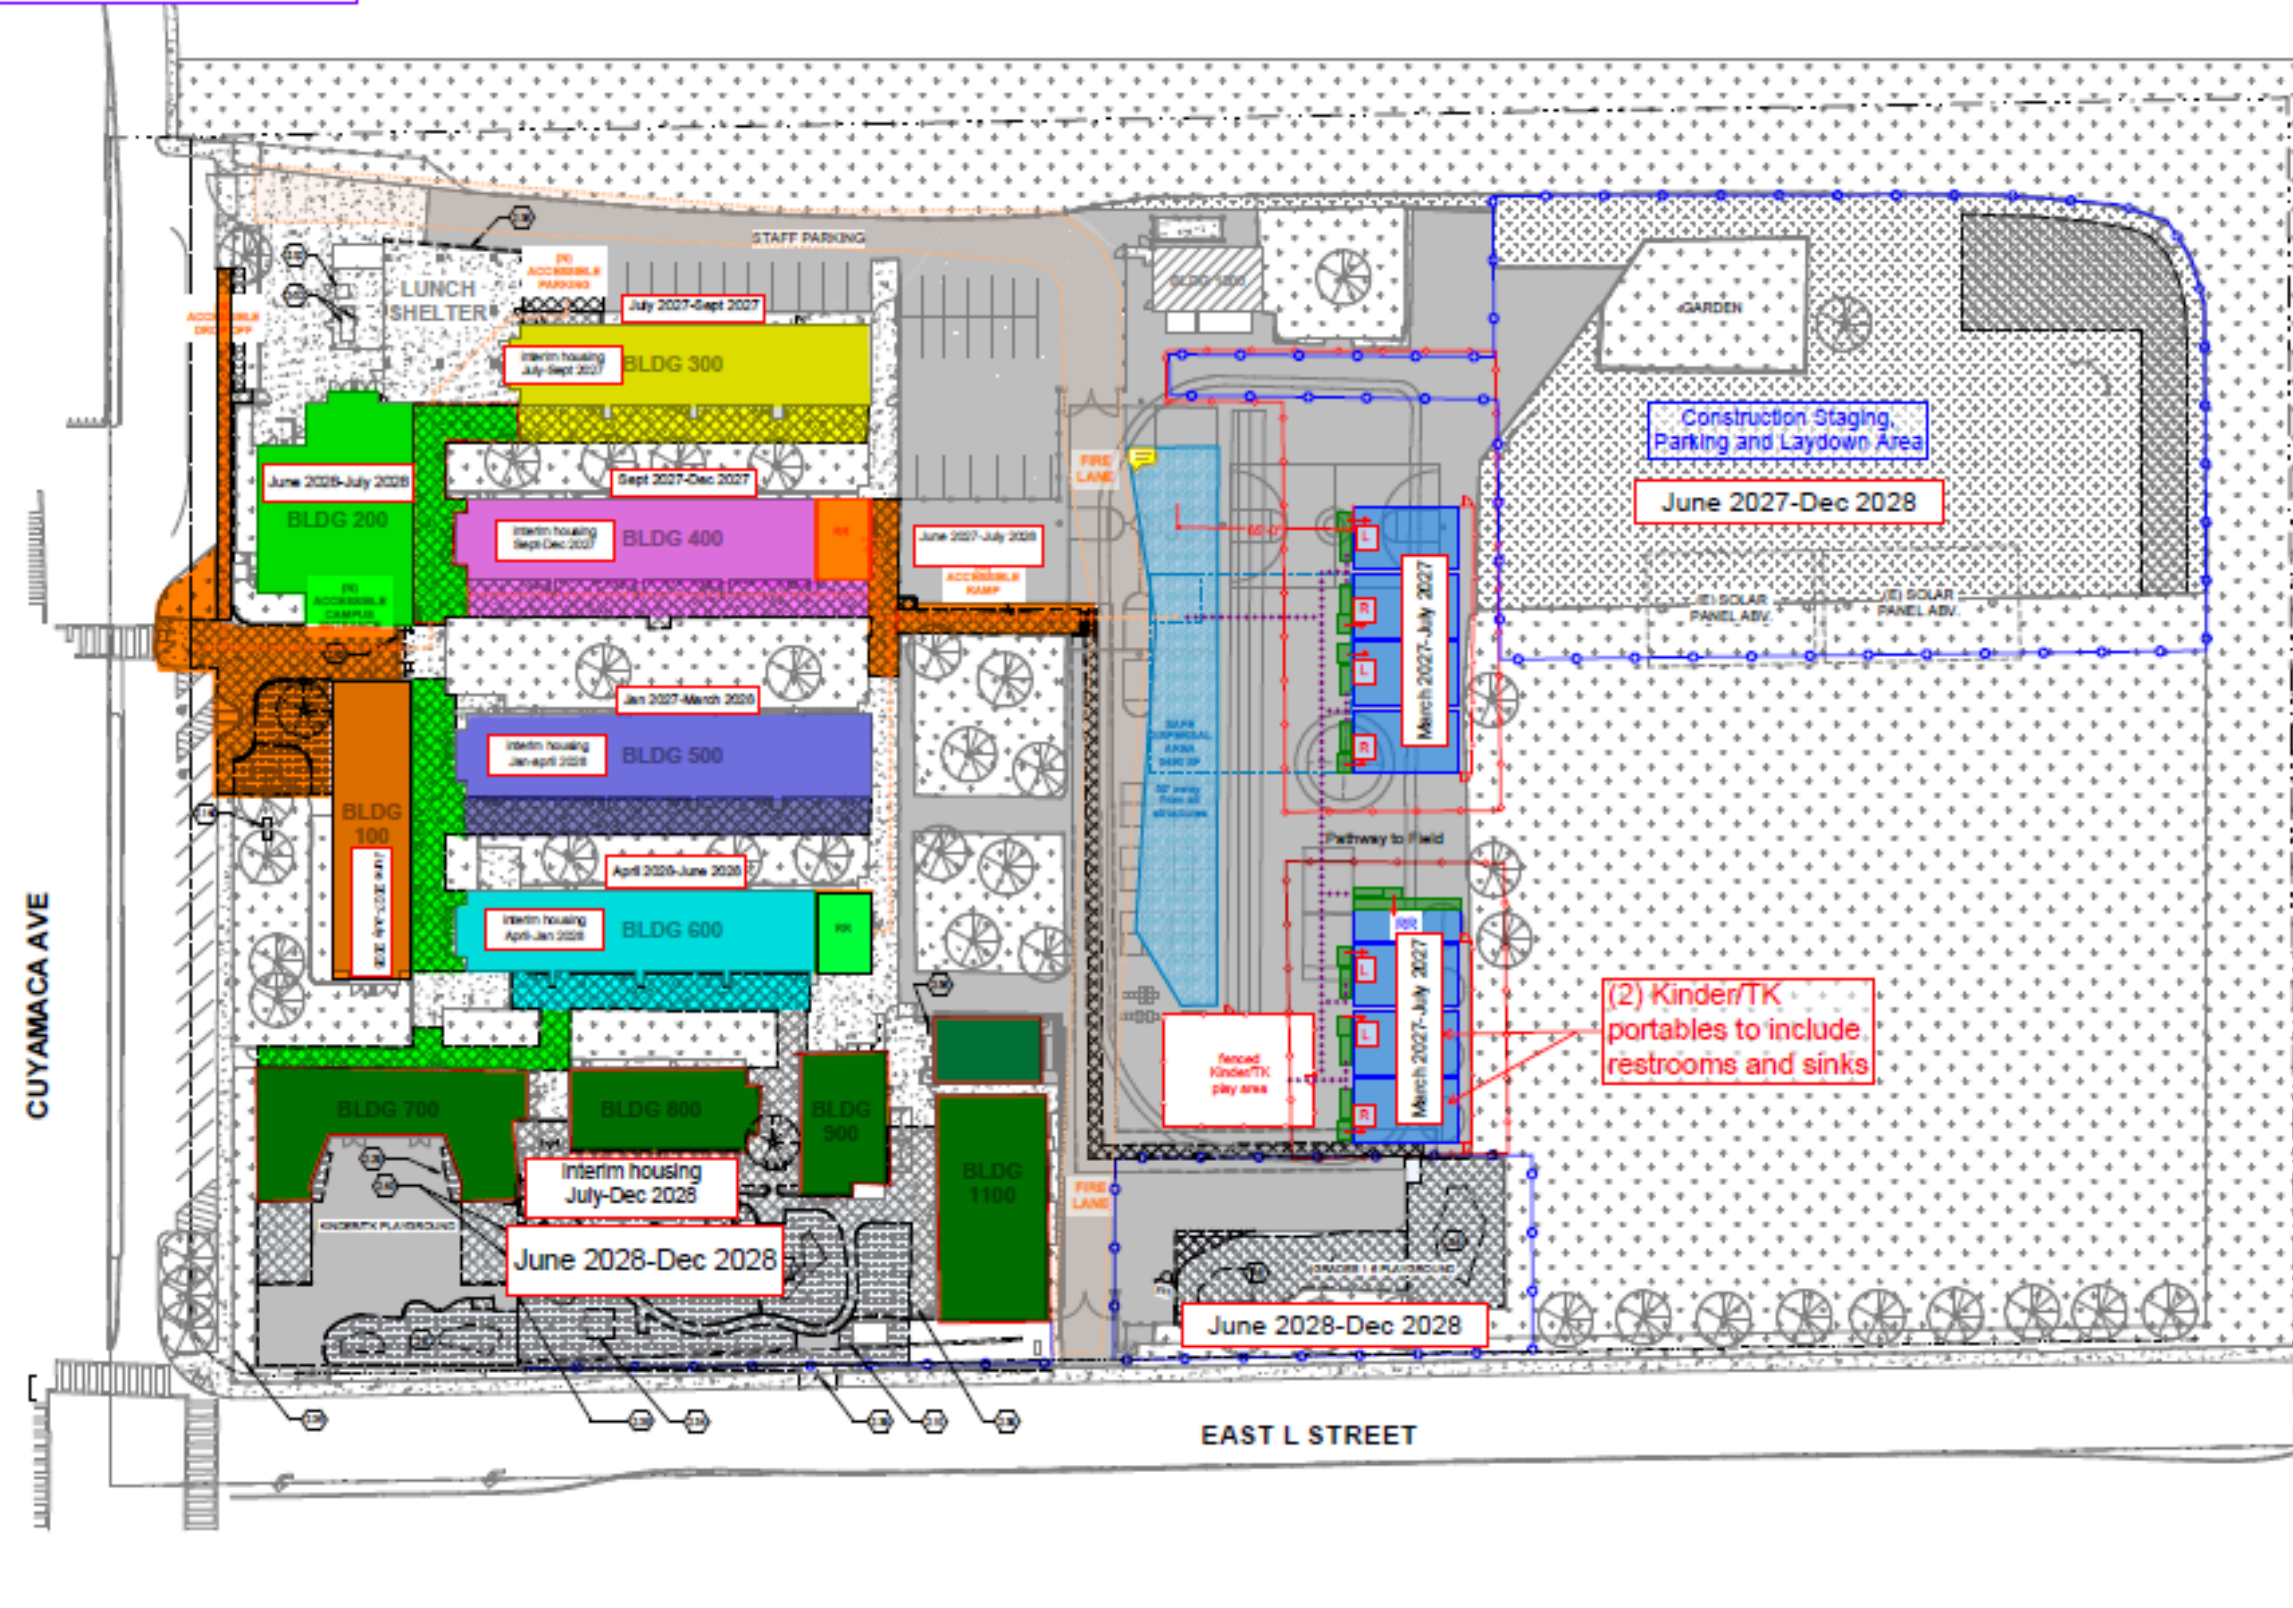

Phasing Plan

- Interim Housing
 - 7 Portables to accommodate classrooms
 - 1 restroom modular unit (boys, girls, and staff)
 - Portables will be placed at edge of blacktop
- Moving
 - District to provide 40 yd. dumpster(s) – January 2027
 - District to provide boxes and labels – 8 weeks prior to move
 - Teachers and staff to pack their items – Timecard
 - Custodian and District support to move and relocate boxes
 - Teachers and staff to unpack their items – Timecard

School Safety

- Prioritize work over breaks
- Fencing for construction/Background clearance
- Construction Staging Area/Parking
- Noise during construction
 - Break and After Hours
 - Testing Schedules
 - School Events
 - Delivery times
- Ingress/Egress – Separate entrance

Next Steps

- School site committee
- Identifying old supplies/surplus furniture to be removed
- Procurement of portables
- Installing infrastructure for portables (Spring Break)

Thank You

Feedback and Questions

