



Project Update Report

Report Date	9/24/2026
Project Name/Number	International Student Center / 50736
Principal	Dr. Gregory Wickersham
School Contact	Dr. Gregory Wickersham, 678-676-0902, gregory_wickersham@dekalbschoolsga.org
Regional Superintendent	Dr. Michelle Jones
Project Manager	Lo Hurts
Architect	Corgan
Contractor	Winter Construction

Scope of Work

- Phase 1: Upgrade interior finishes, wall graphics, paint refresh, new teacher walls, and kitchen equipment.
- Phase 2: HVAC refresh and renovations to MEP-FP components.

Project Construction Budget \$25,727,039.00

Project Schedule Milestones

- Design Completion – March 2025
- Construction Start – June 2025
- Construction End – October 2026

Current Project Status:


- 98% complete, Behind Schedule.
- Owner/Architect Punch Walk – Complete.
- Install temporary partition wall at stage – Complete.
- Work off punch list – In Progress.
- Fire marshal inspection – Conditionally approved – Pending installation of ADA lift at stage.

4-Week Look Ahead

- Procurement of ADA lift at stage.

End of Project Update Report

Photographs

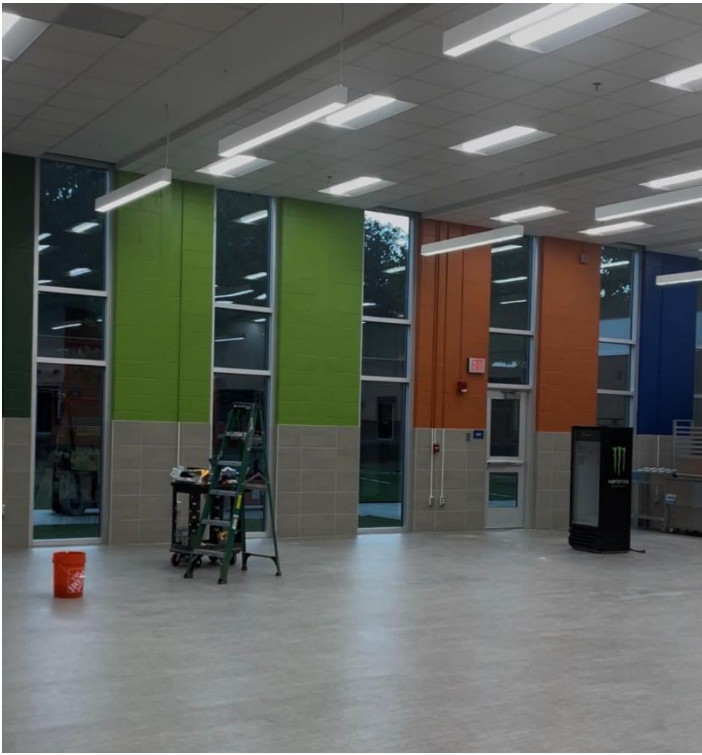

Installation of new light fixtures at cafeteria



Installation of hardscapes at courtyard



Installation of new storefront windows at cafeteria



Installation of new bus canopy
