
	<p align="center">ICS Weekly Project Report January 27, 2020</p>
	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

East Bethel Elementary School

- **Week ending Friday, January 24, 2020**
 - RTX door control wiring
 - Old speaker removal

- **Week ending Friday, January 31, 2020**
 - Finishing Punch List Work

St. Francis Elementary School

- **Week ending Friday, January 24, 2020**
 - Computer room power pole hook-ups
 - Punch list work
 - Students moved back into school from SFMS
- **Week ending Friday, January 31, 2020**
 - Owner training
 - Door Card reader Installation

St. Francis Middle School

- **Week ending Friday, January 24, 2020**
 - 2nd floor area A demolition
 - Ceilings
 - Smartboards
 - Plumbing
 - Electrical
 - Area D east floor grinding and patching VCT
- **Week ending Friday, January 31, 2020**
 - Continue area A demolition
 - Tile setting in cafeteria
 - Drywall in lower A

Weekly Project Report

January 27, 2020

St. Francis High School

- **Week ending Friday, January 24, 2020**
 - Asbestos abatement in area F
 - Structural I beam setting in area F
 - Masonry infill in area F
 - Drywall in Girls Locker room

- **Week ending Friday, January 31, 2020**
 - Continue asbestos abatement in area F
 - Electrical Demo area L
 - Continue structural I beam setting in area F
 - Painting in Girls Locker room

Early Childhood Family Center

- **Week ending Friday, January 24, 2020**
 - Issuance of Contract

- **Week ending Friday, January 31, 2020**
 - General Contractor sub-contracts to be issued.

Cedar Creek Elementary School

- **Week ending Friday, January 24, 2020**
 - Issuance of Contract

- **Week ending Friday, January 31, 2020**
 - General Contractor sub-contracts to be issued.

Weekly Project Report

January 27, 2020


Progress Photos:




SFMS Cafeteria addition



SFMS Cafeteria addition flooring

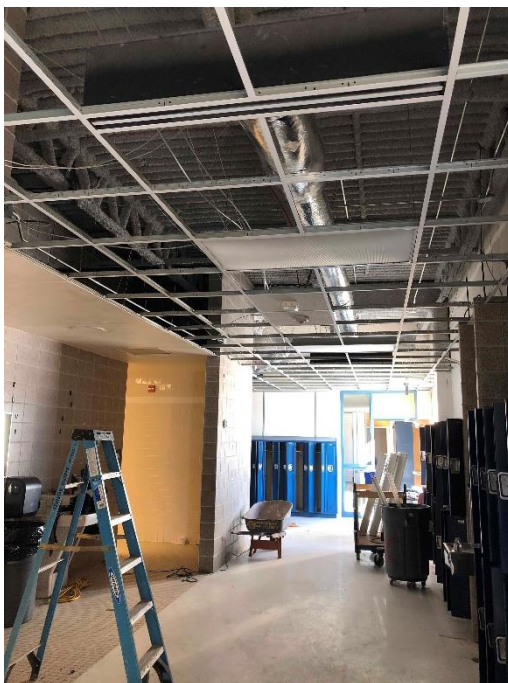

SFMS Upper L Demo

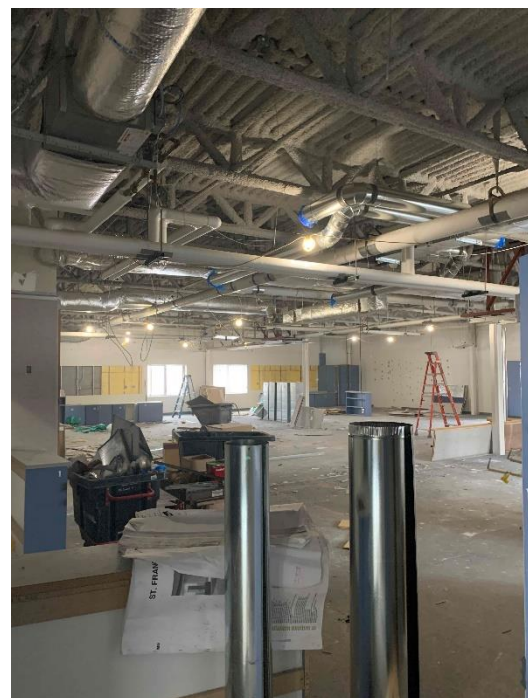

SFMS Upper L Demo

Weekly Project Report

January 27, 2020

Progress Photos:



SFHS Band/Choir I beam placement



SFHS Band/Choir new door frame



SFHS band/choir demo



SFES Completed Hallway Addition

End of Report
