TEMPLE CITY UNIFIED SCHOOL DISTRICT

2012 General Obligation Bond Authorization

Measure S



TC

Citizen's Oversight Committee Report

January 21, 2014

MEASURE S - 2013 SERIES ESTIMATED PROJECT BUDGETS & SCHEDULE

No.	District Goal Number	District Project Name	2013 Series A Estimated Budget	Current Project Phase	Estimated Project Start Date	Project Completion Date
1	0010000	Cloverly Elementary School	\$3,729,332.67	Planning & Construction	July 2014	July 2015
2	0030000	La Rosa Elementary School	4,309,471.67	Planning & Construction	August 2014	August 2015
3	0040000	Longden Elementary School	2,181,360.67	Planning & Construction	September 2014	August 2015
4	0050000	Oak Avenue Intermediate	848,172.67	Planning & Construction	November 2013	February 2014
5	0060000	Temple City High School - Phase 1A	22,955,850.67	Planning & Construction	August 2014	August 2016
6	0070000	Doug Sears Learning Center	602,404.67	Planning & Construction	June 2014	August 2014
7		Series B Projects	4,991,571.35	N/A	N/A	N/A
		COMBINED BUDGET ESTIMATES:	<u>\$39,618,164.35</u>			



τς so

0010000-92100 - Cloverly Elementary School Modernization

No.	Contractor	Trade	Contracted/ Encumbered	Amount Paid	Remaining Balance
1	Digital Networks Group	Interactive WB Systems	\$58,116.68	\$0.00	\$58,116.68
2	NTD Architecture	Architect Fees	281,153.70	(23,335.76)	257,817.94
3	TELACU Construction Management	Construction & Program Management	210,600.00	(23,787.06)	186,812.94
		PROJECT TOTAL:	\$549,870.38	(\$47,122.82)	\$502,747.56

0020000-92200 - Emperor Elementary School Modernization

No.	Contractor	Trade	Contracted/ Encumbered	Amount Paid	Remaining Balance
1	AGC Design Concept, Inc.	Architect Fees	\$52,455.00	\$0.00	\$52,455.00
2	Digital Networks Group	Interactive WB Systems	291,434.66	0.00	291,434.66
3	DSA	Plan Check Fees	8,850.00	(8,850.00)	0.00
4	TELACU Construction Management	Construction & Program Management	44,550.00	(5,031.87)	39,518.13
		PROJECT TOTAL:	\$397,289.66	(\$13,881.87)	\$383,407.79



ΠĘΣ

0030000-92300 - La Rosa Elementary School Modernization

No.	Contractor	Trade	Contracted/ Encumbered	Amount Paid	Remaining Balance
1	Digital Networks Group	Interactive WB Systems	\$144,867.12	\$0.00	\$144,867.12
2	NTD Architecture	Architect Fees	325,603.20	(27,025.07)	298,578.13
3	TELACU Construction Management	Construction & Program Management	245,025.00	(27,582.02)	217,442.98
		PROJECT TOTAL:	\$715,495.32	(\$54,607.09)	\$660,888.23

0040000-92400 - Longden Elementary School Modernization

No.	Contractor	Trade	Contracted/ Encumbered	Amount Paid	Remaining Balance
1	Digital Networks Group	Interactive WB Systems	\$162,345.12	\$0.00	\$162,345.12
2	Guida Surveying, Inc.	Prelimianry Tests	14,680.00	0.00	14,680.00
3	LPA, Inc.	Architect Fees	1,038,354.00	0.00	1,038,354.00
4	TELACU Construction Management	Construction & Program Management	121,500.00	(13,723.30)	107,776.70
		PROJECT TOTAL:	\$1,336,879.12	(\$13,723.30)	\$1,323,155.82



τş

0050000-92700 - Oak Avenue Intermediate School

No.	Contractor	Trade	Contracted/ Encumbered	Amount Paid	Remaining Balance
1	Digital Networks Group	Interactive WB Systems	\$378,599.54	\$0.00	\$378,599.54
2	TELACU Construction Management	Construction & Program Management	22,275.00	(2,889.10)	19,385.90
		PROJECT TOTAL:	\$400,874.54	(\$2,889.10)	\$397,985.44

0070000-92600 - Doug Sears Learning Center

No.	Contractor	Trade	Contracted/ Encumbered	Amount Paid	Remaining Balance
1	Digital Networks Group	Interactive WB Systems	\$40,794.51	\$0.00	\$40,794.51
2	DSA	Plan Check Fees	3,600.00	(3,600.00)	0.00
3	NTD Architecture	Architect Fees	40,000.00	0.00	40,000.00
4	TELACU Construction Management	Construction & Program Management	30,375.00	(3,430.83)	26,944.17
		PROJECT TOTAL:	\$114,769.51	(\$7,030.83)	\$107,738.68



τρ

0060000A-92500 - Temple City High School Phase 1A

No.	Contractor	Trade	Contracted/ Encumbered	Amount Paid	Remaining Balance
1	Aztec Technology	Equipment Costs	\$3,898.93	\$0.00	\$3,898.93
2	Digital Networks Group	Interactive WB Systems	500,778.67	0.00	500,778.67
3	Guida Surveying, Inc.	Prelimianry Tests	39,980.00	(37,700.00)	2,280.00
4	Home Depot	Maintenance Supplies	222.83	(222.83)	0.00
5	LPA, Inc.	Architect Fees	2,435,040.00	(26,828.95)	2,408,211.05
6	Ninyo & Moore	Prelimianry Tests	12,700.00	(12,700.00)	0.00
7	Orbach, Huff & Suarez, LLP	Legal Fees	62,712.50	(8,240.50)	54,472.00
8	Pasadena Star News	Advertisement	493.76	(493.76)	0.00
9	Registrar-Recorder/County Clerk	Advertisement	25,231.40	(25,231.40)	0.00
10	Smitty's Signworks	Advertisement	678.90	(678.90)	0.00
11	TELACU Construction Management	Construction & Program Management	1,322,325.00	(149,075.39)	1,173,249.61
12	Util-Locate, Inc	Prelimianry Tests	24,000.00	(24,000.00)	0.00
		PROJECT TOTAL:	\$4,428,061.99	(\$285,171.73)	\$4,142,890.26




2012 MEASURE S G.O. BOND ELECTION POTENTIAL STATE GRANT FUNDING

The Temple City Unified School District will make every effort to augment its Measure S G.O. Bonds with future State eligible grants. Set forth below are estimated State modernization grant funding amounts that the District may be eligible for under the State's School Facility Program ("SFP"). The estimated timeline for the receipt of these funds is expected in the 2015-2016 Fiscal Year or beyond upon passage of a future State school bond measure and the District's ability to meet the State's required funding criteria.

No.	School Name	Potential State Grant Amount	District Share of Project	Total Project Amount
1	Cloverly Elementary	\$1,313,148.87	\$875,432.58	\$2,188,581.45
2	La Rosa Elementary	1,514,261.76	1,009,507.84	2,523,769.60
3	Longden Elementary	3,032,466.91	2,021,644.61	5,054,111.52
4	Oak Avenue Intermediate	1,963,808.22	1,309,205.48	3,273,013.70
5	Dr. Doug Sears Learning Center	185,497.89	123,665.26	309,163.15
6	Temple City High School	<u>7,168,440.52</u>	<u>4,778,960.35</u>	<u>11,947,400.87</u>
TOTAL ESTIMATED STATE GRANTS:		\$15,177,624.17	\$10,118,416.11	\$25,296,040.28




2012 MEASURE S G.O. BOND ELECTION MEASURE S BOND PROGRAMMING

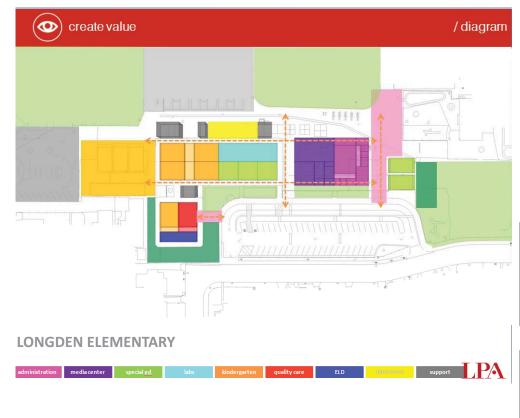


PROGRAMMING PROCESS:

TELACU has developed budget for each project per the Facility Needs Assessment and Improvement plan. Throughout the process, site committees have met with the District and TELACU to develop scope, phasing, and interim housing needs. Site Committees will continue to meet to finalize overall Master Plan for each site.











2012 MEASURE S G.O. BOND ELECTION INTERACTIVE WHITE BOARDS

0 X H



TELACU and the District have met with the sites to identify a location for the proposed Interactive White Boards for classrooms that are not affected by the Bond Projects. The install was completed on schedule and under contractual budget. The contract installation is 150 Eno Board Systems.

Below is a list of Interactive White Board Components:

- (Polyvision-ENO 2810A)
- Included in Interactive White Board systems are: Interactive Board, projector, cabling, document camera, and voice lift systems
- Interactive Stylus



Easiteach Software









DISTRICT WIDE INTERACTIVE WHITE BOARDS: CONSTRUCTION PROGRESS







TEMPLE CITY HIGH SCHOOL NEW CLASSROOM BUILDING





Page 10



TEMPLE CITY HIGH SCHOOL NEW CLASSROOM BUILDING



Temple City Unified School District and TELACU Construction Management are currently working on the complete programming/ planning for the High School.

Below is a list of work in progress:


- LPA hired as Architecture firm for this project (Board Approved)
- Meetings with site committee
- Site utility locating
- Master Planning
- Design Development
- Interim Housing Design
- Site Survey

Schedule

Planning: Construction: August 2013 to August 2014 August 2014 to August 2016



CLOVERLY ELEMENTARY MASTER PLANNING AND MODERNIZATION

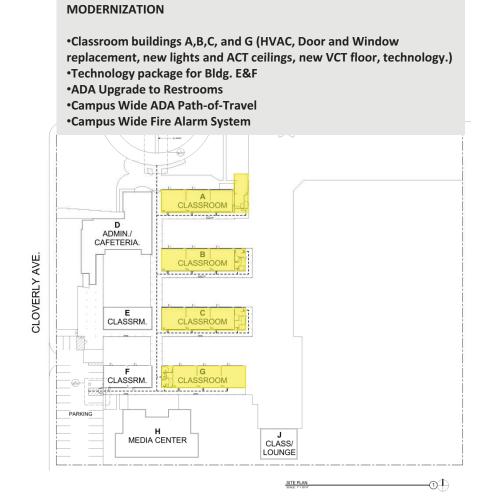

Temple City Unified School District and TELACU Construction Management are currently working on the complete programming/ planning for the Cloverly Elementary Modernization.

Below is a list of work in progress:

- NTD hired as Architecture firm for this project (Board Approved)
- Meetings with site committee: define Scope of Work, Priorities, Budget, and Schedule
- Master Planning
- Design Development
- Hazardous materials survey report

Schedule

Page 12

Planning: Construction: October 2013 to August 2014 August 2014 to August 2015





LA ROSA ELEMENTARY MASTER PLANNING AND MODERNIZATION

MODERNIZATION •Classroom buildings D & E. (HVAC, Door and Window replacement, new lights and ACT ceilings, new VCT floor, technology. •HVAC for Bldg. A & B. •Tech Packages for Bldg. A,B, & C. •ADA Upgrade to Restrooms •Campus Wide ADA Path-of-Travel •Campus Wide Fire Alarm System •(2) New Shade Structures H-3 CLASSRM. D E CLASSRM CLASSRM F CAFETERIA PARKING 4445 PARKING A ADMIN/ CLASSRM. в CLASSRM. CLASSRM. LA ROSA DRIVE ഫ SITE PLAN

Temple City Unified School District and TELACU Construction Management are currently working on the complete programming/ planning for La Rosa Elementary.

Below is a list of work in progress:

- NTD hired as Architecture firm for this project (Board Approved)
- Meetings with site committee: define Scope of Work, Priorities, Budget, and Schedule
- Master Planning
- **Design Development**
- Hazardous materials survey report

Schedule


Planning: October 2013 to August 2014 August 2014 to August 2015 Construction:




ALESSANDRO AVE.



LONGDEN ELEMENTARY MASTER PLANNING AND MODERNIZATION

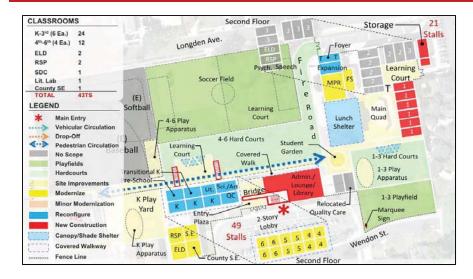



Temple City Unified School District and TELACU Construction Management are currently working on the complete programming/ planning for Longden Elementary

Below is a list of work in progress:


- LPA hired as Architecture firm for this project (Board Approved)
- Meetings with site committee
- Master Planning
- Design Development
- Site Survey

Schedule

Planning:	October 2013 to December 2014
Construction:	January 2015 to August 2016



EMPEROR ELEMENTARY WINDOW REPLACEMENT & ADA UPGRADE PROJECT

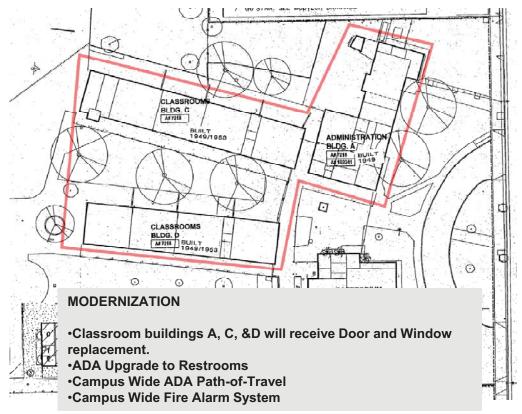

Temple City Unified School District and TELACU Construction Management are currently working on the complete programming/ planning for Emperor Elementary.

Below is a list of work in progress:

- AGC hired as Architecture firm for this project (Board Approved)
- Drawings in DSA and A# has been assigned.
- Hazardous materials survey report

Schedule


Planning: Construction: October 2013 to May 2014 June 2014 to August 2014



DR. DOUG SEARS LEARNING CENTER NEW ADMINISTRATION & CLASSROOM BUILDING

CONSTRUCTION

•Demolition of existing Administration •Installation of Interim Housing

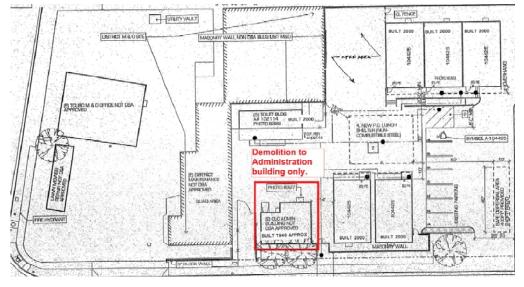

Temple City Unified School District and TELACU Construction Management are currently working on the complete programming/ planning for the Dr. Doug Sears Learning Center.

Below is a list of work in progress:

- NTD hired as Architecture firm for this project (Board Approved)
- Design off of a Piggy-back bid from Silvercreek Industries
- Hazardous materials survey report

Schedule

Planning: Construction: October 2013 to June 2014 June 2014 to August 2014



OAK AVE. INTERMEDIATE TECHNOLOGY UPGRADE

CONSTRUCTION

Installation of Interactive White Boards



Temple City Unified School District and TELACU Construction Management currently installed Interactive White Board Systems throughout Oak Ave. Intermediate.

The Technology upgrade is the only project slated for the series A and B Bond issues.





