



AUGUST 2017
BOND PROJECTS UPDATE
Midlothian ISD

Huckabee



MORE THAN ARCHITECTS

Irvin Replacement (ES #8) & Don Floyd Athletic Complex

Middle School Competition Fields

New Middle School #3

Schedules



Questions

IRVIN REPLACEMENT & DON FLOYD ATHLETIC COMPLEX

Update of Progress

- 7/18** Meeting with HKS, Huckabee and District (including Athletic Director) to discuss site plan
- 8/8** Meeting with HKS, Huckabee and District (including Athletic Director) as a follow-up to the 7/18 meeting
- 8/10** Charrette with Irvin Teachers, Administration and Huckabee on ES #8
- 8/17** Follow-up meeting with all groups involved in the process for ES #8 for the site plan and floor plan


IRVIN REPLACEMENT ELEMENTARY SCHOOL

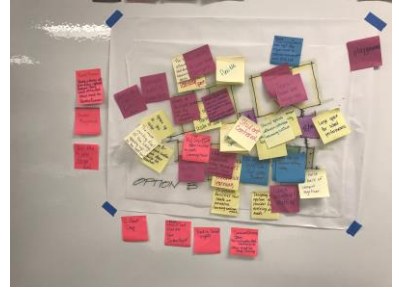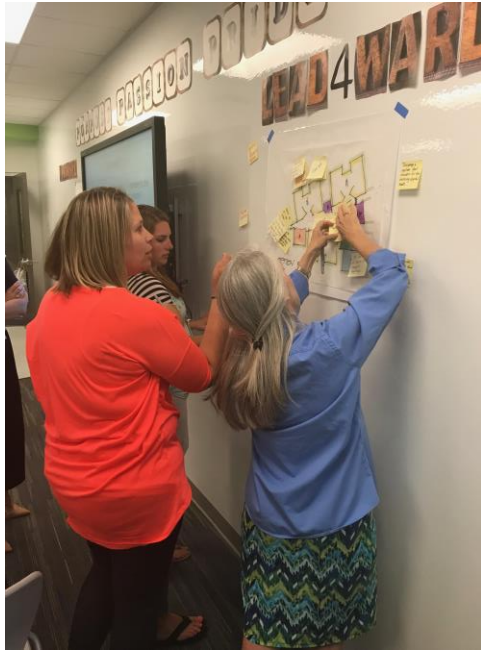

Charrette session at McClatchey with Irvin teachers

MORE THAN ARCHITECTS


IRVIN REPLACEMENT ELEMENTARY SCHOOL

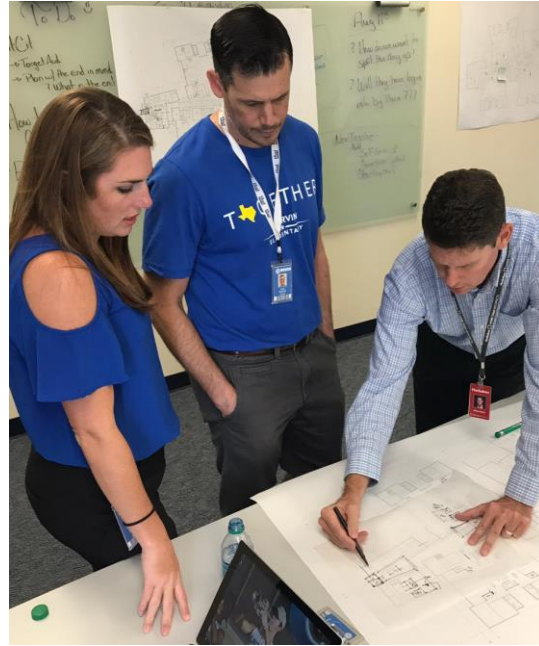

Follow-up session with all groups involved in the process of ES #8

MORE THAN ARCHITECTS

IRVIN REPLACEMENT & DON FLOYD ATHLETIC COMPLEX

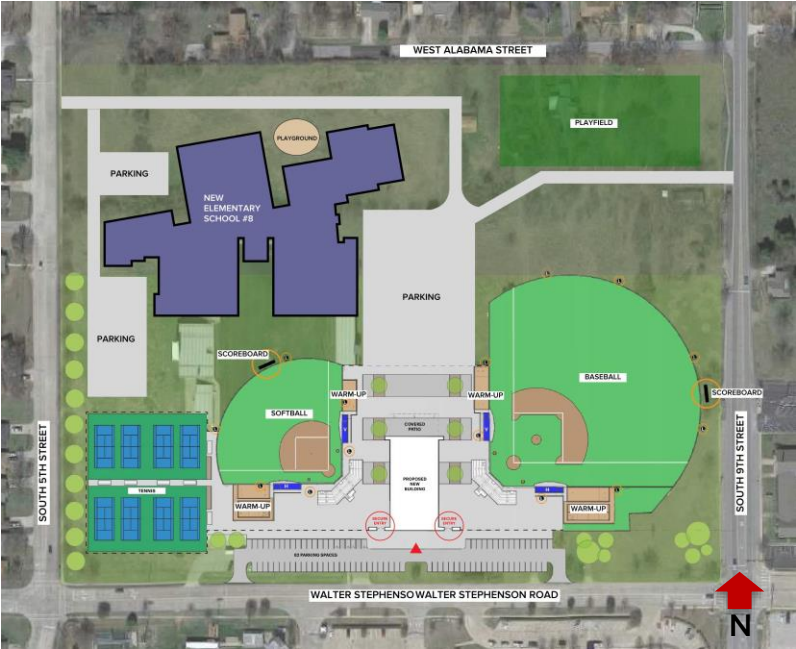

Preliminary Schematic Site Plan



Preliminary Schematic Floor Plan

IRVIN REPLACEMENT & DON FLOYD ATHLETIC COMPLEX

Next Steps

- 8/23** Meeting with HKS, Huckabee and District (including Athletic Director) as a follow-up to the 8/8 meeting
- 9/1** Meeting with Huckabee and District to discuss massing and elevations and precedent images
- 9/13** Follow up meeting with Huckabee and District to finalize the exterior character of the building
- 9/18** Present Schematic Design package to School Board

MIDDLE SCHOOL COMPETITION FIELDS

Update of Progress

- 8/8** Meeting with HKS, Huckabee and District (including Athletic Director) discussing Middle School Competition Fields

Next Steps

- 8/23** Meeting with HKS, Huckabee and District (including Athletic Director) to discuss developed site plan


MIDDLE SCHOOL COMPETITION FIELDS




Walnut Grove Middle School



Frank Seale Middle School

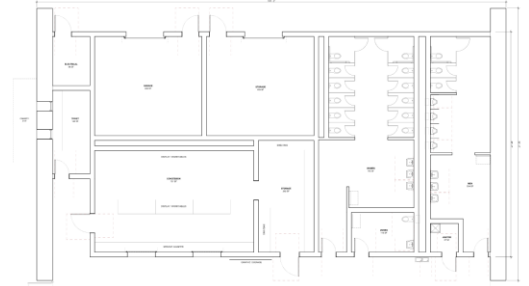

Schematic Plan

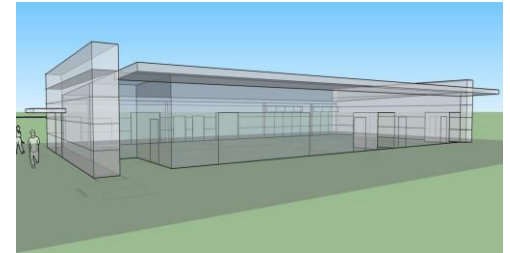

Preliminary Perspective View

NEW MIDDLE SCHOOL #3

Update of Progress

8/29 All-day meeting to discuss the Educational Specifications and Program for the new middle school

Next Steps



9/13 Community meeting to review planning meeting on 8/29

T.B.D. Site visits

T.B.D. Two day design charrette with design committee (review at the end of each day)

T.B.D. Follow-up meeting with design committee

PROJECT SCHEDULES

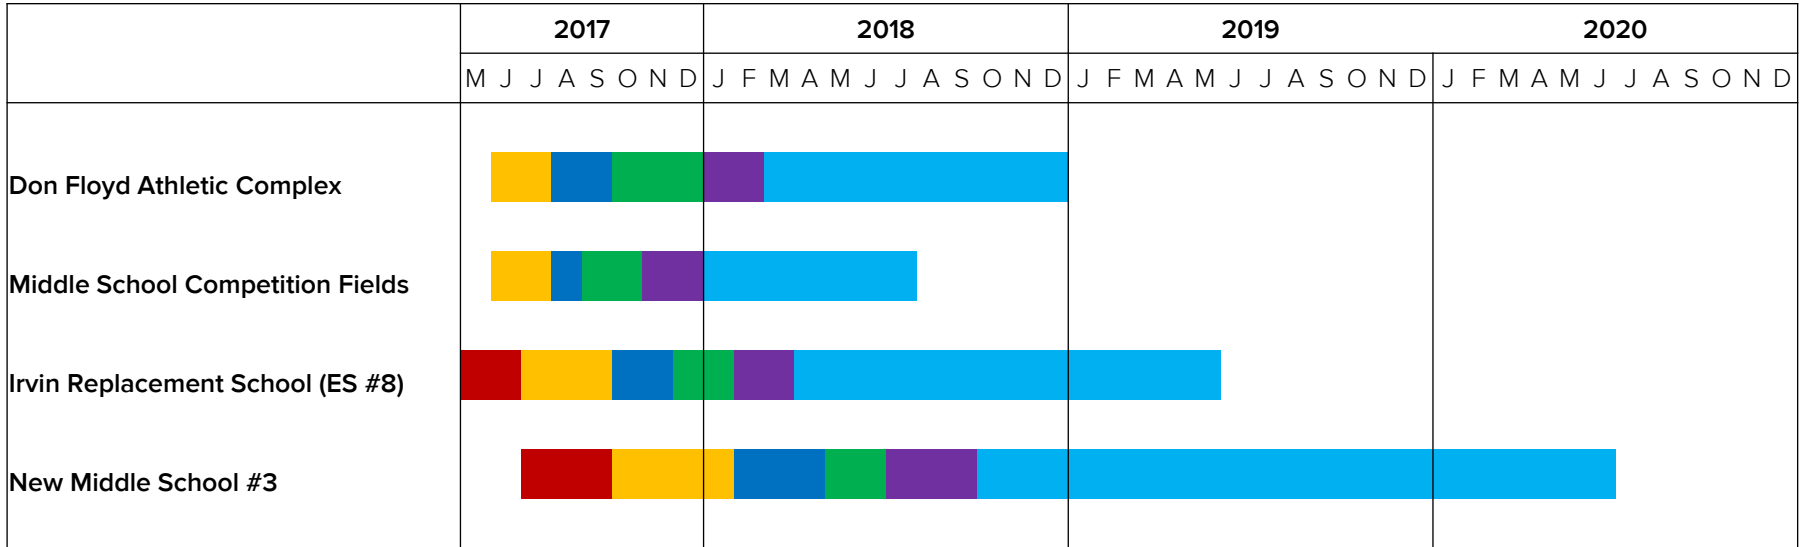

QUESTIONS ?
