



OCTOBER 2017
BOND PROJECTS UPDATE
Midlothian ISD

Huckabee



MORE THAN ARCHITECTS

Irvin Replacement (ES #8)

New Middle School #3

Renovation of Existing Campuses

Schedules


Questions

IRVIN ELEMENTARY SCHOOL REPLACEMENT

Update of Progress

- 9/29** Met with Irvin staff , district administration and consultants to discuss finishes and interior layout of spaces
- 10/09** Weekly internal meetings with Huckabee staff and Consultants
- 10/10** Had first meeting with district food service staff, district administration and food service consultant to review questionnaire and desired layout of kitchen area

IRVIN ELEMENTARY SCHOOL REPLACEMENT

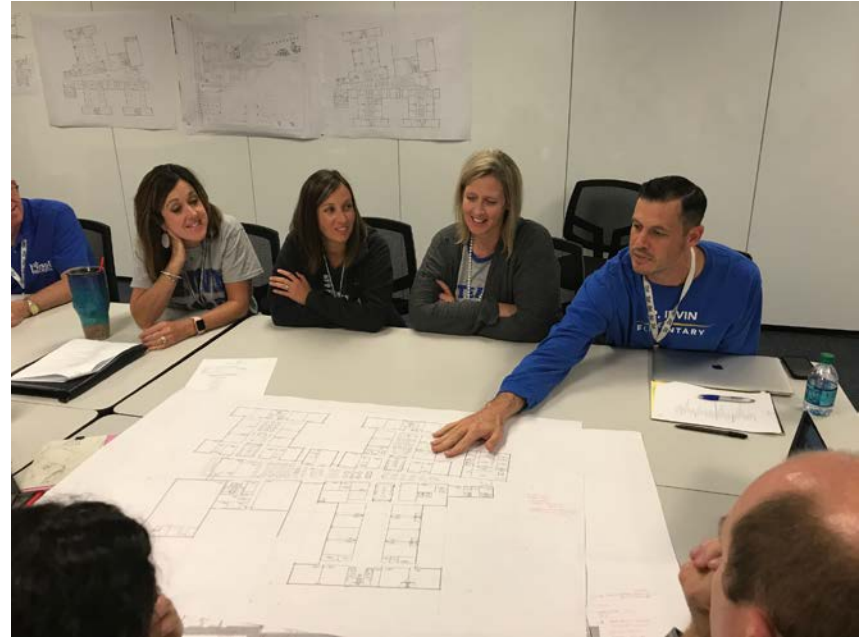

Discussion with staff on interior layouts

MORE THAN ARCHITECTS

IRVIN ELEMENTARY SCHOOL REPLACEMENT



Discussion with staff on interior layouts

MORE THAN ARCHITECTS

IRVIN ELEMENTARY SCHOOL REPLACEMENT

Next Steps

- 10/17** Follow-up meeting with Irvin staff , district administration and consultants to discuss finalized interior layout of spaces and exterior material pallet and options for learning commons aesthetic
- Weekly** Meetings with Huckabee staff and Consultants
- T.B.D** Tours of furniture dealer showrooms to get an idea of the direction the district wants to go
- 11/13** Design Development presentation to board for approval

NEW MIDDLE SCHOOL #3

Update of Progress

- 9/26** Site visits to Alvarado Junior High and Shirley Hall Middle School in Weatherford
- 9/28** Tour group met with Huckabee and MISD Administration to give feedback from site visits
- 10/3-10/4** Conducted a two day design charrette with design committee, MISD Administration and Consultants

MIDDLE SCHOOL #3



Tours with design group



MORE THAN ARCHITECTS

MIDDLE SCHOOL #3





Discussion and adjustment to program



Discussion on concept sketches

MORE THAN ARCHITECTS

MIDDLE SCHOOL #3



Feed back on concept options

MORE THAN ARCHITECTS



MIDDLE SCHOOL #3




Further refinement of selected options

MORE THAN ARCHITECTS

MIDDLE SCHOOL #3

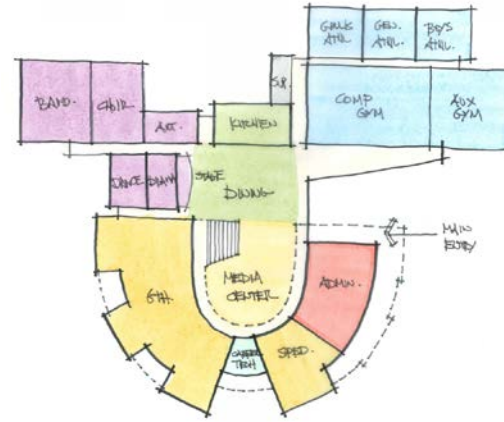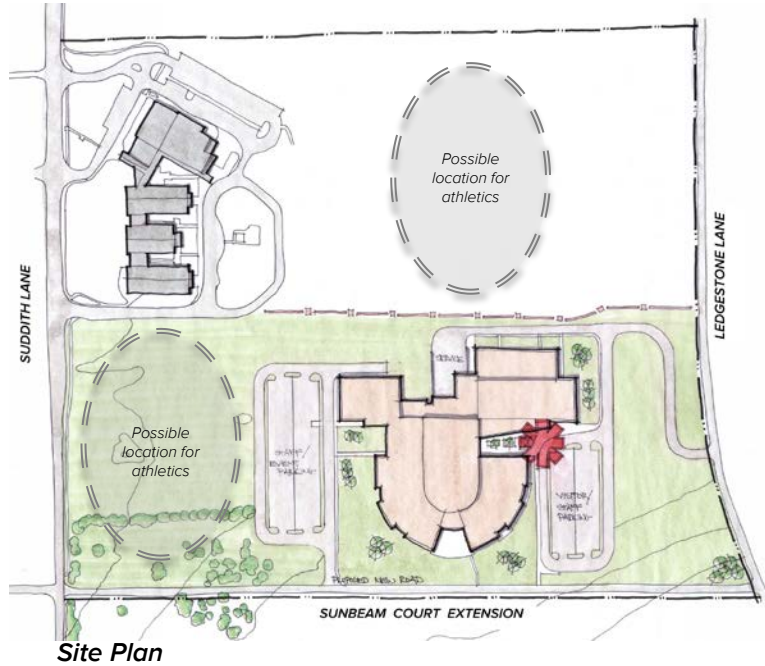

First Floor Plan

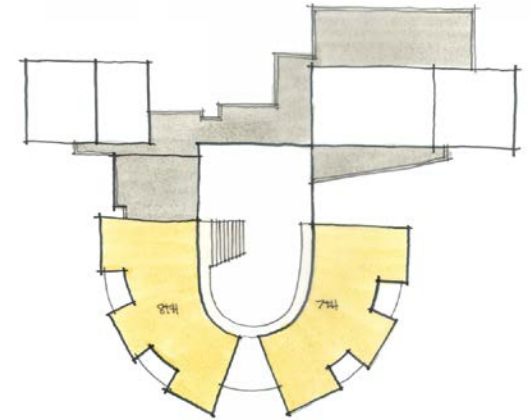

Second Floor Plan

Conceptual site plan and floor plan options selected



MORE THAN ARCHITECTS

NEW MIDDLE SCHOOL #3

Next Steps

- 11/14** Tentative follow-up meeting with design committee to finalize layouts, start looking at precedent images and massing options
- T.B.D.** Follow-up meetings with design group on massing and elevation options and selection
- 01/15** SD Presentation to Board for approval

PROJECT SCHEDULES

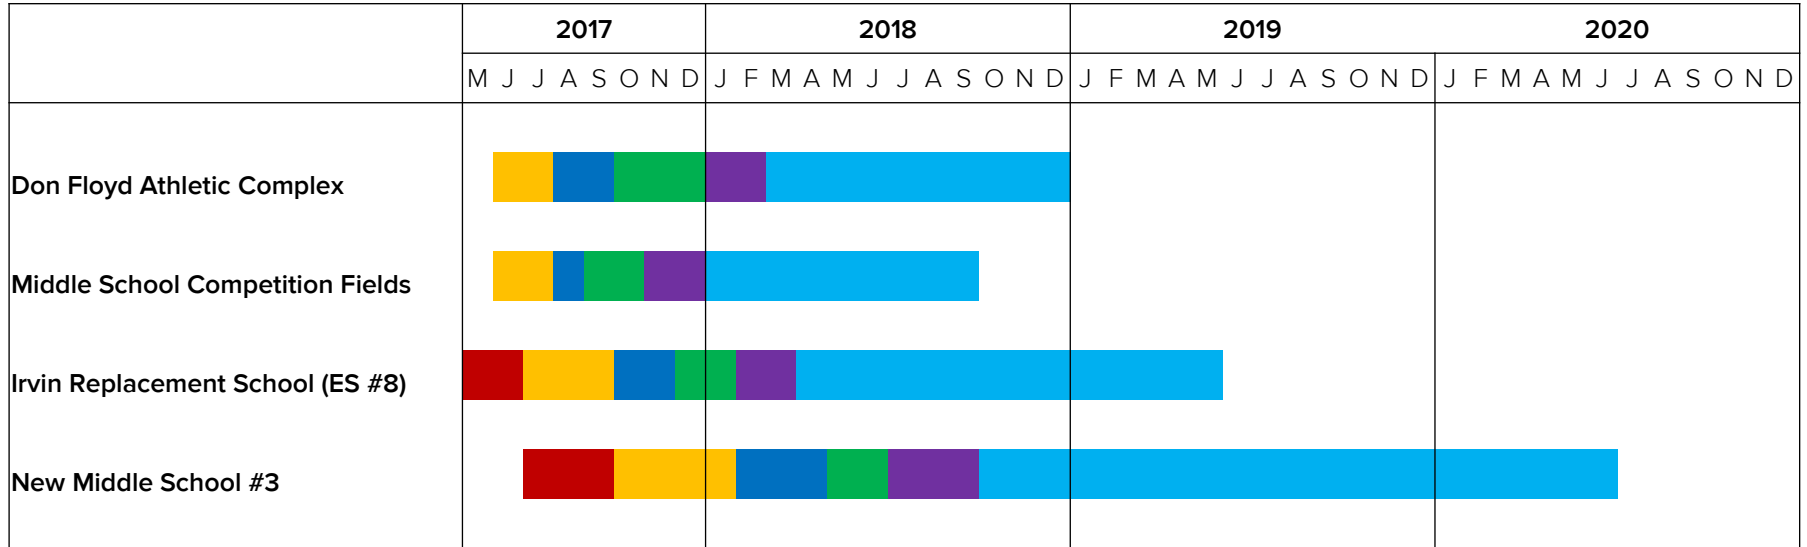

RENOVATION TO EXISTING CAMPUSES

Next Steps

- 10/18** Visit Baxter, Longbranch, Vitovsky and Mt. Peak
- T.B.D.** Develop formalized scope with campus administration, Pogue and MISD administration
- T.B.D.** Price scope to determine what items are included in projects

QUESTIONS ?
