



SEPTEMBER 2017
BOND PROJECTS UPDATE
Midlothian ISD

Huckabee



MORE THAN ARCHITECTS

Irvin Replacement (ES #8) & Don Floyd Athletic Complex

Middle School Competition Fields

New Middle School #3

Renovation of Existing Campuses


Schedules

Questions

IRVIN REPLACEMENT & DON FLOYD ATHLETIC COMPLEX

Update of Progress

- 9/13** Met with Irvin staff and district administration to review massing and elevations
- 9/18** September Board Update

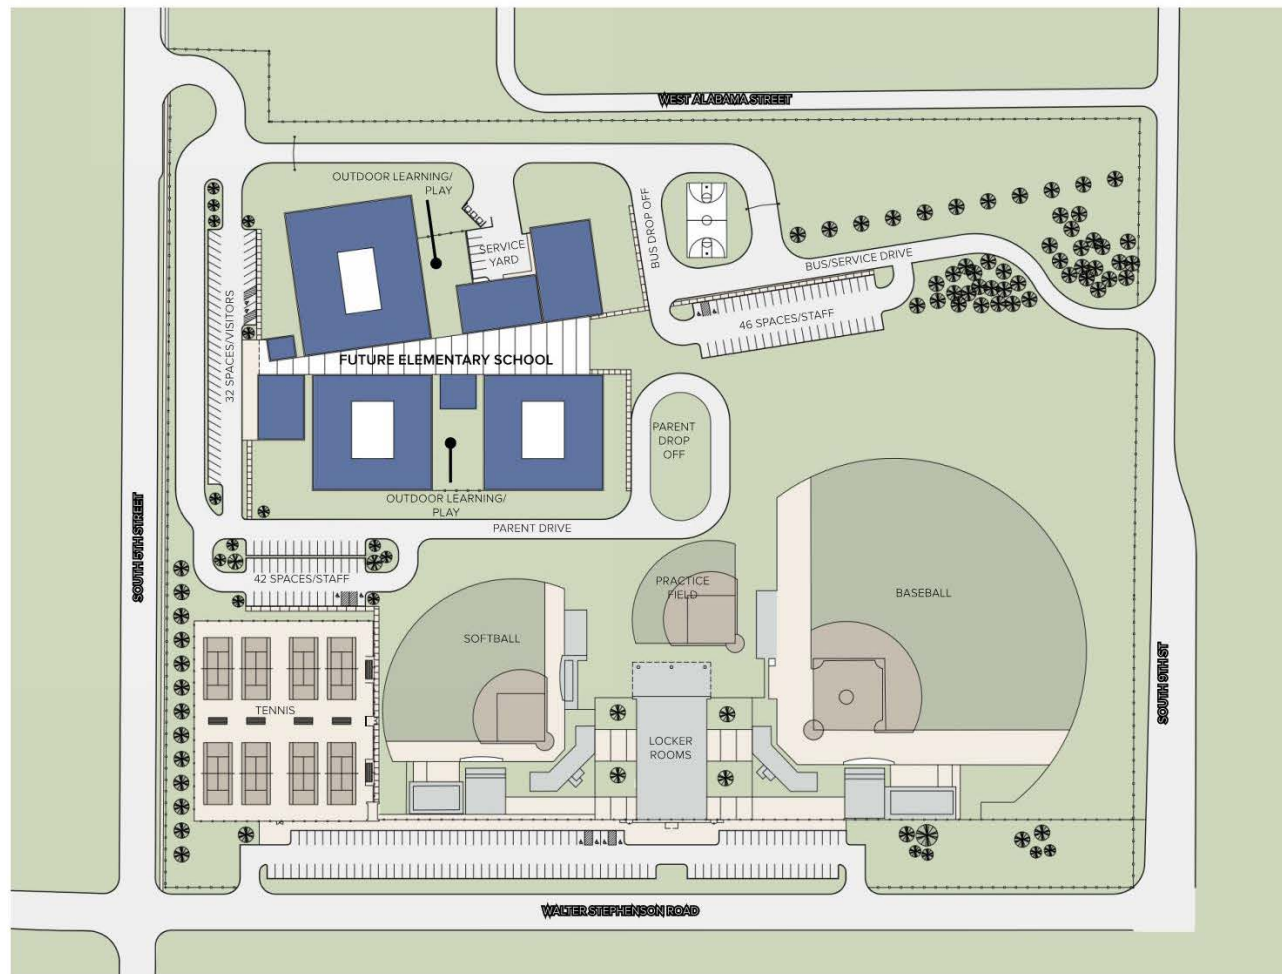

COLOR LEGEND	
	Pavement/Roads
	Sidewalks
	Grass
	Playing Fields
	Track/Infields/Tennis
	Buildings
	Surrounding Property/Context



- COLOR LEGEND**
- Administration
 - Academic
 - Library
 - Dining
 - Athletics
 - Fine Arts
 - Circulation
 - Restrooms/Support Spaces

Huckabee

NEW ELEMENTARY SCHOOL #8 | MIDLOTHIAN INDEPENDENT SCHOOL DISTRICT



FLOOR PLAN





PERSPECTIVES

Huckabee

NEW ELEMENTARY SCHOOL #8 | MIDLOTHIAN INDEPENDENT SCHOOL DISTRICT

PERSPECTIVES

IRVIN REPLACEMENT & DON FLOYD ATHLETIC COMPLEX

Next Steps

- 9/25** Schematic Design Presentation to Board at Workshop for approval
- 9/28** Start Design Development Phase of Project
- T.B.D** Meeting with staff and administration to start planning interior spaces
- T.B.D** Meeting with staff and administration to discuss the role furniture will play at this campus

MIDDLE SCHOOL COMPETITION FIELDS

Next Steps

- 9/19** Meeting with HKS, Huckabee and District (including Athletic Director) to finalize program
- T.B.D.** Meeting with HKS, Huckabee and District (including Athletic Director) to finalize plan
- T.B.D.** Schematic Design Presentation to Board for approval

NEW MIDDLE SCHOOL #3

Update of Progress

Currently working on compiling program from meeting on 8/29 with district

Next Steps

- 9/22** Deliver preliminary program for district review prior to charrettes
- 9/26** Site visits
- 10/3-10/4** Two day design charrette with design committee (review at the end of each day)
- T.B.D.** Follow-up meeting with design committee

RENOVATION TO EXISTING CAMPUSES

Update of Progress


9/13 Walked Midlothian High School, Frank Seale, Walnut Grove and Irvin Elementary School campuses with district to determine scope and priority

Next Steps

T.B.D. Develop formalized scope with Pogue and MISD

T.B.D. Price scope to determine what items are included in projects

PROJECT SCHEDULES

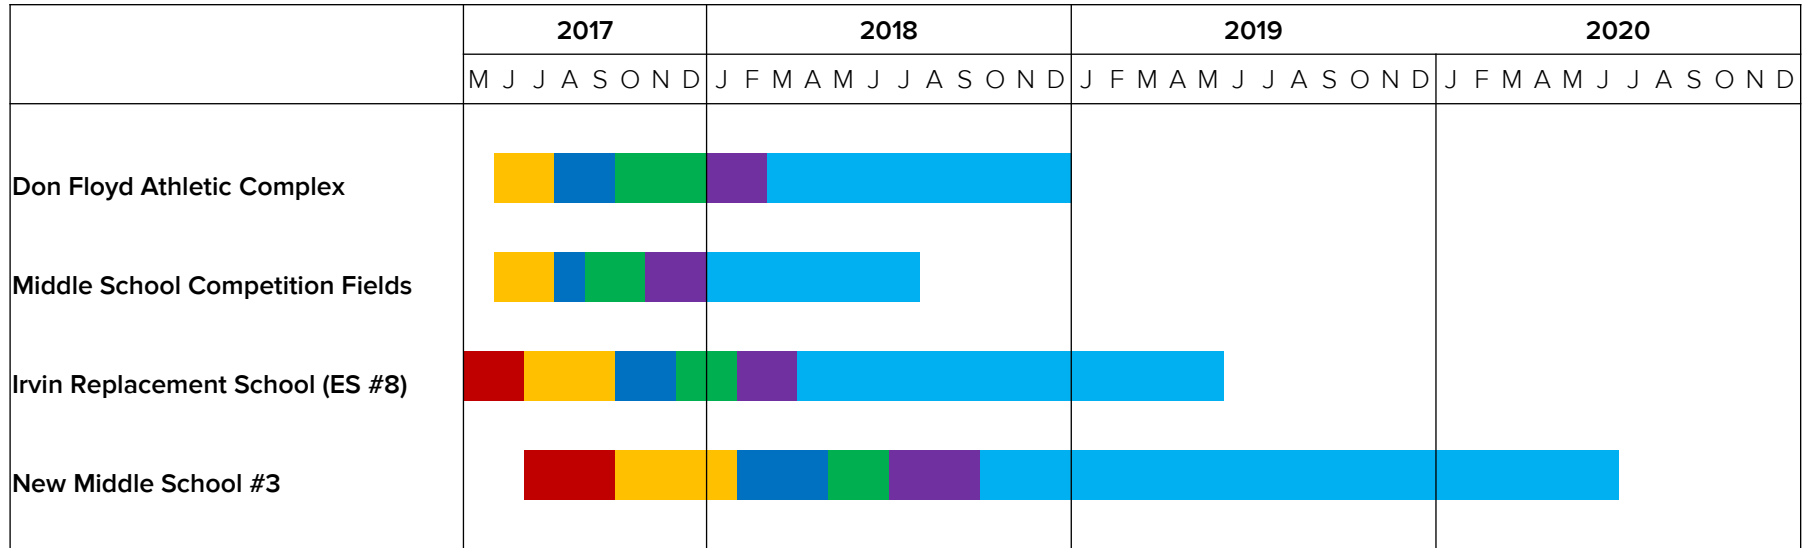

Planning
 Schematic Design
 Design Development
 Construction Documents
 Bid
 Construction

MORE THAN ARCHITECTS

QUESTIONS ?
