

Projects Update

April 26, 2021

Bond 2017 Project:
Leadership Support Center

Bond 2020 Projects:
ES North Classroom Addition
ES South Classroom Addition

Bond 2020 Projects:
Intermediate School North
Intermediate School South



FRONT RENDERING



LEADERSHIP SUPPORT CENTER BOND 2017



PROJECT SCHEDULE

COMPLETE - Package 1: Demolition, Earthwork, Building Pad and Underground Utilities

- Demolition – Complete

January 15th – March 15th 2020

COMPLETE - Package 2: Foundation, Structural Steel Purchase and MEP Underslab

- Building Pad: Completed on Schedule:
- Drill & Pour Foundation Piers/Grade Beams Complete:
 - *PCI to give status update of project time line*

Package 3: Remaining Building Package

- Construction Documents Issue for Proposal: Complete April 6th 2020
- Issue for Permit: Complete April 9th 2020
- Develop GMP present to BOT for Approval/Award: Complete May 18th 2020
- **Construction Start - Substantial Completion: May 19th 2020 - June 15th 2021**
- **Move – In: July 15th 2021**



BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – Eagle Drive Front Exterior Elevation



BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – Front Exterior Elevation - Board Room Main Entrance

BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – Front Exterior Elevation - Main Lobby Entrance



BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – Rendering of Boardroom Plaza Eagle Statue



BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – J Justin Jenson Conference Center Entrance



BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – J Justin Jenson Conference Center Steps



HALL OF HISTORY



BACK OF BUILDING RENDERING

BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – Hall of History and Parking Lot



BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – Hall of History Gyp. Board Tape and Float, Electrical Installations in Progress

OFFICE PORTAL ENTRY RENDERING



FINANCE

BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – Typical Entrance into Office Suites



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SOUTH ADDITIONS



ESS CLASSROOM ADDITION RENDERING



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



Area B - Classroom Wing - Brick



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



Area B – Typical Classroom Paint, Ceiling Grid and Lights



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITION



ESS LIBRARY ADDITION RENDERING

LIBRARY

ART ROOM



ESS ART ROOM ADDITION RENDERING

ESS LIBRARY ADDITION



ESS ART ROOM ADDITION PROGRESS

ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



Area C – Library Exterior Elevation - Brick



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



Area C - Library Exterior Elevation - Brick



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



Area C - Library Paint, Ceiling Grid and Lights



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITION



Area C - Library Paint, Ceiling Grid and Lights



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY NORTH ADDITIONS



BOND 2020 ESN CLASSROOM ADDITIONS



Classroom Addition East Side

ELEMENTARY NORTH NEW ADDITIONS

ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



Area A & B – Classroom Wing Exterior Elevation



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



Area C & D – Classroom Wing Exterior Elevation



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



Typical Classroom Casework, Paint, Ceiling Grid and Lights



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



Typical Classroom Casework, Paint, Ceiling Grid and Lights

ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS




BOND 2020 INTERMEDIATE SCHOOL NORTH




FRONT RENDERING

BOND 2020 INTERMEDIATE SCHOOL NORTH

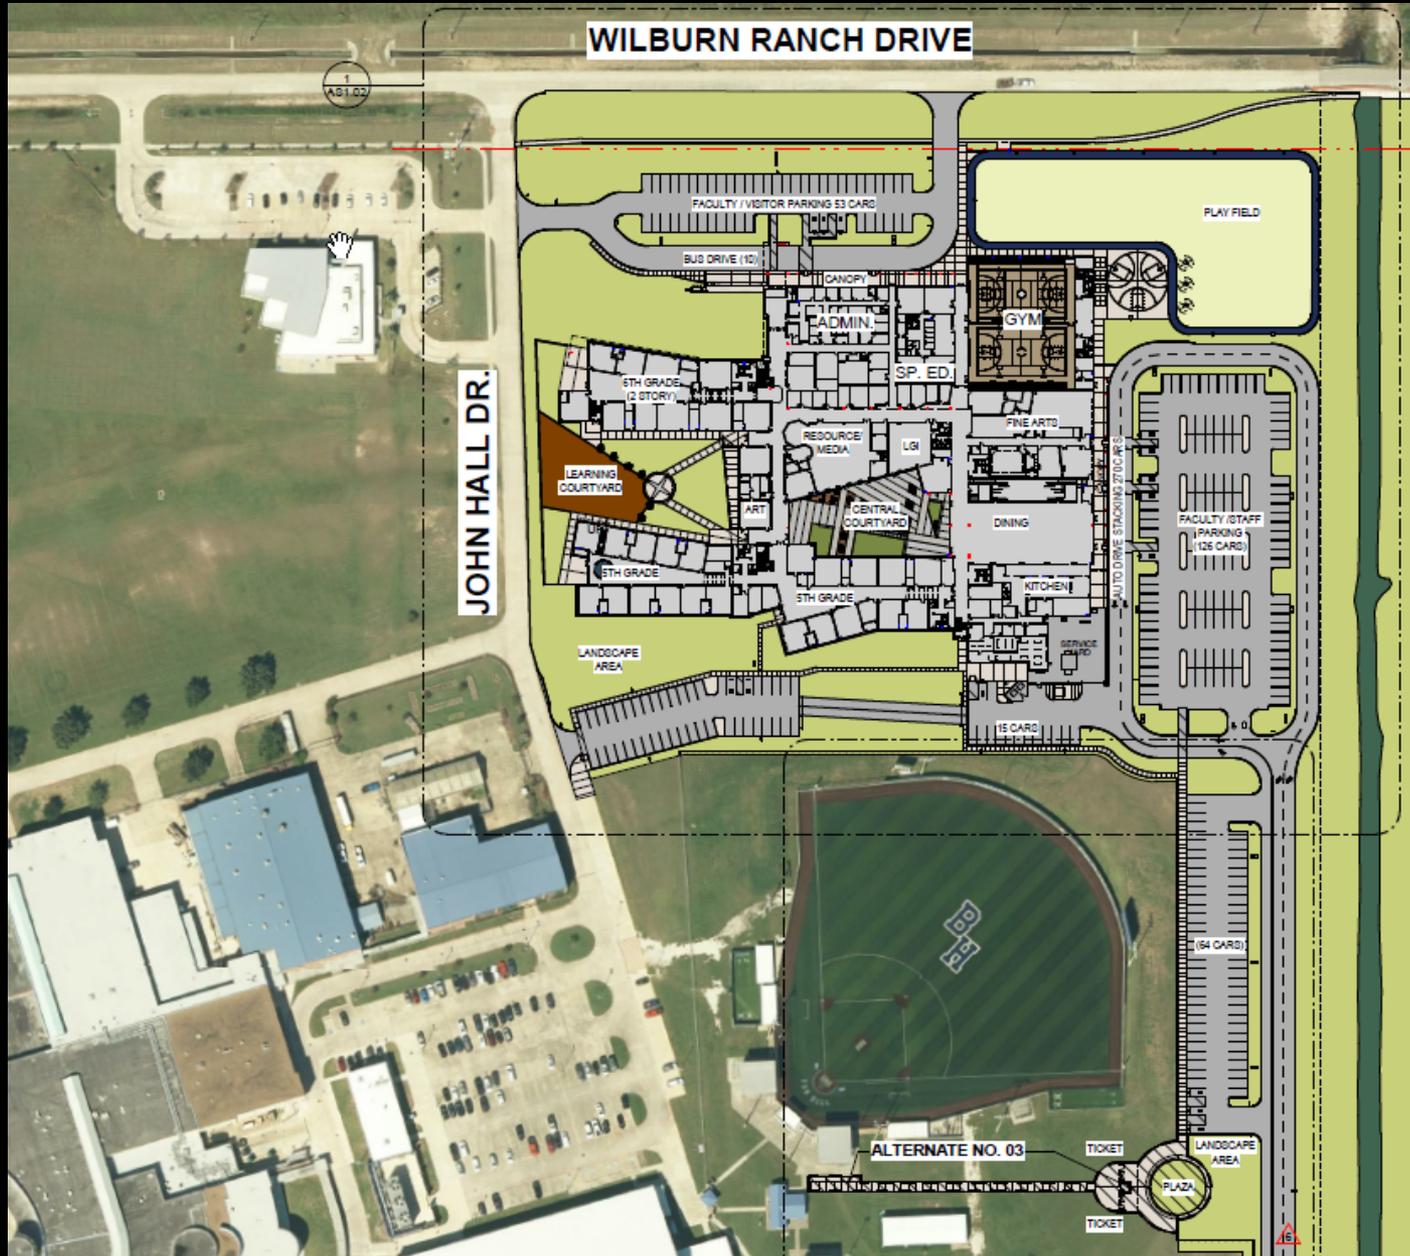

BOND 2020 INTERMEDIATE SCHOOL NORTH

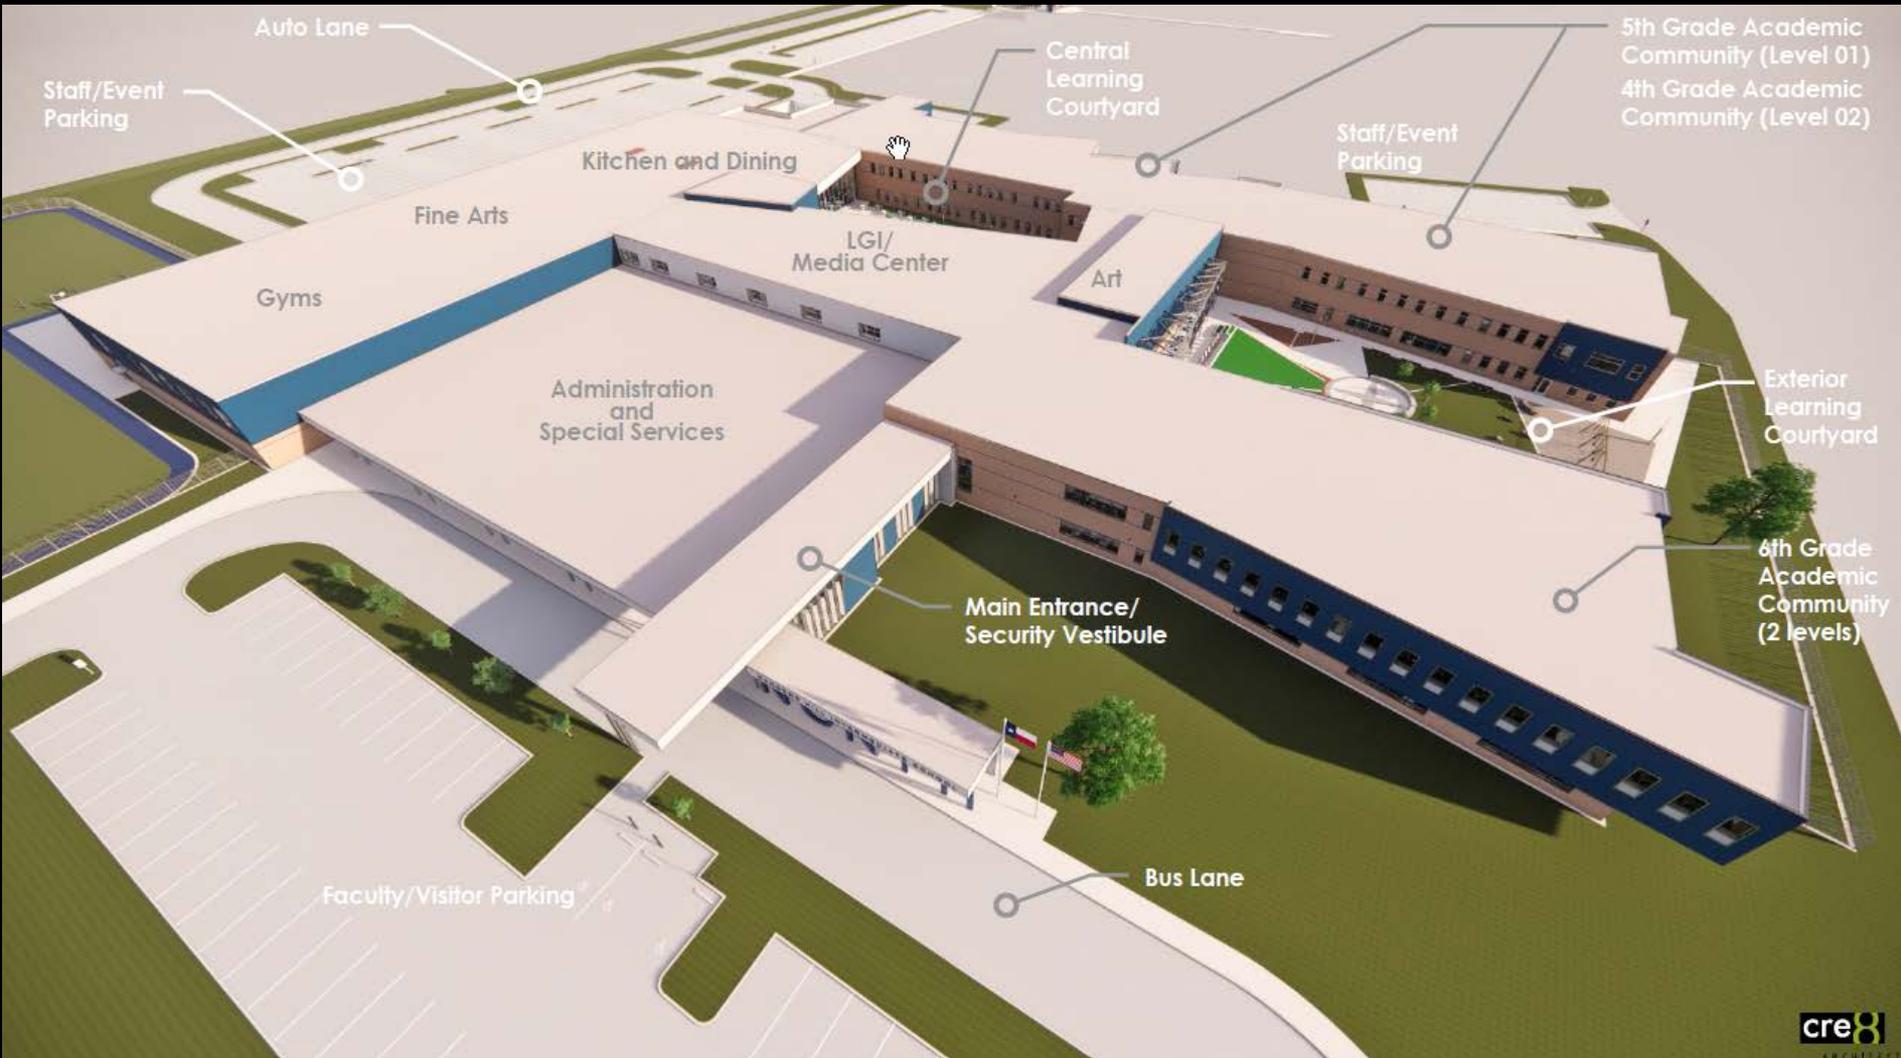

BUILDING RENDERING

ISN Car-Rider Entrance off Perry Rd.



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



Aerial – Steel Erection Areas E, F, G – Grade Beams & Structural Concrete Slab Prep Area H



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



Area B Concrete Slab – Steel Erection in Progress



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN




INTERMEDIATE SCHOOL SOUTH



BOND 2020 INTERMEDIATE SCHOOL SOUTH


EAGLE'S perch




connected

"Learn how to see. Realize that everything connects to everything else."

-Leonardo da Vinci



educational process
focused on connections
=
well-rounded product of
exceptionally educated,
individually focused citizens

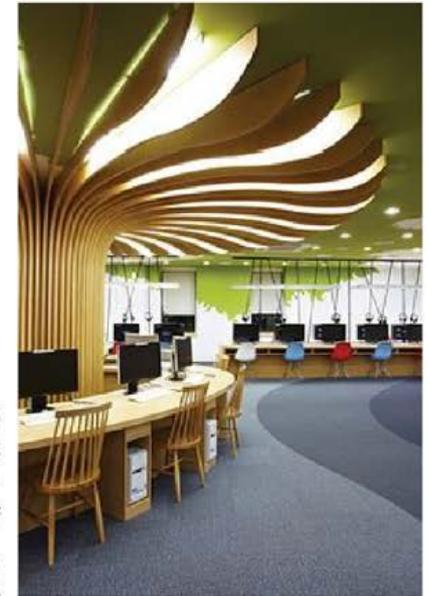

BARBERS HILL INTERMEDIATE south

ISS BUILDING DESIGN THEME – EAGLE'S PERCH

Barbers Hill
Independent School District

BOND 2020 INTERMEDIATE SCHOOL SOUTH



BUILDING RENDERING



FM 565 EAST

**GILL PARKWAY
(PERRY ROAD)**

BOND 2020 – INTERMEDIATE SCHOOL SOUTH





FM 565 EAST

**GILL PARKWAY
(PERRY ROAD)**

BOND 2020 – INTERMEDIATE SCHOOL SOUTH



Aerial – Staff Parking, Area E and F Steel Erection in Progress



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



Aerial – Area E/F Steel Erection - Concrete Slabs Complete
for Area G – and Staff and Visitors Parking Lots



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – ACTION ITEM HS PRACTICE FIELD EXPANSION



Area where partial practice field will become full-size:



Approximate location of full size practice field:

Ruler

Line Path Polygon Circle 3D path 3D poly

Measure the distance between multiple points on the ground

Length: 230.54 Yards


Show Elevation Profile

Show Navigation Save Clear

BOND 2020 – ACTION ITEM HS FINISHES RENOVATION TO ORIGINAL BUILDING SECTIONS – SCOPE OF WORK 1ST FLOOR:

Renovation Finish Legend


- Carpet & Paint
- Carpet, LVT, & Paint
- LVT & Paint
- LVT & Paint Partial
- LVT & Paint Railing
- LVT, Entrance & Paint Partial
- No Finish Work
- Paint
- Paint Railing

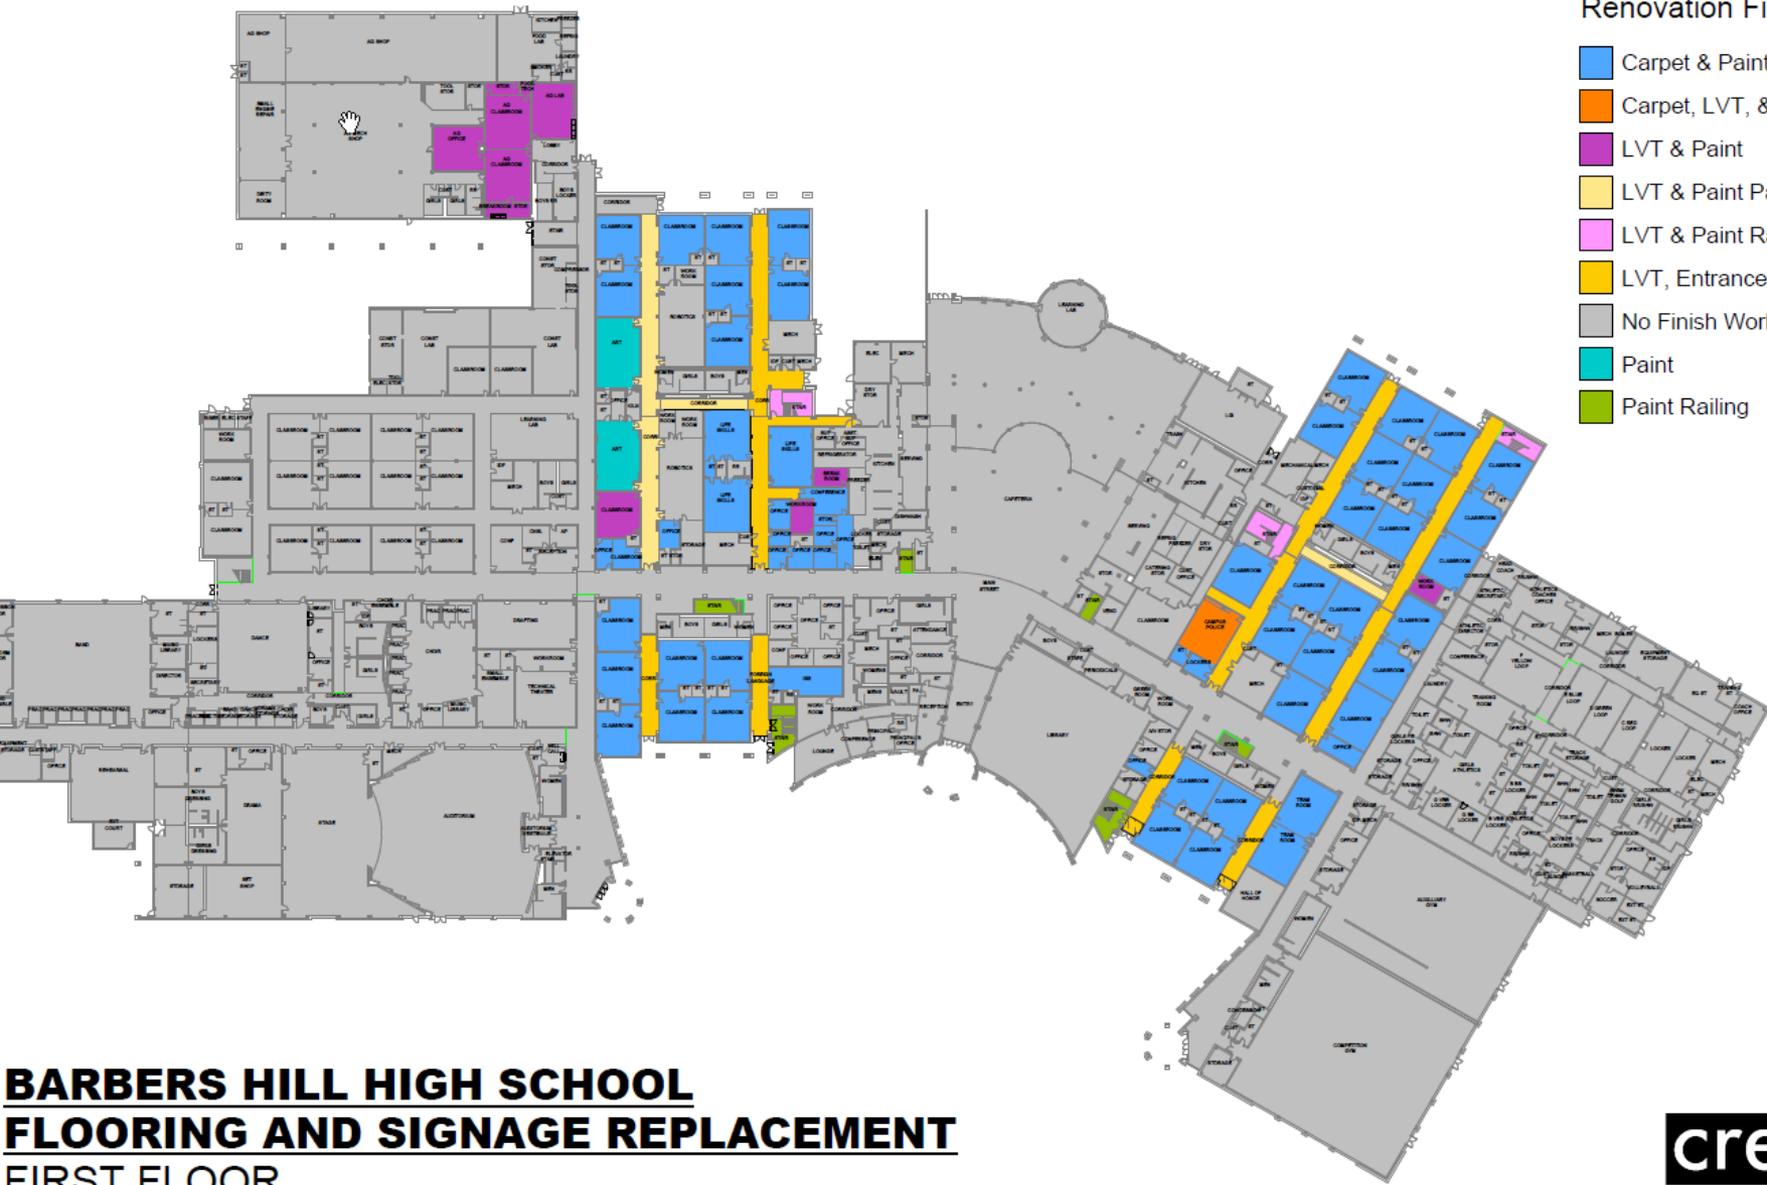

BARBERS HILL HIGH SCHOOL **FLOORING AND SIGNAGE REPLACEMENT** FIRST FLOOR



BOND 2020 – ACTION ITEM HS FINISHES RENOVATION TO ORIGINAL BUILDING SECTIONS – SCOPE OF WORK 2ND FLOOR

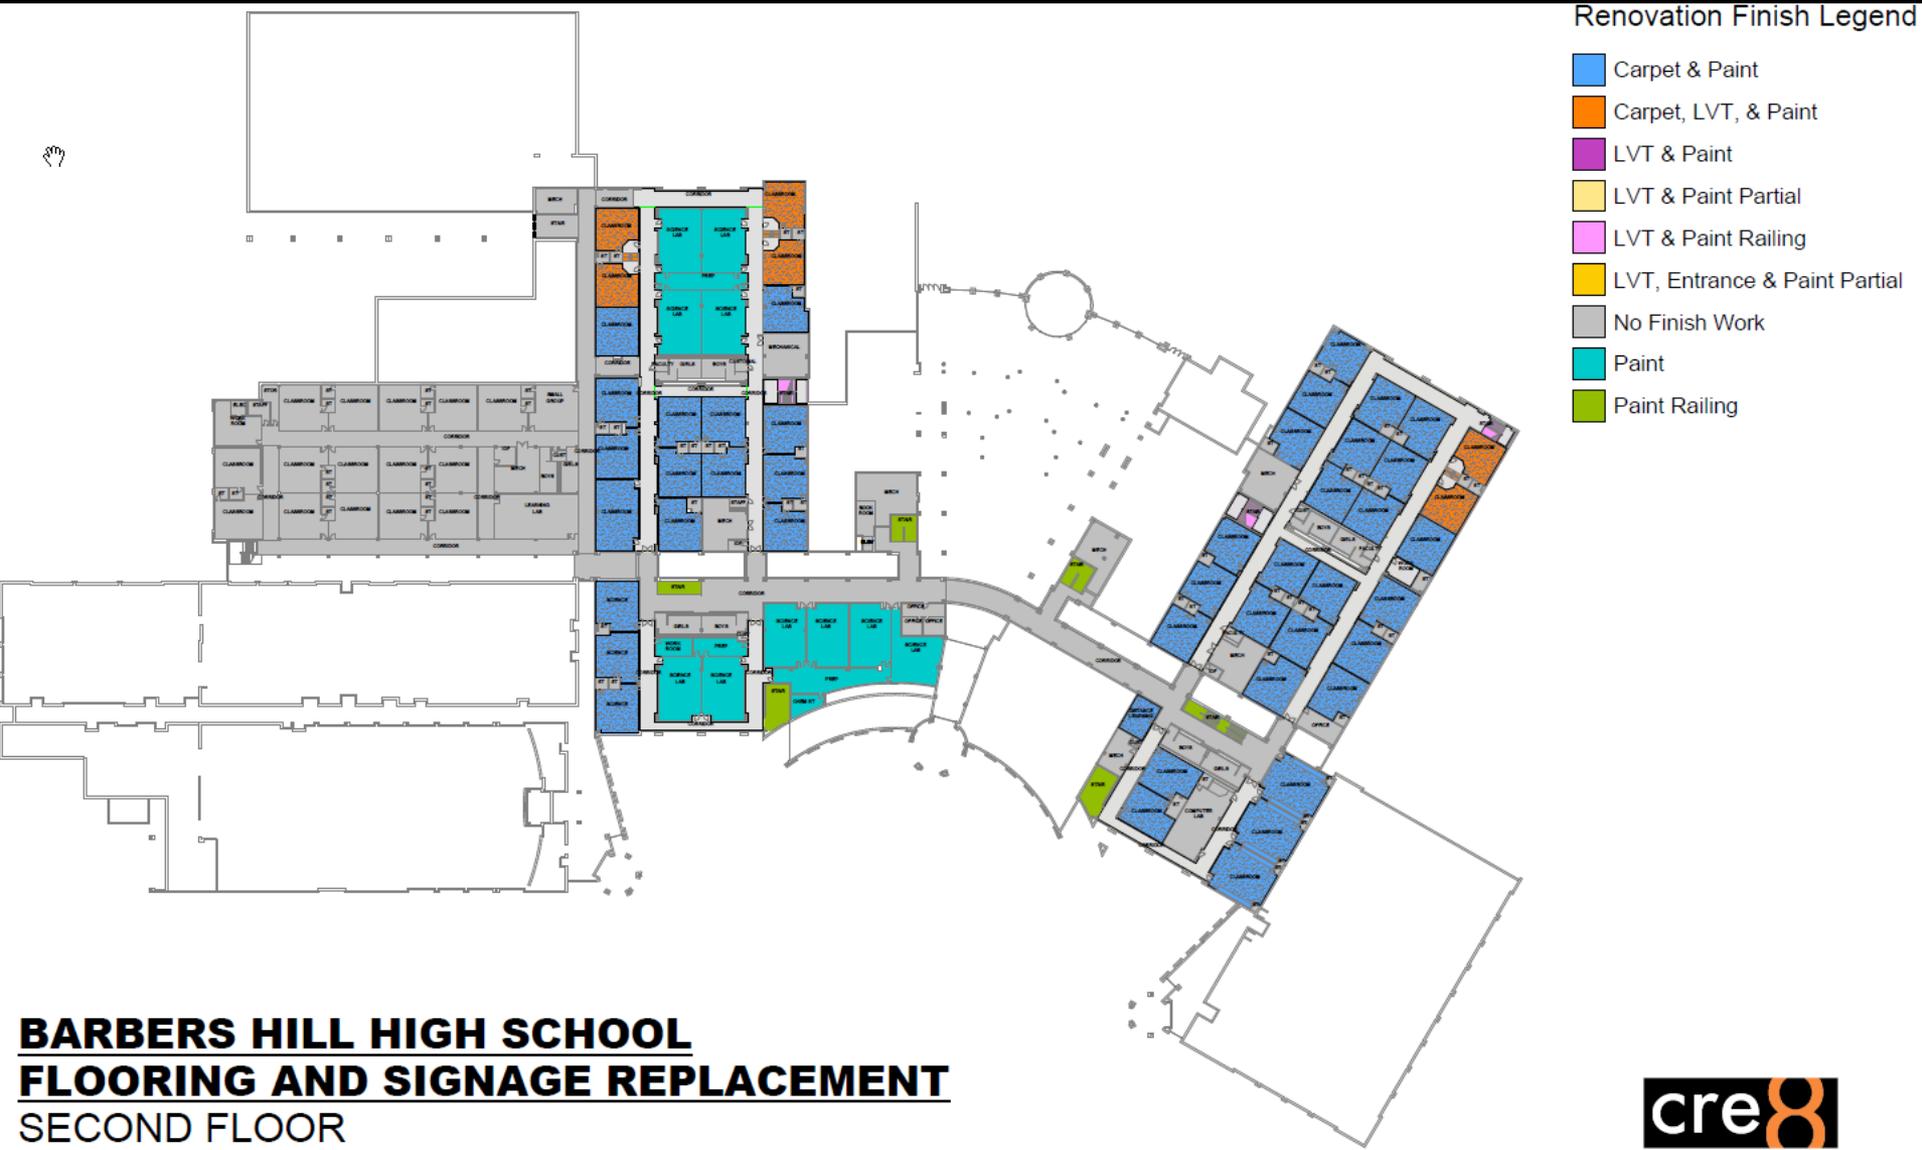

- Renovation Finish Legend**
- Carpet & Paint
 - Carpet, LVT, & Paint
 - LVT & Paint
 - LVT & Paint Partial
 - LVT & Paint Railing
 - LVT, Entrance & Paint Partial
 - No Finish Work
 - Paint
 - Paint Railing

BARBERS HILL HIGH SCHOOL FLOORING AND SIGNAGE REPLACEMENT SECOND FLOOR



THE END

THANK YOU!



cre8
ARCHITECT
