



Projects Update

March 22, 2021

Bond 2017 Project:
Leadership Support Center

Bond 2020 Projects:
ES North Classroom Addition
ES South Classroom Addition

Bond 2020 Projects:
Intermediate School North
Intermediate School South



PROJECT SCHEDULE

COMPLETE - Package 1: Demolition, Earthwork, Building Pad and Underground Utilities

- Demolition – Complete

January 15th – March 15th 2020

COMPLETE - Package 2: Foundation, Structural Steel Purchase and MEP Underslab

- Building Pad: Completed on Schedule:
- Drill & Pour Foundation Piers/Grade Beams Complete:
 - *PCI to give status update of project time line*

Package 3: Remaining Building Package

- Construction Documents Issue for Proposal: Complete April 6th 2020
- Issue for Permit: Complete April 9th 2020
- Develop GMP present to BOT for Approval/Award: Complete May 18th 2020
- Construction Start - Substantial Completion: May 19th 2020 - June 15th 2021
- Move – In: July 15th 2021



BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – Main Building Lobby Entrance Aerial View



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – Main Building Lobby Entrance

BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – Boardroom North Elevation


BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER

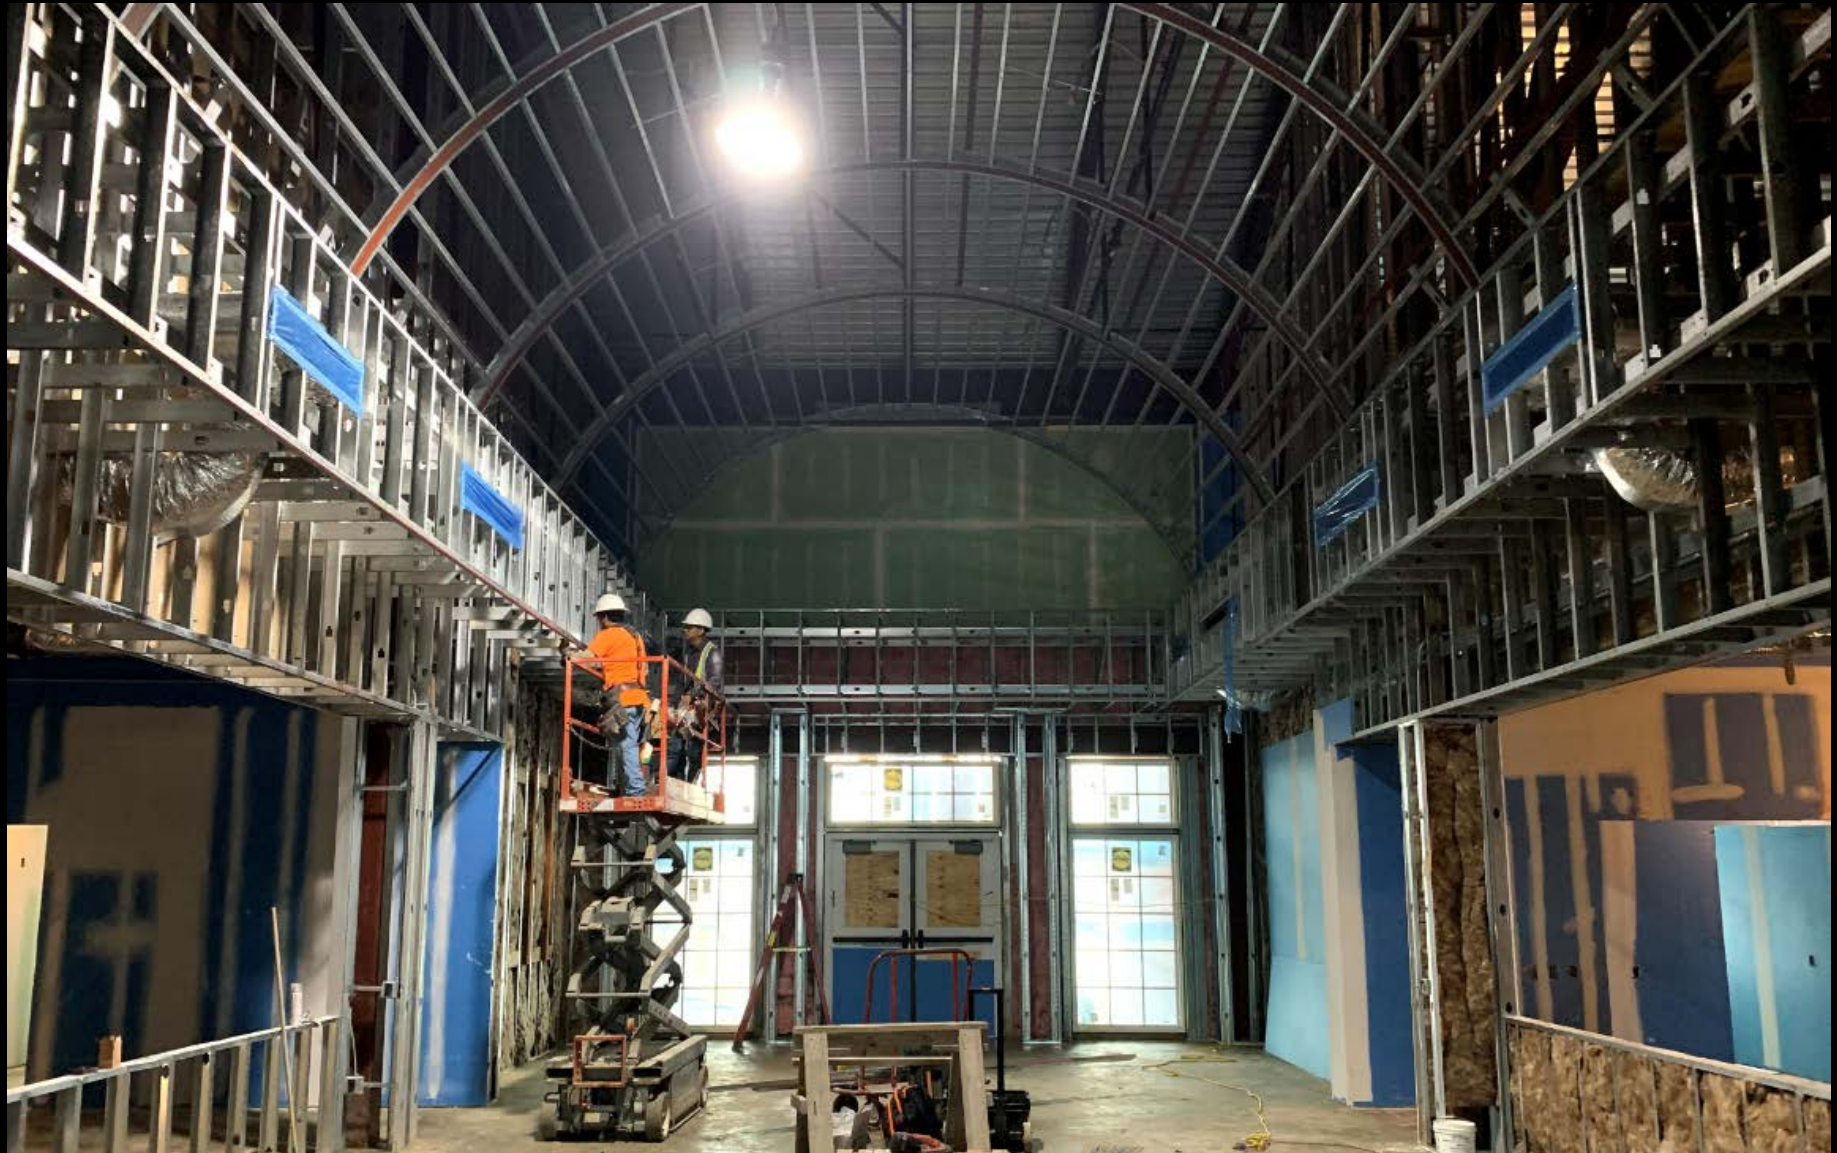

BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – Board Conference Room


BOND 2017 – LEADERSHIP SUPPORT CENTER



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS

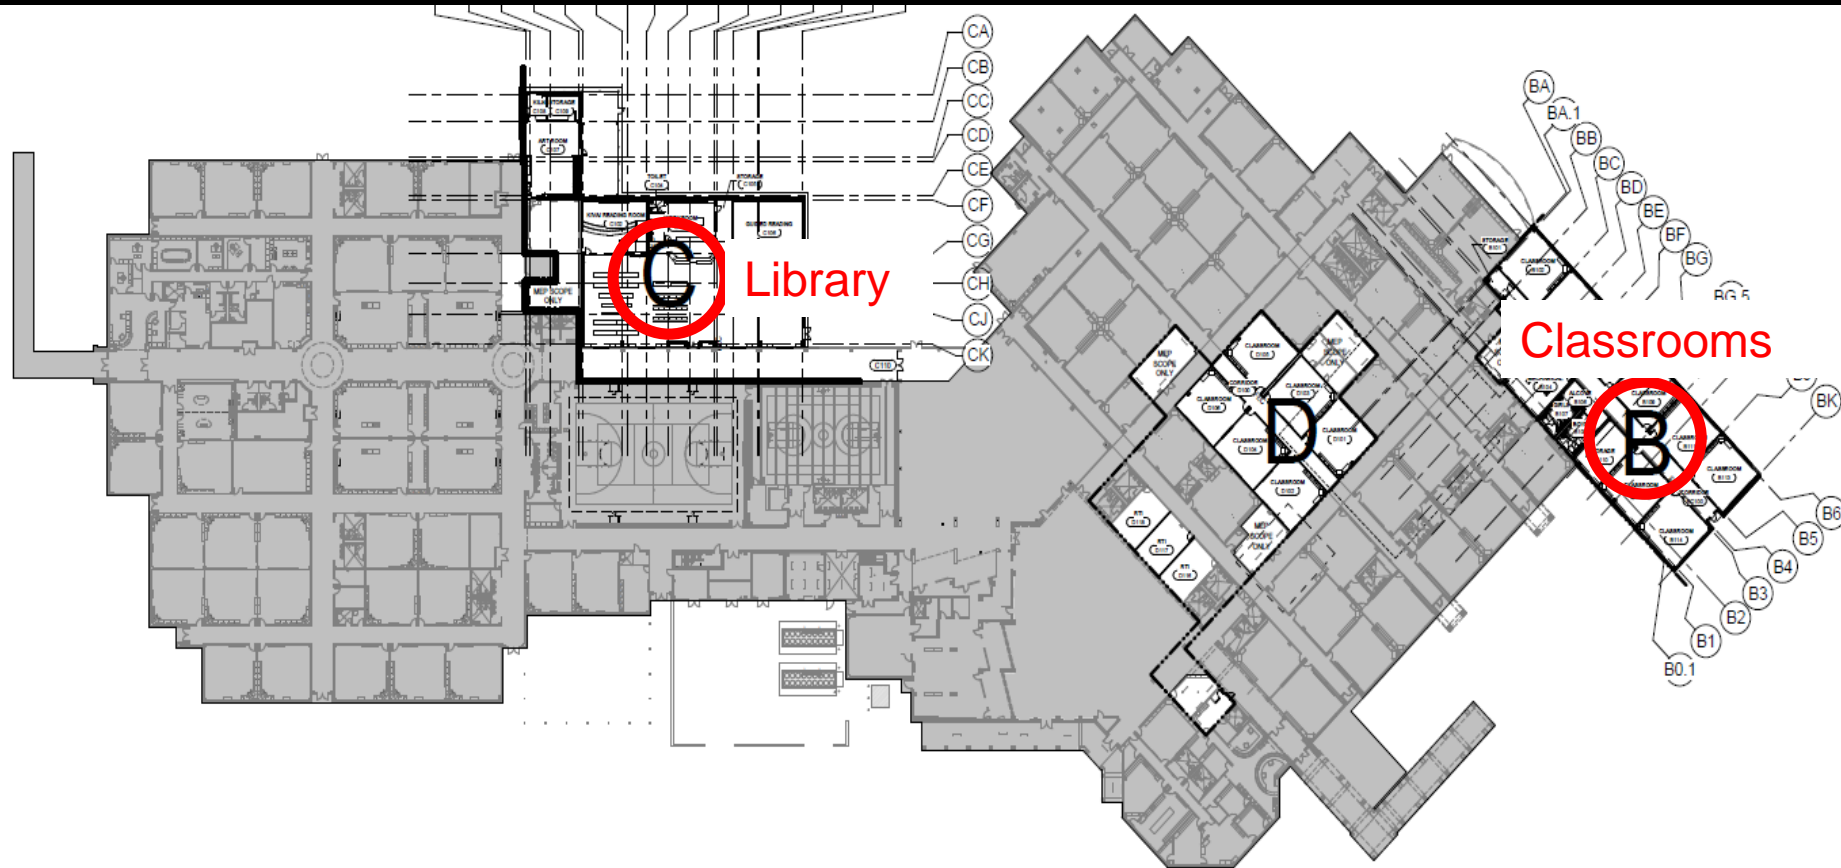

PHASING SCHEDULE

PHASE 1: AREA B & C
WORK TO BEGIN SUMMER 2020

PHASE 2: AREA D
WORK TO BEGIN SUMMER 2021

ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS

New Classroom Addition



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS




ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS

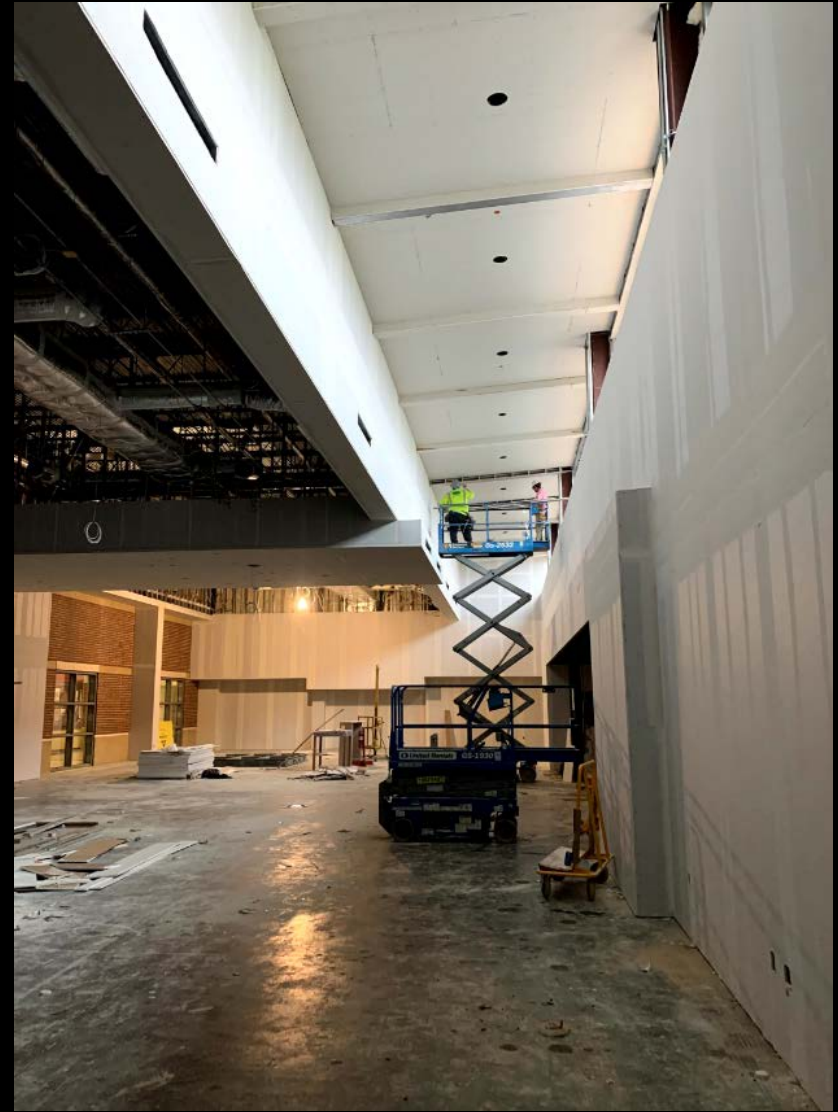

Area C - Library Clearstory – Taping and Floating of Gypboard

ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS




Area C – Library – Taping and Floating of Gypboard

ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY NORTH ADDITIONS

ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS

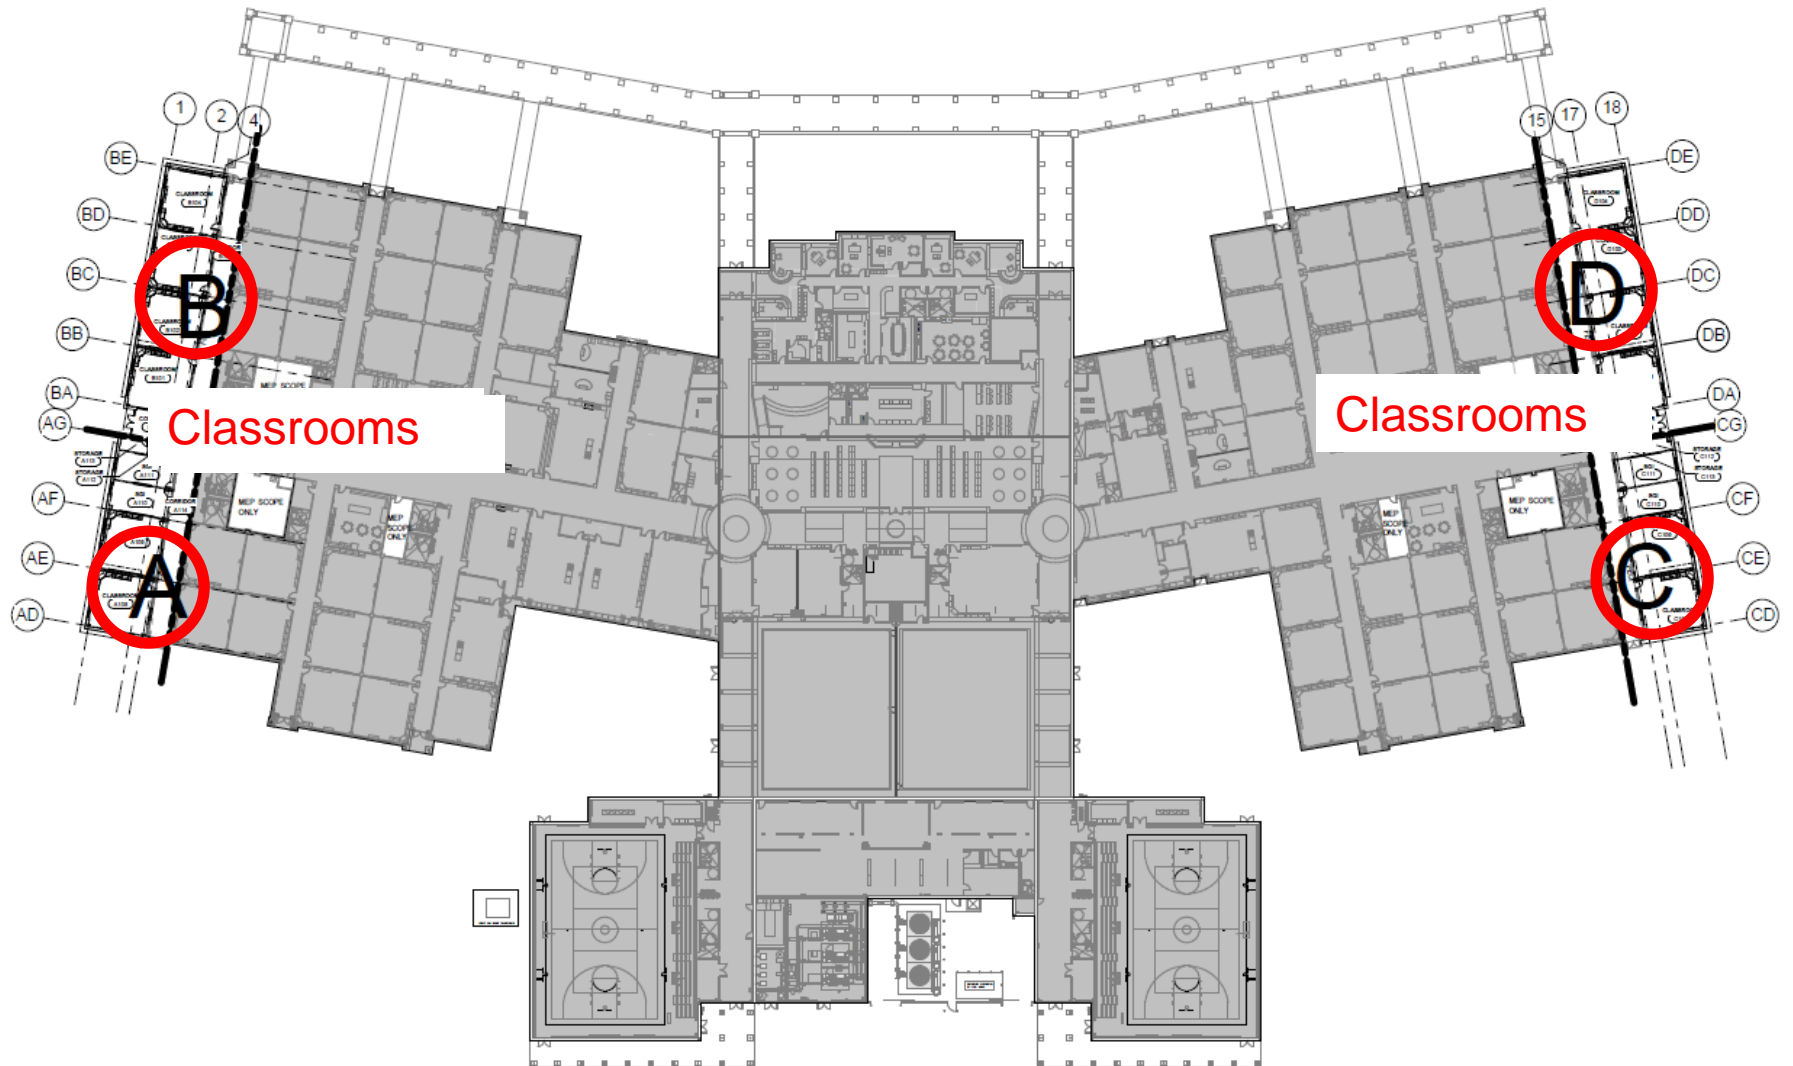

ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS

Classroom Addition East Side



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



Classroom Addition West Side

ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



Area A&B – Adjacent Classrooms Existing Corridor

BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



INTERMEDIATE SCHOOL SOUTH



W 31° 21' 42" E
1350.07'

OVERFLOW PARKING
FACULTY/STAFF PARKING (SEE CAMPUS)
WELDING WIRE FENCE
PLAY FIELD
WELDING WIRE FENCE

CLACKING
275' DAPS

SERVICE
CANOPY

INTRO
CANYON

RECEIVING
COURTYARD

LOI

RESOURCES
MEDIA

FINE ARTS

PEACE

GYM

ADMIN

1ST FLOOR

2ND FLOOR

3RD FLOOR

4TH FLOOR

5TH FLOOR

6TH FLOOR

7TH FLOOR

8TH FLOOR

9TH FLOOR

10TH FLOOR

11TH FLOOR

12TH FLOOR

13TH FLOOR

14TH FLOOR

15TH FLOOR

16TH FLOOR

17TH FLOOR

18TH FLOOR

19TH FLOOR

20TH FLOOR

21ST FLOOR

22ND FLOOR

23RD FLOOR

24TH FLOOR

25TH FLOOR

26TH FLOOR

27TH FLOOR

28TH FLOOR

29TH FLOOR

30TH FLOOR

31ST FLOOR

32ND FLOOR

33RD FLOOR

34TH FLOOR

35TH FLOOR

36TH FLOOR

37TH FLOOR

38TH FLOOR

39TH FLOOR

40TH FLOOR

41ST FLOOR

42ND FLOOR

43RD FLOOR

44TH FLOOR

45TH FLOOR

46TH FLOOR

47TH FLOOR

48TH FLOOR

49TH FLOOR

50TH FLOOR

51ST FLOOR

52ND FLOOR

53RD FLOOR

54TH FLOOR

55TH FLOOR

56TH FLOOR

57TH FLOOR

58TH FLOOR

59TH FLOOR

60TH FLOOR

61ST FLOOR

62ND FLOOR

63RD FLOOR

64TH FLOOR

65TH FLOOR

66TH FLOOR

67TH FLOOR

68TH FLOOR

69TH FLOOR

70TH FLOOR

71ST FLOOR

72ND FLOOR

73RD FLOOR

74TH FLOOR

75TH FLOOR

76TH FLOOR

77TH FLOOR

78TH FLOOR

79TH FLOOR

80TH FLOOR

81ST FLOOR

82ND FLOOR

83RD FLOOR

84TH FLOOR

85TH FLOOR

86TH FLOOR

87TH FLOOR

88TH FLOOR

89TH FLOOR

90TH FLOOR

91ST FLOOR

92ND FLOOR

93RD FLOOR

94TH FLOOR

95TH FLOOR

96TH FLOOR

97TH FLOOR

98TH FLOOR

99TH FLOOR

100TH FLOOR

Faculty Parking Lot
Front Parking Area



**Building Pad: Structural Slab &
Grade Beams in Progress**

Intermediate School South Aerial Site Plan

BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH




BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH - SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN

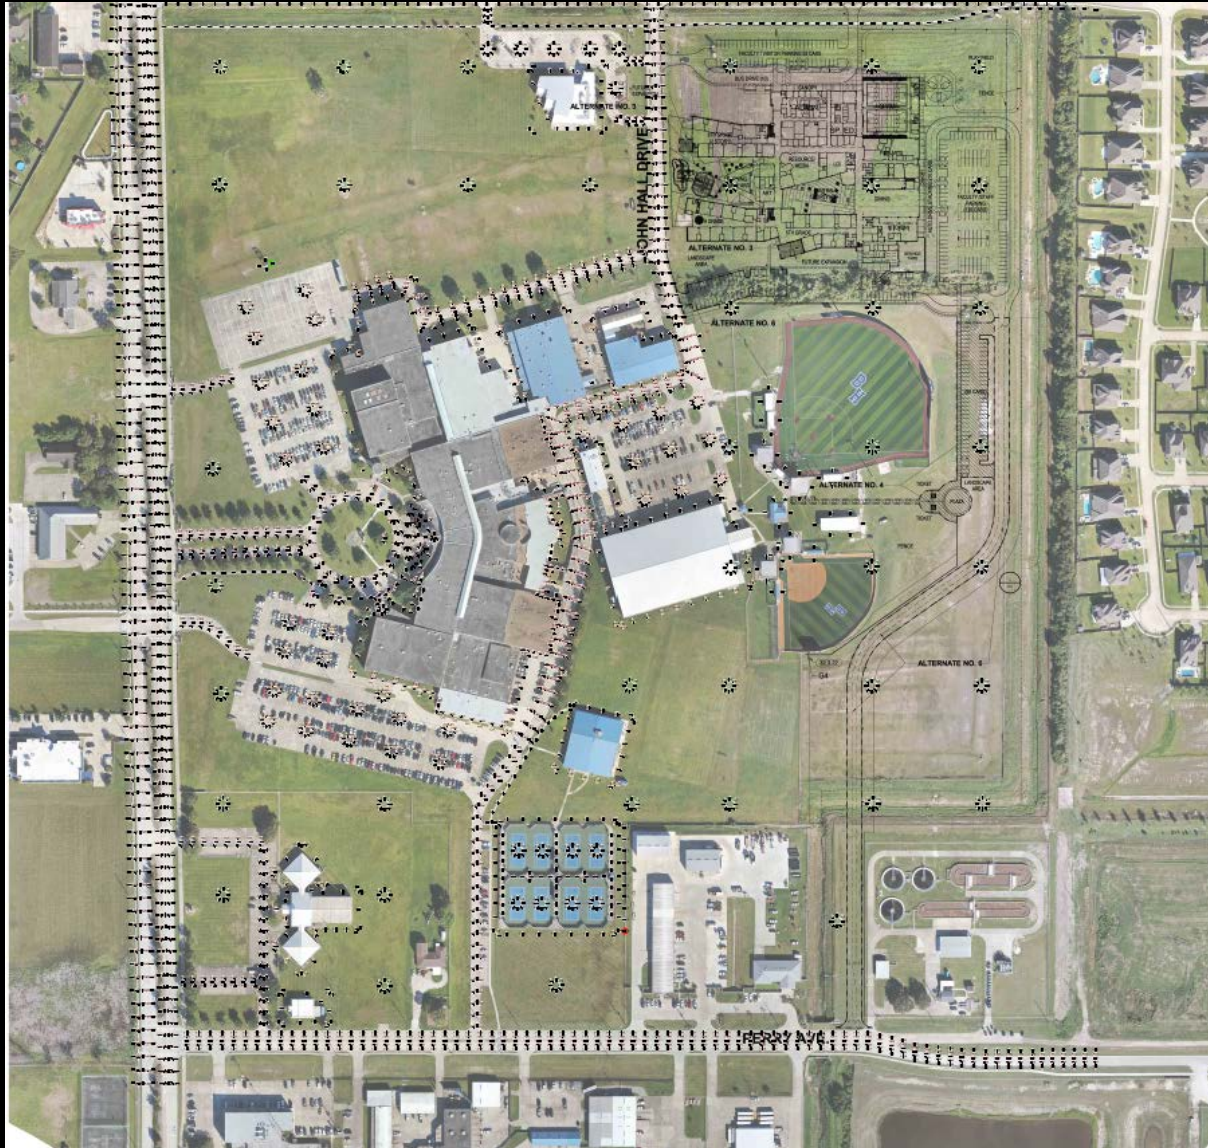

ISN Entrance off Perry Rd.



New BB/SB Parking / ISS Drive Paving



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH




BOND 2020 – INTERMEDIATE SCHOOL NORTH




Structural Steel Erection in Progress / Grade Beam
Excavations in Preparation for Structural Slab Pour

REPLACE CHAINLINK IN LEFT/RIGHT FIELD CORNERS WITH MATCHING METAL FENCING TO ALLEVIATE HITTERS SEEING INTO PARKING LOT THROUGH CURRENT CHAINLINK: 2-23-21

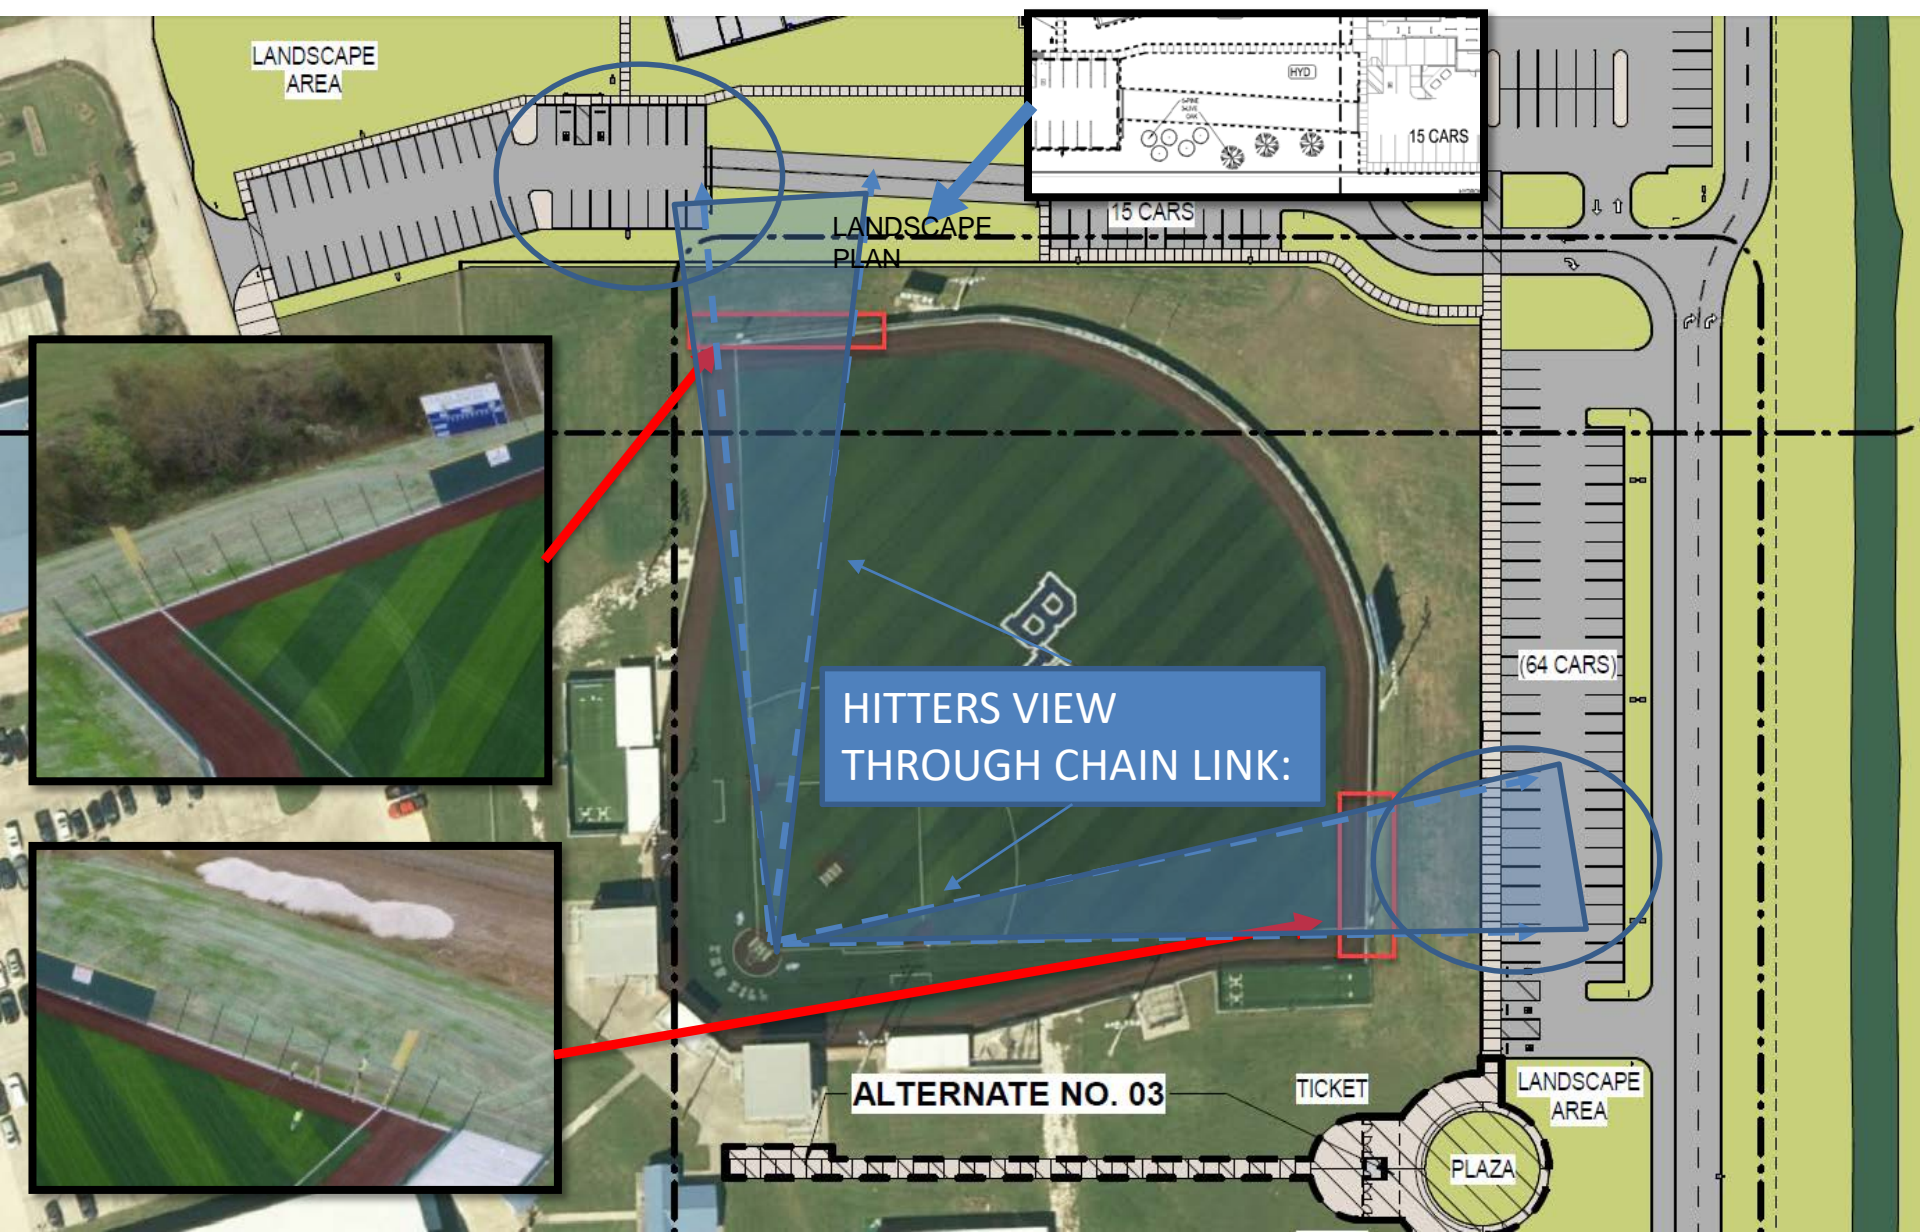



REPLACE CHAINLINK FENCE
WITH METAL PANEL FENCE
TO MATCH EXISTING &
REPAINT ALL.



THANK YOU

