



Projects Update

June 28, 2021

Bond 2017 Project:
Leadership Support Center

Bond 2020 Projects:
ES North Classroom Addition
ES South Classroom Addition

Bond 2020 Projects:
Intermediate School North
Intermediate School South

Additional Summer Projects:
District-Wide



PROJECT SCHEDULE

COMPLETE - Package 1: Demolition, Earthwork, Building Pad and Underground Utilities

- Demolition – Complete

January 15th – March 15th 2020

COMPLETE - Package 2: Foundation, Structural Steel Purchase and MEP Underslab

- Building Pad: Completed on Schedule:
- Drill & Pour Foundation Piers/Grade Beams Complete:
 - *PCI to give status update of project time line*

Package 3: Remaining Building Package

- Construction Documents Issue for Proposal: Complete April 6th 2020
- Issue for Permit: Complete April 9th 2020
- Develop GMP present to BOT for Approval/Award: Complete May 18th 2020
- Construction Start - Substantial Completion: May 19th 2020 - June 15th 2021
- Move – In: July 16th 2021



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



Slate Roof Shingles installation in Progress



BOND 2017 – LEADERSHIP SUPPORT CENTER



Slate Roof Shingles installation in Progress

BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



Board Room Front Entry Lobby

BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER




BOND 2017 – LEADERSHIP SUPPORT CENTER



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS

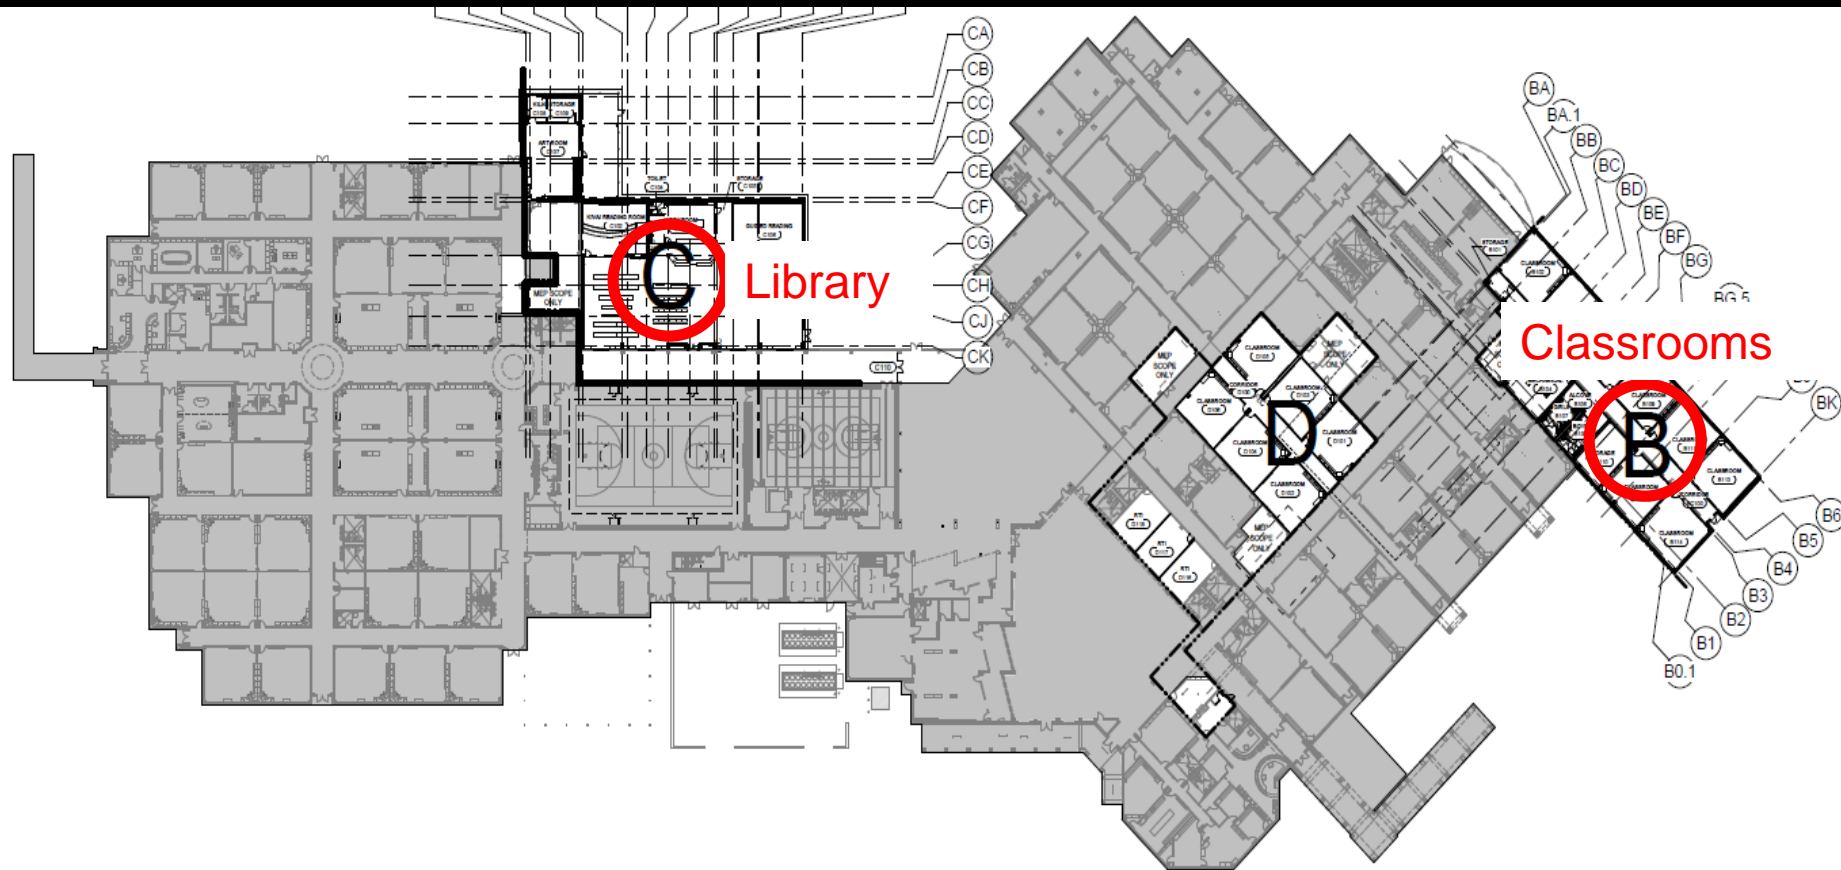

PHASING SCHEDULE

PHASE 1: AREA B & C
WORK TO BEGIN SUMMER 2020

PHASE 2: AREA D
WORK TO BEGIN SUMMER 2021

ELEMENTARY SCHOOL SOUTH - LIBRARY ADDITION



ELEMENTARY SCHOOL SOUTH - LIBRARY ADDITION



ELEMENTARY SCHOOL SOUTH CLASSROOMS ADDITION



Area B – Typical Classroom

ELEMENTARY SCHOOL SOUTH CLASSROOMS ADDITION




ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY NORTH ADDITIONS

ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS

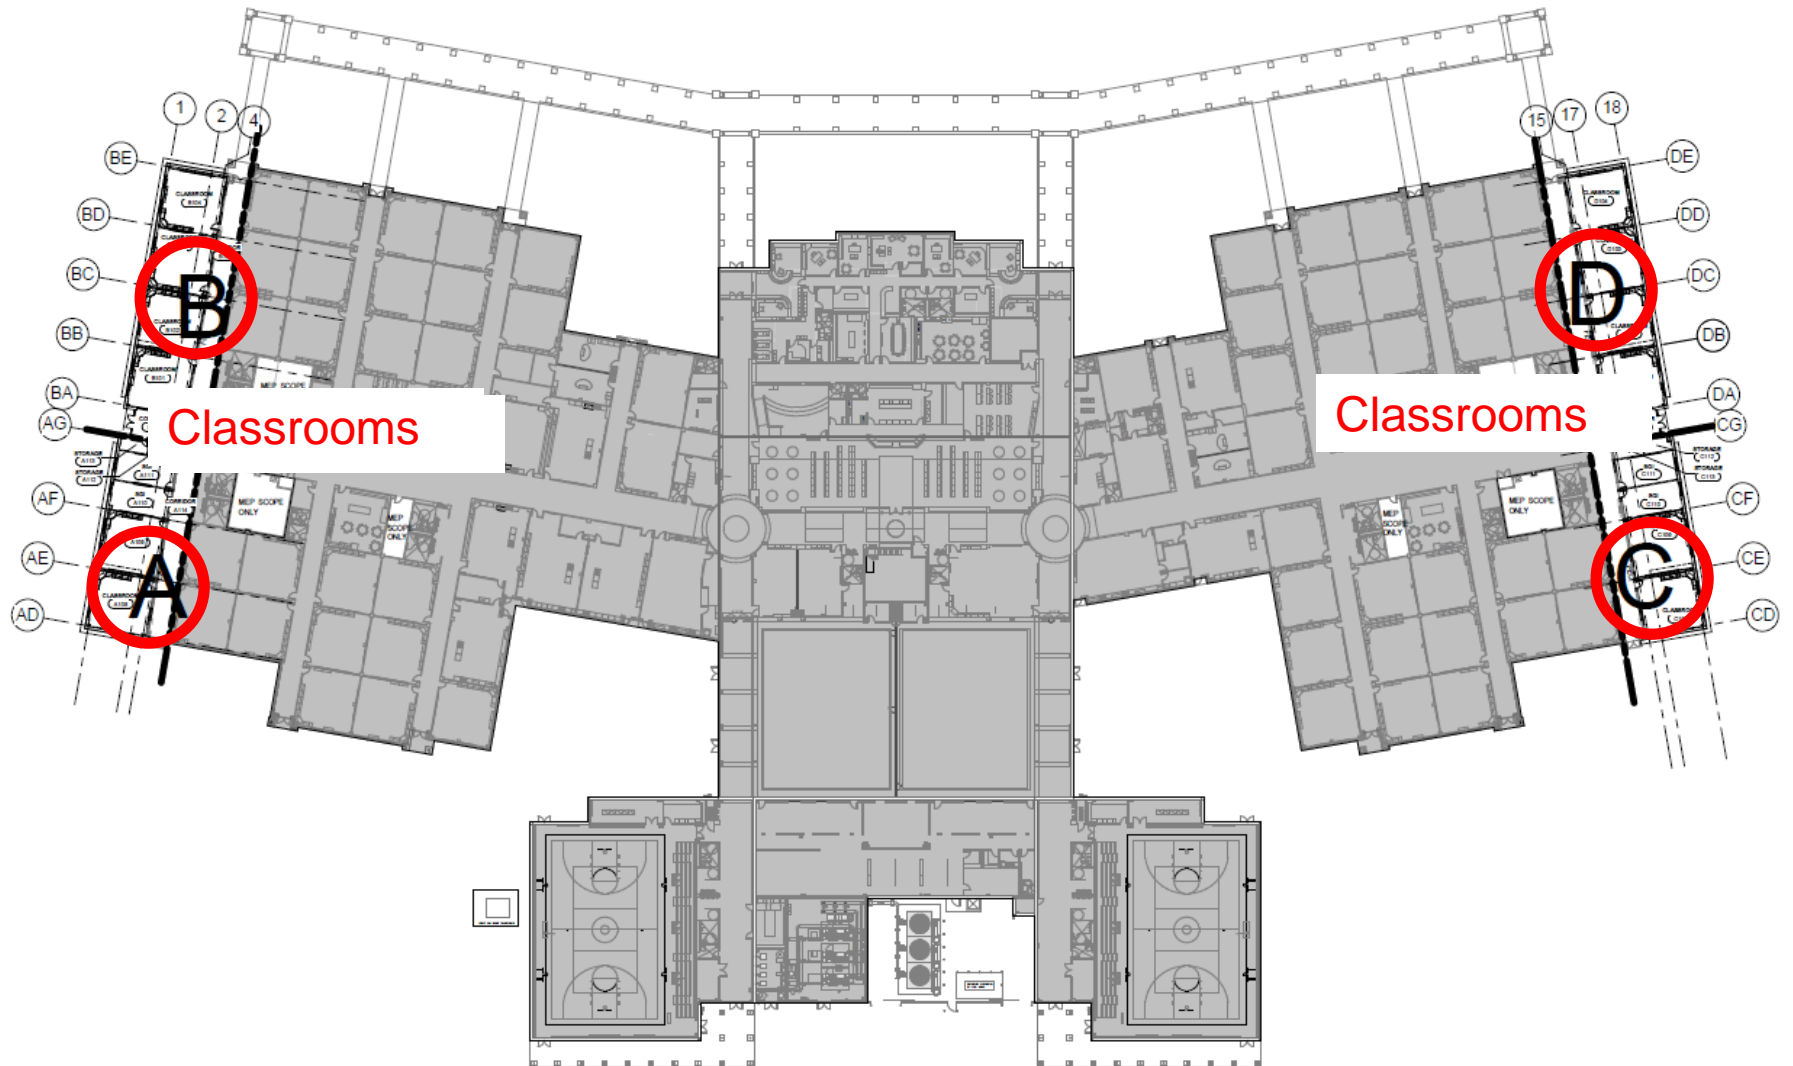

ELEMENTARY SCHOOL NORTH CLASSROOMS ADDITION



BOND 2020 – High School Renovations




HIGH SCHOOL RENOVATIONS

BOND 2020 – INTERMEDIATE SCHOOL NORTH - SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN

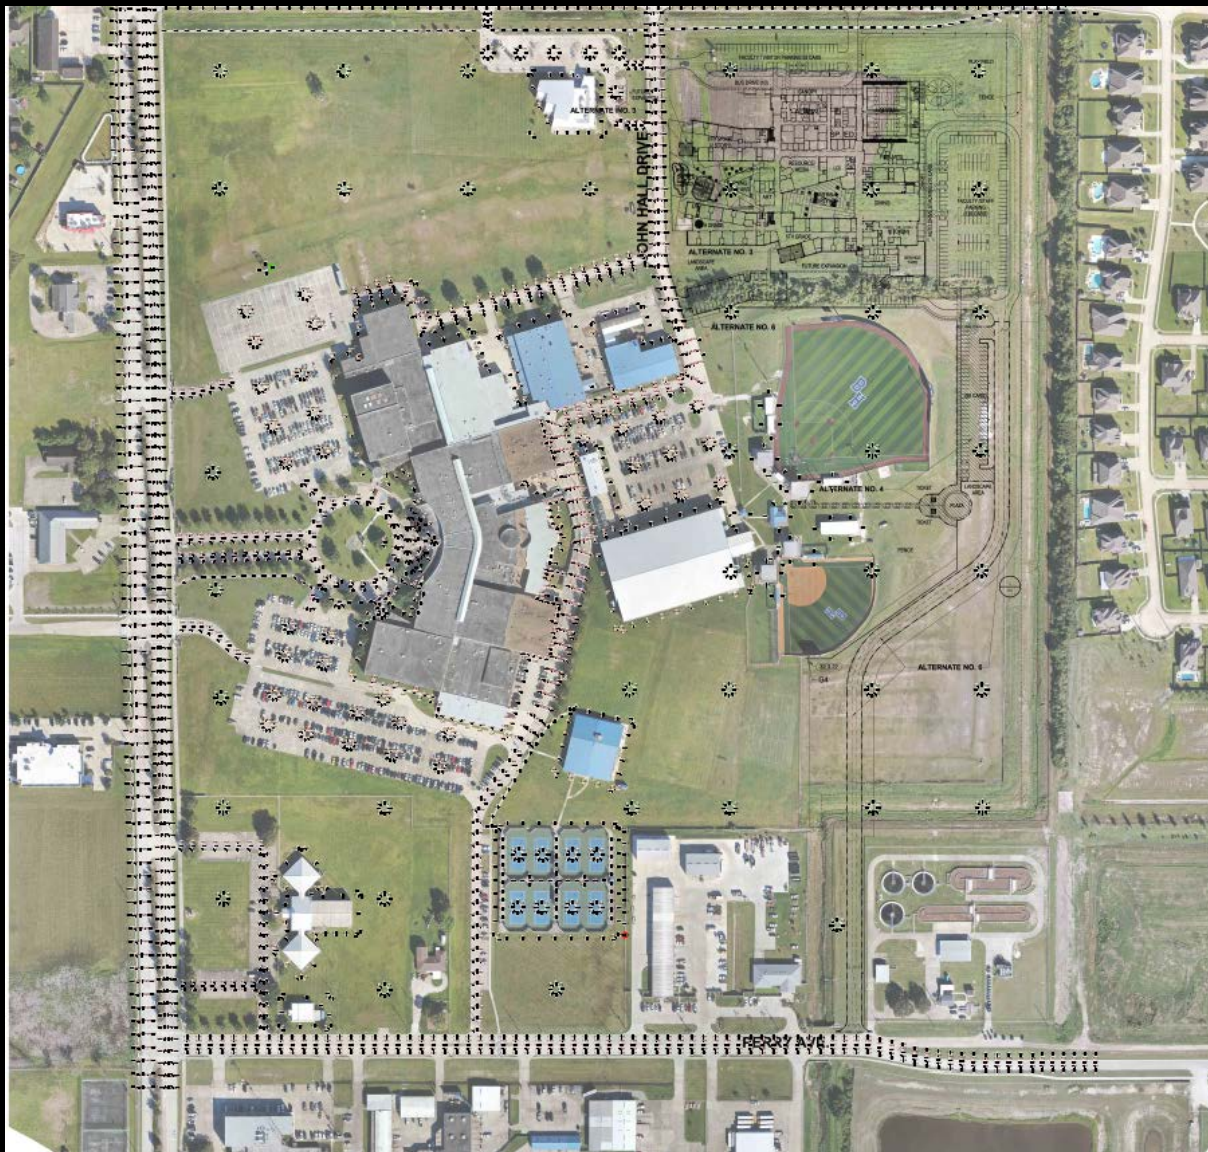

BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL NORTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



INTERMEDIATE SCHOOL SOUTH



[illegible]

BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH




BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH – FF&E PROGRAMMING

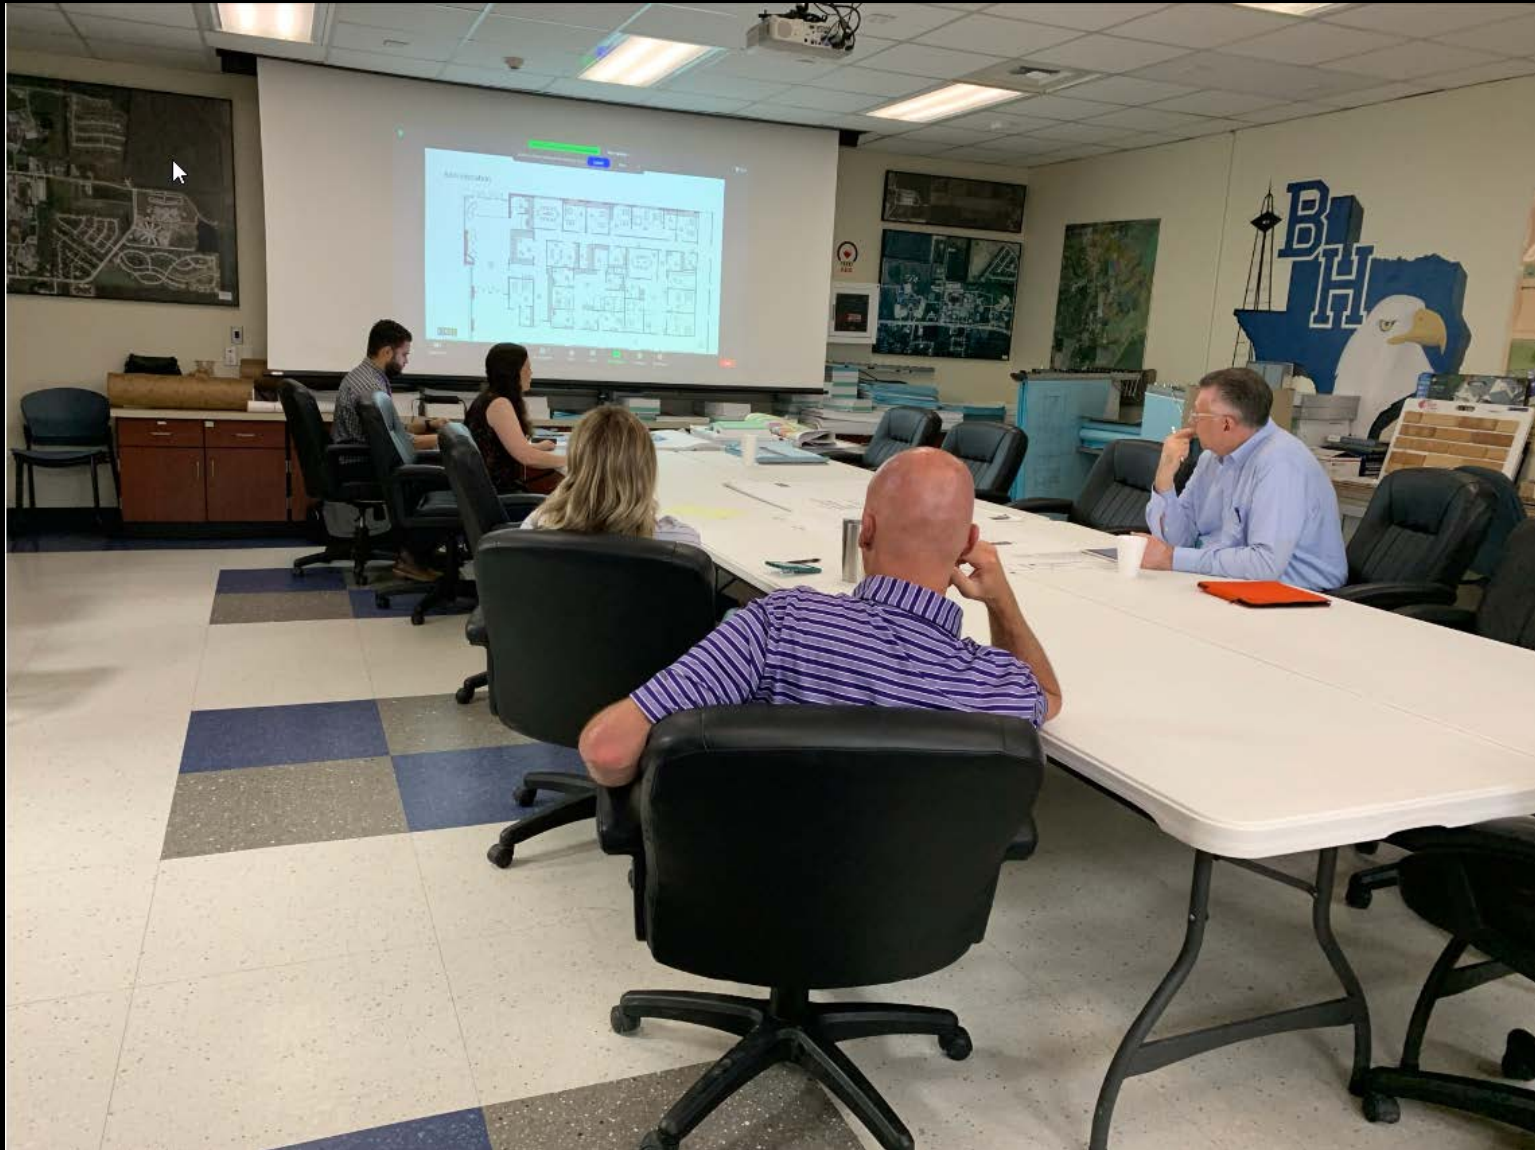

ADDITIONAL SUMMER PROJECTS: BOND 2020



BOND 2020 – Auxiliary Field Overhead Power Relocation – Visitor Bleacher Pad Location



JOC PROJECT CONSTRUCTION MASTERS HOUSTON

BOND 2020 – Auxiliary Field Overhead Power Relocation



BOND 2020 – Auxiliary Field Overhead Power Relocation



BOND 2020 – Auxiliary Field Press Box Renovations



BOND 2020 – Auxiliary Field Press Box Renovations



LMB Steel & CMHOU Weatherproofing & Re-skinning Press Box
Metal Siding



BOND 2020 – Auxiliary Field Press Box Renovations



LMB Steel & CMHOU Weatherproofing & Re-skinning Press Box
Metal Siding



BOND 2020 – Auxiliary Field Press Box Renovations – Bleacher Pad for New SturdiSteel Bleachers



JOC PROJECT CONSTRUCTION MASTERS HOUSTON

Home-side Bleacher Pad Ready for New SturdiSteel Bleachers:
Schedule – installation crew set to begin July 12th



BOND 2020 – High School Summer Renovations for Flooring & Painting



JOC PROJECT CHATHAM CONSTRUCTION



Removing Carpet Typical Corridor



BOND 2020 – High School Summer Renovations



BOND 2020 – High School Summer Renovations



BOND 2020 – High School Summer Renovations



BOND 2020 – High School Summer Renovations



BOND 2020 – MSN Kitchen Flooring Summer Renovations



JOC PROJECT CHATHAM CONSTRUCTION



Kitchen Flooring to be Replaced



BOND 2020 – MSN Kitchen Flooring Summer Renovations



BOND 2020 – MSN Kitchen Flooring Summer Renovations



BOND 2020 – MSN Kitchen Flooring Summer Renovations



New Epoxy Kitchen Floor

BOND 2020 – MSN Kitchen Flooring Summer Renovations



New Epoxy Kitchen Floor

BOND 2020 – MSN Competition Gym New HVAC Roof-Top Units (2) & Associated Ductwork:



JOC PROJECT CONSTRUCTION MASTERS HOUSTON

New Roof Top Curbs Preparing to Install for HVAC Units

BOND 2020 – MSN Competition Gym New HVAC Roof-Top Units (2) & Associated Ductwork:



New Roof-Top HVAC Unit Being Installed

BOND 2020 – MSN Competition Gym New HVAC Roof-Top Units (2) & Associated Ductwork:




New Roof-Top HVAC Unit Being Installed

BOND 2020 – MSN Competition Gym New HVAC Roof-Top Units (2) & Associated Ductwork:



New Ductwork for Southside Roof-Top Unit (before painting)

BOND 2020 – MSN Competition Gym New HVAC Roof-Top Units (2) & Associated Ductwork:

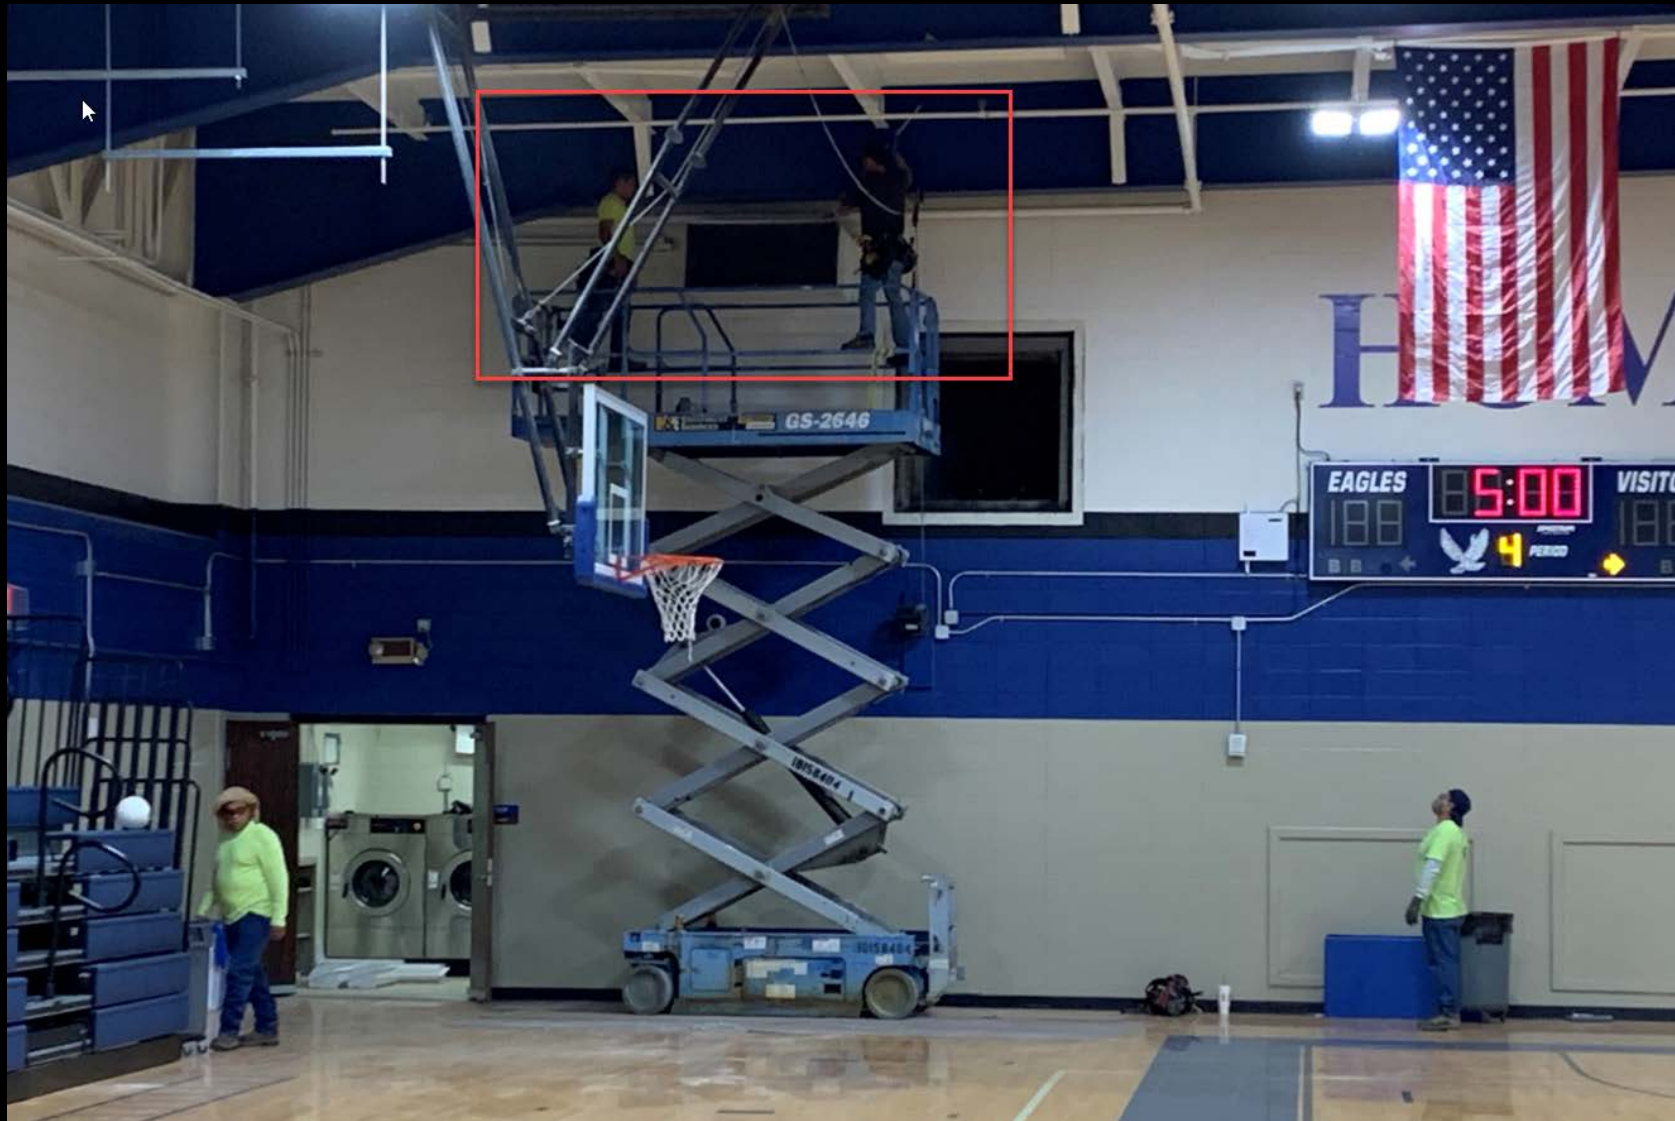

New Ductwork for Northside Roof-Top Unit Getting Started

BOND 2020 – Auxiliary Field New Scoreboard (Sponsored by BHISD Education Foundation)




Schedule: Demo existing scoreboard 7-6; Install new structural beams 8-6; New Scoreboard installed 8-9

BOND 2020 – New Hellas Construction Artificial Turf Eagle Stadium



New Turf Approved Color Rendering

BOND 2020 – New Hellas Artificial Turf Eagle Stadium

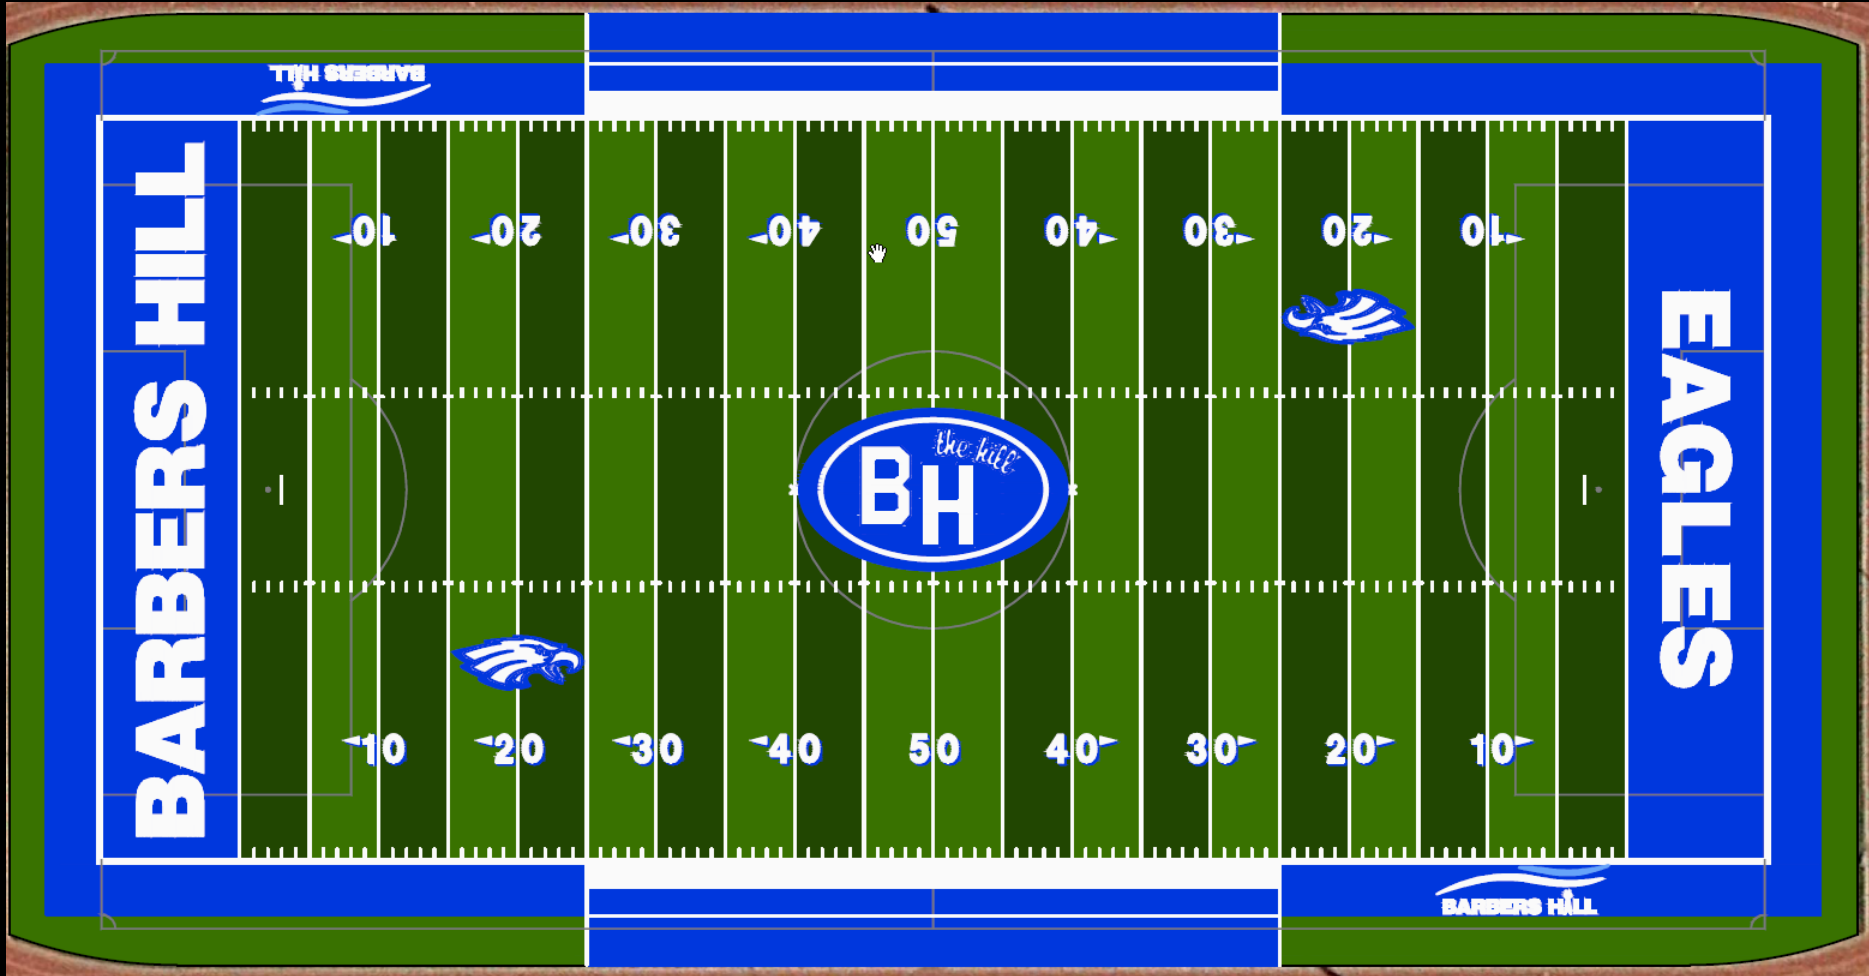

New Turf Approved Color Rendering

BOND 2020 – New Hellas Artificial Turf Eagle Stadium



Schedule: Hellas now has all materials on site. This week the Cushdrain® shock attenuation pad will be installed & next week turf installation will start. Per Hellas today despite the Force Majeure notice on Polyurethane binder, the project is back on schedule.

BOND 2020 – New Hellas Artificial Turf Eagle Stadium




Schedule: Hellas now has all materials on site. This week the Cushdrain[®] shock attenuation pad will be installed & next week turf installation will start. Per Hellas today despite the Force Majeure notice on Polyurethane project is back on schedule.

BOND 2020 – New Hellas Artificial Turf Eagle Stadium



BOND 2020 – HS PRACTICE FIELD EXPANSION

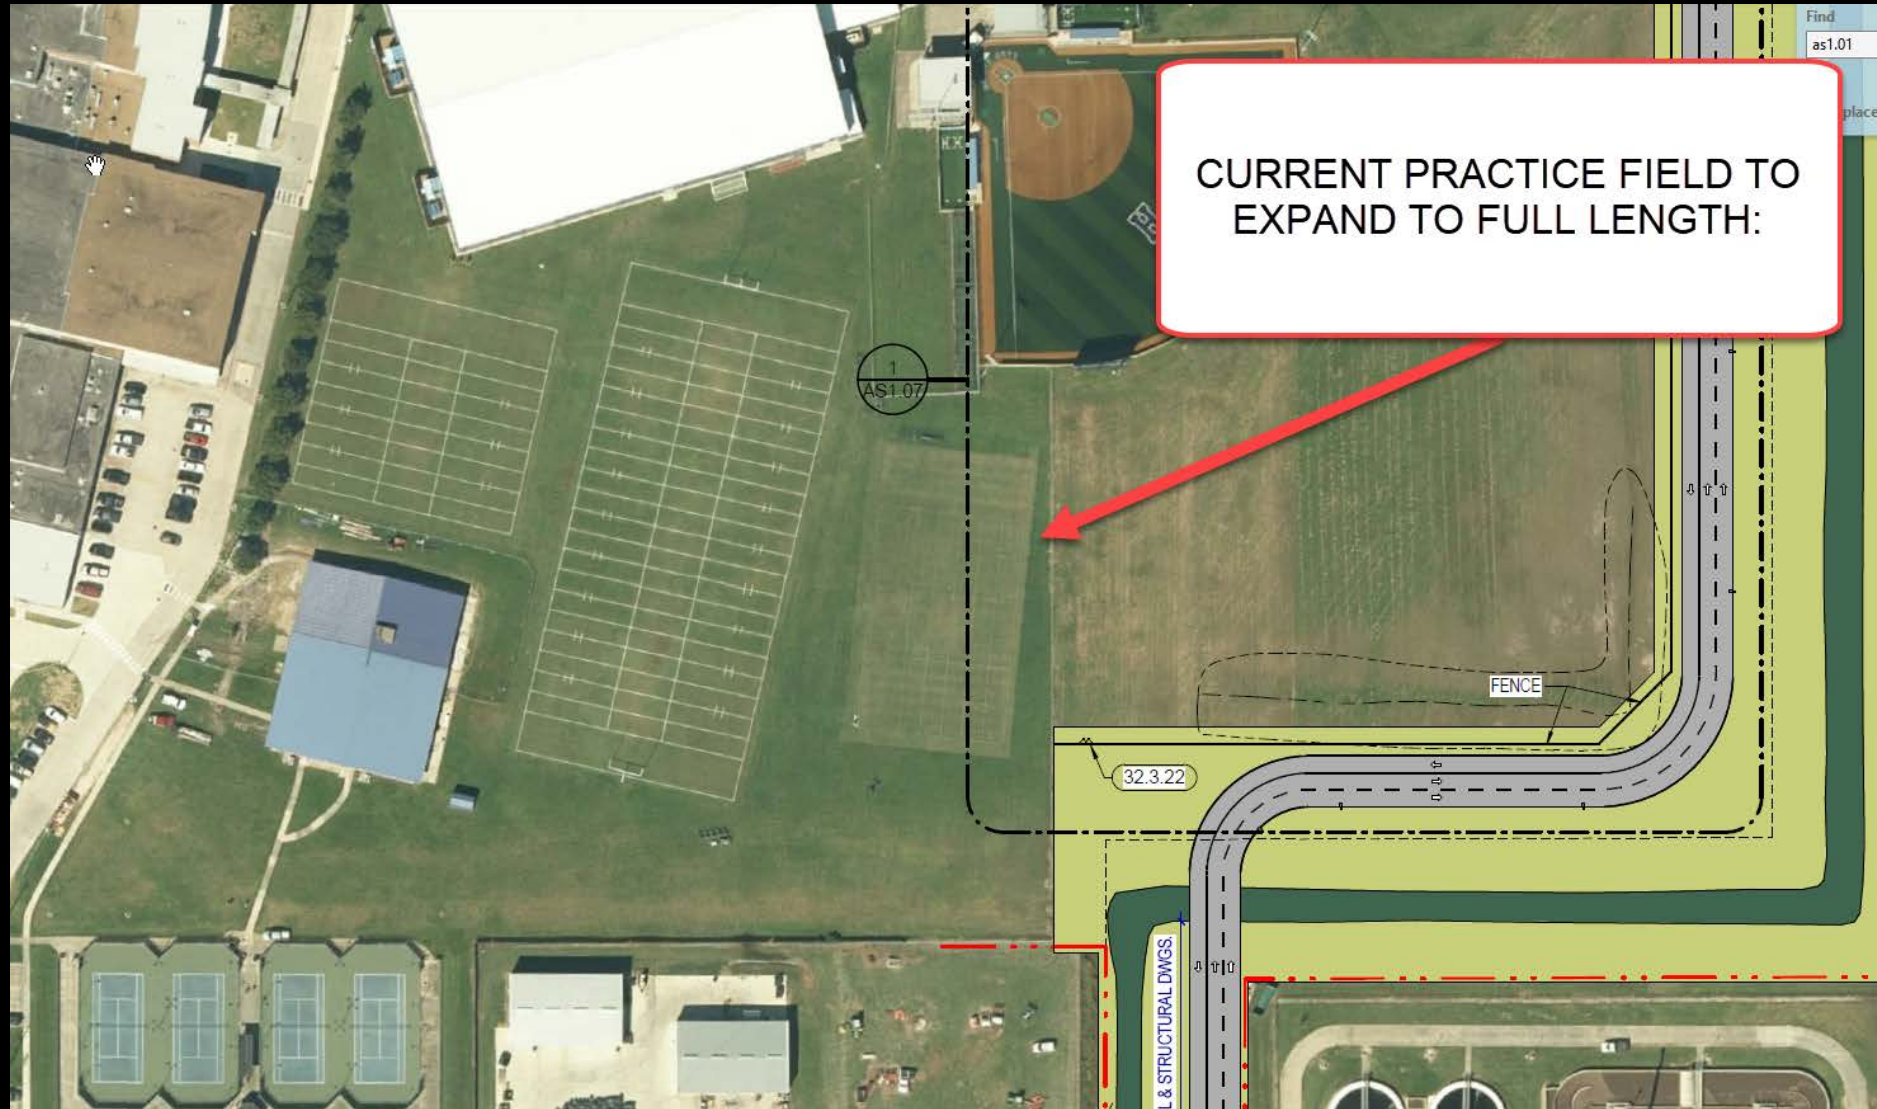

INTERLOCAL PURCHASING COOP FIELDERS CHOICE CONSTRUCTION

Expanding current partial field to full length and width:

BOND 2020 – HS PRACTICE FIELD EXPANSION



Expanding current partial field to full length and width:

BOND 2020 – HS PRACTICE FIELD EXPANSION




Expanding current partial field to full length and width:

BOND 2020 – HS PRACTICE FIELD EXPANSION



Expanding current partial field to full length and width:

Location of new Baseball Natural Grass Practice Infield:

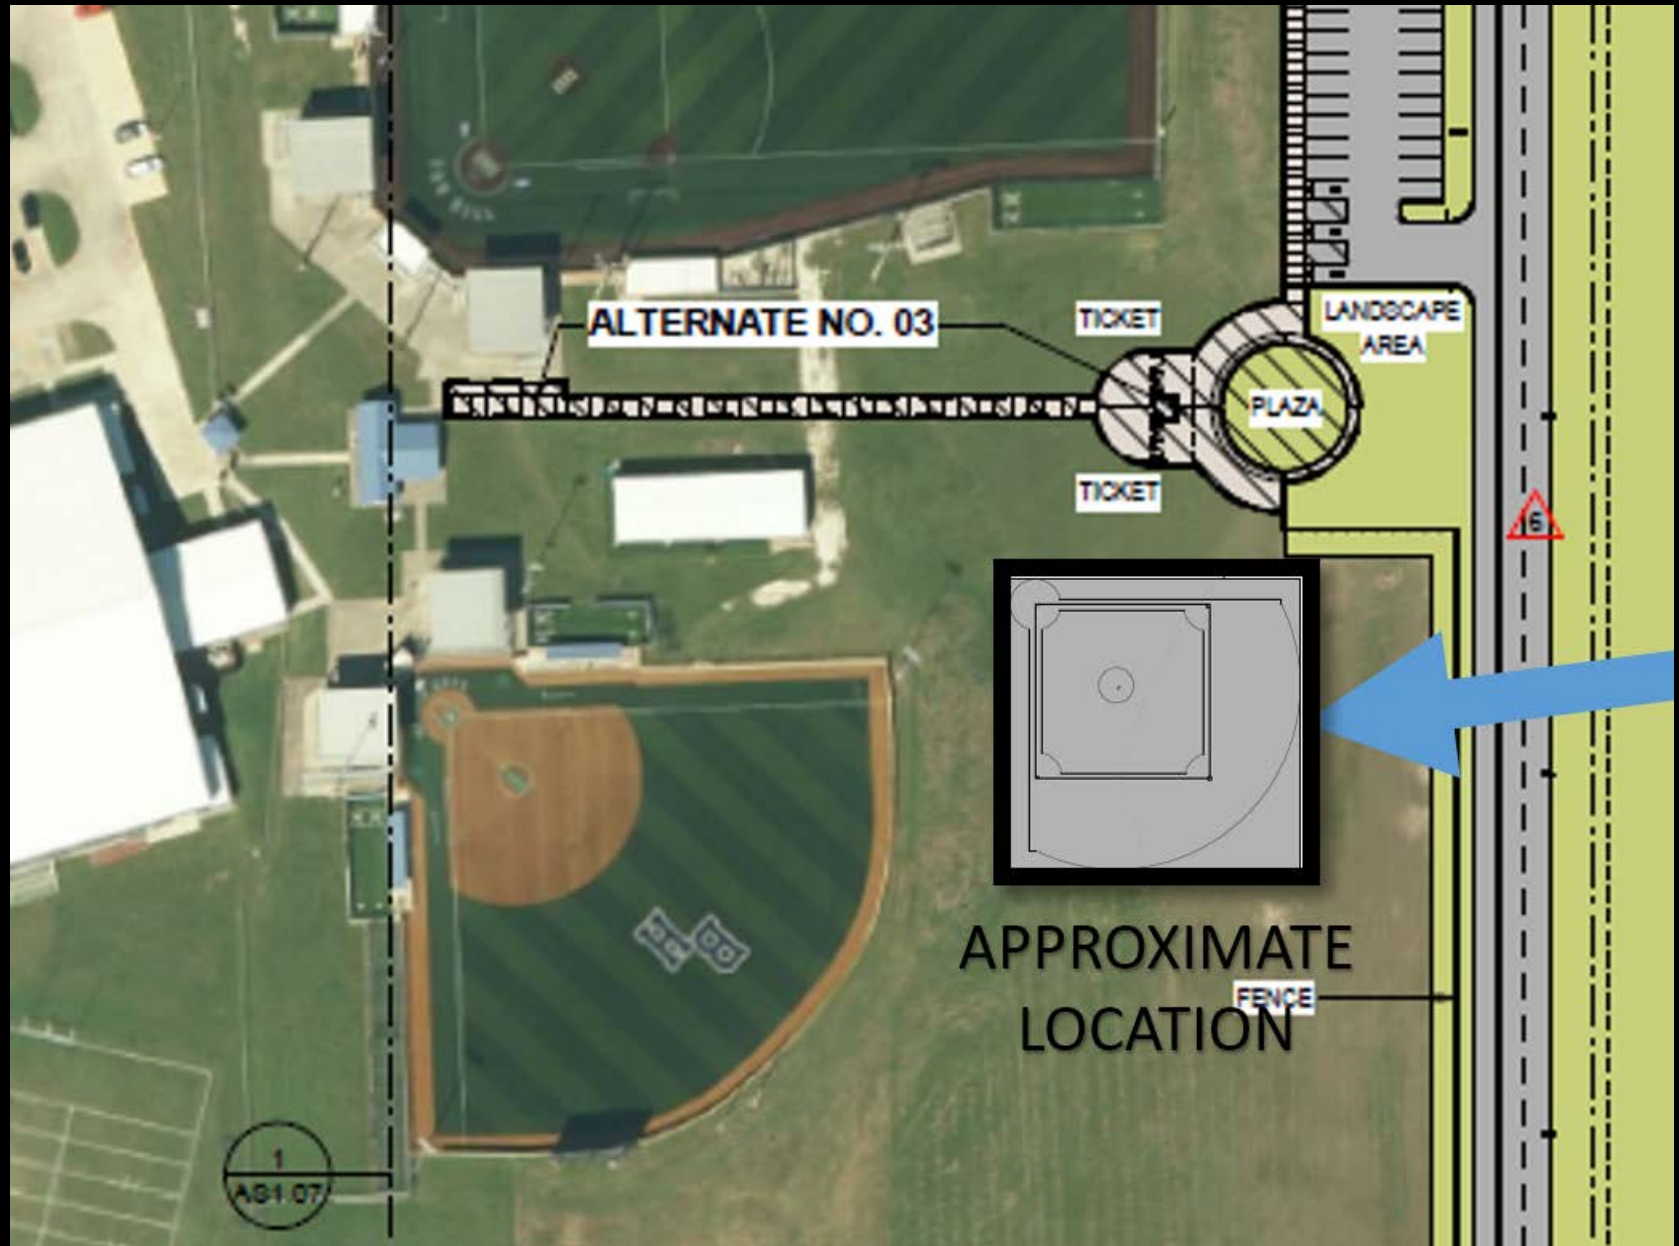

High School Competition Gym Floor Repairs



Schedule: Floor has been dried out, weather-proofing has occurred and repairs are scheduled to begin next week.

THANK YOU

