

# MINUTEMAN VOCATIONAL TECHNICAL REGIONAL HIGH SCHOOL PROGRESS

May 14<sup>th</sup>, 2018 – June 18<sup>th</sup>, 2018

**SKANSKA**

**Gilbane**

**KAESTLE BOOS**  
associates, inc  
architects

 **MINUTEMAN**  
A REVOLUTION IN LEARNING

## June 15th

View of Area A & B – North Elevation  
Exterior CMU walls completed.  
Window blocking and column  
enclosures in progress



## June 18th

View of Area A & B – East Elevation  
Exterior framing and sheathing  
activities substantially comple



June 15<sup>th</sup>

View of Area A & B – Low & High Roof  
Roofing system substantially complete  
on all three levels of roof..



May 24<sup>th</sup>

View of Area A & B – Lower Level  
First section of slab on grade placed.  
Saw cutting of control joints in  
progress.



June 18<sup>th</sup>

View of Area A & B – Lower Level  
Insulation & vapor barrier being  
installed to support final slab on  
grade placement in Area A & B.




## June 18th

View of Area A & B – Lower Level  
Interior CMU wall construction & in-  
wall MEP's in progress.



## June 18th

View of Area A & B – Upper Level  
Interior wall layout complete.  
Overhead MEP's in progress

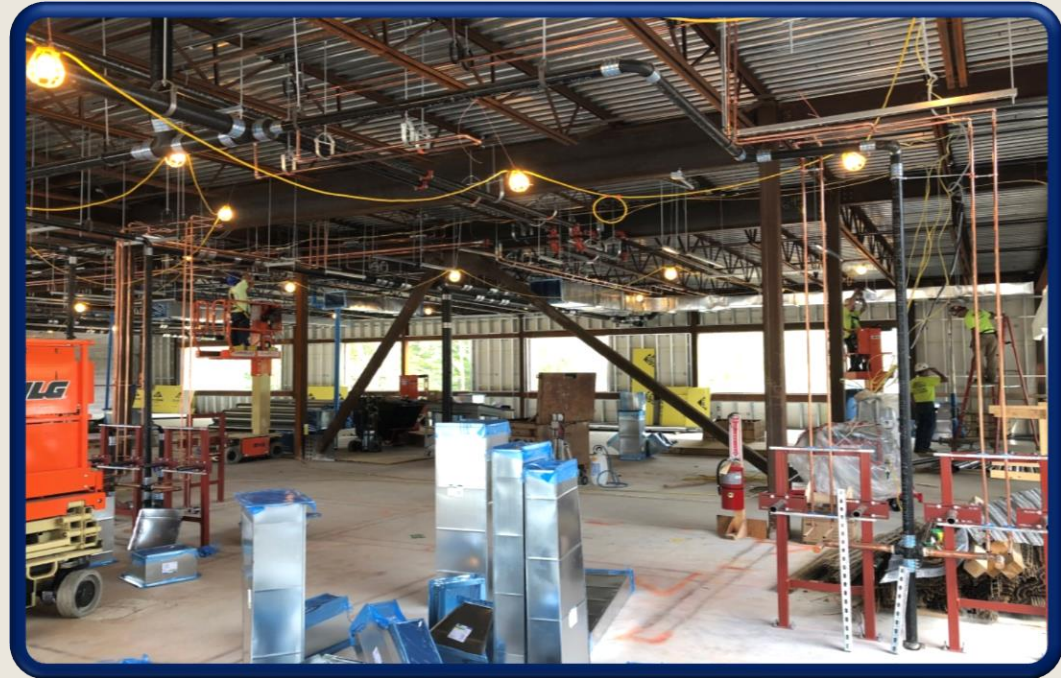

## June 15th

View of Area G – Facing North  
Exterior Framing, Sheathing and  
Waterproofing Activities in progress.



## June 18th

View of Area G – Roof Level  
Roofing assembly in progress,  
working from East to West.



June 15<sup>th</sup>

View of Area F – Lower Level  
Exterior wall framing & sheathing in  
progress.



June 18<sup>th</sup>

View of Area F – Roof Level  
Roof blocking for MEP equipment  
complete.  
Roof assembly in progress.





June 18<sup>th</sup>

View of Area D+E – South Elevation

All slab on deck placements completed.

Parapet Framing at Roof levels in progress.

Exterior wall lay-out and framing in progress.



June 15th

View of Area E – Lower Level  
Excavation & installation of  
underground utilities in progress.




June 18th

View of Area E – Bridge Level  
Placement & finishing of slab on deck  
in progress.





Main Entry Approach

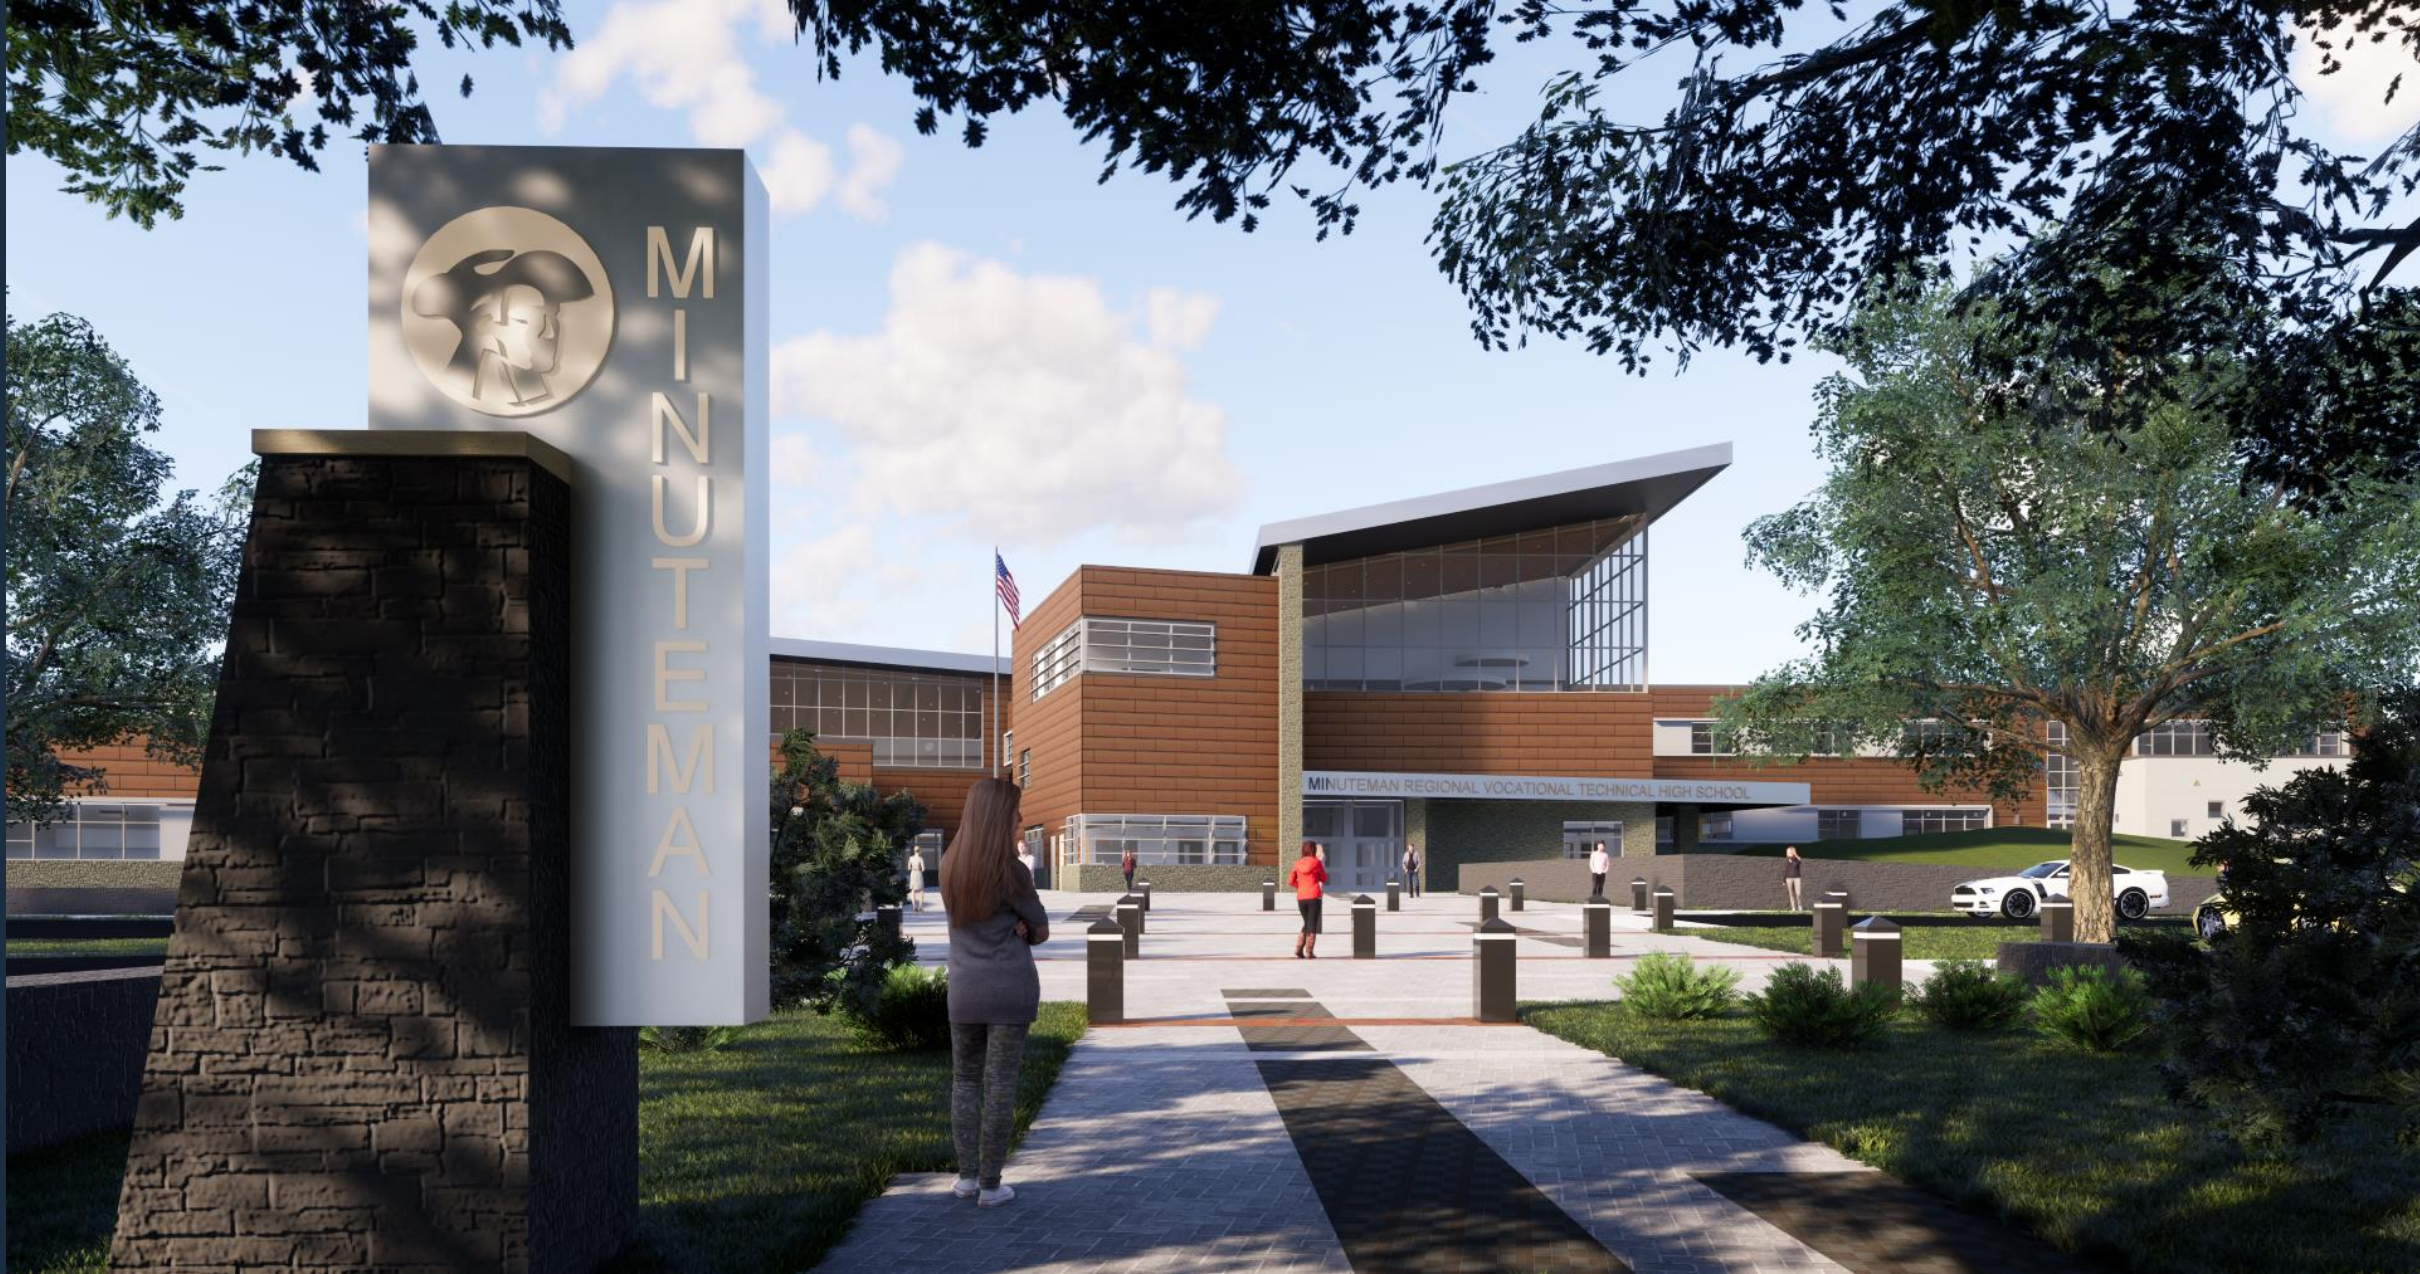

Main Entry Approach



Entry Hall



Entry Hall



Court Yard



Court Yard





Cafeteria



Cafeteria

# June Construction Schedule Look Ahead:

- **Area A+B**
  - Place final concrete slab on grade.
  - Complete exterior CMU masonry walls.
  - Continue with installation of overhead MEP's on Upper Level.
  - Continue with interior CMU masonry walls.
  - Continue with installation of waterproofing materials on exterior walls.
  - Commence steel fire proofing activities.
- **Area G**
  - Place concrete slab on grade.
  - Complete exterior LGMF framing walls on both floors.
  - Complete roofing installation activities.
  - Continue with installation of waterproofing materials on exterior walls.
  - Continue exterior CMU masonry walls and stairwell shafts.
  - Continue with installation of overhead MEP hangers on Upper Level.
- **Area E**
  - Continue with excavation and installation of underground utilities.
  - Continue with roof parapet framing and wood sheathing at Roof Level.
- **Area F**
  - Complete roofing installation activities.
  - Continue exterior LGMF framing walls on Lower Level.
  - Commence with installation of waterproofing materials on exterior walls.
- **Area D**
  - Continue roof parapet framing and wood sheathing.
  - Continue exterior LGMF framing walls.
  - Commence roofing installation activities.
- **Area C**
  - Complete steel decking and detailing activities in these remaining areas.
  - Place concrete slab(s) on grade.

