

MINUTEMAN VOCATIONAL TECHNICAL REGIONAL HIGH SCHOOL PROGRESS

July 15th 2019 – August 19th 2019

SKANSKA

Gilbane

KAESTLE BOOS
associates, inc
a r c h i t e c t s




MINUTEMAN
A REVOLUTION IN LEARNING

August 19th

View of Typical Classroom Spaces

Classrooms have been final cleaned and furniture installed.

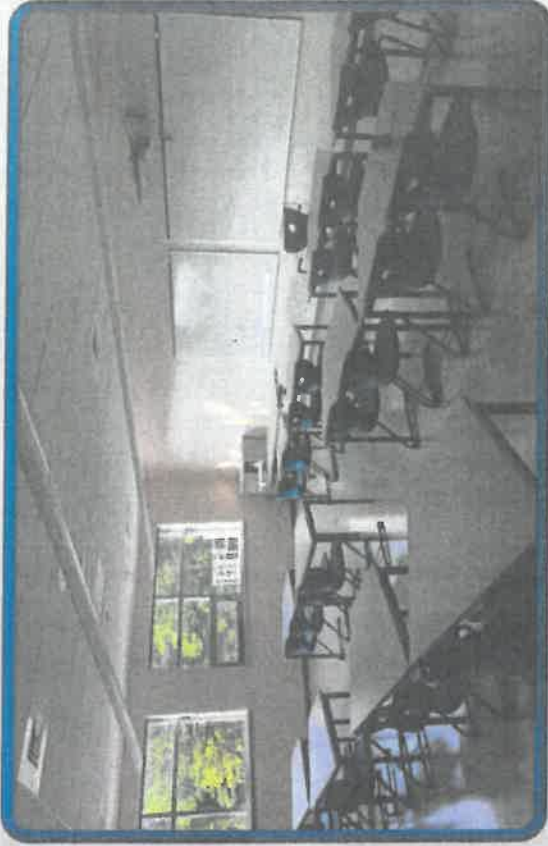

August 19th

View of Engineering Labs

Existing equipment has been relocated to the new building. Final MEP connections in progress



August 19th

View of Area D - Gymnasium


Bleacher construction complete.
Wall pad substantially complete.
Scoreboard installation complete.



August 19th

View of Area E – Upper Level

Media center furniture install
complete

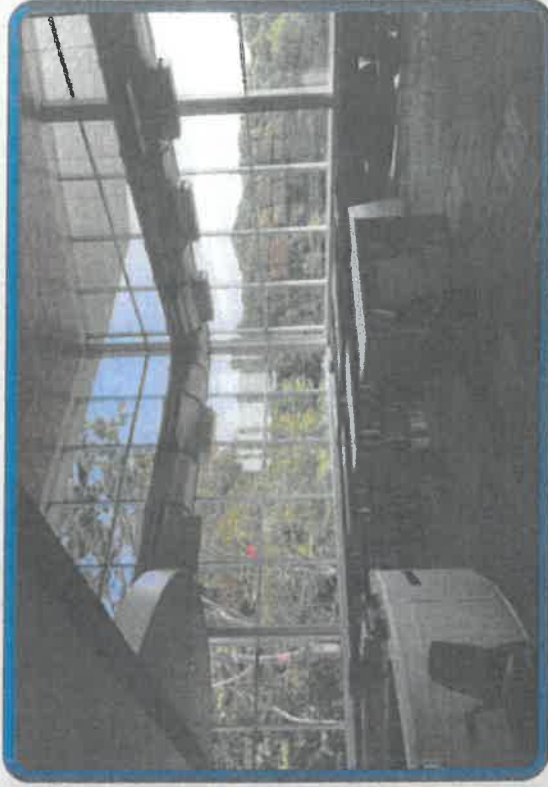

August 19th

View of Area E – Lower Level

Main entrance corridor.



August 19th

View of Area E+F - Cafeteria

Vinyl floor tile floor protection removed
& cleaned.


Audio Visual Assembly complete



August 19th

View of Area E+F - Lower Level


Kitchen Servery area complete & final
cleaned

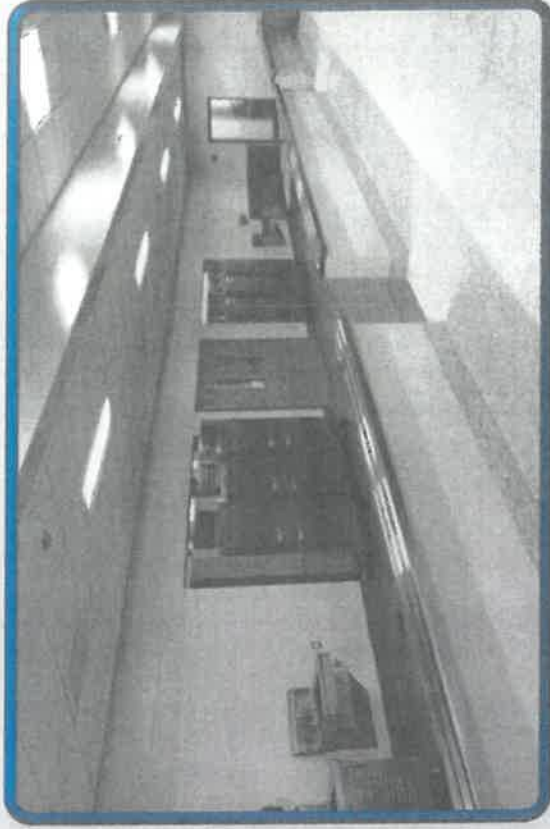

August 19th

View of Area F - Lower Level

Culinary Kitchen area equipment set &
connected. Space final cleaned

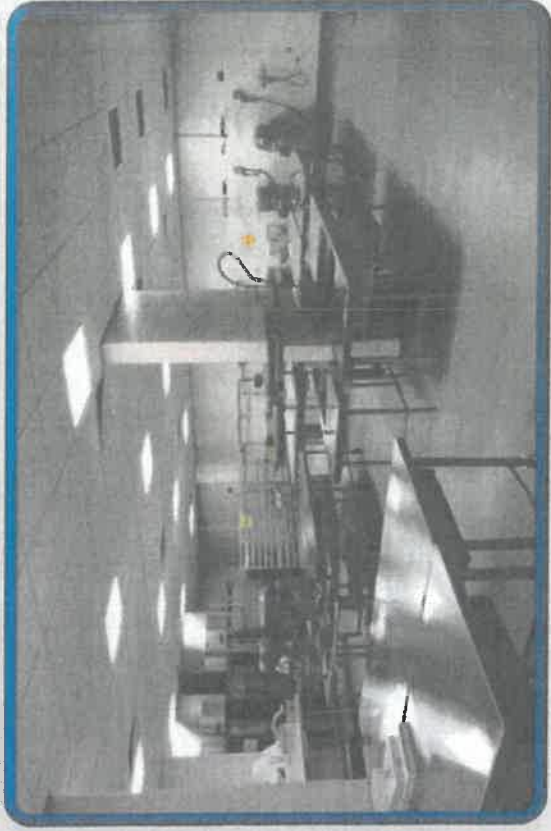

July 15th

View of Area F - Lower Level

Millwork & Flooring installation complete.
Spaces have been final cleaned.
Furniture being installed and set.



August 19th

View of Area C - Theater

Millwork panel installation
substantially complete.


Flooring at Stage & Pit Lift in
progress.

Cleaning of Upper Levels in progress



August 19th
View of Faculty Parking Lot

Landscaper pavers complete.
Plantings complete.
Sod & Seeding in progress

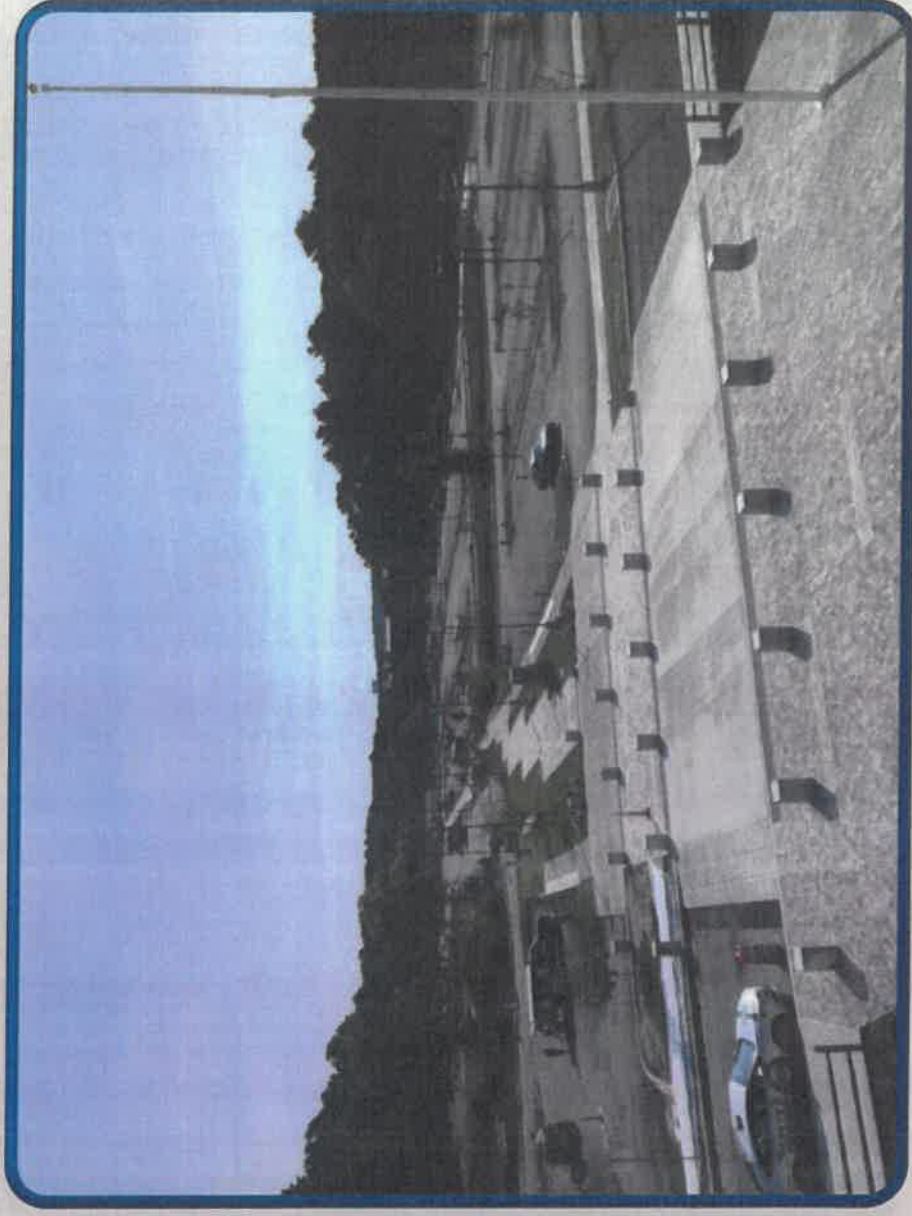

August 19th
View of Student Parking Lot

Radial sitting wall complete

Landscape pavers in progress


Cedar Post fence installation in progress



August 19th

View of Student Parking Lot

Binder Pavement Complete
Concrete sidewalks & plaza Complete
Planting Islands in progress

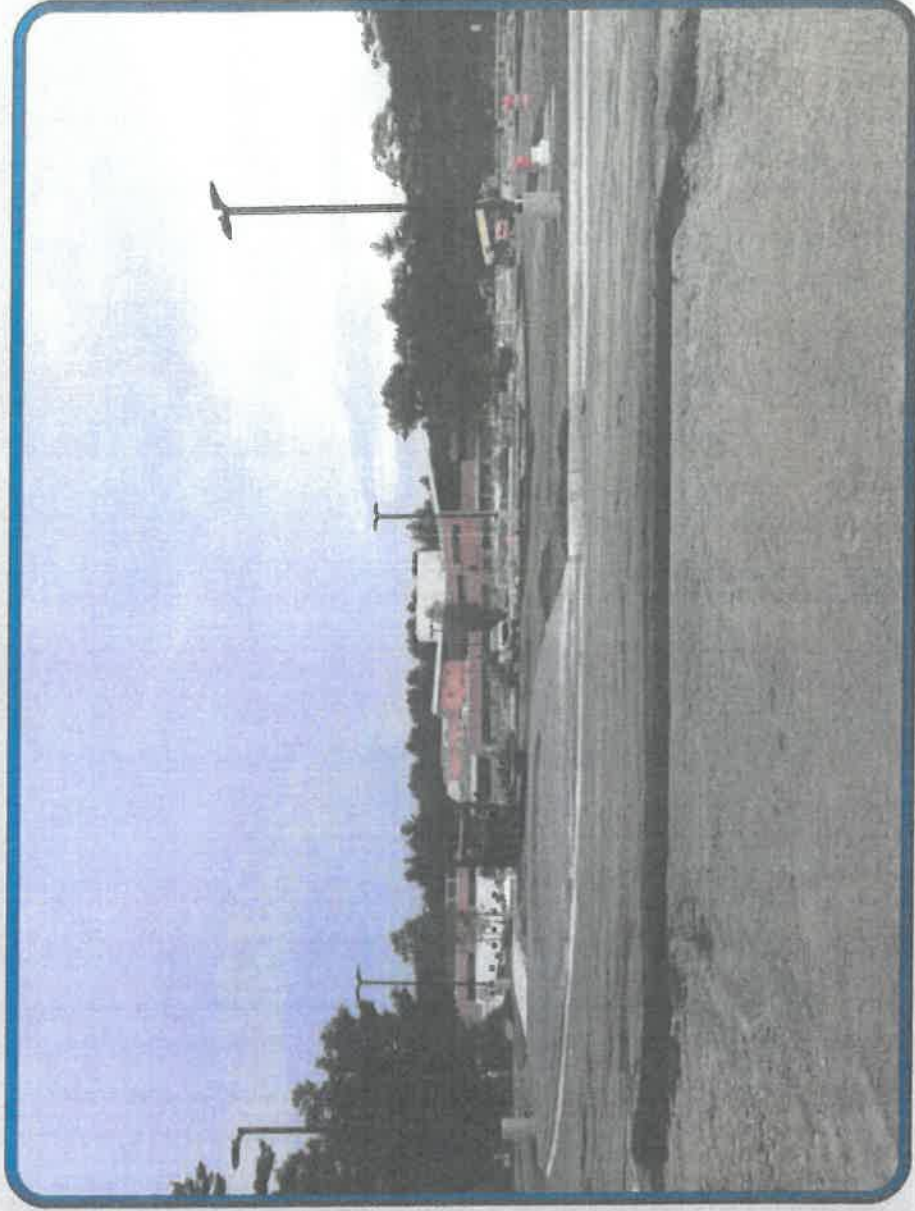

August 19th

View of Faculty Parking Lot

Landscape pavers complete

Planting installation complete



Project Turn-Over Schedule Look Ahead:

Activities	Start	End
New Furniture Delivery	7/8	7/26
Temp Certificate of Occupancy – STAFF	7/25	
Building Construction Punch List	7/26	9/24
Mover moves Administration	7/29	7/30
Administration Staff in New School	8/5	
Mover moves Shops & Classrooms:	7/29	8/15
Temp Certificate of Occupancy – STUDENTS	8/23	
Managers/Leads Return	8/26	8/28
ALL STAFF ORIENTATION	8/29	
Teachers Meeting & Student Orientations	9/3	
Teachers Meeting & Student Orientations	9/4	
ALL Students first day of school	9/5	
C of O – Substantial Completion	9/25	

