Indian Woods Middle School Construction Report 11/12/21



This Week

November 8th - November 12th

- Detailing structural steel
- Prepping metal deck for concrete



Site Overview

Next Week

November 15th - November 19th

- Pouring slab on deck
- Finish detailing structural steel
- Complete air barrier on mockup




Building Mock-up



Indian Woods Middle School

SHAWNEE MISSION SCHOOL DISTRICT

Construction Report 11/12/21

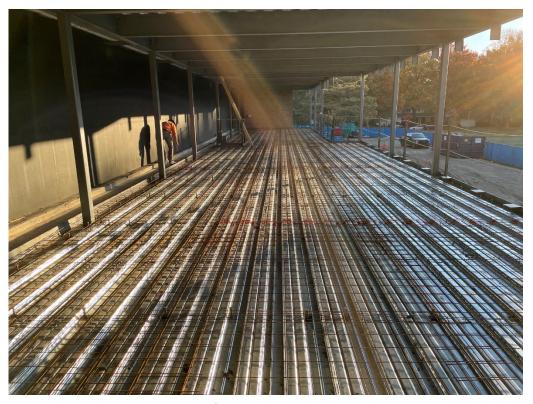

2nd Floor Metal Deck



3rd Floor Metal Deck



Indian Woods Middle School Construction Report 10/29/21



This Week

October 22nd - October 29th

Structure Steel Columns Installed on Addition



Door and Hardware Installation

Next Week

November 1st - November 5th

• Finish Setting Structural Steel



Steel Column Installation




Indian Woods Middle School Construction Report 10/01/21



This Week

September 27th - October 1st

- Restroom Renovations Are Completed and Turned Over to SMSD.
- Completed the Building Pad Fill.
- Installed the Clean Rock for the Slab-on-Grade.

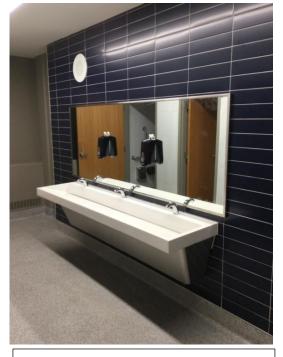

Toilet 120

Next Week

September 20th - September 24th


- Install Vapor Barrier and Mesh for Slab-on-Grade.
- Pour Slab-on-Grade



Slab-On-Grade Prep.



Indian Woods Middle School Construction Report 10/01/21

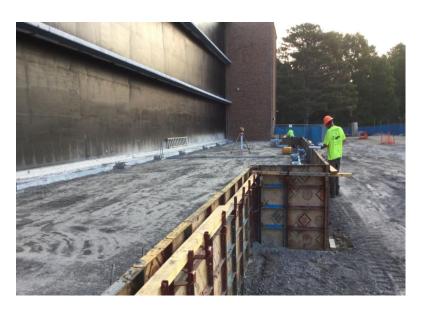

Building Pad Fill



Retaining Wall Footing



Electrical Rough-in



Stem Wall Formwork




Indian Woods Middle School Construction Report 09/17/21



This Week

September 13th - September 17th

- Installed Accessories in Toilet 121.
- Poured Footings for the Addition.
- Installed the Fire Line to the Building.

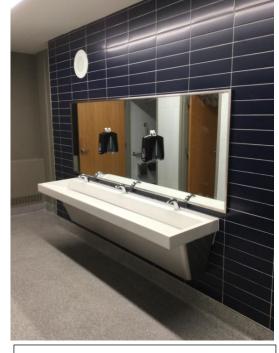

Toilet 120

Next Week

September 20th - September 24th

- Complete the Concrete Stem Wall and Pilasters on the addition
- Open Toilet 120 to the Students & Staff
- Punchlist walk in Toilet 121



Concrete Footings



Indian Woods Middle School

Construction Report 09/17/21






Locker in Toilet 121



Fire Line Vault

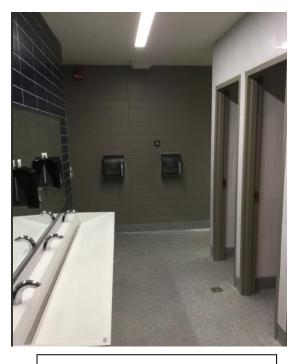

Toilet 120



Shower in Toilet 121

