

Cleveland ISD

Santa Fe Elementary School
+ Santa Fe Middle School

Construction Update: December 2021

Substantial Completion:

ES6 – Scheduled for May 2022

MS2 – Scheduled for July 2022




Lockwood, Andrews
& Newnam, Inc.
A LEO A DALY COMPANY



Huckabee
MORE THAN ARCHITECTS



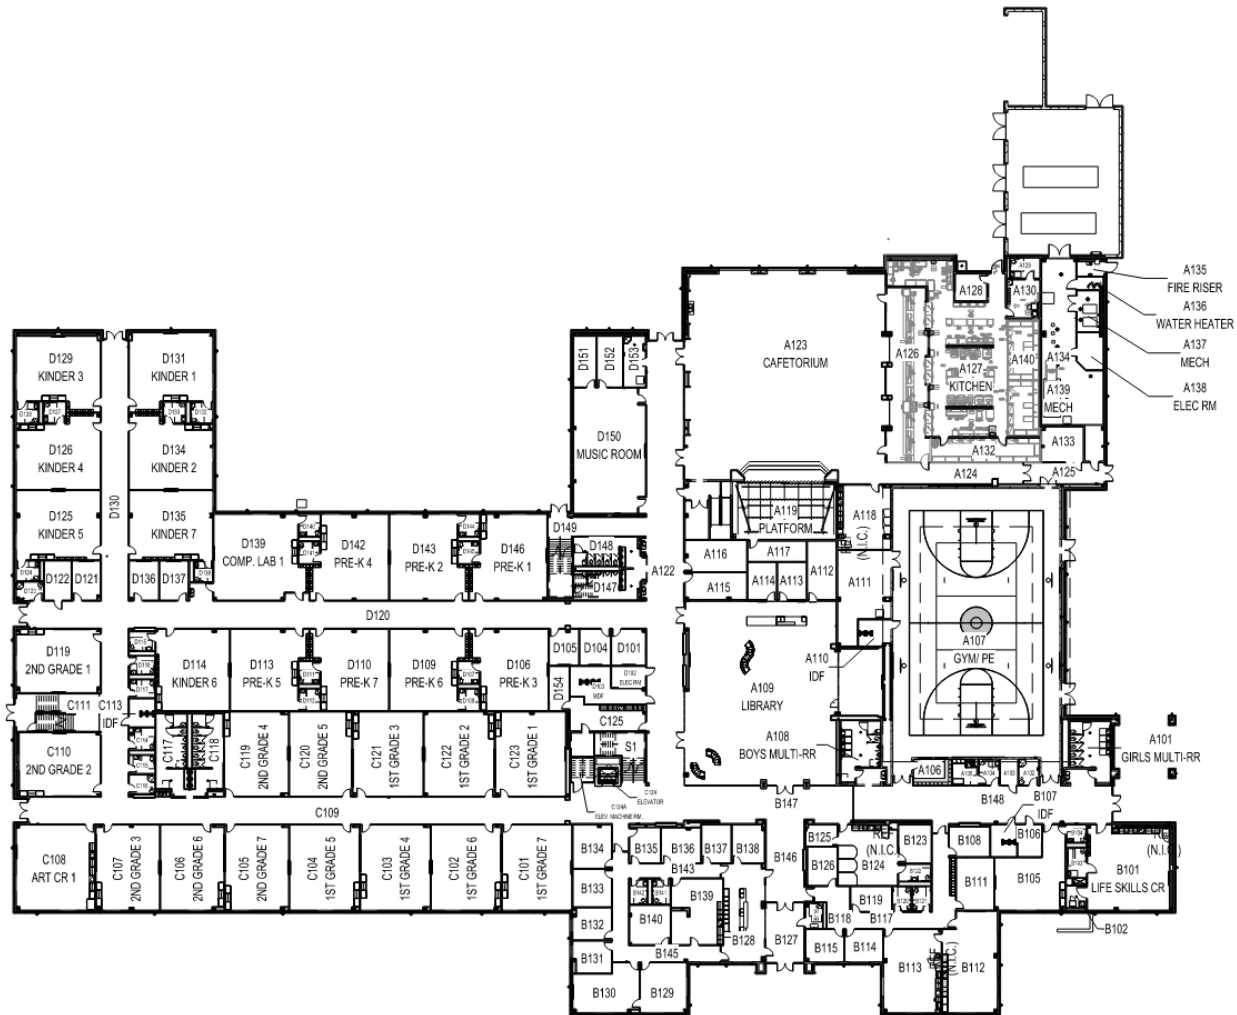


Phase Name	% Complete
Site Grading	95%
Site Paving	80%
Site Utilities	100%
ES Foundation	100%
ES Steel	100%
ES Second Floor Slab	100%
ES Interior Wall Construction	90%
ES Exterior Wall Construction	95%
ES Roofing	50%
ES Interior Finishes	0%
ES Ext. Doors/Windows	55%
ES Int. Doors/Windows	0%

LAN Lockwood, Andrews & Newnam, Inc.
A LEO A DALY COMPANY

POGUE CONSTRUCTION
POWERED BY PEOPLE

Huckabee
MORE THAN ARCHITECTS

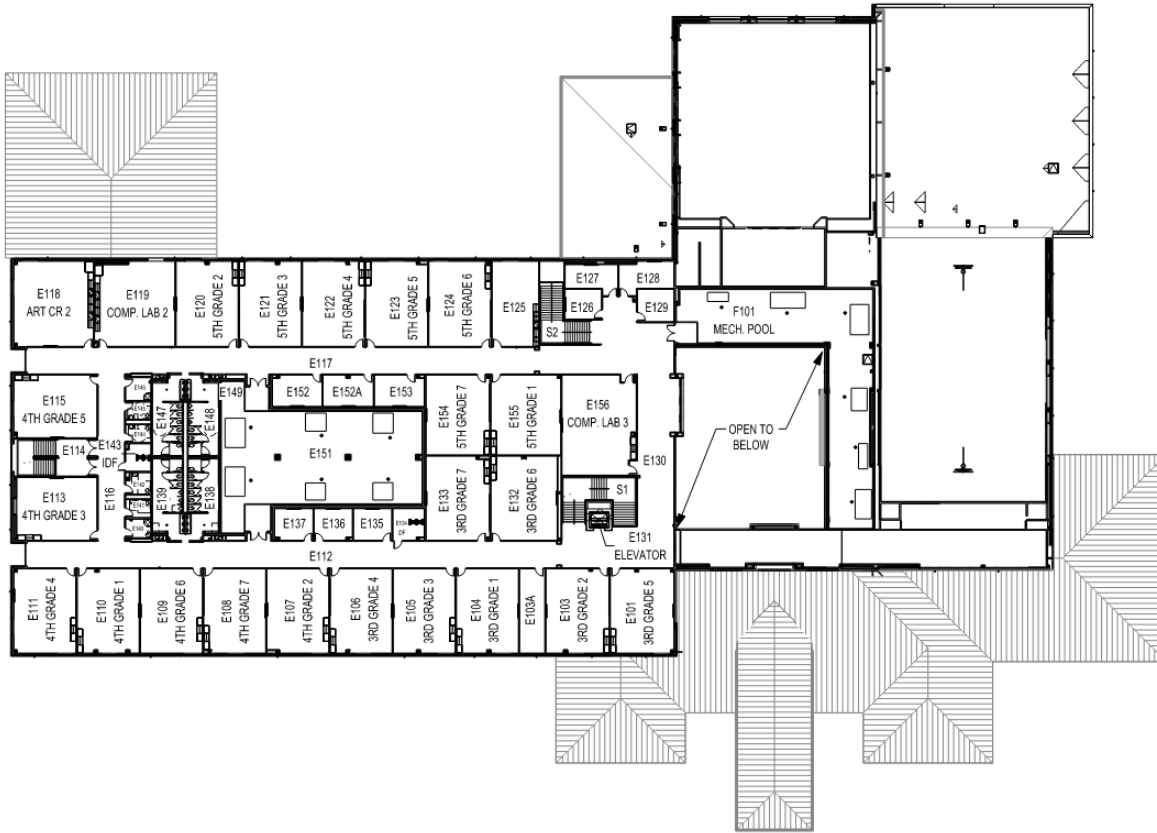

Phase Name	% Complete
ES Mechanical	55%
ES Electrical	50%
ES Plumbing	60%
ES Technology	50%
ES Overall Progress	55%
Substantial Completion	ES6: May 2022


LAN Lockwood, Andrews & Newnam, Inc.
A LEO A DALY COMPANY

POGUE
CONSTRUCTION
POWERED BY PEOPLE

Huckabee
MORE THAN ARCHITECTS




- Overall Eastern Aerial

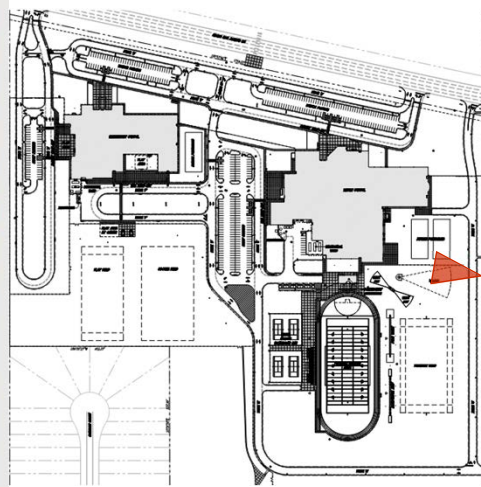




- Santa Fe ES
Northwest Aerial

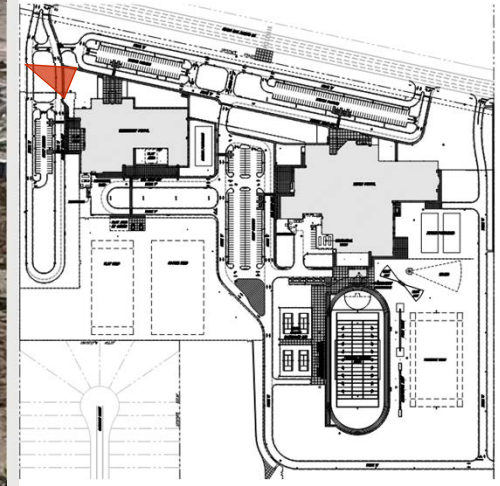




- Santa Fe ES
Southern Aerial

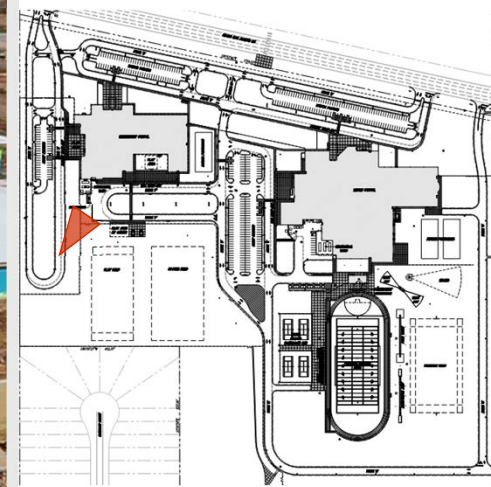




- Santa Fe ES
Southeastern Aerial

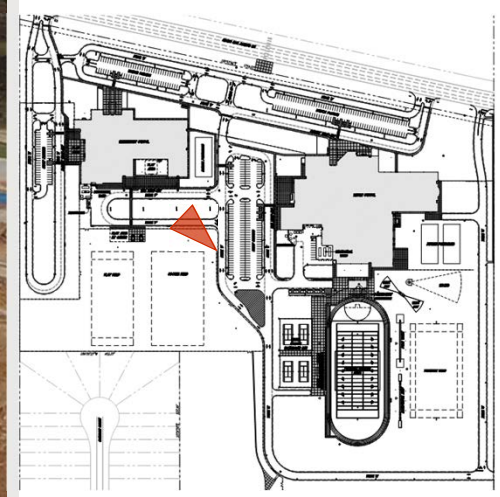




- Santa Fe ES
Eastern Aerial

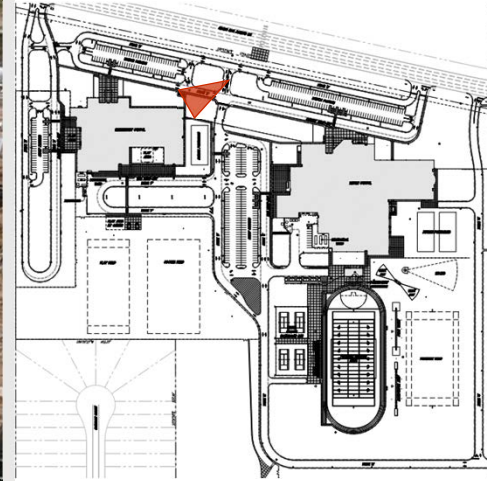




- Santa Fe ES
Northern Aerial

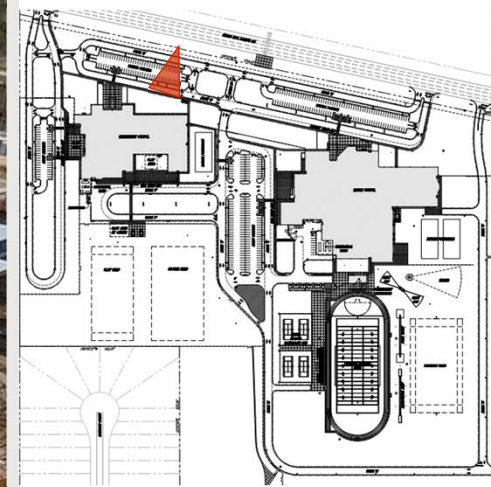




- Santa Fe ES
Northwestern Exterior

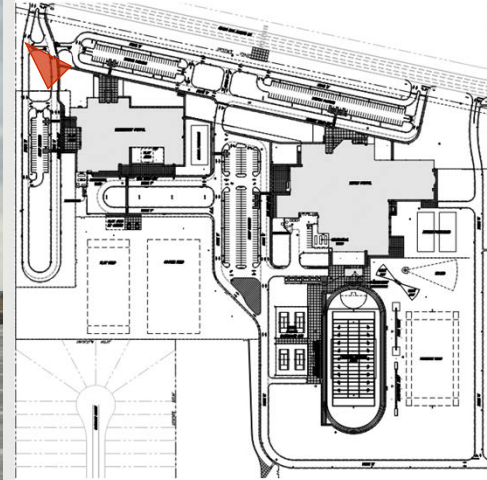




- Santa Fe ES
Western Exterior

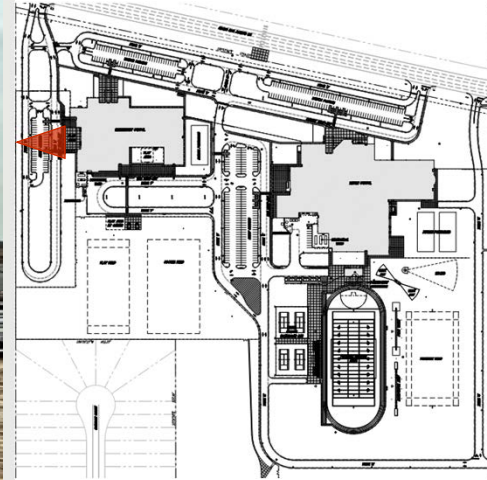



- Santa Fe ES
Southern Exterior

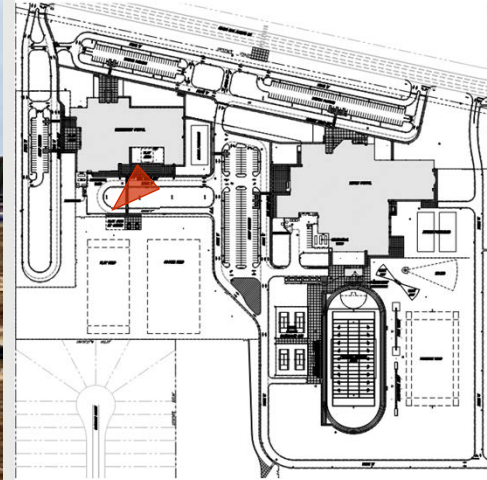



- Santa Fe ES Life Skills





- Santa Fe ES Gym





- Santa Fe ES Cafetorium Stage





- Santa Fe ES Library






- Santa Fe ES Academic Corridor





- Santa Fe ES Group Restroom

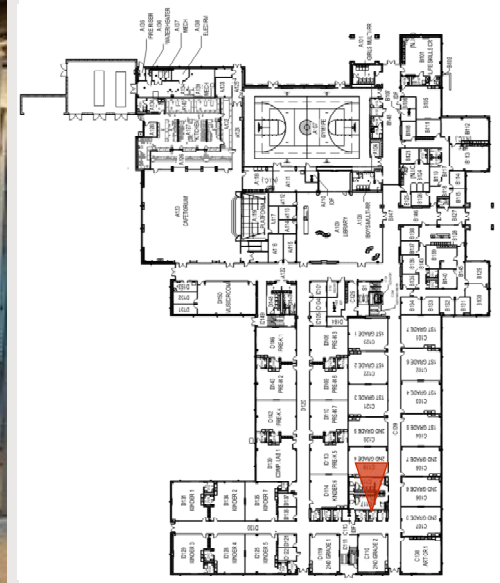




- Santa Fe ES - 2nd Floor Mechanical Room






- Santa Fe ES – 2nd Floor Academic Wing

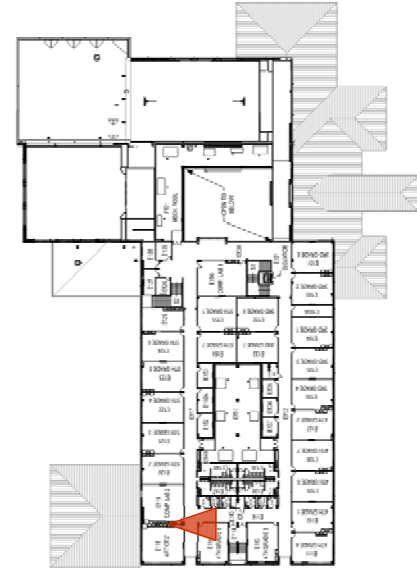



- Santa Fe ES – 2nd Floor Academic Corridor



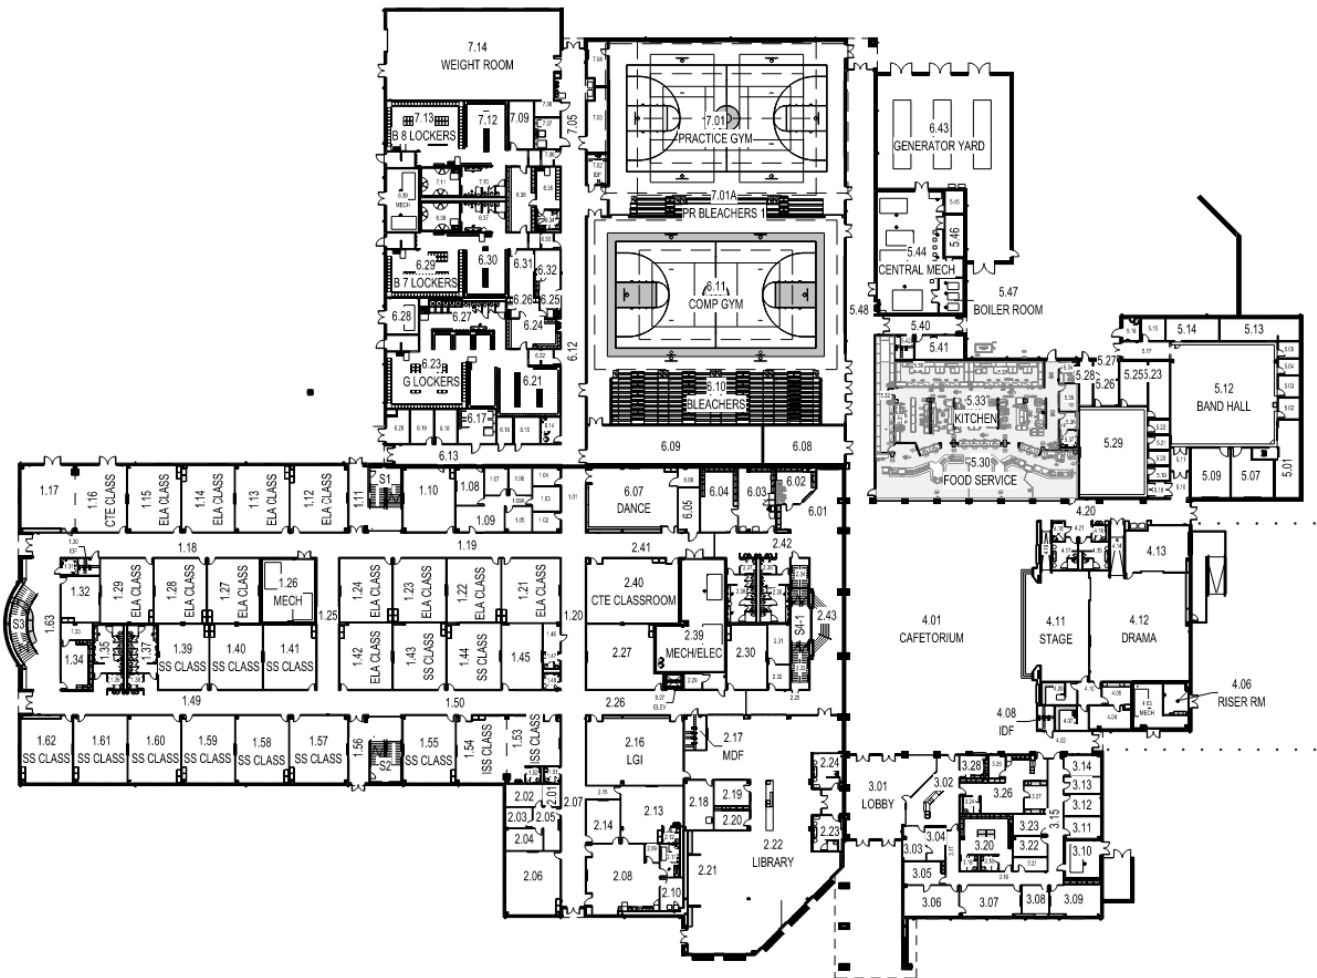


Phase Name	% Complete
MS Foundation	100%
MS Steel	90%
MS Second Floor Slab	100%
MS Interior Wall Construction	40%
MS Exterior Wall Construction	35%
MS Roofing	40%
MS Interior Finishes	0%
MS Ext. Doors/Windows	15%
MS Int. Doors/Windows	0%


Lockwood, Andrews & Newnam, Inc.
 A LEO A DALY COMPANY


POGUE CONSTRUCTION
 POWERED BY PEOPLE


Huckabee
 MORE THAN ARCHITECTS

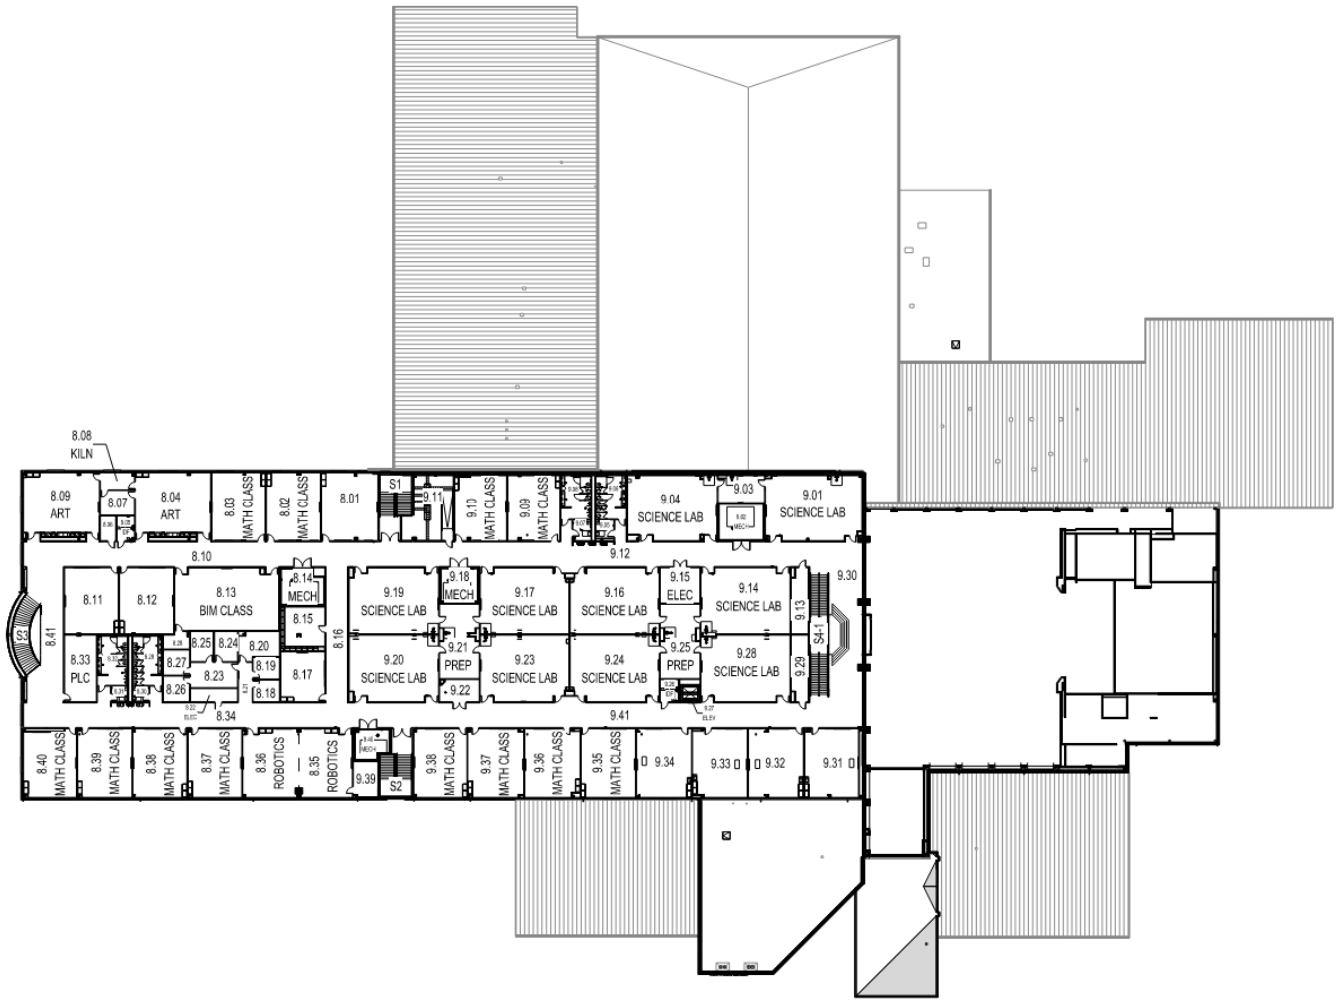

Phase Name	% Complete
MS Mechanical	25%
MS Electrical	35%
MS Plumbing	40%
MS Technology	5%
MS Overall Progress	35%
MS Substantial Completion	MS: July 2022



Lockwood, Andrews & Newnam, Inc.
 A LEO A DALY COMPANY


POGUE CONSTRUCTION
 POWERED BY PEOPLE


Huckabee
 MORE THAN ARCHITECTS




- Santa Fe MS
Northwestern Aerial

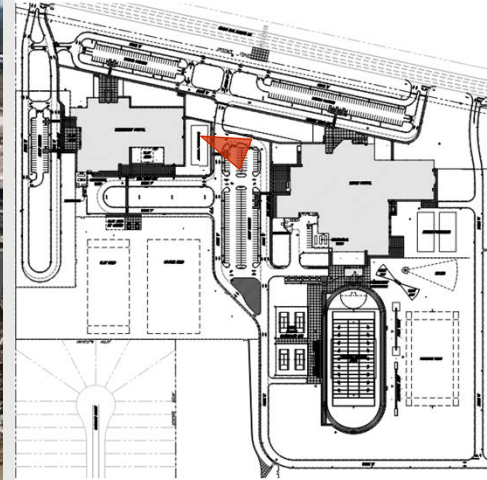




- Santa Fe MS
Northern Aerial

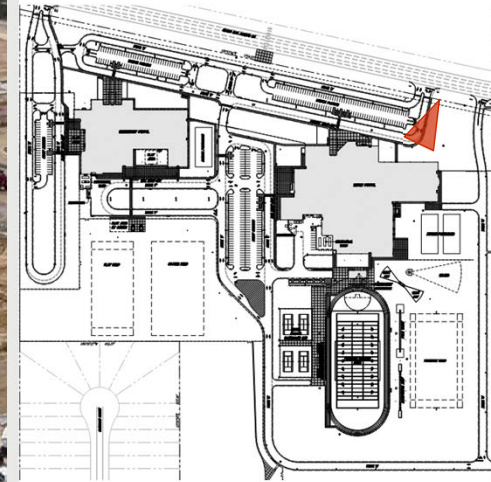




- Santa Fe MS
Northeastern Aerial

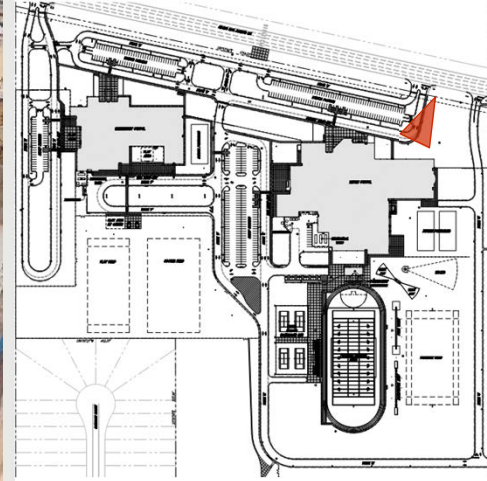




- Santa Fe MS
Western Aerial

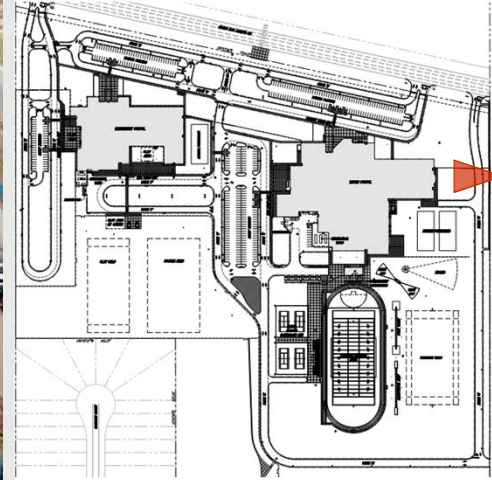




- Santa Fe MS
Southern Aerial

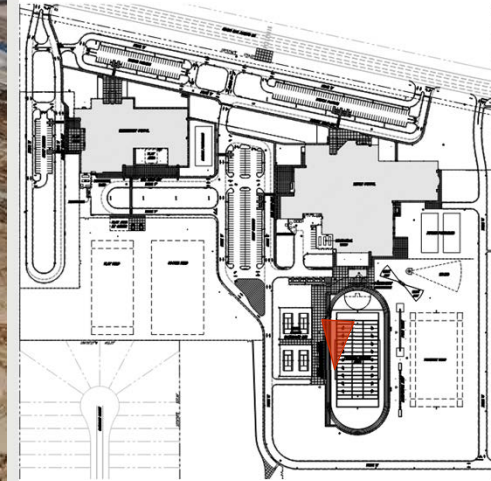



- Santa Fe MS
Front Entry

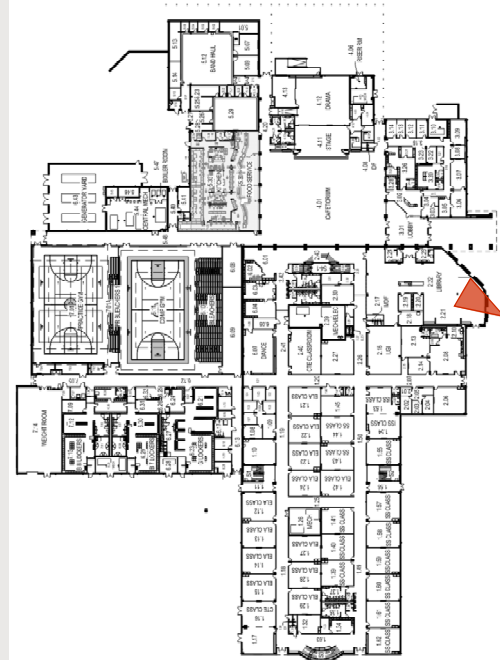




- Santa Fe MS Academic Wing






- Santa Fe MS
Admin/Cafetorium

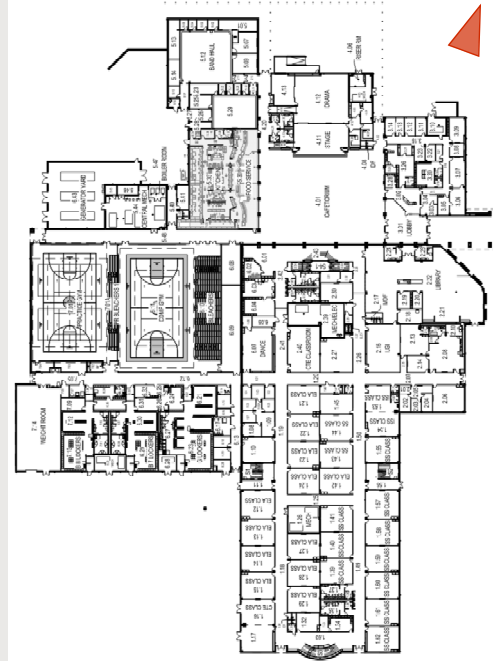




- Santa Fe MS Band/Choir

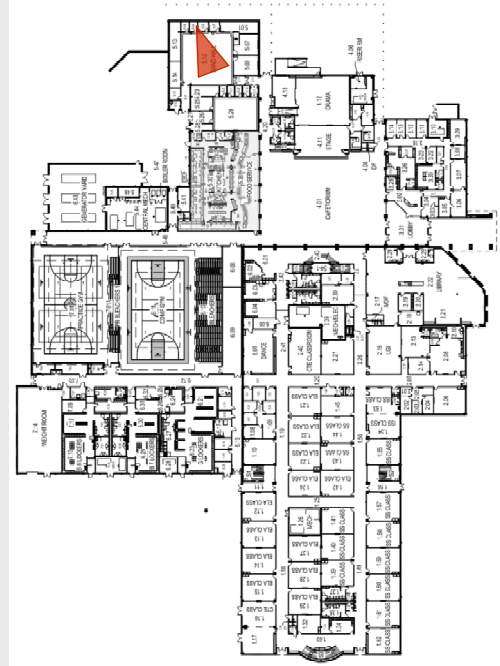




- Santa Fe MS Academic Corridor

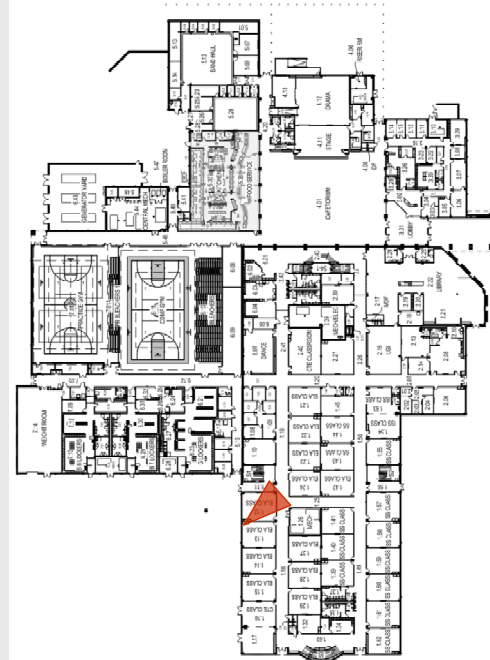





- Santa Fe MS Administration

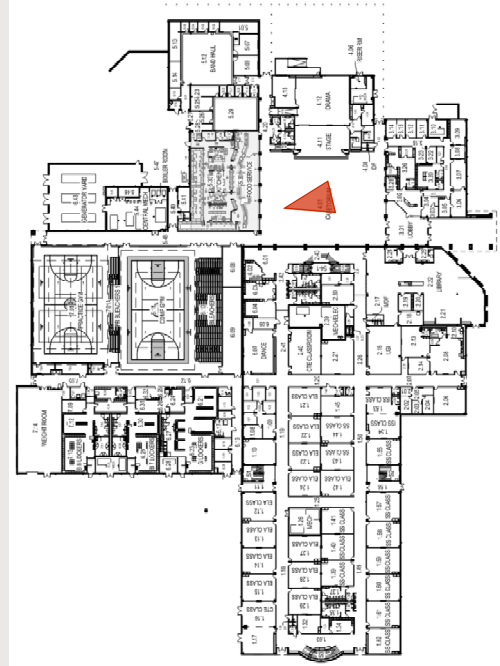




- Santa Fe MS - 2nd Floor Academic Wing

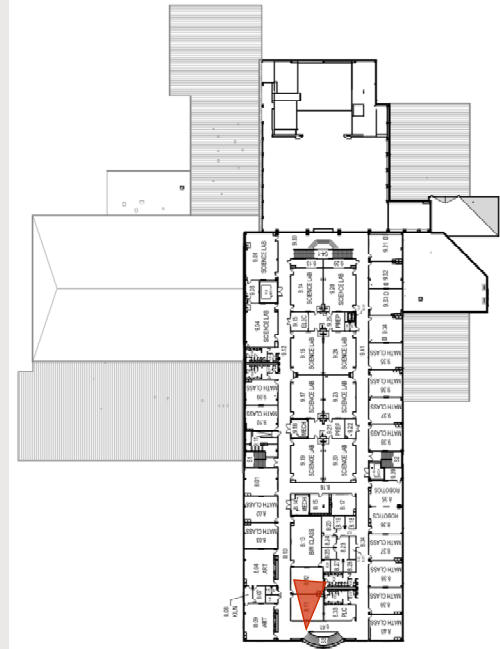

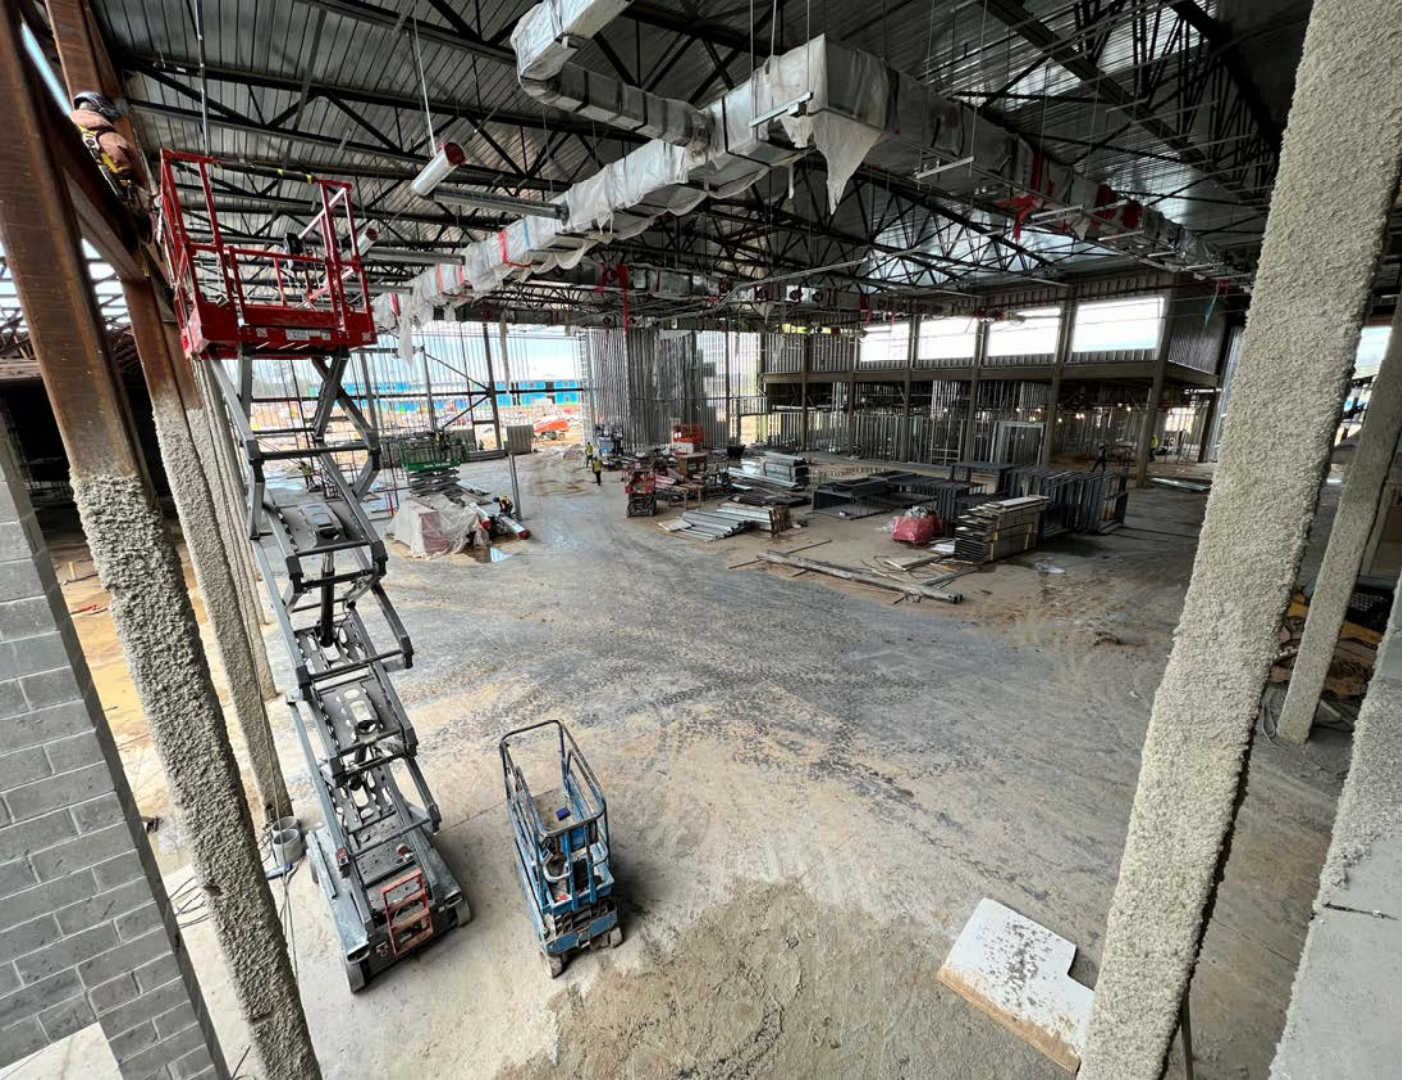

- Santa Fe MS Cafetorium

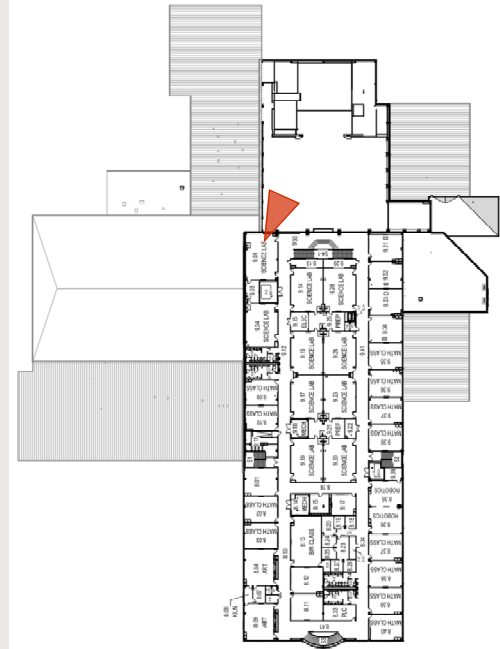



Lockwood, Andrews
& Newnam, Inc.
A LEO A DALY COMPANY

Huckabee
MORE THAN ARCHITECTS

POGUE
CONSTRUCTION
POWERED BY PEOPLE
