

# Crown Point Community School Corporation Construction Projects

## Board Report May 23, 2022




# Table of Contents

## Crown Point Community School Corporation Construction Projects

### Board Report May 23, 2022

- **New Robert Taft Middle School**
- **High School Additions & Renovations**
- **Timothy Ball Elementary Additions & Renovations**

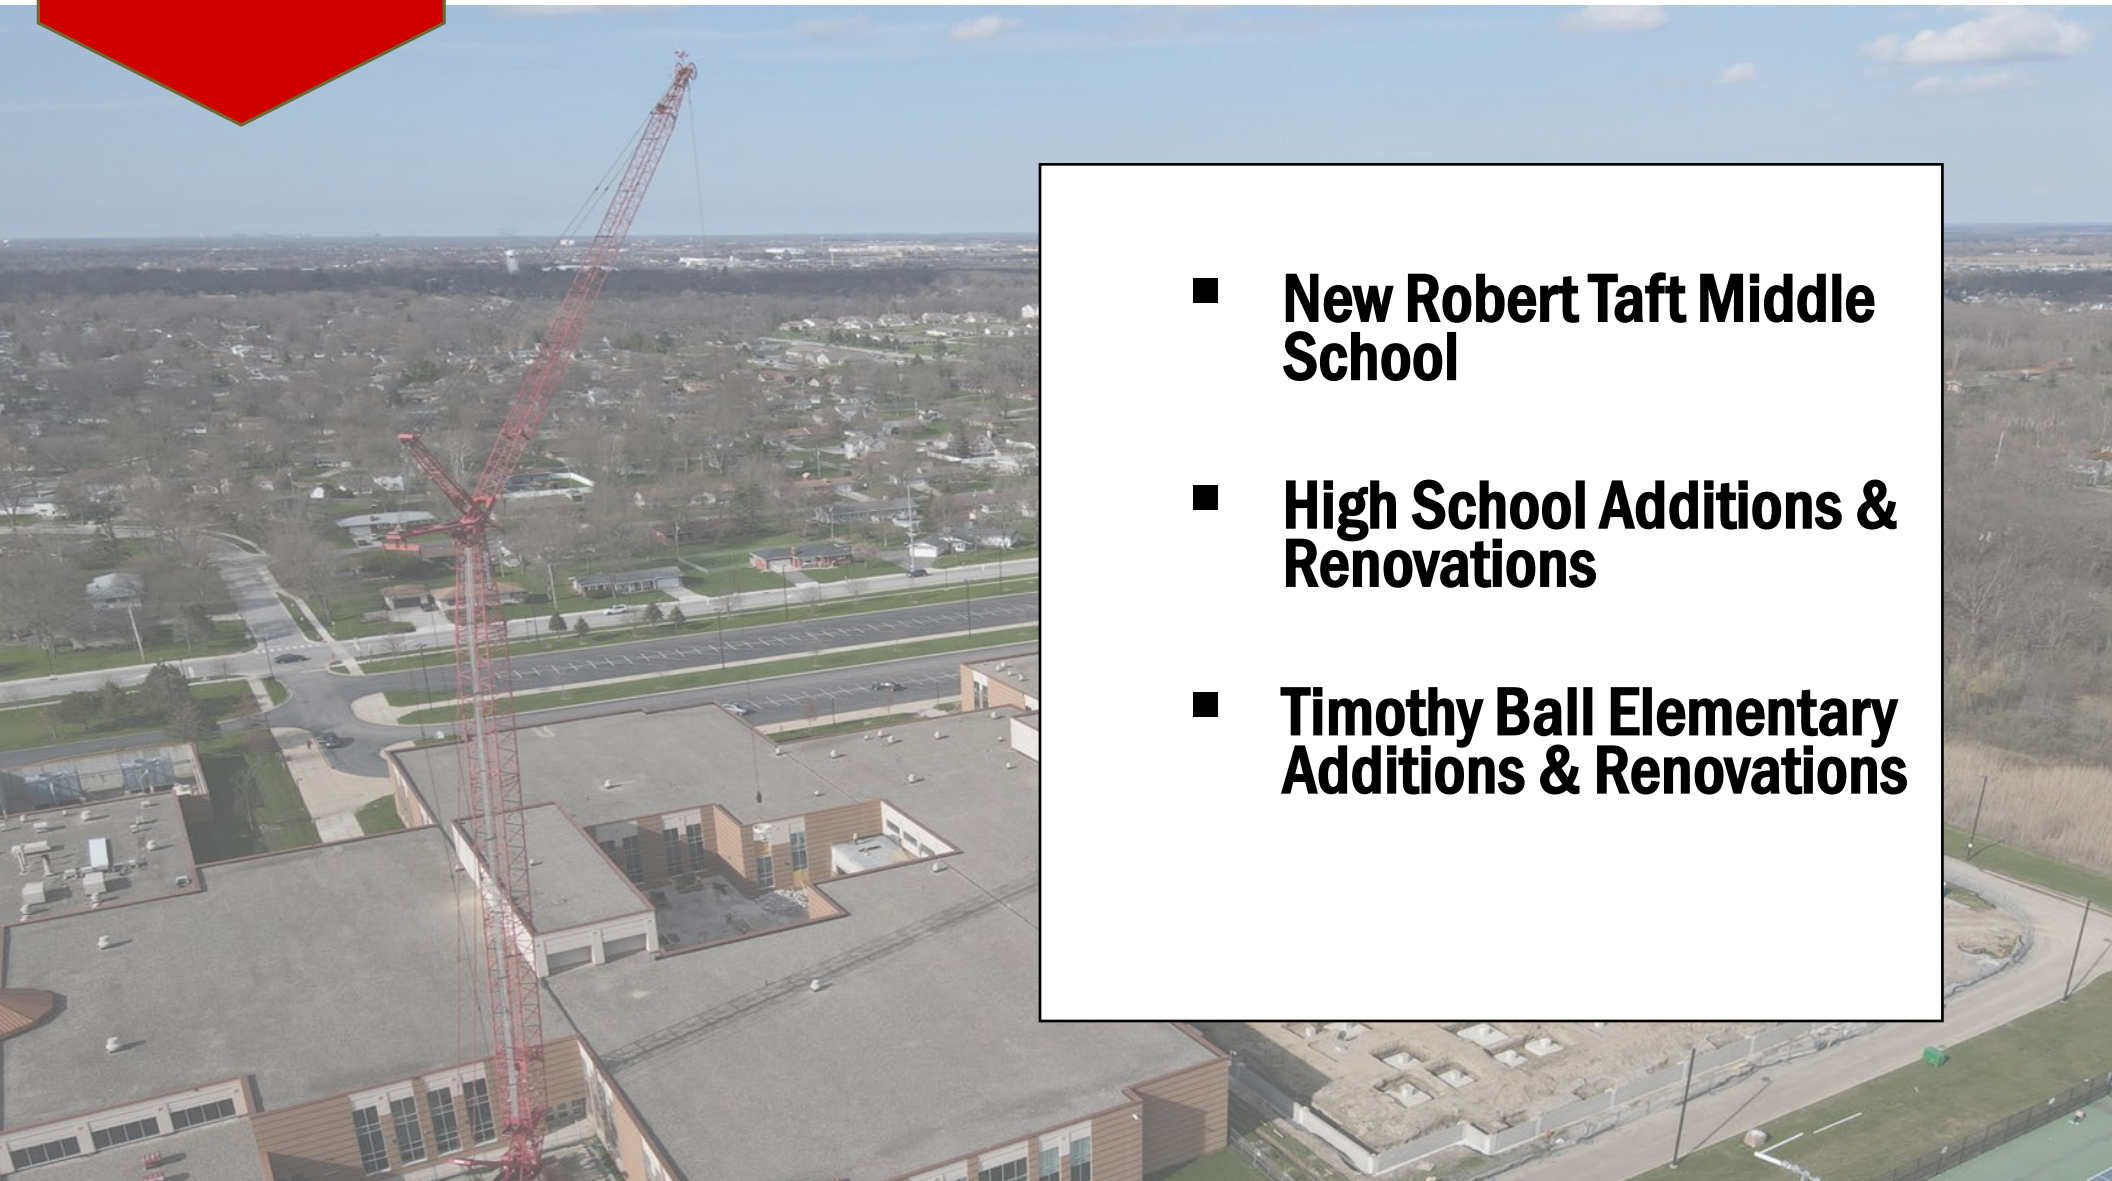





# Progress Photographs



## New Robert A. Taft Middle School:

- Began roofing on southern section of academic wing
- Began laying concrete masonry units for auditorium
- Began setting and detailing structural steel in administration and cafeteria section
- Began prepping and grading academic wing for slab-on-grade
- Poured concrete slab on deck for mechanical mezzanine in academic wing



**Administration and Cafeteria**



# Progress Photographs



**Gymnasiums and Locker Area**

## New Robert A. Taft Middle School:

### **Next Four Weeks**

- Begin setting temporary lighting in academic wing
- Begin laying concrete masonry units for auditorium
- Continue setting and detailing structural steel in gym and locker room areas
- Pour concrete slab on grade in academic wing





# Progress Photographs



**Courtyard Infill**

## **High School Additions & Renovations:**

- Completed media center structural demolition to west end
- Completed overhead utility piping to classroom and athletic additions
- Completed courtyard footings and foundations
- Poured slab-on-grade in courtyard
- Began athletic addition footings and foundations



# Progress Photographs



**Athletic Addition**

## High School Additions and Renovations:

### Next Four Weeks

- Begin sitework for performing arts addition
- Continue laying CMU foundations for athletic addition
- Continue interior corridor above ceiling mechanical piping
- Begin fire suppression piping
- Backfill classroom addition
- Start plumbing underground rough-ins for classroom addition





# Progress Photographs



**Classroom Addition**

## Timothy Ball Additions & Renovations:

- Stripped topsoil for new classroom addition
- Demolished west playground set
- Installed west storm water system
- Graded playground area





# Progress Photographs



**Sitework**

## **Timothy Ball Additions and Renovations:**

### **Next Four Weeks**

- Begin stripping topsoil on east side for new additions
- Begin demolishing canopies at west and east entrances of school
- Install new electric service to school
- Reroute gas service around classroom addition
