

2017 BOND PROJECTS – BOARD UPDATE

Stratford High School Addition and Renovations

Spring Branch Independent School District
SBISD Project No. 67220
PBK Project No. 18148
March 31, 2022



1) PROJECT TEAM:

Owner:	Spring Branch ISD	Assoc. Superintendent for Ops:	Travis Stanford
		Director of P&C:	Max Buja
		Project Manager:	Geoff Bay
Architect:	PBK	Partner-in-Charge:	Brandon Ross
		Project Manager:	Philip Stewart
CM-at-Risk:	Satterfield & Pontikes Construction, Inc.		

2) GENERAL SCOPE OF WORK:

- Addition of a 1,000-seat auditorium to the existing school. Also included are a roof replacement, safety & security, site lighting and site improvements for the campus.

3) BOND PLAN PROJECT TIMELINE:

- The following project is included in year four of the bond program. The Project Advisory Team is involved from the Schematic Design (SD) to the Design Development (DD) phase.

PROJECT ADVISORY TEAM	MARCH 2019 – SEPTEMBER 2019
SCHEMATIC DESIGN	MARCH 2019 – APRIL 2019
DESIGN DEVELOPMENT	APRIL 2019 – SEPTEMBER 2019
CM@R SELECTION	MAY 2019 – JUNE 2019
CONSTRUCTION DOCUMENTS	SEPTEMBER 2019 – DECEMBER 2019
PERMITTING	DECEMBER 2019 – FEBRUARY 2020
BIDDING / BOARD APPROVAL	FEBRUARY 2020 – MARCH 2020
CONSTRUCTION PHASE	MARCH 2020 – FEBRUARY 2022
OCCUPANCY	MARCH 2022

Current Point

4) PROJECT STATUS OVERVIEW:

- The OAC meetings are scheduled bi-weekly.
- Punch list items are in progress.
- Paving work at Auditorium Plaza is near completion.
- Roof work at existing campus is near completion.
- West parking lot restriping is on-going.

5) PAST 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:


The following activities have taken place:

- Stage lighting and Audio trainings.

6) NEXT 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:

- Progressing with paving at Auditorium Plaza.
- Progressing with West parking lot restriping and last lane extension.
- Progressing with Scene Shop teaching wall.
- Trainings for new systems.


7) PHOTOGRAPHS:

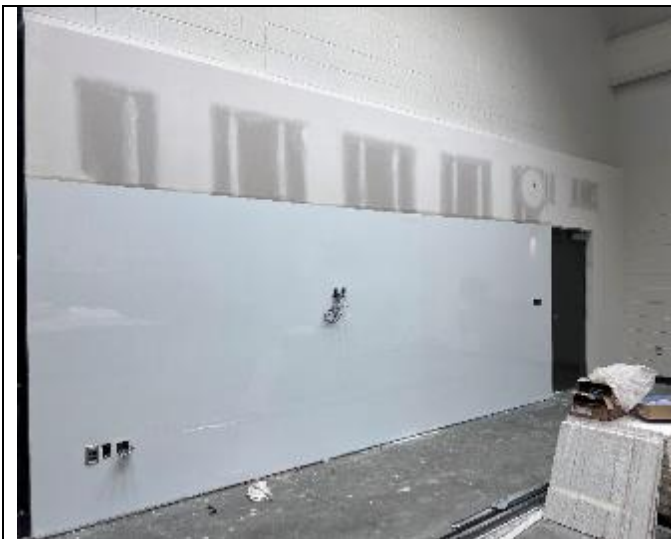

Scene shop teaching wall being prepared.



Scene Shop drinking fountain has been installed.

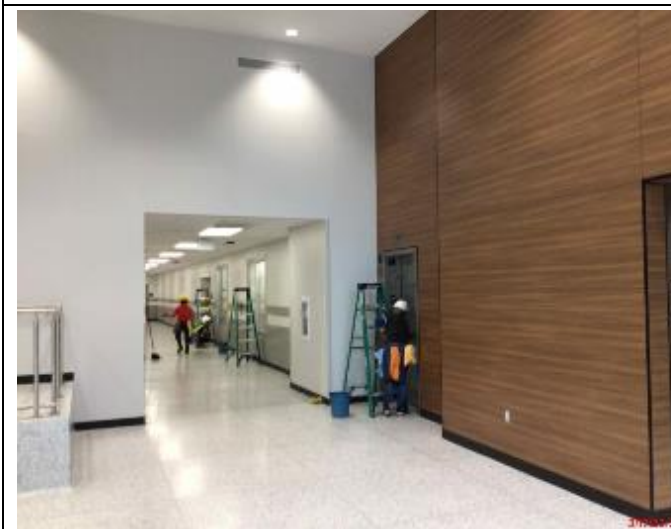

Auditorium corridor and lobby being cleaned.



Paving at Auditorium Plaza is near completion.



West parking lot lane being extended.



Signage at West parking lot.



Roof work at existing campus side is on-going.
