

2017 BOND PROJECTS – BOARD UPDATE

Stratford High School Addition and Renovations

Spring Branch Independent School District
SBISD Project No. 67220
PBK Project No. 18148
January 31, 2022



1) **PROJECT TEAM:**

Owner:	Spring Branch ISD	Assoc. Superintendent for Ops:	Travis Stanford
		Director of Planning & Construction:	Max Buja
		Project Manager:	Geoff Bay
Architect:	PBK	Partner-in-Charge:	Brandon Ross
		Project Manager:	Philip Stewart
CM-at-Risk:	Satterfield & Pontikes Construction, Inc.		

2) **GENERAL SCOPE OF WORK:**

- Addition of a 1,000-seat auditorium to the existing school. Also included are a roof replacement, safety & security, site lighting and site improvements for the campus.

3) **BOND PLAN PROJECT TIMELINE:**

- The following project is included in year four of the bond program. The Project Advisory Team is involved from the Schematic Design (SD) to the Design Development (DD) phase.

PROJECT ADVISORY TEAM	MARCH 2019 – SEPTEMBER 2019
SCHEMATIC DESIGN	MARCH 2019 – APRIL 2019
DESIGN DEVELOPMENT	APRIL 2019 – SEPTEMBER 2019
CM@R SELECTION	MAY 2019 – JUNE 2019
CONSTRUCTION DOCUMENTS	SEPTEMBER 2019 – DECEMBER 2019
PERMITTING	DECEMBER 2019 – FEBRUARY 2020
BIDDING / BOARD APPROVAL	FEBRUARY 2020 – MARCH 2020
CONSTRUCTION PHASE	MARCH 2020 – FEBRUARY 2022
OCCUPANCY	MARCH 2022

Current Point

4) **PROJECT STATUS OVERVIEW:**

- The OAC meetings are scheduled weekly.
- Punch list items are in progress.
- Roof coping at existing side is on-going.
- ActivPanels installation is on-going.
- School logos are being installed.

5) **PAST 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:**

The following activities have taken place:

- Mirrors and lighting have been installed in Dressing and Makeup rooms.

6) NEXT 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:

- Progressing with concrete paving and pavers at Auditorium Plaza.
- Theatrical consultant has visited Auditorium and provided punch list.
- Contractor is working through the punch list in the Auditorium.

7) PHOTOGRAPHS:




Roof work at existing side of campus is on-going



Detention pond mowing has been completed.



Paving at Auditorium Plaza is on-going

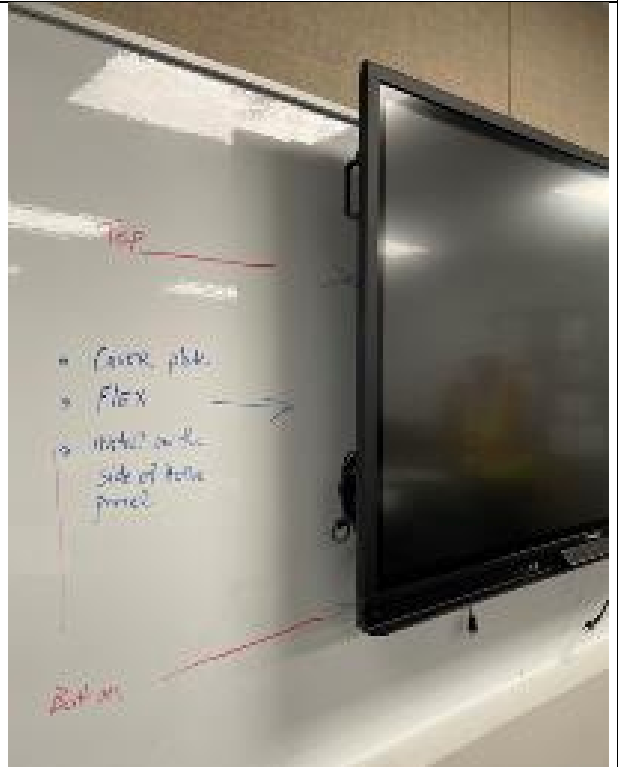

Active Panel Installation



Dressing Room mirrors and lighting




Makeup room mirrors and lighting



Stage floor has been repainted



School Logo at Auditorium Lobby

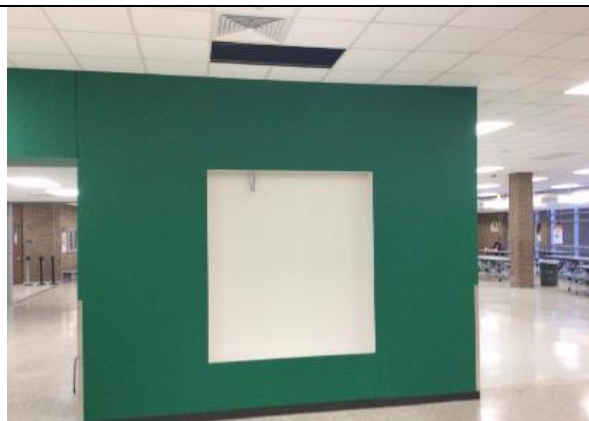

Cafeteria wall is being prepared to receive logo.
