



2017 BOND PROJECTS – BOARD UPDATE

Landrum MS Replacement

Spring Branch Independent School District

Stantec Project No. 214000653

July 31, 2021

1) PROJECT TEAM:

Owner:	Spring Branch ISD	Assoc. Supt. For Operations:	Travis Stanford
SBISD Project No.	67213	Project Managers:	Kris Drosche / Geoff Bay
Architect:	Stantec Architecture, Inc.	Partner-in-Charge:	Jennifer Henrikson
		Project Manager:	Gary Dunn
CM@Risk:	Durotech		

2) GENERAL SCOPE OF WORK:

Replacement of Landrum Middle School with new 1100 student campus on existing site. Scope includes demolition of existing campus, added drainage detention, construction of new building and associated site work.

Off-Site Transition:

Conceptual studies have revealed on site transition is feasible.

3) BOND PLAN PROJECT TIMELINE:

PROJECT ADVISORY TEAM	JANUARY 2019 – NOVEMBER 2019
CM@R SELECTION	MARCH 2019
CONCEPTUAL SITE STUDY	AUGUST 2018 – DECEMBER 2018
SCHEMATIC DESIGN	JANUARY 2019 – MARCH 2019
DESIGN DEVELOPMENT	MARCH 2019 – MAY 2019
CONSTRUCTION DOCUMENTS	MAY 2019 – AUGUST 2019
PERMIT RECEIVED	MARCH 30, 2020
BIDDING / BOARD APPROVAL	SEPTEMBER 2019 – NOVEMBER 2019
CONSTRUCTION PHASE	DECEMBER 2019 – OCTOBER 2021
OCCUPANCY	JUNE 2021 – AUGUST 2021

← Current Point

4) PROJECT STATUS OVERVIEW

Project is in Construction Phase.

5) PAST 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:

- Phase II Parking Areas and most sidewalks now complete
- Temporary Certificate of Occupancy obtained and building is now occupied


6) NEXT 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:

- SCHOOL OPENS AUGUST 16TH
- Complete Metal Panel graphics
- Complete Track and SportCourt surfaces and striping
- Complete Punch List Items
- Complete AV installations
- Continue Phase II site work and landscaping

7) PHOTOGRAPHS:



Front Entry

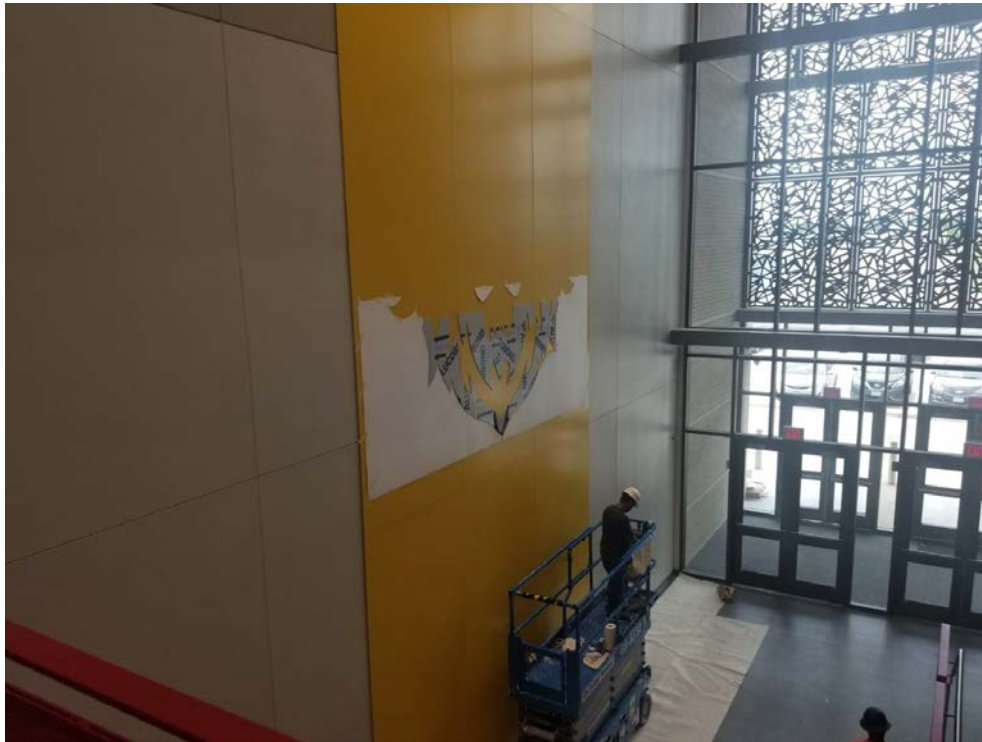


Metal Panel Graphic install



Track Surface




Front parking concrete poured



New Dedication Plaque



Entry Canopy Complete

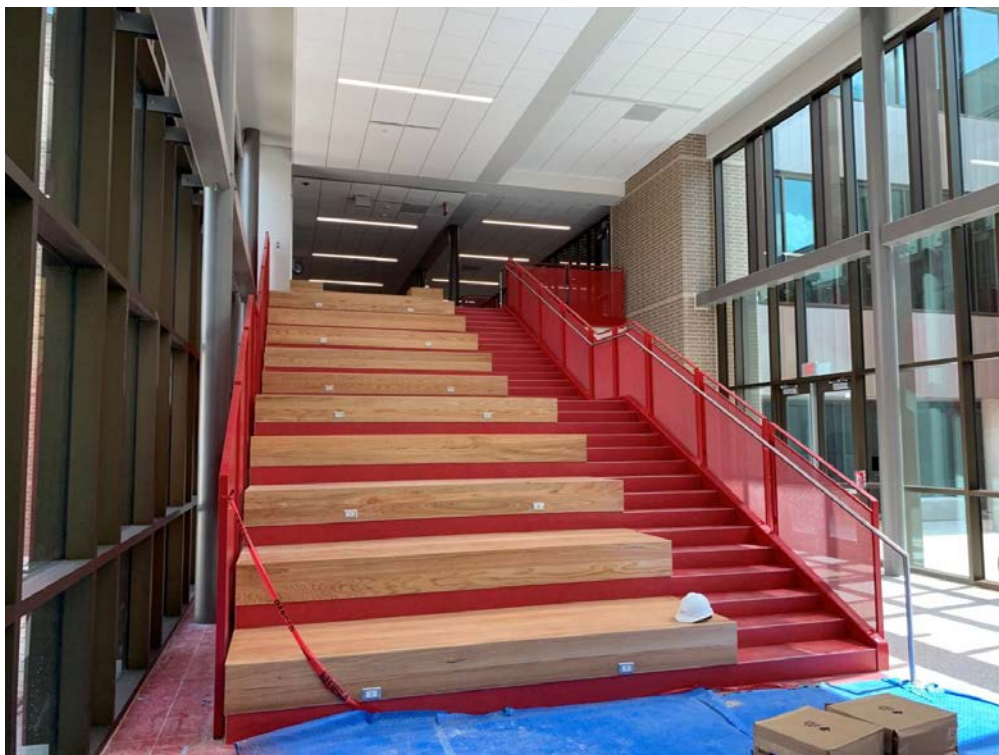

Learning Stair Completed



Auditorium Interior



Library Interior



Gym Interior



Stantec

Stantec Architecture Inc.
910 Louisiana St Suite 2600, Houston TX 77002



Dining Interior
