



**GARMANN
MILLER**
ARCHITECTS
ENGINEERS

Construction Weekly

Project: Elida Local Schools

Week of: 09/21/2020

PROJECT TEAM

Owner: Elida Local Schools
Architect: Garmann/Miller
Construction Manager: Peterson Construction Company

FUTURE MEETING DATES

Date	Time	Location	Topic
09-28-2020	1300hrs	Peterson Job Trailer	Contractor Progress Meeting
09-28-2020	1030hrs	Peterson Job Trailer	Owner Project Update Meeting
10-21-2020	1000hrs	Elida District Office	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- CMU being installed in Unit D, 2nd, C 1st
- Gym roof concrete being poured
- Metal stud installation has started in the Admin area
- Steel installation and decking is taking place in Unit E
- Cast Stone installation has started on Unit B
- Ductwork installation has started
- Veneer work continues at Unit A and started on Unit B

Planned Activities for Next Week:

- Veneer will continue for Unit A and B
- CMU will continue in Unit C and D 2nd floor
- Drywall will be installed where available
- Roof dry in will continue
- Insulation and Z furring for the metal panels will take place
- Concrete pour over the Unit E will be prepped for the pour
- Decking over Unit E for 2nd floor will be installed
- MEP in wall rough continues

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Rebar and Nelson studs installed on gym roof in preparation for concrete



Day 1 of the gym concrete pour taking place


PHOTOS




Ductwork installation started in the Unit B corridor



Round duct installation in the student dining has started

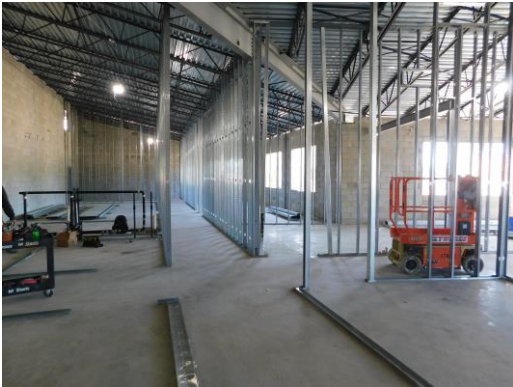

Metal studs are being installed in the administrative area

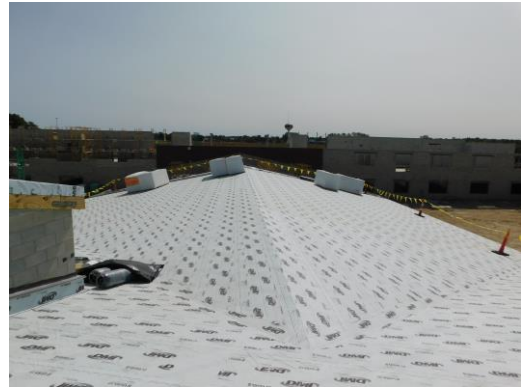

Unit B roof dry in



Veneer installed above the roof line at the B to C connector



Cast stone installation has started at the main entrance

PHOTOS



Veneer work taking place on the east side of the student dining



Unit E bar joists are installed ready for decking



Drains are being installed below the mechanical mezzanine at the student dining



Restroom fixture carriers continue to be installed with wall clean out as well



Vault for the transformer is installed



Insulation and Z furring for metal panels has started to be installed at the student dining
