



Project: Elida Local Schools

Week of: 09/07/2020

PROJECT TEAM

Owner: Elida Local Schools.....
Architect: Garmann/Miller.....
Construction Manager: Peterson Construction Company.....

FUTURE MEETING DATES

Date	Time	Location	Topic
09-14-2020	1300hrs.....	Peterson Job Trailer.....	Contractor Progress Meeting
09-14-2020.....	1030hrs.....	Peterson Job Trailer.....	Owner Project Update Meeting
09-16-2020.....	1000hrs.....	Elida District Office.....	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- CMU being installed in Units C, 2nd
- Floor pours for the media center and admin area are complete
- Electrical rough in for metal studs continues
- Steel installation and decking is taking place in Unit B
- Wood blocking is taking place in Unit A and B
- Deck on the gym has been installed
- Veneer work continues at Unit A and started on Unit B

Planned Activities for Next Week:


- Veneer will continue for Unit A and B
- CMU will continue in Unit C 2nd floor
- Studs will be placed on the gym decking
- Roof dry in will continue
- Electrical home runs being pulled
- Steel installation in B will continue
- Metal stud installation will continue where available
- MEP in wall rough continues

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Veneer work on Unit A

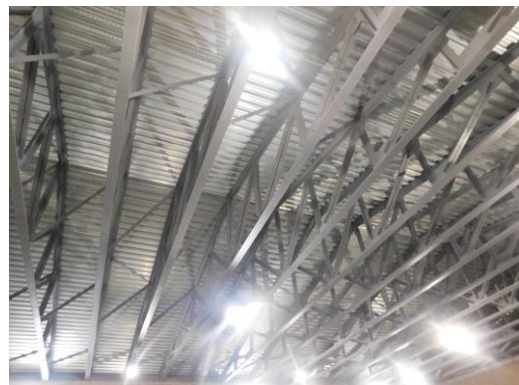

Gym decking installed (view from inside)

PHOTOS



Restroom fixture carriers installation has started



Media center concrete pour is complete



Admin area concrete pour is complete



Smoke hatch layout and cut ins have started above the stage



B to C corridor steel installation



Electrical above ceiling rough in taking place in Unit C


PHOTOS



Scaffold set for veneer installation above roof
at C hub area



Flashing and term bar installation at the above
roof area of Unit C hub

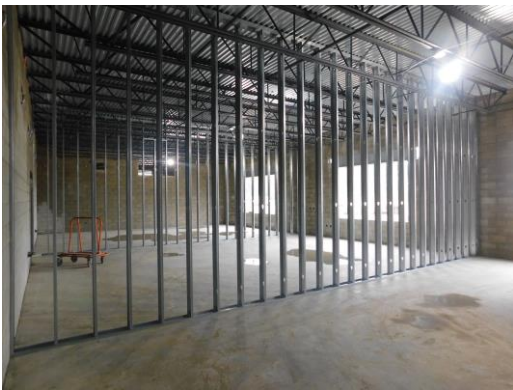

Metal stud installation has started in Unit D 1st
floor



View from Unit D 2nd floor looking at the
stage and student dining areas



Unit C 2nd floor masonry bearing walls being
installed



Unit E corridor walls completed to bearing on
1st floor
