

BARBERS HALL Independent School District Projects Update June 27, 2022

BHISD Bond Projects: Guy Matthews Field/Gordon Speer Stadium: College & Career Center Renovations at the HS Café: DAEP-EPIC Renovations at the PDC: MS North Girls Locker Room Renovations: Eagle Stadium D-Zone Band Bleachers: Transportation Parking & Fuel Station Project: BB/SB Bleacher Project: Intermediate North: Intermediate South:



<u>UPDATE – TASB ENERGY COOPERATIVE – TRANSPORTATION FUEL</u> <u>PURCHASE AGREEMENT – CONTRACT EXECUTED 6-9-2022</u>

			NOT TO	DEXCEE) PRICE		FINAL P	PRICING:		
Regular Unleaded				\$3.50			\$3.	.37		
Ultra-low Sulfur Diesel				\$3.92			\$3.	.77		
TASB C ENERGY										
				со	OPE	RAT	I V E	N		
CONTRACT TERM / DELIVERY PERIOD:										
JUNE 2022 THROUGH DECEMBER 2023										

See Attachment for Full Contract:



BOND 2020 – Guy Matthews Field/Gordon Speer Stadium: Completion 7-31-22



Artificial Turf – Track Resurface Project

BOND 2020 – Guy Matthews Field/Gordon Speer Stadium: Completion 7-31-22



Artificial Turf – Track Resurface Project

BARBER



cre8

Artificial Turf – Track Resurface – Subgrade In Progress





cre8

Artificial Turf – Track Resurface – Subgrade In Progress





cre₈

Artificial Turf – Track Resurface – Polyurethane Liner Complete – Gravel Spreading and Compacting in Progress

BARBERS HALL



cre₈

Artificial Turf – Track Resurface – Polyurethane Liner Complete – Gravel Spreading and Compacting in Progress

BARBERS HALL



Artificial Turf – Track Resurface – Subgrade, Liner & Gravel Complete – Artificial Turf Installation to Begin by 6-28-22

cre₈

BARBERS HILL


HS COLLEGE & CAREER CENTER RENOVATIONS @ HS CAFETERIA ROTUNDA



New Furniture and Mobile Wall Partition Plan Layout



BOND 2020 – College & Career Center Renovations at HS Café: Completion 7-18-22

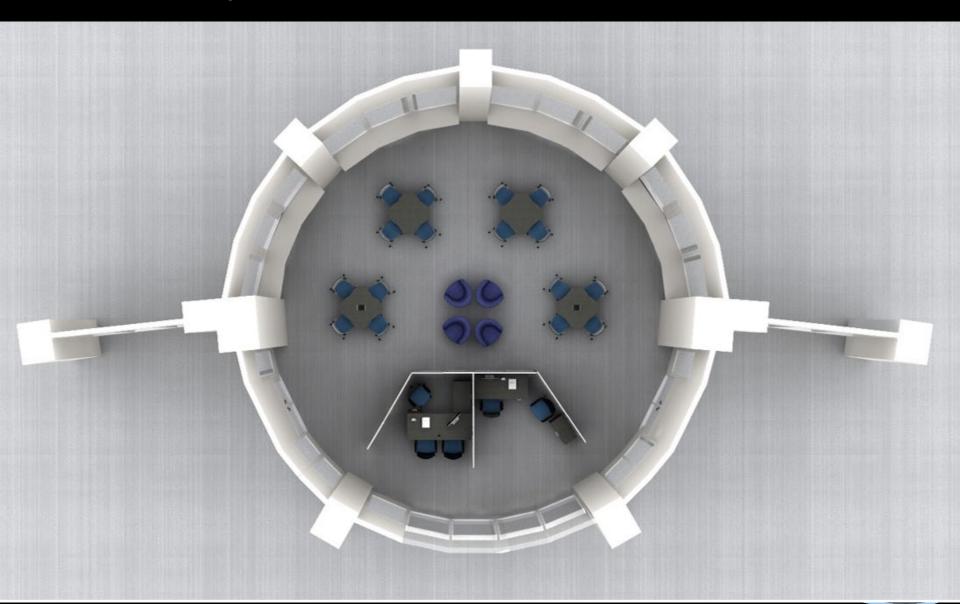


cre8

New Furniture and Mobile Wall Partition Plan Layout



BOND 2020 – College & Career Center Renovations at HS Café

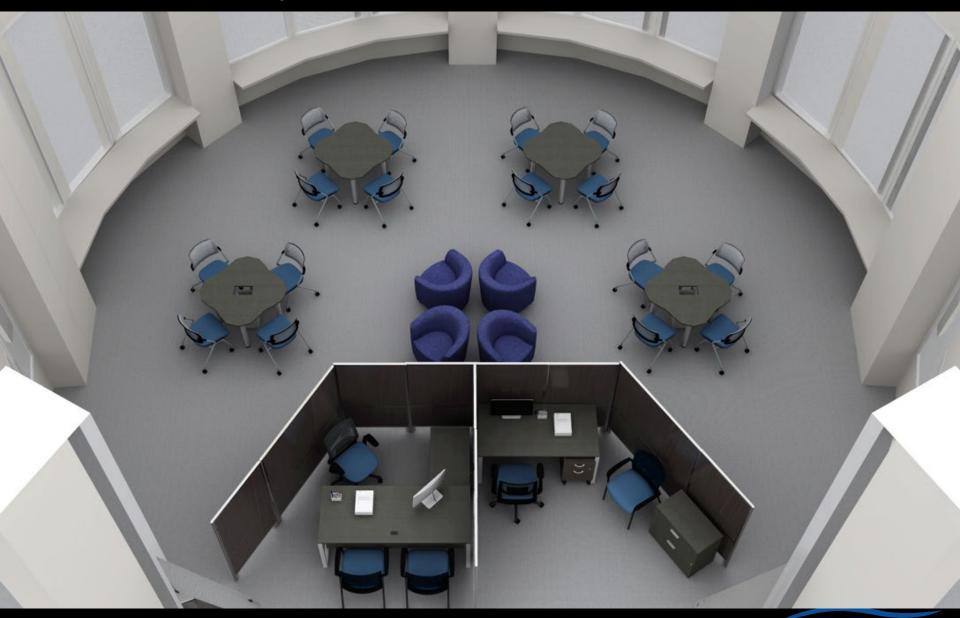

cre₈

New Furniture and Mobile Wall Partition Layout



BOND 2020 – College & Career Center Renovations at HS Café




cre₈

Student Tables and Soft Seating



BOND 2020 – College & Career Center Renovations at HS Café





LEFT SIDE

RIGHT SIDE




CENTER



New Vinyl Graphics on Existing Storefront Glass



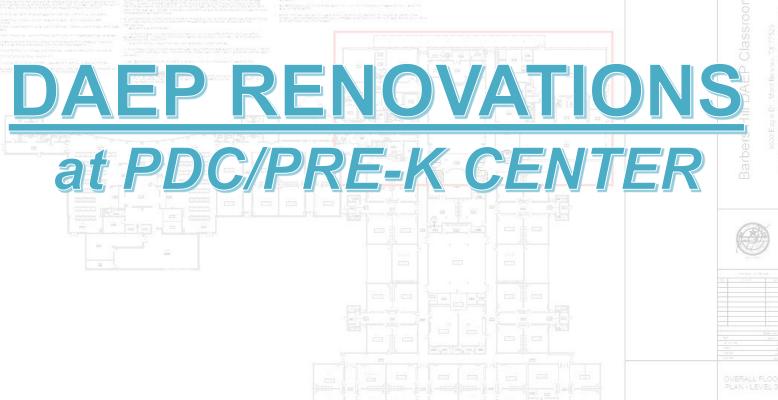

Plan Indicating New DAEP/EPIC Area

BARBERS

cre

ELECTRICAL GENERAL NOTES:

INVESTIGATION AND APPLICATIONS. THE PURPORE AND APPLICATION OF THE DOCUMENTS INTERACTOR THE PROJECT IS TO POLICY AND THE OWNER TO THE PURPORE TO THE OWNER AND A THE OWNER AND

NOT SCALE FROM DRAWINGS AS MINITING DISTORTS SCALE, WORK SHALL BE LAD OUT FROM DISE

UPALIED TO THE CONTRACTOR

- WORK INVELOP INTRODUCED IN ACCORDANCE WITH BUT FORME, ITSTE, AND OR LOOK, BUER, MODULATIONS IT MACHINE AND IMPETY INCLUSION OF A
- INTERNAL FORMATION AND ALL WORK INTERLINE INVALIDE IN ACCORDANCE WITH LOCAL, ITALY, AND AND CODES

- LONG TORHO CODERS. MEMORY AND REAL THAT SHELL INCLUDENT WHITE ANY LOAD IF CARE OF COMPLETE OF MEMORY AND THAT AND DEAL THAT AND ANY LOAD IF ANY LOAD IF CARE OF COMPLETE OF MEMORY AND AND AND ANY LOAD IN ANY LOAD INTERNET. AND THE CARE OF MEMORY ATTACANT AND LATER.
- AND ALL APPLICABLE CODES, BLUES, MO REQUISIONS THAT MAY APPLY TO THE PERMONANCE OF MOS
- NOLIZING BUT NOT LIMITED TO COOKE AN GULLETING BATTY, MORENG CONDITIONS, NORE AND CIVER UTLITER SURVISION TRUCTOR AND UND OF HIGH DOLE MATTRIX, 5 (8)

- NORTWORK WORK OUTSIDE CO INFORME AFTER HOURS OF HE WETLINGS, COOK VERYING & COORDINGT ACHICULING WITH OWNER IN ACHICA.
- TACTOR AND COORDINATION WITH COMPA TRADER.
- exercise, obvious, contractor, or weighted would be hear contracts a standard state the contractor annual state of a state of the state and contractors, subvises, status as no root or setting works or contractors, and a state of the state work or state of the state of the
- OFFICE OF OFFICE AND ADDRESS OF A COMPACT AND ADDRESS TO ALL DOCUMENTS CONDUCT IN CONDUCTIONS TO SHE READED ACT OF AT, COMPLANCE INTO
- PROVIDENT OR OTHER A CONFLICT IN THE CONTRACTOR RELEASEBUTY TO BRAIN ALL PLANSAND INCORPORTED IN A CONFLICT INCOMENTATION OF THE PROJECT REQUIREMENTS.
- CORE DEVICE WITH AND FEED TABLE FLOR RANGE, BURNERS, BURN
- IS UTLIV OUT ITS RECTION DEVICES, FTC.

- Y. ALL RUCCIAL COMPARIES OF RELEVANT HALL BE LIFTED AND LARLING FUNCTIONS LARGEOVER OF COMPARIES AND LARGE AND LARGE OF REVISELY COMPARIES OF AN AREAS, VEHICLE AND COMPARIES OF COMPARIES AND LARGE AND LARGE OF REVISELY COMPARIES OF AN AREAS. APPROVED LETTER ADDRESS APPROVED AND DARLING THE INCIDENT IN WITHOUT AN INCIDENTIAL PROVIDENT OF THE INCIDENT IN WITHOUT AN INFORMATION OF THE INCIDENT IN WITHOUT AN INFORMATION OF THE INCIDENT IN WITHOUT AND INCIDENT APPROVED IN THE INCIDENT IN WITHOUT AND INCIDENT APPROVED IN THE INCIDENT APPROVED INTO APPROVED INTO APPROVED INTO APPROVED INTO APPROVED APPROVED INTO APPROVED APPRO INITIALA TON REGISTRATIONE 18 Al WEND INTERS HALL SENTILIZO WEN A MENALUS OF AN ERS. CONSUCTORS WHETHER INSUE OF MALT MAL, INAL IN METALIZO CONTRICUES MICHAE AN FORMULE FROM TRADIL, FORT TO TERMIN, FORT HALL MECONCINUES IN MACHINELY RECARDED TO BE EXPORED, OF RECARDED TO BE DOLES, CONTRACT THE INCIDENT FOR CLAR PROFILED FROM TO BETALLING MY BLOW WORK AD-CARDINER, IN MENANTERCIPE INCLUSION OF OPPORTE SIDE OF ANL, S TO THEY ARE NOT IN THE MARE UNITING, CAMPER, JACOBER FEDERAL REPORTED AND ARE NOT ALL DE ACCOMMENTE COMMENDER DE ACCOMMENTE PRESENTATIONES VANIES, LA COMPARTE DE ALCOMMENTE DA CAMPERATE DE ACCOMMENTE DE ACCOMMENTE PRESENTATIONES VANIES, LA COMPARTE DE ALCOMMENTE DA CAMPERATE DE ACCOMMENTE DE ACCOMMENTE ACCOMPANY DE ACCOMPANY DE ACCOMPANY DE ACCOMPANY DE ACCOMMENTE DE ACCOMPANY DE ACCOMMENTE DE ACCOMPANY D ADDA OF THE BARE MALL PROVED INC.

Data Section And a Count That And a Table To 9. Street to apport to that we is it for them and the section and the section and appointed and appointed that appointed the section and appointed of the section appointe

IDAMO BY THE AND STRUCT UNLIAS OTHERWISE SHOWN ON PLANS. IF IN DOUBT, CONTROLTING ENGINEER PRICE TO DOUBLING IN ANY WORK.

ON BOUNTING HEARTS TO CEL IND RURPINGED DEVICES AND TO SOTTOM OF DEVICE U.O.K.

Investigation of the anti-tendence of any science with an other submanished contact for investigation and contact and submanished and the submanished and submanished submanished and submanished on the submanished and submanished submanished submanished on the submanished and submanished and submanished submanished and submanished on the submanished and submanished and submanished and submanished on the submanished and submanished

NETALL RELEVANT ANTERNAL FOR IN ETACT ACCORDANCE VETA AVAILANCE MEDIA INCOMENDATION DESCRIPTION // PLOGENIC TWENT THE DESCRIPTION ACCESS & CONTRACT SOCIALITYS, ADVAID THE INCOME MOD TO INFOLUCTION FOR CONTINUOUS CONTRACTS AND ACCESS AND ACC

Contractional Control of Control of Control Control of Control

- HE JUNCTION BOARD LOCKTO ABOVE ACCESSIBLE CRUMCE BALL BE LOCATED NO MORE THAN OF ABOVE CRUMCE LIVEL LABLE ROCK ACCESSIBLE OF BOOK VERY A REPAIRMENT MARKED OF IN ACCORDANCE WITH THE INCREMENTARY AND A PROPERTY AND A PR
- Contraction (Heat Rouge Establish Contraction Carl As Indicated for the Rouge Rouge with a second in Contraction (Language Contraction Heat Contraction States) Contraction (Heat Information Research Heat Rouge Contraction)
 Research Heat Rouge Contraction (Heat Rouge Contraction)
- IF ADDITIONAL CONDUCTOR AND RUN IN THE SAME CONDUCT WITH THOSE RECEASED CONTINUED REALL DRIVER RUL. CONSIDER CONTINUE CONDUCTORS FREI HEIC AND REALLY AND UMBER CONDUCT AS REQUERED FREI HEIC ADDIT AND ANNE CO.

- DIMATIONAL CONFLICTA, ERRORA, AND GRANNENNA NEL CONTONI IN LES CONCIDER NET MARK ITC. FOR ISLIMINET AND THE MARK INFORMATION IN BRITONAURLING OF THE RUIDANCE OF THE RUIDANCE AND RUIDANCE C. FUER OF RESERVE THRE ROOM CUTLETINGUES, AS INCLUDED ON PLAN, INAL, BELICENTED BY DEFINITIONS
 - NO ADVECTOR INVESTIGATION OF ANY CONFLICTS, STREAM, OWERGINS, ECT. AT LEAST THE DAVE THIS TO BE DATE, TO BE DATE,
- NOW THE REPORT FOR WALL WERE TRED SPACED INCOMES AND A PROVIDE NO. AND TO CRAFTER OF DRVICE FUCTS AND FOLING METWEEN D CO. WHEN CONFECTS AND POLICE METWOOD DOWNERS, Service, on these of Incurrence of the Confects of the Confects of Concentration of BARLANELY ACTIVE ACHIEVED AND AND A CONCENTRATION.
 - IN ORACION FROM SPECIFICATIONS OF FLIMS REQUIRES FROM INSTITUTIONS, FROM THE S
 - IN WRITES NO. ATTR TWO THE SAME PRICE TO THE BO GATE. THE WAR AN OPPO OF HOLATE, OF MOVENTS BY UT HO OF WALFACTURES HITS
 - AND OF MALE AND A REAL AND A ALL POLIFICITY BRALL MITPHEN

GENERAL NOTES (POWER)

- THEN CLASSING CREATER HIS HOMEIN. BACK MANCH CREAT SHALL BE MICHIED WITH A CONDUCTOR. SECURITO HIS TWO HOMEING CONDUCTORS INVAL BE CONSISTED AND HAD IF ADDITIONAL CONDUCTORS AND RUN IN THIS AMIN'S CONDUCT WITH THOSE INDUCKTION, CONTRACTOR INVELLORS CARE INT CARE IN IS CONDUCTORS AND HIR KICCIDE IN FROM AND UNDER CONDUCT AN INCLUSION PROVIDED TO AN INCLUSION
- THES IN MIC 100/2/04 CONCUTS SHATING & CONSIGN NO MUTWIN MANOY CIRCL
- DENTRY THE INVESTIGATION OF CONTRACTORS IN A REAL AND A

ELECTRICAL DEMOLITION NOTES:

- A SOTTO LIKE ROCKTETERS FOR RENOVAL (JON, WID THE ROLE LIKES HOCKTE EXETING THE TO RENAM
- C. CONTRACTORIE PROVIDERS TO SCANY WAT OF THE WORK RECEIVED HEREON EVALUATE THE ART AND DETERMINE TO HIS INTERACTOR THAT THEY MAY COMPLETE ALL WORK REQUISED FOR THE SE WHICH HE PROPOSES.
- THE CONTRACTOR BALL MATTAIN THE CONTRACTOR POSITING RELETS THAT CONTRACTING RELEASED THAT ARE TO REMAIN WHEN CONTRACTOR BALL MATTAINAL DEACH OF CONTRACTOR THAT CONTRACTOR OF RELEASED TO REMAIN ARE LET TO THE CONTRACTOR REPORT OF THE CONTRACTOR CONTRACTOR OF RELEASED ARE DEACHDONED TO REMAIN ARE LET TO THE CONTRACTOR REPORT OF THE CONTRACTOR OF RELEASED THAT CONTRACTOR OF RELEASED TO REMAIN ARE LET TO THE CONTRACTOR REPORT OF THE CONTRACTOR OF RELEASED THAT CONTRACTOR OF RELEASED TO REMAIN ARE LET TO THE CONTRACTOR REPORT OF REMAINSTRACTOR OF RELEASED TO REMAIN ARE LET TO
- CONTRACTOR BLALL MICHING REPAIL ALL
- CARAL BALAL VACTED BY PROJECT TOB OF THE
- A PROVIDE ALL PROVIDE THE CONTRACTORS WORK WALL AS INCODED WITH MAY THE WRITTEN HIM NAME DESCRIPTION AND ADDRESS OF THE ROOM WARE OF HUMBERS FROM THE DESCRIPTION CONTRACTOR AND ADDRESS AND THE REAL WAS THEN. ROOM WARE THE CONTRACTOR ADDRESS AND ADDRE ADDRESS AND ADDRESS UPT OVER CROLT MEMORY AND AND A SHOULD TO OVER AND ME WALLS AS ANALS IN THE FIGURE
- THE RECEIPTION OF THE CONDUCTORS FOR OWNERS (PETABLE) FT. BRIES REPORTS BACK TO RESIDE. ON NOT LONG CONTRACTOR BALL MOTOR HIS BRIES ANY REPORT MULTI PLODE OF CRUMCH WHERE DRUCK DATE OF THE REAL PROTOK HIS PROVIDENT PROVIDENT CONTRACT. NAME,


INTERCOMPANIES INTERCOMPANIES AND THE DESCRIPTION ADDRESS ADDRE ADDRESS ADDRES

Ť

-80.80


F

3-8



TABLED NOTES TO HER SCIENCED EVEL & ROUTE TO DEFINITE THE

creX

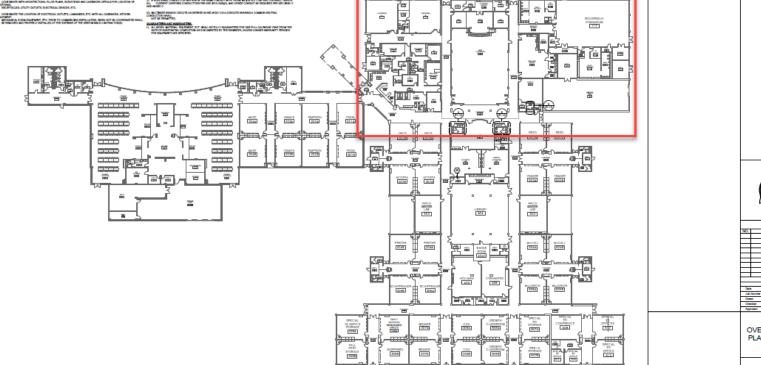

O CATERALL POWER FLOOR PLAN-LEVEL OF

Plan Indicating New DAEP/EPIC Area

BARBERS HALL

∯

E1.00

Press Nation

cre

ACTINUITS TO ANOD CONFLICT WITH ANY OTHER BUILDING INTERNAL WITHY MARK COTICUE, ELECTICAL, TECHNICARY AND ELECTICAL WATER LISCUENT INCLUSION INCLUSION IN MICH.



cre New Storefront Wall – Room Side – For Increased Supervision






New Storefront Wall Complete Corridor Side – Improved Line of Sight for Supervison



BOND 2020 – MS North Girls Locker Room Renovation

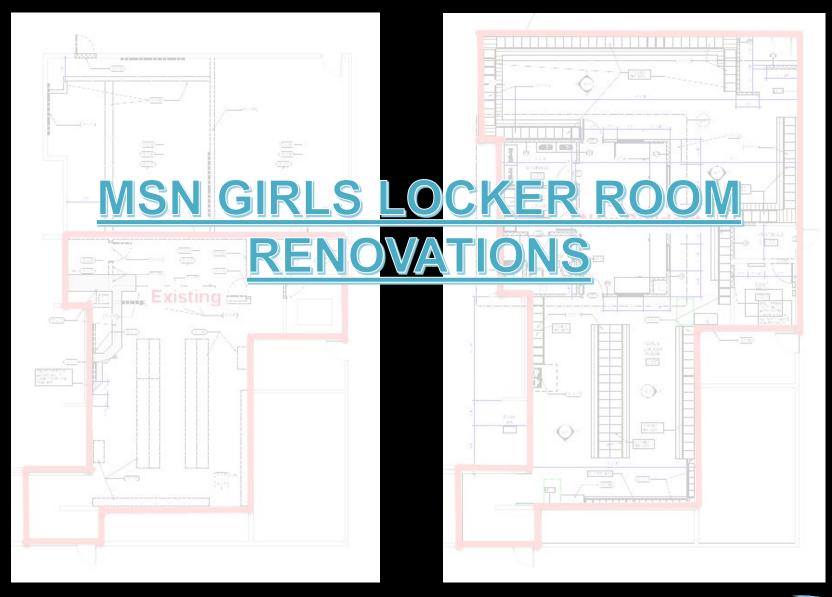



cre₈

Plan of Existing and New Buildout



BOND 2020 – MS North Girls Locker Room Renovation

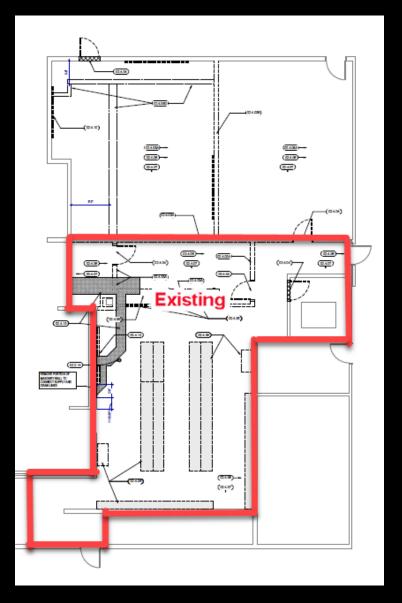

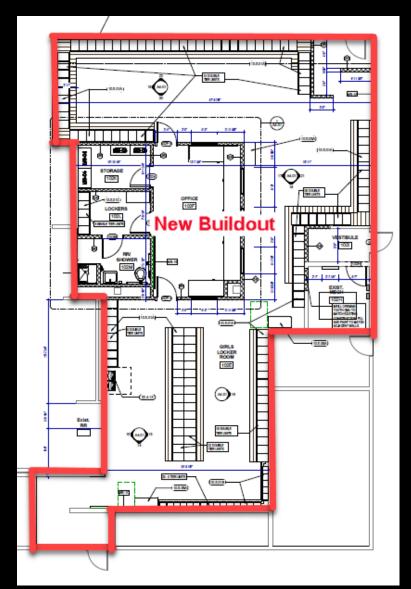




Plan of Existing and New Buildout




BOND 2020 – MS North Girls Locker Room Renovation: Completion 8-3-22

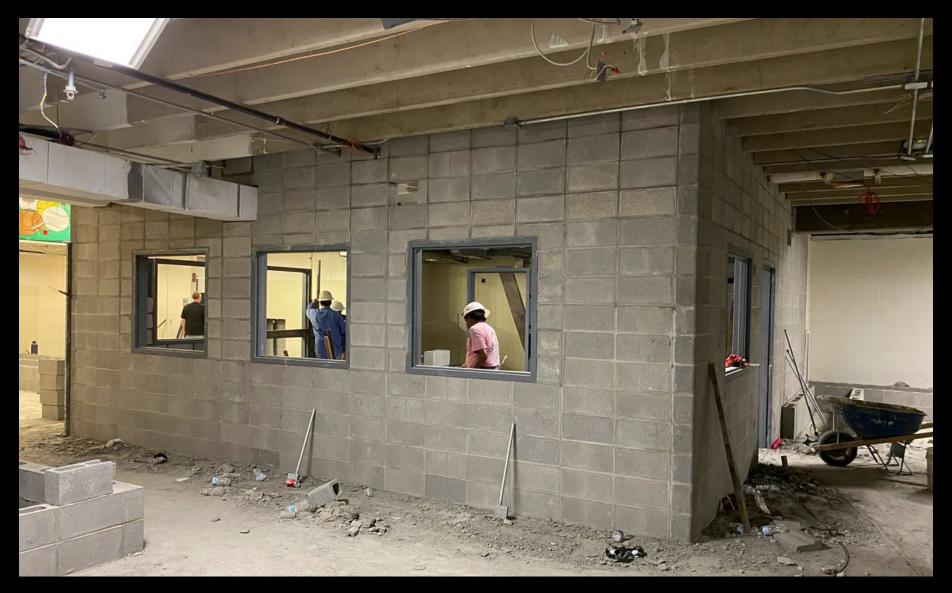

Cre8 New Coaches Office – CMU and Window Frames in Progress



BOND 2020 – MS North Girls Locker Room Renovation

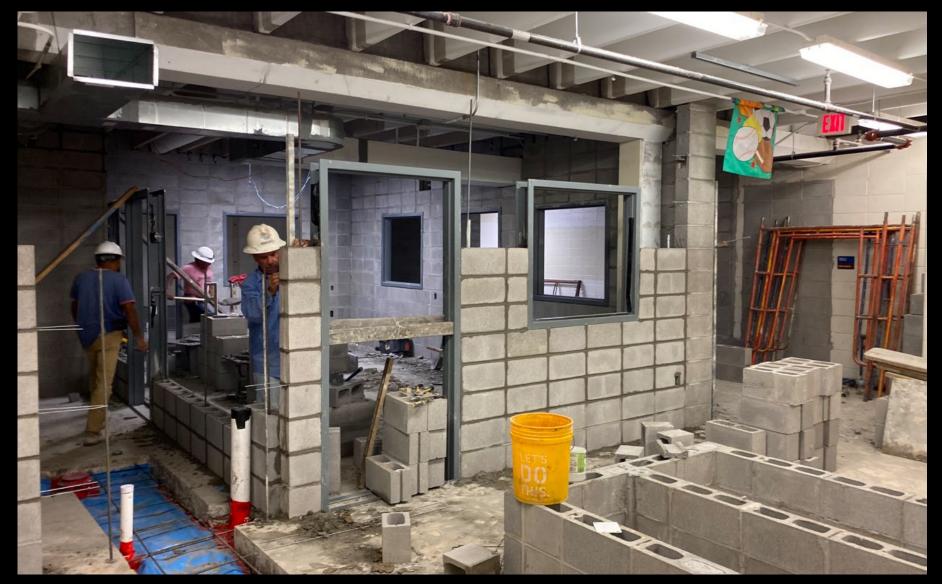

cre8 New Coaches Office – CMU and Window/Door Frames in Progress



New Fuel Station and Work Package No. 01 – Paving & Fencing



Site Plan – Becky Nelson Transportation Center

Completion of WP#1 & Fuel Station 8-05-22

creX



BOND 2020: <u>Becky Nelson Transportation Center Renovation Project</u> New Fuel Station and Work Package No. 01 – Paving & Fencing



cre8

Site Plan – Becky Nelson Transportation Center Completion of WP#1 & Fuel Station 8-05-22



New Fuel Station and Work Package No. 01 – Paving & Fencing



Site Plan – Becky Nelson Transportation Center

cre₈

Completion of WP#1 & Fuel Station 8-05-22



BOND 2020: Becky Nelson Transportation Center Renovation Project



cre 8 Concrete Saw Cut & Sub Grade Prep In Progress for New Fuel Station



BOND 2020: Becky Nelson Transportation Center Renovation Project



cre₈

Concrete Saw Cut & Sub Grade Prep In Progress for New Fuel Station (Taking proposals for WP#2 7/7/22



BOND 2020 – Eagle Stadium New Band Bleachers: Completion 7-15-22




New Bleacher Plan Layout in North D-Zone of Track



cre₈

BOND 2020 – Eagle Stadium New Band Bleachers: Completion 7-15-22

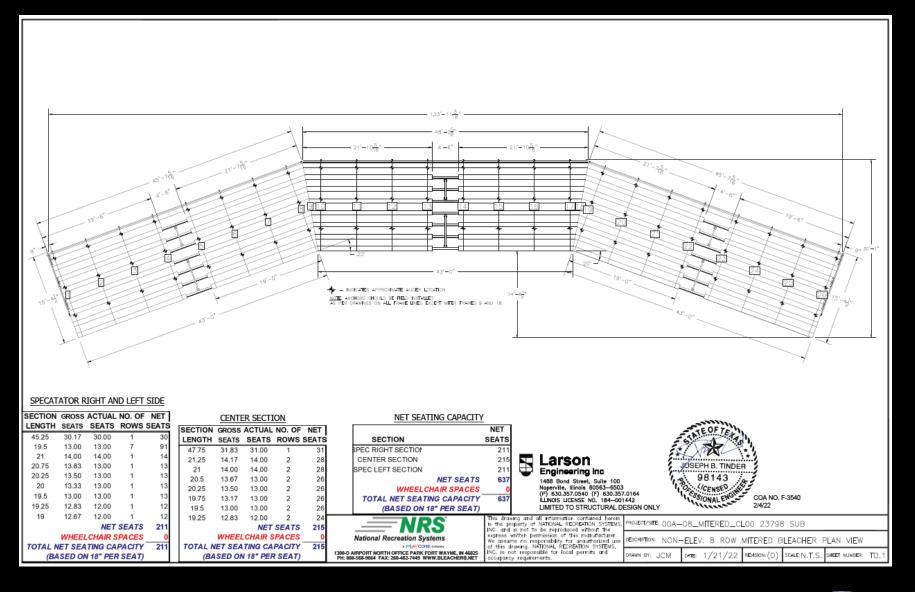

New Bleacher Plan Layout in North D-Zone of Track



cre₈

BOND 2020 – Eagle Stadium New Band Bleachers



cre₈

Bleacher Assembly in Progress



BOND 2020 – Eagle Stadium New Band Bleachers



End Zone View – Bleacher Installation in Progress

cre₈



BOND 2020 – Eagle Stadium New Band Bleachers




End Zone View – Bleacher Installation in Progress

cre₈



BOND 2020 – Baseball/Softball Bleacher Expansion: Complete 7-29-22

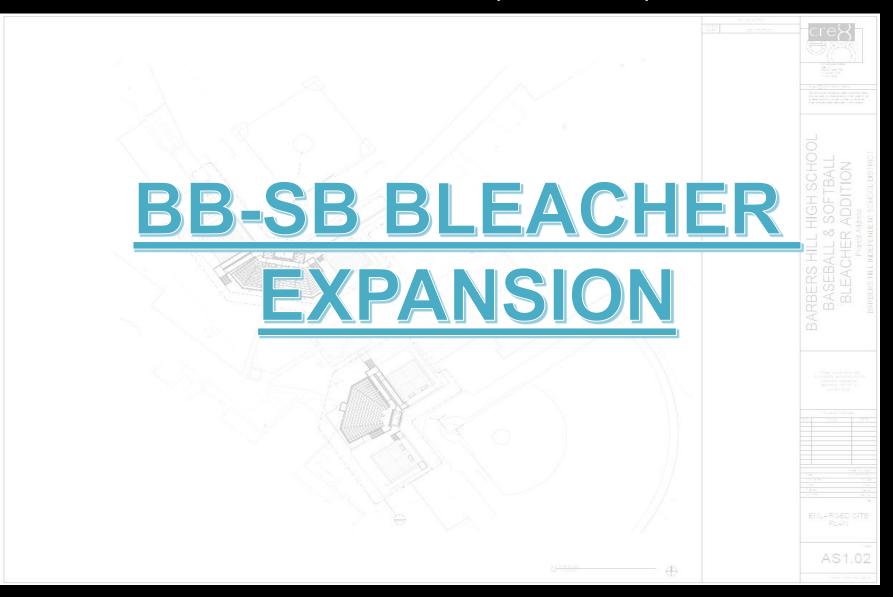


BB-SB Site Plan Indicating New Bleacher Locations

cre



BOND 2020 – Baseball/Softball Bleacher Expansion: Complete 7-29-22

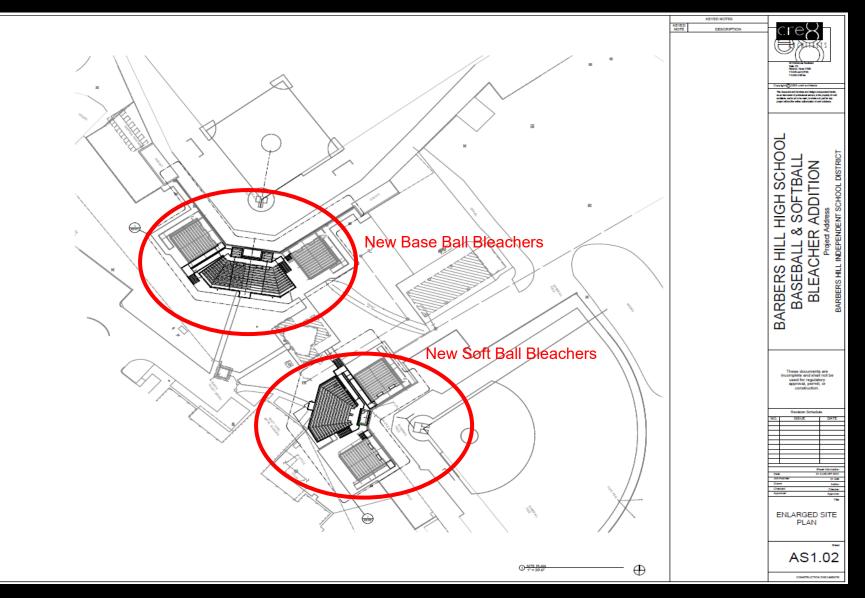

BB-SB Site Plan Indicating New Bleacher Locations

cre₈



BOND 2020 – Baseball/Softball Bleacher Expansion



cre8 Soft Ball Pavement & Foundations Complete Ready for Steel Erection



BOND 2020 – Baseball/Softball Bleacher Expansion



cre₈

Softball Bleacher Installation in Progress





cre₈





cre₈





cre₈






cre₈









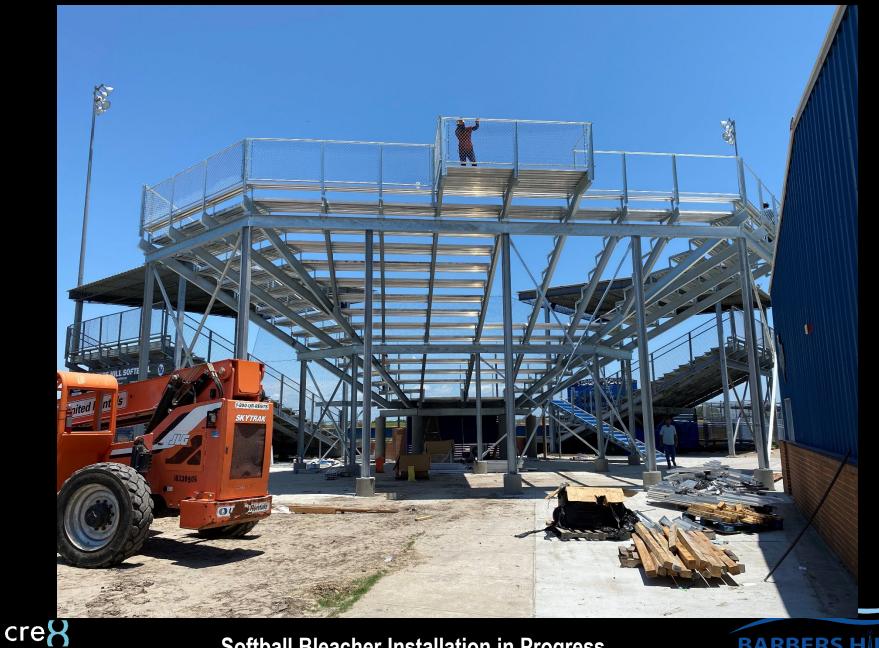

























Base Ball Bleachers Installation In Progress Near Complete

cre₈





cre<mark>8</mark>



BOND 2020 - INTERMEDIATE SCHOOL NORTH - SITE PLAN

INTERMEDIATE SCHOOL

NORTH

INTERMEDIATE SCHOOL NORTH

cre₈



BOND 2020 – INTERMEDIATE SCHOOL NORTH - SITE PLAN




INTERMEDIATE SCHOOL NORTH

cre₈



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN

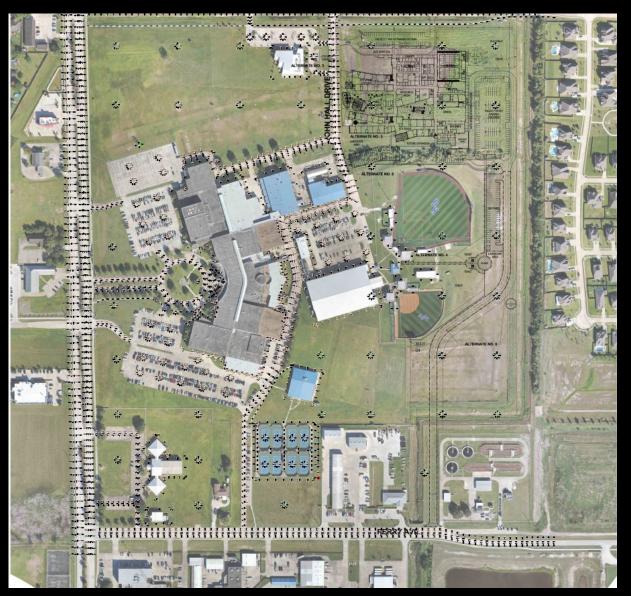

cre₈

Intermediate School North Site Plan





cre₈

BB Field – Ticket Booth & Parking Complete





cre8

Parent Drop Off Canopy & Drive, Faculty and Visitor Parking Complete





cre 8 Mechanical Service Yard and Associated Pavement Compete





Cre8 Classroom Wings – Landscape and Perimeter Fencing in Progress





CreCIassroom Wings & Courtyard – Landscape and Perimeter Fencing in Progress





cre₈

Bus Drop-Off and Front Entry Off Wilburn Ranch Road





Aerial View of Faculty Parking, Parent Drop Off Drive Canopy, Gyms, Administration Area, Bus Drop Off and Main Entrance off Wilburn Ranch RoadBARBERS HAL





Aerial View of Pumping Concrete at Central Learning Courtyard





Cre8 Aerial View of Completed Concrete at Central Learning Courtyard





cre₈

Central Learning Courtyard Pavement and Landscaping In Progress





Cre8 Landscaping In Progress – Planted Trees Next to Front Entry





cre8

Library - View to Exterior Court Yard





CreX Library Kiva Ceiling Grid and Panel Installation in Progress





Cre Staging Furniture Deliveries in Cafeteria – Ceilings, Flooring Complete





Delivery, Arrival and Mobilization in Cafeteria Area

cre₈





cre₈

Elevators are Complete and Fully Operational





Cre8 All Administration Offices are Near Complete – Furniture Deliveries in Progress



BOND 2020 - INTERMEDIATE SCHOOL SOUTH - SITE PLAN

INTERMEDIATE SCHOOL SOUTH



cre8 INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN




INTERMEDIATE SCHOOL SOUTH

cre₈



BOND 2020 - INTERMEDIATE SCHOOL SOUTH - SITE PLAN

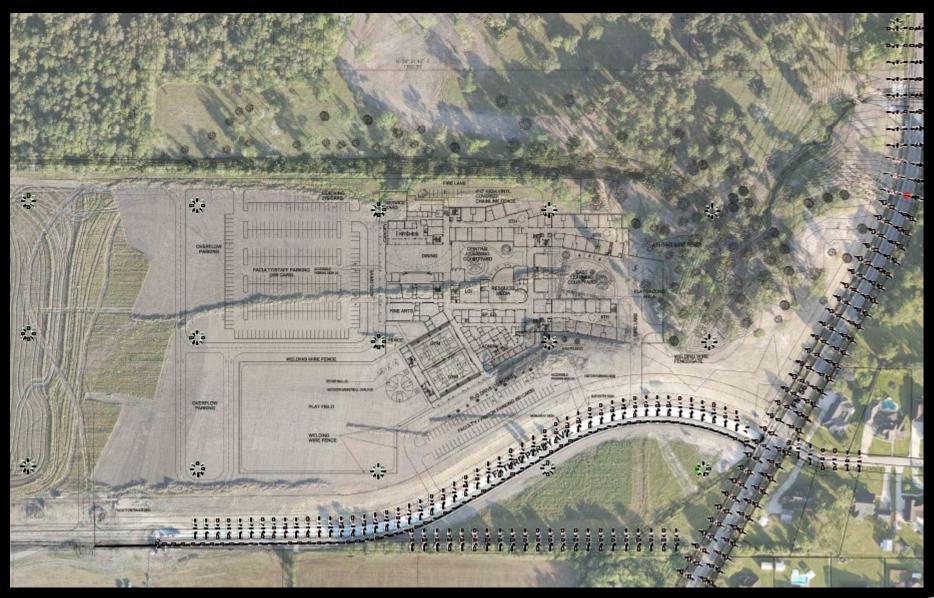

cre₈

Intermediate School South Site Plan







Aerial View Looking East – Play Area, Concrete Walks, Perimeter Fencing and Sub Grade Complete: Landscaping in Progress





cre8

Car-Rider Drop Off Pavement and Canopy at Cafeteria Complete: Landscaping in Progress





Cre8 Classroom Wings: Exterior Learning Courtyards in Progress





cre8

Aerial Plan View of Central Learning Courtyard in Progress





cre₈

View of Exterior Learning Courtyard from Art Classroom





Cre Aerial : Main Entry and Bus Drop Off Canopy and Faculty/Visitor Parking






cre8

Widening of Gill Parkway in Progress – Four Lanes In Front of School Property, Traffic Light is Also Planned at FM 565



CreR Furniture Staging in Cafeteria – Wall Graphics in Progress, Ceilings & Flooring Complete



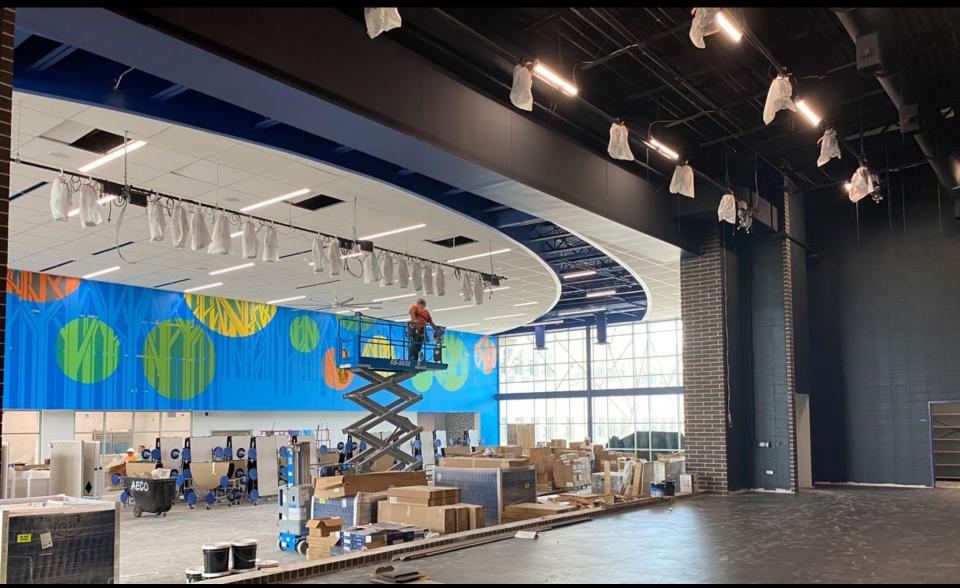

cre₈

Cafeteria Dining View From Stage





cre₈

Typical Restrooms and Drinking Fountains, Near Complete





CreR Typical Science Classrooms Complete, Furniture Installation in Progress





cre₈

Typical Classrooms Complete, Furniture Installation in Progress





cre₈

Typical Classrooms Complete, Furniture Installation in Progress





CreR Typical Collaboration Corridor Flooring, Ceilings & Wall Panels Complete








Building Interior Wall Graphics in Progress in All Areas




BOND 2020 – FACILITY PRESERVATION – PAINTING THE ORIGINAL SECTION OF VISITOR BLEACHERS AT EAGLE STADIUM

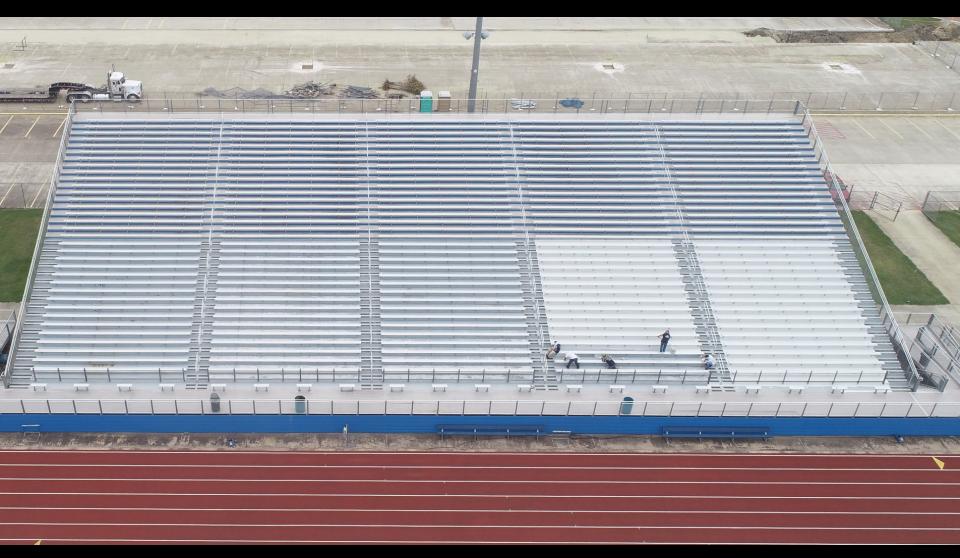

cre **PREP & PAINTING OF EAGLE STADIUM VISITOR BLEACHERS**



BOND 2020 – FACILITY PRESERVATION – PAINTING THE ORIGINAL SECTION OF VISITOR BLEACHERS AT EAGLE STADIUM

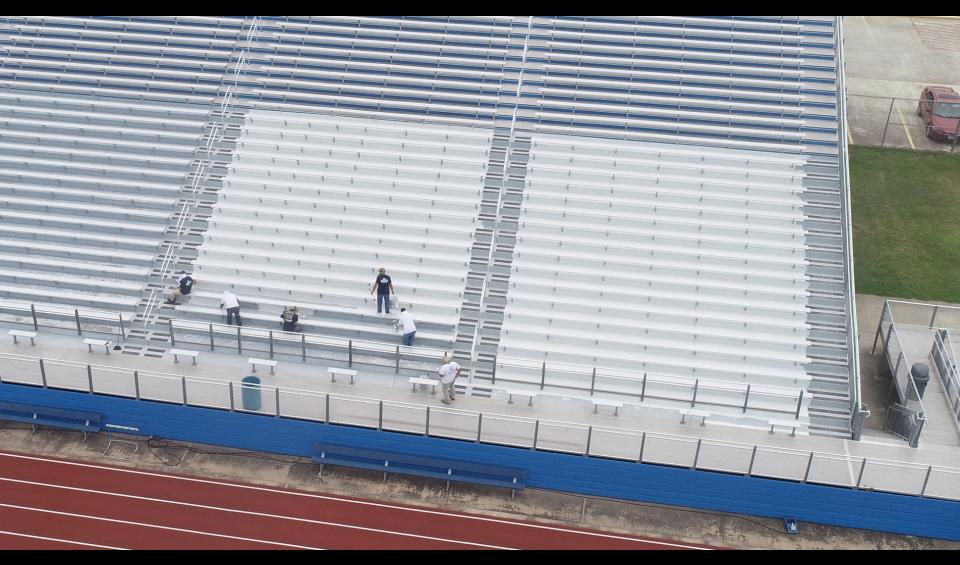

cre **PREP & PAINTING OF EAGLE STADIUM VISITOR BLEACHERS**



