

Crown Point Community School Corporation Construction Projects

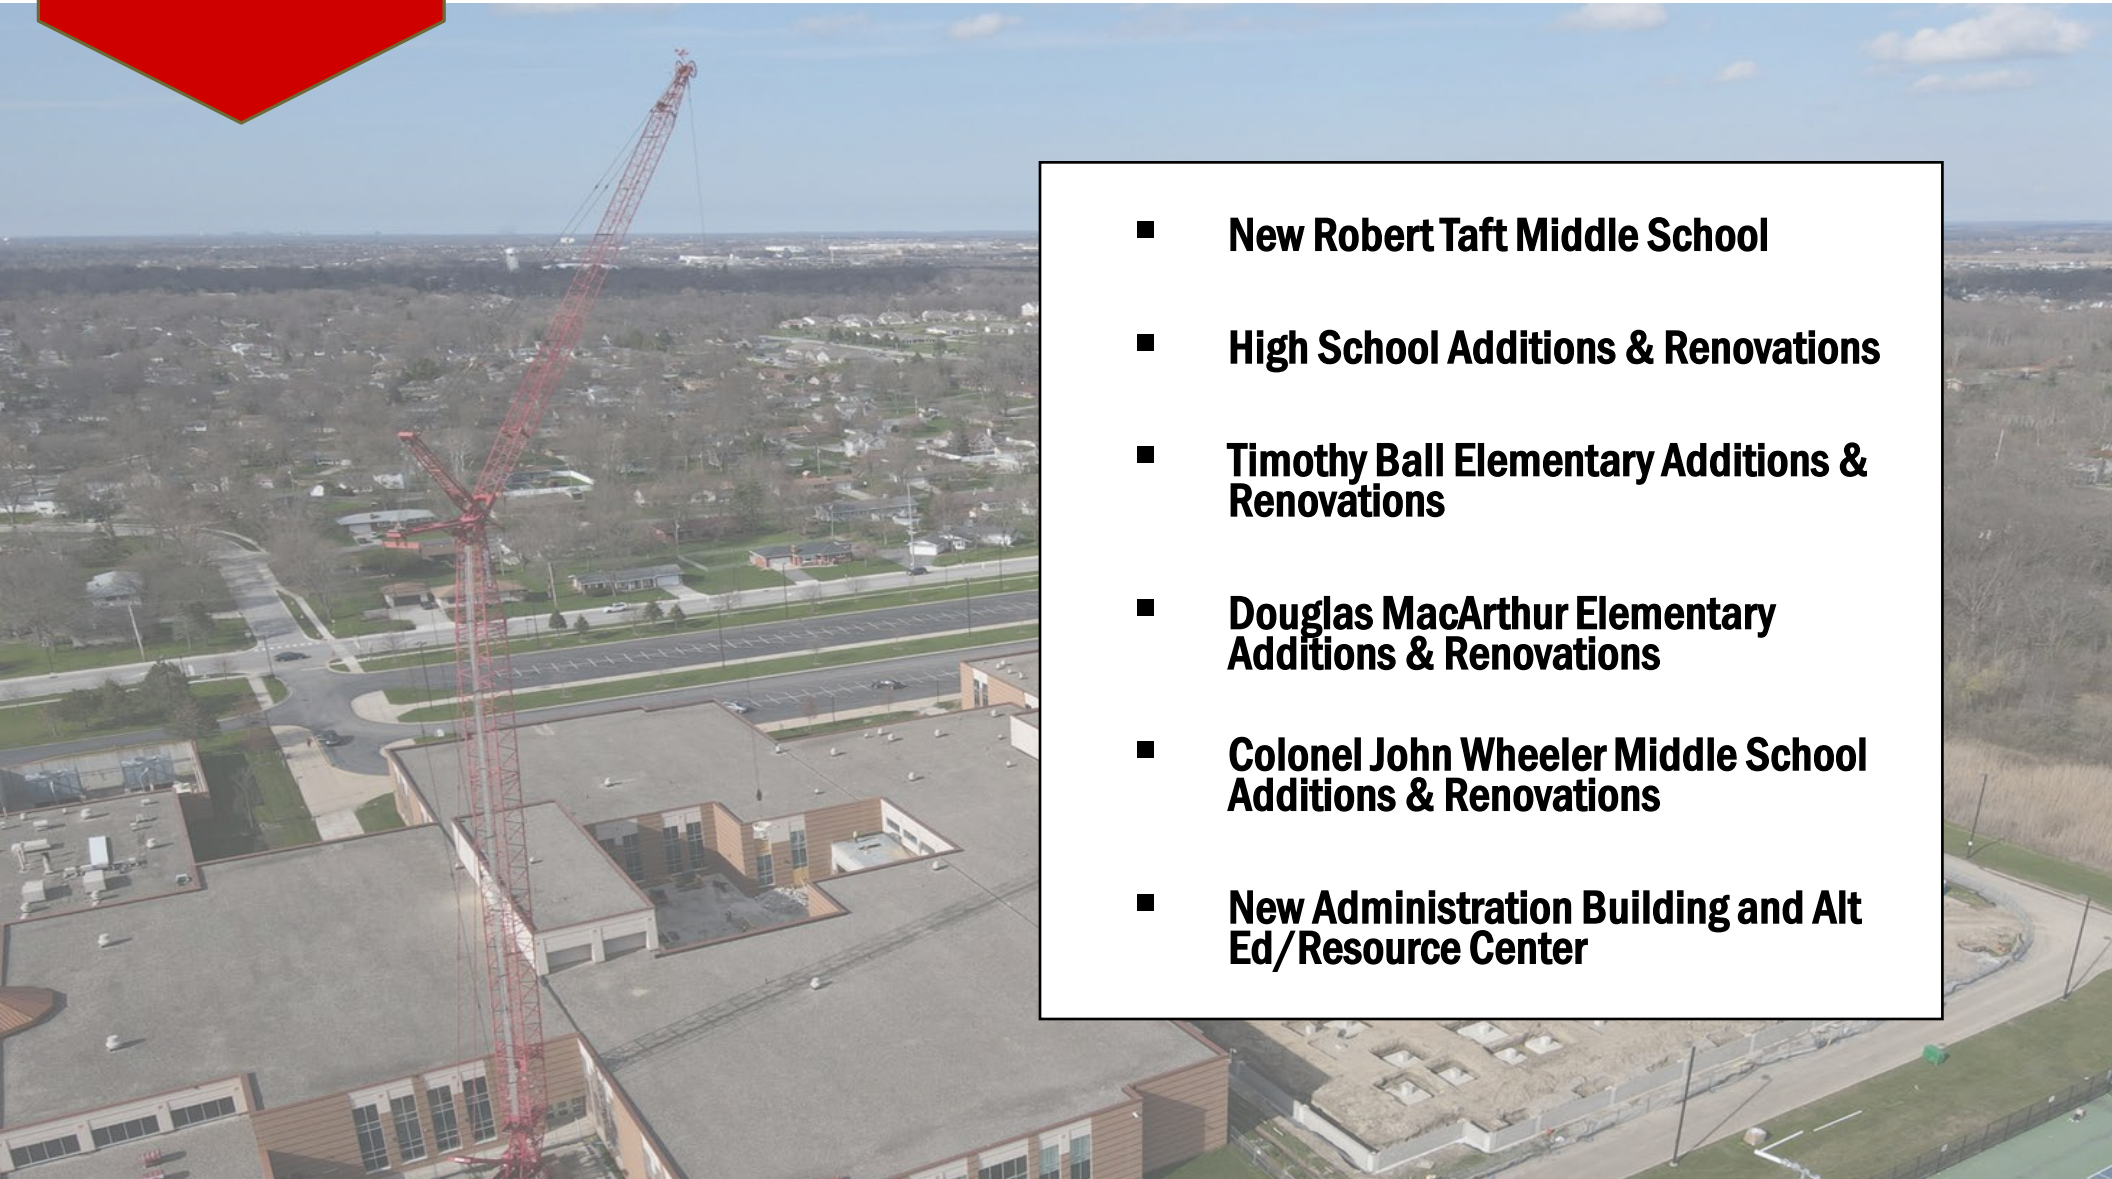
Board Report July 25, 2022



Table of Contents

Crown Point Community School Corporation Construction Projects

Board Report July 25, 2022

- 
- **New Robert Taft Middle School**
 - **High School Additions & Renovations**
 - **Timothy Ball Elementary Additions & Renovations**
 - **Douglas MacArthur Elementary Additions & Renovations**
 - **Colonel John Wheeler Middle School Additions & Renovations**
 - **New Administration Building and Alt Ed/Resource Center**



Progress Photographs



New Robert A. Taft Middle School:

- Completed exterior sheathing of academic wing
- Completed roofing of academic wing
- Continued pouring slab-on-grade in academic wing
- Continued interior metal stud walls in academic wing
- Continued above ceiling piping in academic wing
- Continue pouring slab on grade in academic wing
- Began setting structural steel in auditorium
- Began brick veneer on main gymnasium



Auditorium Structural Steel



Progress Photographs



Academic Wing Hallway

New Robert A. Taft Middle School:

Next Four Weeks

- Complete pouring slab on grade in academic wing
- Complete roofing of administration/cafeteria area
- Continue interior metal stud walls in academic wing
- Continue above ceiling piping in academic wing
- Continue grading football fields
- Begin sheathing interior walls in academic wing



Progress Photographs



Roof Structure Removal

High School Additions & Renovations:

- Completed ductwork in satellite kitchen area
- Unit B roof structure removed for second story Unit A (classroom addition) tie in
- Completed boiler installation
- Completed CMU foundations for performing arts addition
- Installed new scoreboard
- Continued hanging mechanical piping in athletic areas running to new athletic addition
- Began re-roofing of auditorium



Progress Photographs



New Scoreboard

High School Additions and Renovations:

Next Four Weeks

- Continue re-roof work of entire building
- Pour slab-on-grade and slab-on-deck for classroom addition
- Begin setting structural steel for new classroom addition
- Begin setting structural steel for Unit F (courtyard infill)
- Begin setting structural steel for athletic addition
- Begin interior metal stud walls of Unit F



Progress Photographs



Classroom Addition

Timothy Ball Additions & Renovations:

- Poured concrete curbs
- Completed load bearing CMU walls for classroom addition
- Completed all underground site utilities
- Began structural steel for classroom addition
- Began brick veneer on classroom addition
- Began paving binder of West parking lot
- Began digging footings for East additions



Progress Photographs



East Side Sitework

Timothy Ball Additions and Renovations:

Next Four Weeks

- Complete detailing structural steel for classroom addition
- Complete digging footings for East additions
- Complete brick veneer on classroom addition
- Pour slab-on-grade for East additions
- Begin interior metal stud framing in classroom addition
- Begin roofing of classroom addition
- Begin electrical work in classroom addition



Progress Photographs



Classroom Addition Building Pad

Douglas MacArthur Additions & Renovations:

- Completed demolition of Southeast parking lot
- Installed underground storm structures and piping in Southeast parking lot
- Established and grading building pad for new classroom addition
- Continued demolition of front office, administration, clinic, and music rooms



Progress Photographs



Southeast Parking Lot

Douglas MacArthur Additions and Renovations:

Next Four Weeks

- Install new Nipsco service feed
- Pave Southeast parking lot
- Continue interior CMU walls and patching
- Continue excavation and grading of East detention pond
- Continue work on all above ceiling mechanical piping feeding new classroom addition
- Begin to pour footings for new classroom addition



Progress Photographs



Auditorium Addition and West Pond

John Wheeler Additions & Renovations:

- Completed demolition of studio/media area
- Completed interior metals studs in studio/media area
- Completed interior CMU walls in clinic area
- Continued sitework for new parking lots
- Continued digging and grading West pond



Progress Photographs



New South Parking Lots

John Wheeler Additions and Renovations:

Next Four Weeks

- Complete West pond
- Complete drywall in studio/media area
- Complete drywall in clinic area
- Complete ceiling tiles in studio/media area
- Complete ceiling tiles in clinic area
- Complete painting of studio/media area
- Complete painting of clinic area
- Begin site utilities



Progress Photographs



New Administration Building and Alt Ed/Resource Center:

- Mobilized
- Completed demo of existing parking lot
- Completed demo of existing underground utilities
- Completed building pad
- Began earthwork for back drive

New Administration Center Sitework



Progress Photographs



New Administration Building Pad

New Administration Building and Alt Ed/Resource Center :

Next Four Weeks

- Complete earthwork for back drive
- Install new Nipsco utility poles
- Begin installing new storm system
- Begin digging footings
- Begin pouring foundations
