

BOND UPDATE #167

8.5.22

Here's what is going on with our bond projects. Great things are happening! Enjoy!

1. Thank you to everyone who visited the Bond Oversight Committee display during Old Settlers' Days last weekend.
2. Work on the FHS campus has continued to progress during the past week. Some of the highlights are outlined below:

Athletic Wing

- Wall paneling installation began this week in the Main Gym while sound panel installation continues. Wall pad installation has also begun.
- Installation of the rubberized flooring was completed this week in the P.E. room.
- Wall board installation in the Auxiliary Gym has begun.
- Brick sealer application work continues on the exterior of the building.
- Plumbing fixtures continue to be installed this week.

Academic Wing & Commons

- Great progress continues in the main boiler room in the Commons! The boilers, hot water heaters and hydroponic water systems are expected to be installed by the end of August.
- Bathroom tile installation continues on the first floor.
- Ductwork welding is underway in the Culinary Arts room.
- Whiteboards and tackable wall systems (AKA bulletin boards) are being installed.
- Mechanical and electrical wall trim out – which is putting the finishing touches on the wall switches and receptacles – has begun.
- Interior door and hardware installation on the first floor is ongoing.
- The Academic Wing is scheduled to be occupied after Winter Break this school year in early 2023.

CTE Village


- Crews installing the pre-engineered metal Agricultural Science building in the CTE Village made great progress this week.
- Underground gas line installation is underway this week in this area.

Old Gymnasium

- Demolition of the Old Gym is going well. The process is expected to be complete near early September.

Site Work

- Grading and forming for sidewalks started this week on the east side of the Athletic Wing.
 - The underground stormwater system is being completed this week at the south parking lot.
3. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
 4. Below is the FHS project timeline as of June 30. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

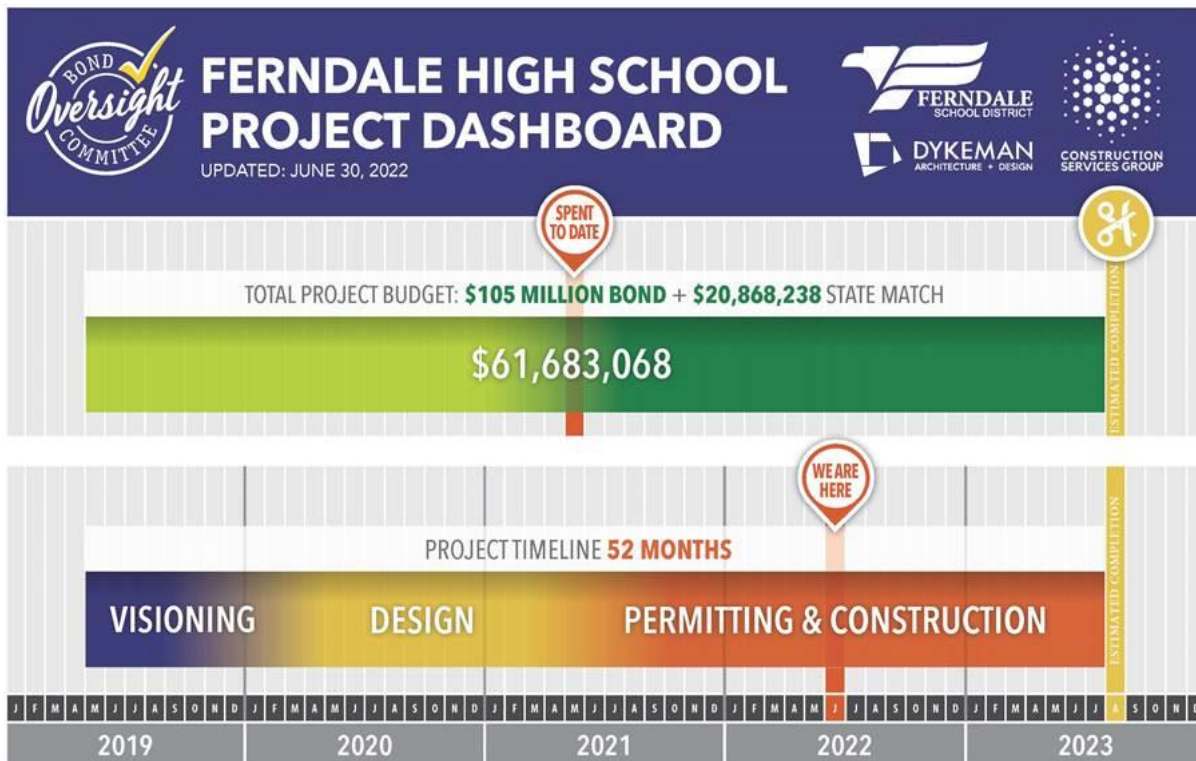

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



The metal framework for the Agriculture Science building went up this week



Demolition of the Old Gym is moving along very quickly



Installation of the new PE room's rubberized Mondo flooring



Bathroom tile installation in the Academic Wing



Fume hoods are being installed in the science labs



A temporary ramp is being built to allow full access to the new Athletic Wing
