

BOND UPDATE #168

8.12.22

Here's what is going on with our bond projects. Enjoy!

Kristi

1. Work on the FHS campus has continued to progress during the past week. Some of the highlights are outlined below:

Athletic Wing

- The wall paneling and sound absorbing panels have been completed and the gym is ready for bleacher installation next week.
- Wall pads have been installed.
- The wallboard is mostly hung in the Auxiliary Gym, and taping and finishing work is ongoing. Wall paint should get started there over the next week or so.
- Brick sealer application work continues on the exterior of the building.
- Plumbing lines are now being filled with water and tested. Fixtures are starting to come online in this area.
- Concrete floor grinding and polishing is coming along nicely.

Academic Wing & Commons

- Light fixtures are now being installed on the first floor. This is always a good indication that the area is getting close to completion!
- Welding of ductwork is underway in the culinary arts room and should be complete soon.
- Crews are making good progress on whiteboard and tackable wall installation.
- Mechanical and electrical wall trim out is ongoing and looking good.
- Interior doors and hardware installation is ongoing.

CTE Village


- All three buildings – Greenhouse, Agricultural Science and Aquaculture – now have completed structures and are ready for roofing and siding. This work will occur over the next couple of months.

Old Gymnasium

- The gold gym is now gone. The athletic building behind the gym should be removed over the next week or two.

Site Work

- Crews are grading, forming and pouring the sidewalks on the north side of the new gym this week, and this work will likely wrap up next week. These sidewalks will provide access to the gym this fall.
 - Work on the underground storage detention system began this week on the north side of the new gym. This system is under the new bus loops and must be completed before work on the bus loops begin.
2. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
 3. Below is the FHS project timeline as of June 30. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

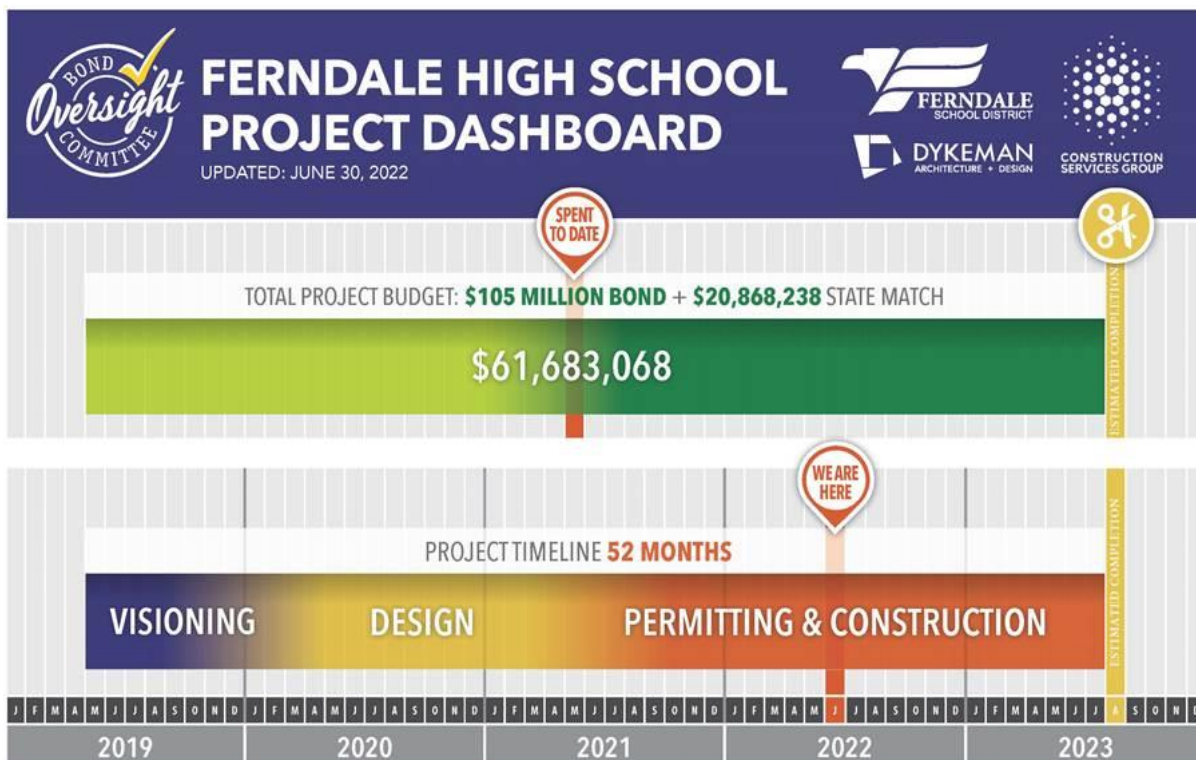

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



Wall padding, paneling and soundboard in the new gym. The large uncovered spot is where the new bleachers will go.



Concrete floor grinding and polishing in the corridor between the new gym and the P.E. room



Auxiliary Gym wallboard in progress



Agricultural Science building framework is now complete and ready for roofing and walls



The old gym has been completely torn down



Sidewalks being poured on the north side of the new gym

