

# BOND UPDATE #169

8.19.22

Here's what is going on with our bond projects.

Enjoy!

Kristi

1. Cornerstone General Contractors recently guided us through another video tour of the FHS campus construction! To see this bond update's accompanying video, click here: <https://youtu.be/tWcmlHvVjy0>
2. Work on the FHS campus has continued to progress during the past week. Some of the highlights are outlined below:

## Athletic Wing

- Bleacher installation in the Main Gym started this week and is nearly complete. We are very close to wrapping up with the gym.
- Brick sealer was applied this week. The exterior of the building is looking good!
- The wallboard is hung in the Auxiliary Gym. Taping and finishing was completed there this week, and the area is ready for next week's painting.
- Plumbing fixtures are now functioning and were part of the health department's inspection this week. Final approval was granted by the department for students to move in at the start of the school year.
- Removable batting cages will be installed in the P.E. Room next week.
- Final ceiling tiles are being installed throughout the wing.

## Academic Wing & Commons

- Light fixture installation was completed on the first floor. Crews will get rolling on the second floor next week.
- The Culinary Arts classroom is now having cabinets installed. Other final finishes will begin soon.
- Whiteboard and tackable walls have been installed on the first floor and crews are making their way across the second floor.
- Mechanical and electrical wall trim out is ongoing and making good progress.
- Final ceiling tile installation will begin next week on the first floor.
- Crews are in the process of starting up the air handling units and water pumps. Next week, the hydronic heating water will be energized and testing will begin.
- Final finishes are now in progress on all three levels of the Academic Wing.

## CTE Village


- All three buildings – Greenhouse, Agricultural Science and Aquaculture – now have completed structures and are ready for roofing and siding. This work will occur over the next couple of months.

#### Old Gymnasium

- The debris from the old Gym has now been hauled off-site and demolition of the old Athletic building has begun. This process should be complete by the end of next week.

#### Site Work

- The sidewalks on the north side of the Athletic Wing are now complete and ready to be used by students and staff when school begins.
  - The underground stormwater detention system excavation is now complete. On one day during the excavation, dump trucks with trailers made 116 trips hauling dirt. In total, about 500 trips were made to complete the excavation.
3. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
  4. The Bond Oversight Committee will hold their next regular meeting on Tuesday, August 23 at Mountain View. The Committee will discuss feedback from their recent Old Settlers Days display, maintenance and security, and more.
  5. Below is the FHS project timeline as of June 30. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

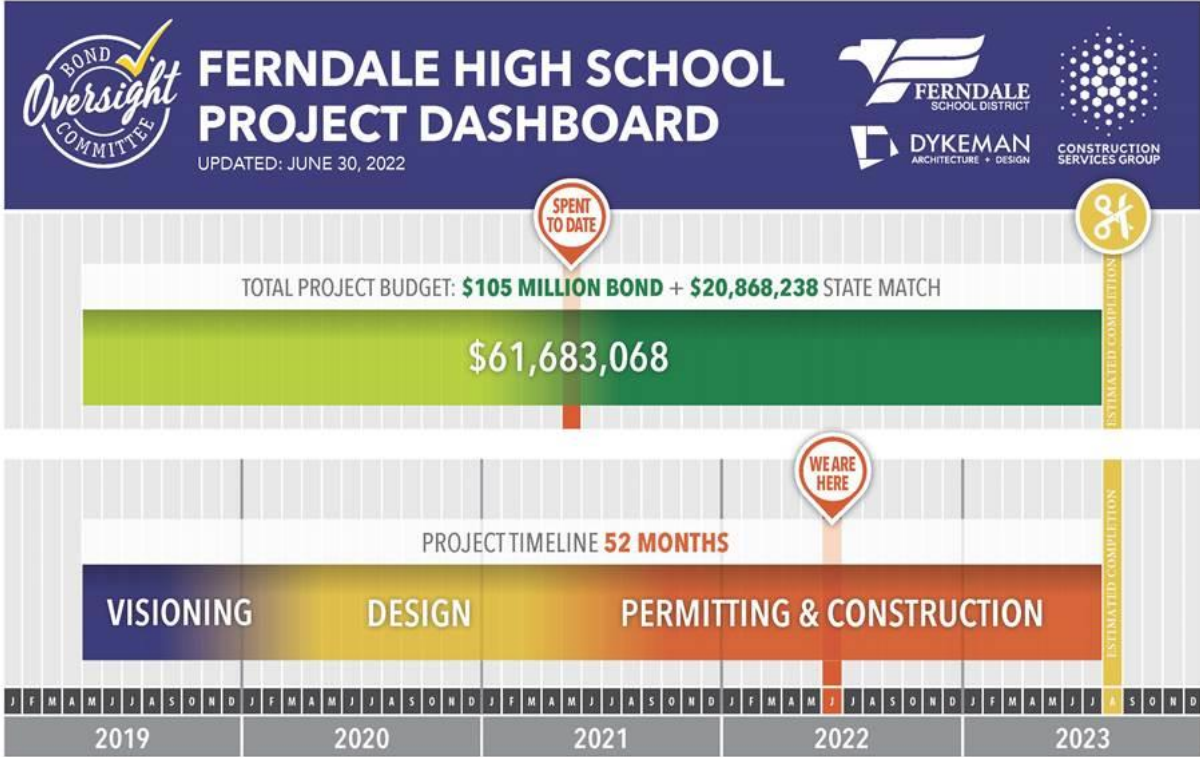

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



**Bleacher installation in the Main Gym**



**High-density sports equipment storage system being assembled**





**Bathroom stall installation in the locker room**



**Finished flooring in the sports medicine room**



**Cabinet installation in the Academic Wing**





**Underwater stormwater detention system excavation on the north side of the Athletic Wing**
